

		2021		2021		2021		2021		2021		2021		2021		2021		2021																		
		January		February		March		April		May		June		July		August																				
		03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
WORKS PROGRAMME (01V3)		672	02-Mar-20	11-Jun-22	361	01-Dec-20 A	21-Feb-22																													
DESIGN SUBMISSION & APPROVAL		672	02-Mar-20	11-Jun-22	250	01-Dec-20 A	06-Oct-21																													
GENERAL		375	02-Mar-20	09-Jun-21	242	01-Dec-20 A	25-Sep-21	GENERAL																												
Design Memorandum		0	02-Mar-20	02-Mar-20	138	08-Jan-21 A	29-Jun-21																													
A229426091	Design Memorandum - 4th Review	0			5	08-Jan-21 A	13-Jan-21 A	Design Memorandum - 4th Review																												
A229428882	Design Memorandum - 5th Sub	0			5	14-Jan-21 A	19-Jan-21 A	Design Memorandum - 5th Sub																												
A229428892	Design Memorandum - 5th Review	0			23	20-Jan-21 A	18-Feb-21 A	Design Memorandum - 5th Review																												
A229429360	Design Memorandum - 6th Sub	0			29	19-Feb-21 A	24-Mar-21 A	Design Memorandum - 6th Sub																												
A229429370	Design Memorandum - 6th Review	0			19	25-Mar-21 A	20-Apr-21 A	Design Memorandum - 6th Review																												
A229431000	Design Memorandum - 7th Sub	0			22	21-Apr-21 A	17-May-21 A	Design Memorandum - 7th Sub																												
A229431150	Design Memorandum - 6th Review	0			35	18-May-21 A	29-Jun-21	Design Memorandum - 6th Review																												
A22690	Design Memorandum - Approval	0		02-Mar-20	0		29-Jun-21	Design Memorandum - Approval																												
Construction Traffic Impact Assessment - Kai Tak Area		0	10-Jun-20	10-Jun-20	167	12-Dec-20 A	10-Jul-21																													
A229426161	CTIA Kai Tak Area - Resubmission	0			33	12-Dec-20 A	22-Jan-21 A	CTIA Kai Tak Area - Resubmission																												
A229426171	CTIA Kai Tak Area - 4th Sub	0			0		22-Jan-21 A	CTIA Kai Tak Area - 4th Sub																												
A229426181	CTIA Kai Tak Area - 4th Review	0			20	23-Jan-21 A	11-Feb-21 A	CTIA Kai Tak Area - 4th Review																												
A229429380	CTIA Kai Tak Area - Resubmission	0			32	12-Feb-21 A	24-Mar-21 A	CTIA Kai Tak Area - Resubmission																												
A229429390	CTIA Kai Tak Area - 5th Sub	0			0		24-Mar-21 A	CTIA Kai Tak Area - 5th Sub																												
A229429400	CTIA Kai Tak Area - 5th Review	0			37	25-Mar-21 A	30-Apr-21 A	CTIA Kai Tak Area - 5th Review																												
A229431090	CTIA Kai Tak Area - Resubmission	0			35	03-May-21 A	12-Jun-21	CTIA Kai Tak Area - Resubmission																												
A229431100	CTIA Kai Tak Area - 6th Sub	0			0		12-Jun-21	CTIA Kai Tak Area - 6th Sub																												
A229431110	CTIA Kai Tak Area - 6th Review	0			28	13-Jun-21	10-Jul-21	CTIA Kai Tak Area - 6th Review																												
A22720	CTIA Kai Tak Area - Approval	0		10-Jun-20	0		10-Jul-21	CTIA Kai Tak Area - Approval																												
Durability Assessment Report		0	07-May-20	07-May-20	139	19-Jan-21 A	13-Jul-21																													
A229426141	Durability Assessment Report - 5th Sub	0			0		19-Jan-21 A	Durability Assessment Report - 5th Sub																												
A229426151	Durability Assessment Report - 5th Review	0			29	20-Jan-21 A	25-Feb-21 A	Durability Assessment Report - 5th Review																												
A229431010	Durability Assessment Report - Resubmission	0			30	26-Feb-21 A	01-Apr-21 A	Durability Assessment Report - Resubmission																												
A229431020	Durability Assessment Report - 6th Sub	0			0		01-Apr-21 A	Durability Assessment Report - 6th Sub																												
A229431030	Durability Assessment Report - 6th Review	0			28	02-Apr-21 A	10-May-21 A	Durability Assessment Report - 6th Review																												
A229431120	Durability Assessment Report - Resubmission	0			24	11-May-21 A	08-Jun-21	Durability Assessment Report - Resubmission																												
A229431130	Durability Assessment Report - 7th Sub	0			0		08-Jun-21	Durability Assessment Report - 7th Sub																												
A229431140	Durability Assessment Report - 7th Review	0			28	09-Jun-21	13-Jul-21	Durability Assessment Report - 7th Review																												
A22730	Durability Assessment Report - Approval	0		07-May-20	0		13-Jul-21	Durability Assessment Report - Approval																												
ACABAS - Western Tunnel Portal and Concrete Finishes for Retaining Struc		50	10-Aug-20	08-Oct-20	136	16-Dec-20 A	05-Jun-21	lining Structure																												
B18010	DDA - Further information required by SO	22	10-Aug-20	03-Sep-20	56	16-Dec-20 A	25-Feb-21 A	DDA - Further information required by SO																												
B18020	DDA - 2nd Sub	0		03-Sep-20	0		25-Feb-21 A	DDA - 2nd Sub																												
B18030	DDA - 2nd Review by SO	35	04-Sep-20	08-Oct-20	100	26-Feb-21 A	05-Jun-21	DDA - 2nd Review by SO																												
B18040	DDA - SO Consent for Construction	0		08-Oct-20	0		05-Jun-21	DDA - SO Consent for Construction																												
ACABAS- Footbridge FB-02		78	09-Oct-20	12-Jan-21	78	07-Jun-21	07-Sep-21	ACABAS- Footbridge FB-02																												
B266491	DDA - Draft - Preparation by Designer	48	09-Oct-20	04-Dec-20	48	07-Jun-21	03-Aug-21	DDA - Draft - Preparation by Designer																												
B266421	DDA - Draft - Final Review and prepare for 1st Sub	30	05-Dec-20	12-Jan-21	30	04-Aug-21	07-Sep-21	DDA - Draft - Final Review and prepare for 1st Sub																												
CLP Substation - Building Services and Underground Utilities Design		0	01-Jun-20	01-Jun-20	0	05-Jun-21	05-Jun-21																													
B266841	DDA - SO Consent for Construction	0		01-Jun-20	0		05-Jun-21	DDA - SO Consent for Construction																												
CLP Substation - ABWF		0	19-Jun-20	19-Jun-20	0	04-Jun-21	04-Jun-21																													
B266931	DDA - SO Consent for Construction	0		19-Jun-20	0		04-Jun-21	DDA - SO Consent for Construction																												
DDA Project Alignment		0	20-May-20	20-May-20	71	11-Dec-20 A	11-Mar-21 A																													
B2596021	DDA - 3rd Sub	0			0		11-Dec-20 A	DDA - 3rd Sub																												
B2596031	DDA - 3rd Review by SO	0			35	12-Dec-20 A	15-Jan-21 A	DDA - 3rd Review by SO																												
B2596611	DDA - Further information required by SO	0			11	16-Jan-21 A	28-Jan-21 A	DDA - Further information required by SO																												


◆ Milestone
 Planned Bar
 Critical Activity
◆ Actual Milestone
 Actual Work
◆ Baseline Milestone
 Baseline Bar
▶ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

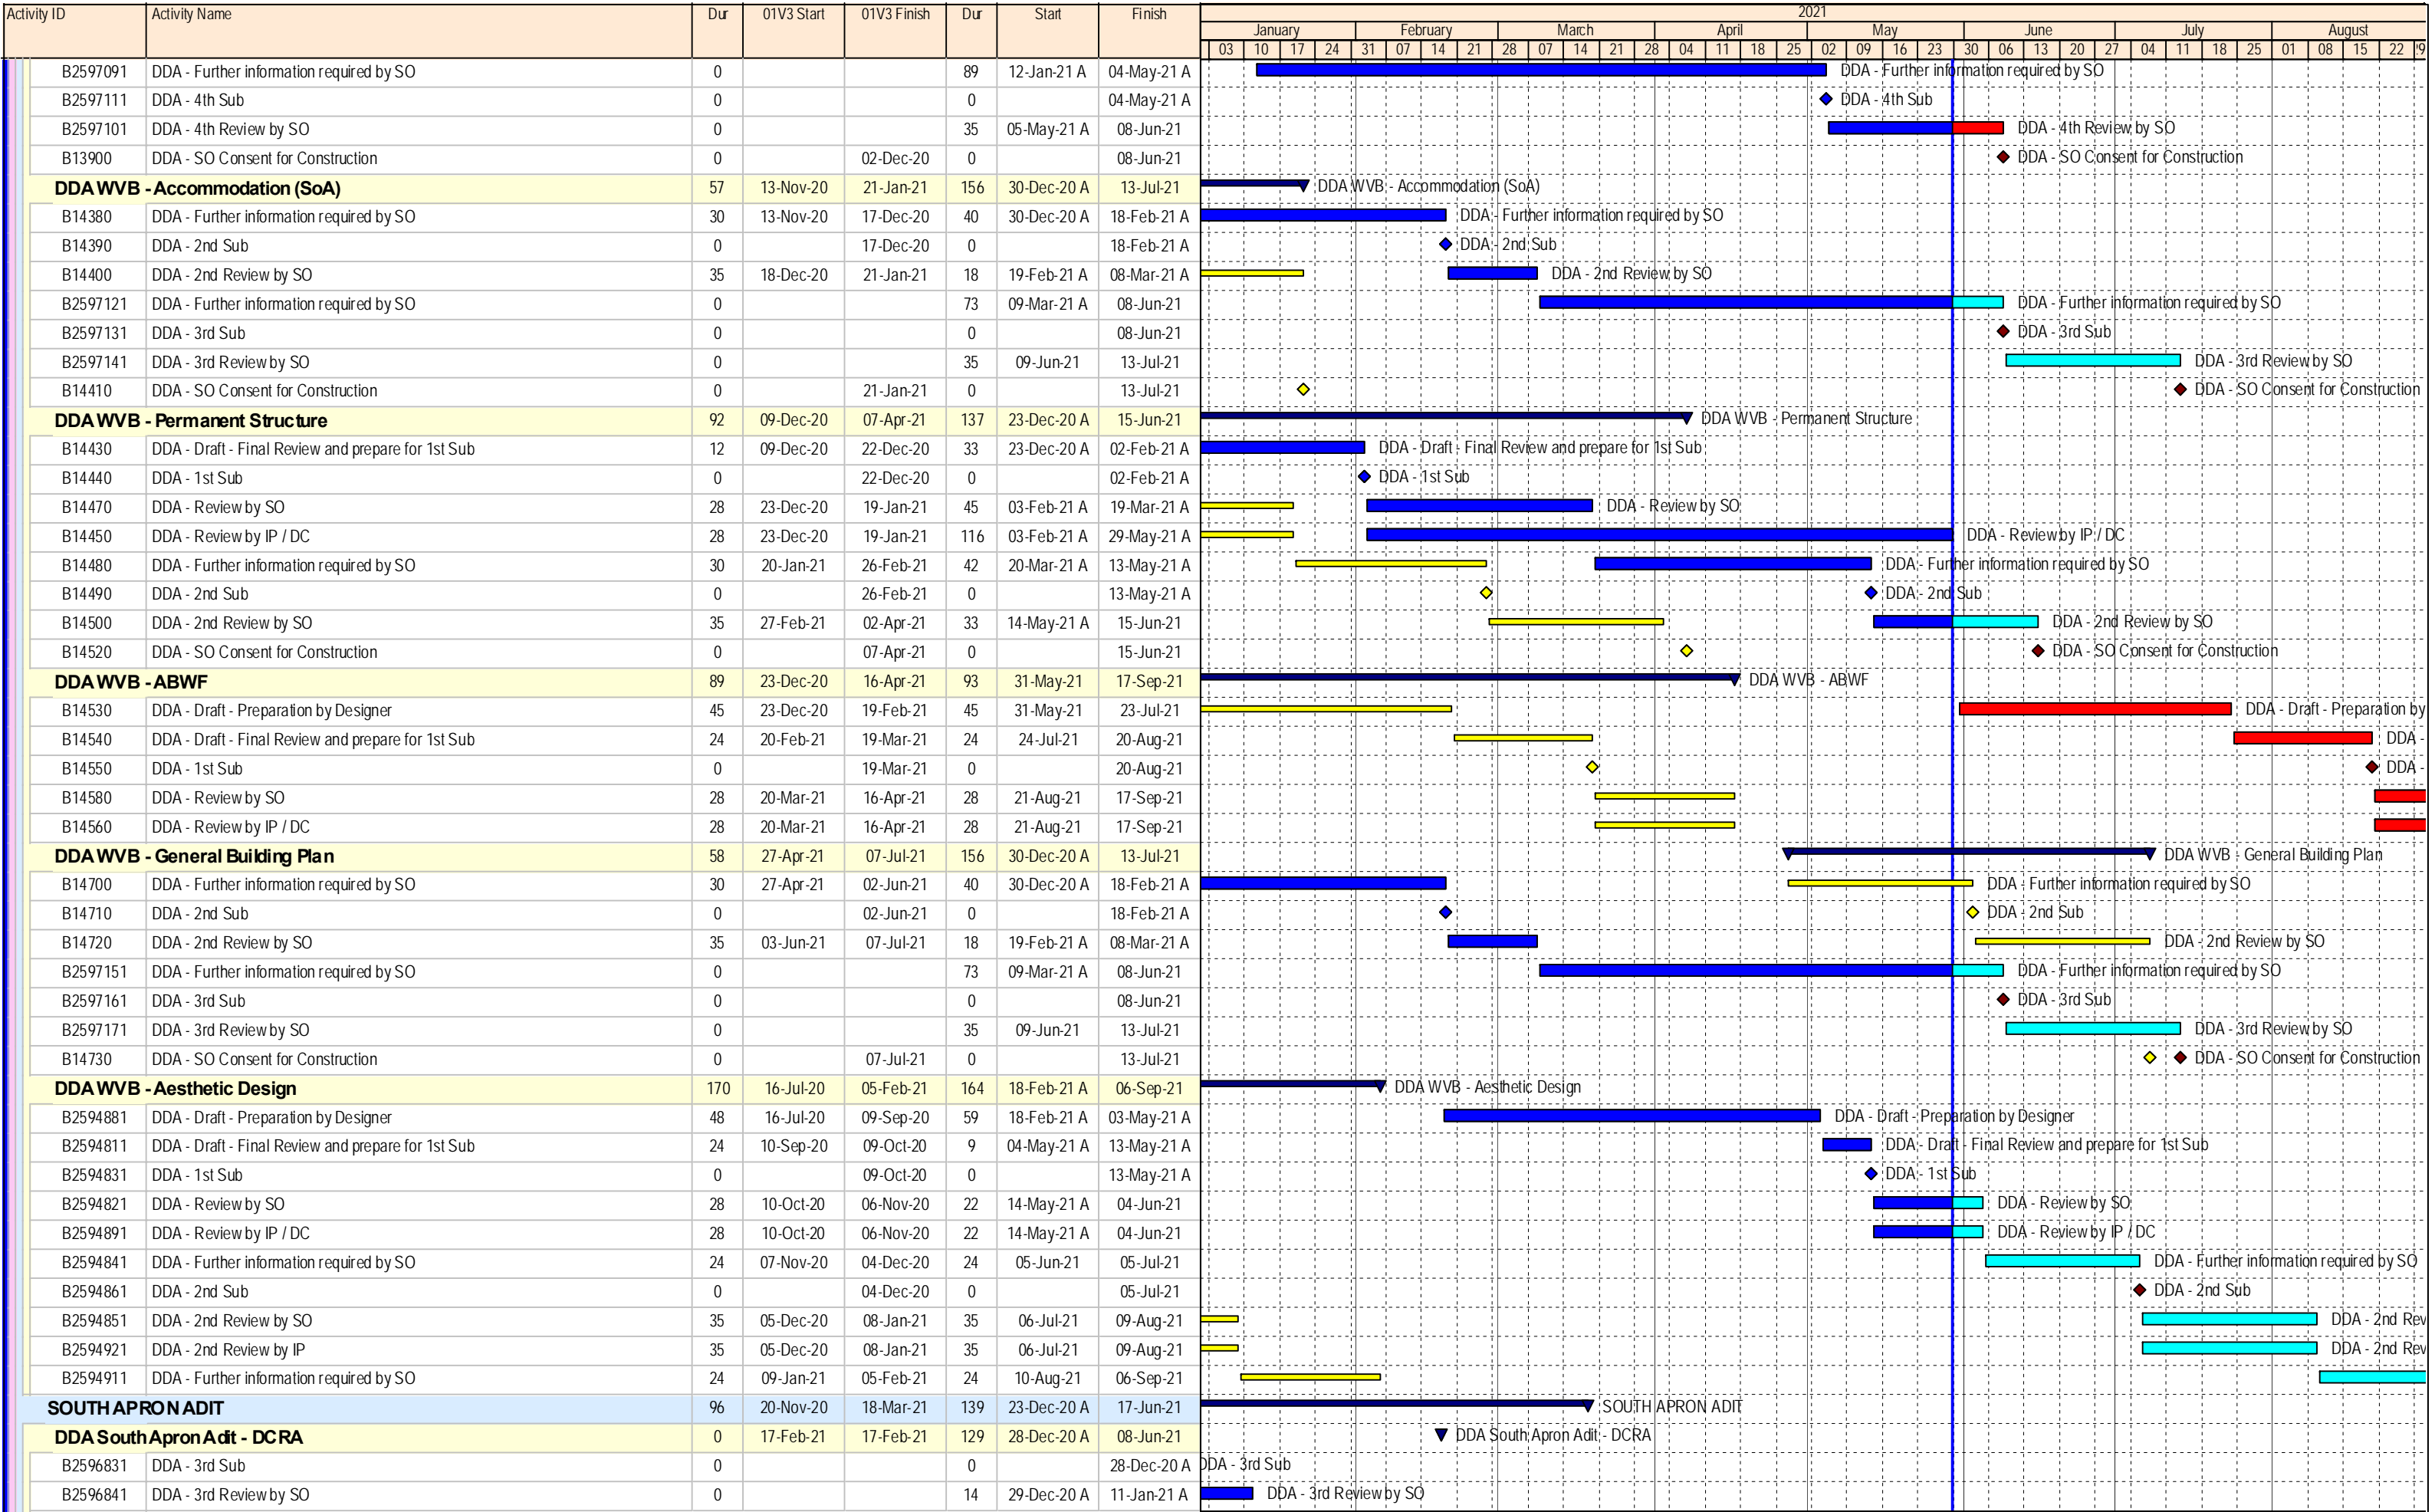

Page 4 of 26
Data Date: 29-May-21

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu


Activity ID	Activity Name	Dur	01V3 Start	01V3 Finish	Dur	Start	Finish	2021																										
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04
B2597181	DDA - Further information required by SO	0			89	12-Jan-21 A	04-May-21 A	DDA - Further information required by SO																										
B2597201	DDA - 4th Sub	0			0		04-May-21 A	◆ DDA - 4th Sub																										
B2597191	DDA - 4th Review by SO	0			35	05-May-21 A	08-Jun-21	DDA - 4th Review by SO																										
B15030	DDA - SO Consent for Construction	0		17-Feb-21	0		08-Jun-21	◆ DDA - SO Consent for Construction																										
DDA South Apron Add - Permanent Structure		96	20-Nov-20	18-Mar-21	139	23-Dec-20 A	17-Jun-21	DDA South Apron Add - Permanent Structure																										
B15150	DDA - Draft - Final Review and prepare for 1st Sub	24	20-Nov-20	17-Dec-20	33	23-Dec-20 A	02-Feb-21 A	DDA - Draft - Final Review and prepare for 1st Sub																										
B15160	DDA - 1st Sub	0		17-Dec-20	0		02-Feb-21 A	◆ DDA - 1st Sub																										
B15190	DDA - Review by SO	28	18-Dec-20	14-Jan-21	45	03-Feb-21 A	19-Mar-21 A	DDA - Review by SO																										
B15170	DDA - Review by IP / DC	28	18-Dec-20	14-Jan-21	118	03-Feb-21 A	31-May-21	DDA - Review by IP / DC																										
B15200	DDA - Further information required by SO	24	15-Jan-21	11-Feb-21	42	20-Mar-21 A	13-May-21 A	DDA - Further information required by SO																										
B15210	DDA - 2nd Sub	0		11-Feb-21	0		13-May-21 A	◆ DDA - 2nd Sub																										
B15220	DDA - 2nd Review by SO	35	12-Feb-21	18-Mar-21	35	14-May-21 A	17-Jun-21	DDA - 2nd Review by SO																										
B15230	DDA - SO Consent for Construction	0		18-Mar-21	0		17-Jun-21	◆ DDA - SO Consent for Construction																										
SOUTH APRON ROAD WORKS		540	12-Aug-20	11-Jun-22	243	01-Dec-20 A	27-Sep-21																											
DDA Road S20 - Alignment, Traffic Sign, Road Marking and Traffic Light		0	14-Aug-20	14-Aug-20	60	10-Dec-20 A	25-Feb-21 A																											
SOR		0	14-Aug-20	14-Aug-20	60	10-Dec-20 A	25-Feb-21 A																											
B2596141	DDA - 6th Sub	0			0		10-Dec-20 A																											
B2596151	DDA - 6th Review by SO	0			16	11-Dec-20 A	31-Dec-20 A	DDA - 6th Review by SO																										
B2596401	DDA - Further information required by SO	0			26	02-Jan-21 A	01-Feb-21 A	DDA - Further information required by SO																										
B2596411	DDA - 7th Sub	0			0		01-Feb-21 A	◆ DDA - 7th Sub																										
B2596421	DDA - 7th Review by SO	0			18	02-Feb-21 A	25-Feb-21 A	DDA - 7th Review by SO																										
B253301	DDA - SO Consent for Construction	0		14-Aug-20	0		25-Feb-21 A	◆ DDA - SO Consent for Construction																										
DDA Road S20 - Roadworks and Street Furniture		0	14-Aug-20	14-Aug-20	93	15-Dec-20 A	14-Apr-21 A																											
SOR		0	14-Aug-20	14-Aug-20	93	15-Dec-20 A	14-Apr-21 A																											
B2596171	DDA - 7th Sub	0			0		15-Dec-20 A	Sub																										
B2596181	DDA - Further information required by SO	0			38	16-Dec-20 A	01-Feb-21 A	DDA - Further information required by SO																										
B2596851	DDA - 7th Review by SO	0			1	01-Feb-21 A	01-Feb-21 A	DDA - 7th Review by SO																										
B2596861	DDA - 8th Sub	0			0		01-Feb-21 A	◆ DDA - 8th Sub																										
B2596871	DDA - 8th Review by SO	0			18	02-Feb-21 A	25-Feb-21 A	DDA - 8th Review by SO																										
B2597221	DDA - Further information required by SO	0			21	26-Feb-21 A	22-Mar-21 A	DDA - Further information required by SO																										
B2597211	DDA - 9th Review by SO	0			16	23-Mar-21 A	14-Apr-21 A	DDA - 9th Review by SO																										
B253401	DDA - SO Consent for Construction	0		14-Aug-20	0		14-Apr-21 A	◆ DDA - SO Consent for Construction																										
B2597231	DDA - 9th Sub	0			0		14-Apr-21 A	◆ DDA - 9th Sub																										
TD		0			93	16-Dec-20 A	14-Apr-21 A																											
B2595761	DDA - Under review by TD	0			93	16-Dec-20 A	14-Apr-21 A	DDA - Under review by TD																										
AIP Road L10 (S)		0	03-Oct-20	03-Oct-20	127	01-Dec-20 A	10-May-21 A																											
B2596211	AIP - 2d Review by SO	0			64	01-Dec-20 A	02-Feb-21 A	AIP - 2d Review by SO																										
B2597241	AIP - Further information required by SO	0			23	03-Feb-21 A	04-Mar-21 A	AIP - Further information required by SO																										
B2597261	AIP - 3rd Review by SO	0			19	04-Mar-21 A	22-Mar-21 A	AIP - 3rd Review by SO																										
B2597251	AIP - 3rd Sub	0			0		04-Mar-21 A	◆ AIP - 3rd Sub																										
B2597271	AIP - Further information required by SO	0			26	23-Mar-21 A	26-Apr-21 A	AIP - Further information required by SO																										
B2597281	AIP - 4th Sub	0			0		26-Apr-21 A	◆ AIP - 4th Sub																										
B2597291	AIP - 4th Review by SO	0			14	27-Apr-21 A	10-May-21 A	AIP - 4th Review by SO																										
B255892	AIP - SO Consent for DDA Submission	0		03-Oct-20	0		10-May-21 A	◆ AIP - SO Consent for DDA Submission																										
DDA Road L10 (S) + Outfall 2 - Permanent Utility Design		77	02-Nov-20	02-Feb-21	123	21-Dec-20 A	26-May-21 A	DDA Road L10 (S) + Outfall 2 - Permanent Utility Design																										
B263761	DDA - Draft - Final Review and prepare for 1st Sub	12	02-Nov-20	14-Nov-20	7	21-Dec-20 A	30-Dec-20 A	DDA - Draft - Final Review and prepare for 1st Sub																										
B263781	DDA - 1st Sub	0		14-Nov-20	0		30-Dec-20 A	DDA - 1st Sub																										
B263771	DDA - Review by SO	28	15-Nov-20	12-Dec-20	41	31-Dec-20 A	09-Feb-21 A	DDA - Review by SO																										
B263831	DDA - Review by IP / DC	28	15-Nov-20	12-Dec-20	51	31-Dec-20 A	19-Feb-21 A	DDA - Review by IP / DC																										
B263791	DDA - Further information required by SO	12	14-Dec-20	29-Dec-20	6	10-Feb-21 A	19-Feb-21 A	DDA - Further information required by SO																										

Page 5 of 26
Data Date: 29-May-21


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ▬ Actual Work
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

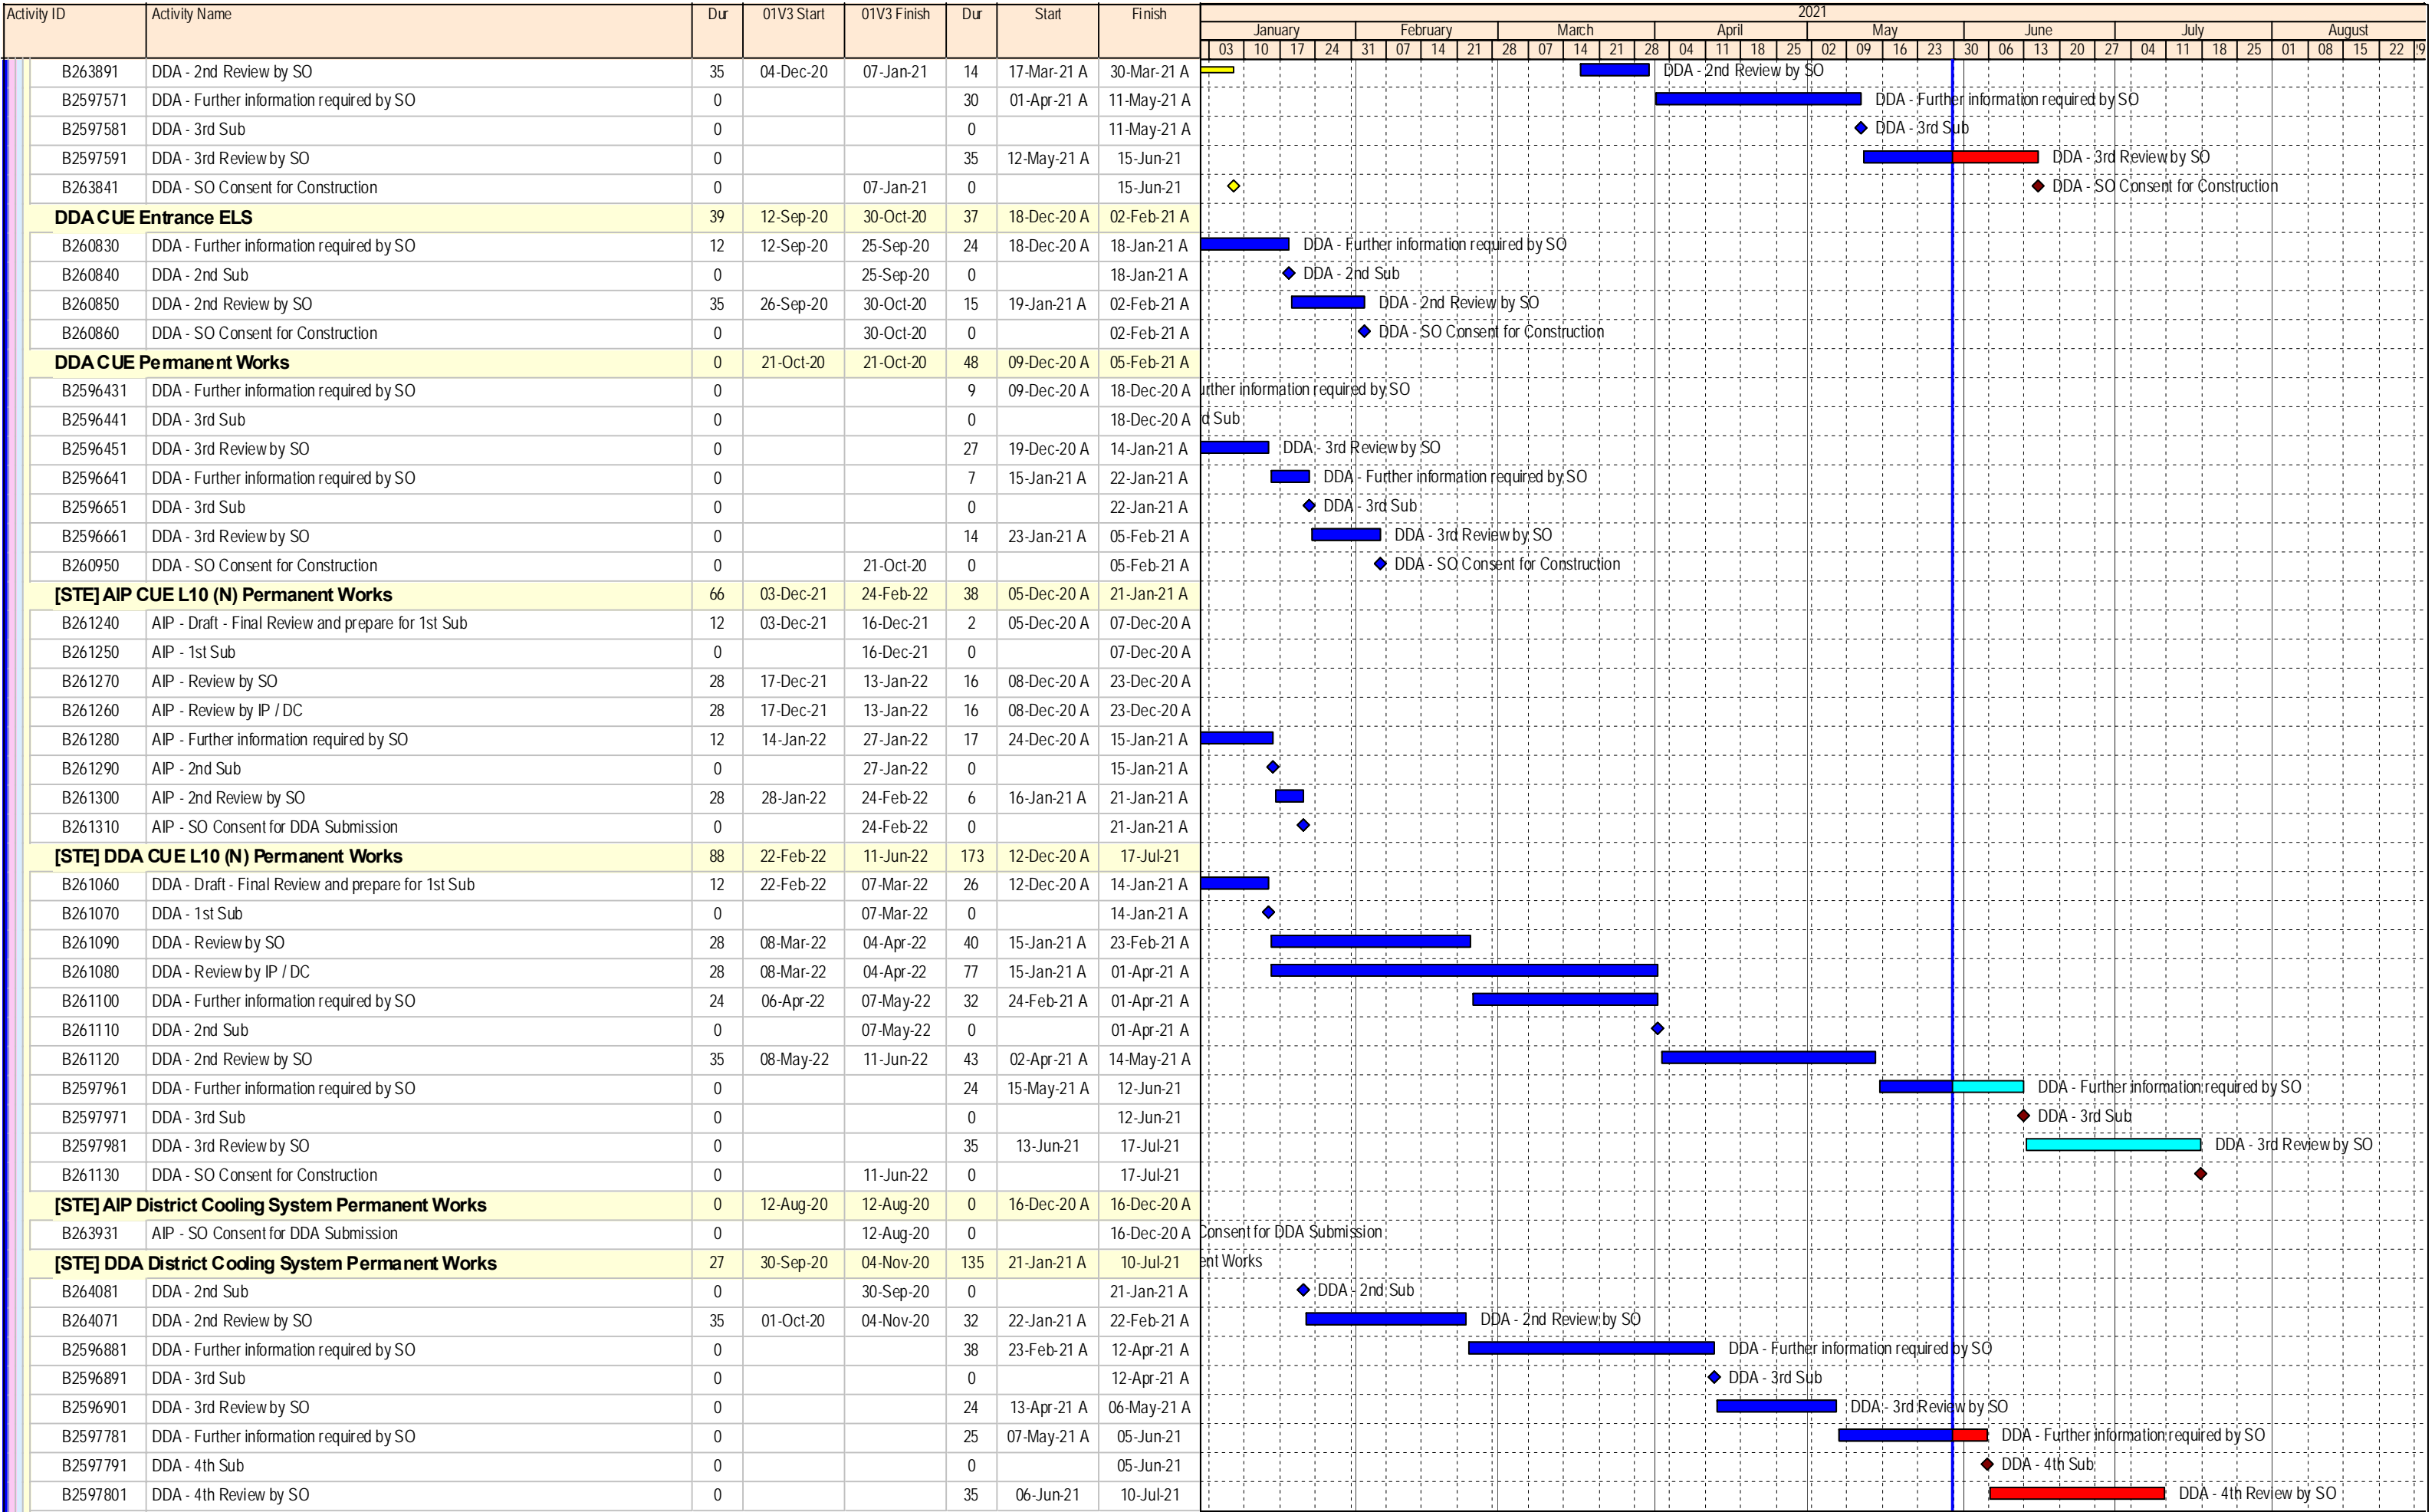

Page 7 of 26
Data Date: 29-May-21

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

Activity ID	Activity Name	Dur	01V3 Start	01V3 Finish	Dur	Start	Finish	2021																																		
								January				February				March				April				May				June				July				August						
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
B264021	DDA - SO Consent for Construction	0		04-Nov-20	0		10-Jul-21	◆ DDA - SO Consent for Construction																																		
[STE] AIP District Cooling System Temporary Works		0	14-Aug-20	14-Aug-20	33	08-Dec-20 A	19-Jan-21 A																																			
B2596231	AIP - 3rd Sub	0			0		08-Dec-20 A																																			
B2596241	AIP - 3rd Review by SO	0			14	09-Dec-20 A	22-Dec-20 A	3rd Review by SO																																		
B2596461	AIP - Further information required by SO	0			9	23-Dec-20 A	05-Jan-21 A	■ AIP - Further information required by SO																																		
B2596471	AIP - 4th Sub	0			0		05-Jan-21 A	◆ AIP - 4th Sub																																		
B2596481	AIP - 4th Review by SO	0			14	06-Jan-21 A	19-Jan-21 A	■ AIP - 4th Review by SO																																		
B258970	AIP - SO Consent for DDA Submission	0		14-Aug-20	0		19-Jan-21 A	◆ AIP - SO Consent for DDA Submission																																		
[STE] DDA District Cooling System Temporary Works		29	05-Oct-20	09-Nov-20	62	11-Dec-20 A	01-Mar-21 A	Temporary Works																																		
B259040	DDA - 2nd Sub	0		05-Oct-20	0		11-Dec-20 A	◆ DDA - 2nd Sub																																		
B259050	DDA - 2nd Review by SO	35	06-Oct-20	09-Nov-20	27	12-Dec-20 A	07-Jan-21 A	■ DDA - 2nd Review by SO																																		
B2596671	DDA - Further information required by SO	0			10	08-Jan-21 A	19-Jan-21 A	■ DDA - Further information required by SO																																		
B2596681	DDA - 3rd Sub	0			0		19-Jan-21 A	◆ DDA - 3rd Sub																																		
B2596691	DDA - 3rd Review by SO	0			10	20-Jan-21 A	29-Jan-21 A	■ DDA - 3rd Review by SO																																		
B2596911	DDA - Further information required by SO	0			11	30-Jan-21 A	11-Feb-21 A	■ DDA - Further information required by SO																																		
B2596921	DDA - 4th Sub	0			0		11-Feb-21 A	◆ DDA - 4th Sub																																		
B2596931	DDA - 4th Review by SO	0			18	12-Feb-21 A	01-Mar-21 A	■ DDA - 4th Review by SO																																		
B259060	DDA - SO Consent for Construction	0		09-Nov-20	0		01-Mar-21 A	◆ DDA - SO Consent for Construction																																		
[STE] AIP Hoi Bun Road Junction		0	30-Nov-20	30-Nov-20	58	29-Jan-21 A	15-Apr-21 A	Road Junction																																		
B2596501	AIP - 4th Sub	0			0		29-Jan-21 A	◆ AIP - 4th Sub																																		
B2596511	AIP - 4th Review by SO	0			18	30-Jan-21 A	16-Feb-21 A	■ AIP - 4th Review by SO																																		
B2596941	AIP - Further information required by SO	0			10	17-Feb-21 A	27-Feb-21 A	■ AIP - Further information required by SO																																		
B2596951	AIP - 5th Sub	0			0		27-Feb-21 A	◆ AIP - 5th Sub																																		
B2596961	AIP - 5th Review by SO	0			16	01-Mar-21 A	16-Mar-21 A	■ AIP - 5th Review by SO																																		
B2597391	AIP - Further information required by SO	0			13	17-Mar-21 A	31-Mar-21 A	■ AIP - Further information required by SO																																		
B2597401	AIP - 6th Sub	0			0		31-Mar-21 A	◆ AIP - 6th Sub																																		
B2597411	AIP - 6th Review by SO	0			15	01-Apr-21 A	15-Apr-21 A	■ AIP - 6th Review by SO																																		
B259780	AIP - SO Consent for DDA Submission	0		30-Nov-20	0		15-Apr-21 A	◆ AIP - SO Consent for DDA Submission																																		
[STE] DDA Hoi Bun Road Junction - Permanent Utility Design		0	01-Mar-21	01-Mar-21	128	20-Jan-21 A	02-Jul-21	[STE] DDA Hoi Bun Road Junction - Permanent Utility Design																																		
B2596531	DDA - 3rd Sub	0			0		20-Jan-21 A	◆ DDA - 3rd Sub																																		
B2596541	DDA - 3rd Review by SO	0			30	21-Jan-21 A	19-Feb-21 A	■ DDA - 3rd Review by SO																																		
B2596971	DDA - Further information required by SO	0			32	20-Feb-21 A	29-Mar-21 A	■ DDA - Further information required by SO																																		
B2596981	DDA - 4th Sub	0			0		29-Mar-21 A	◆ DDA - 4th Sub																																		
B2596991	DDA - 4th Review by SO	0			31	30-Mar-21 A	29-Apr-21 A	■ DDA - 4th Review by SO																																		
B2597811	DDA - Further information required by SO	0			22	30-Apr-21 A	27-May-21 A	■ DDA - Further information required by SO																																		
B2597821	DDA - 4th Sub	0			0		27-May-21 A	◆ DDA - 4th Sub																																		
B2597831	DDA - 4th Review by SO	0			35	28-May-21 A	01-Jul-21	■ DDA - 4th Review by SO																																		
B259510	DDA - SO Consent for Construction	0		01-Mar-21	0		02-Jul-21	◆ DDA - SO Consent for Construction																																		
[STE] DDA Hoi Bun Road Junction - Alignment, Traffic Sign, Road Marking and Traffic Light		27	25-Jan-21	01-Mar-21	124	03-Feb-21 A	10-Jul-21	[STE] DDA Hoi Bun Road Junction - Alignment, Traffic Sign, Road Marking and Traffic Light																																		
B263261	DDA - 2nd Review by SO	35	26-Jan-21	01-Mar-21	22	03-Feb-21 A	25-Feb-21 A	■ DDA - 2nd Review by SO																																		
B263271	DDA - 2nd Sub	0		25-Jan-21	0		03-Feb-21 A	◆ DDA - 2nd Sub																																		
B2597421	DDA - Further information required by SO	0			27	26-Feb-21 A	29-Mar-21 A	■ DDA - Further information required by SO																																		
B2597441	DDA - 3rd Sub	0			0		29-Mar-21 A	◆ DDA - 3rd Sub																																		
B2597431	DDA - 3rd Review by SO	0			30	01-Apr-21 A	30-Apr-21 A	■ DDA - 3rd Review by SO																																		
B2597841	DDA - Further information required by SO	0			29	03-May-21 A	05-Jun-21	■ DDA - Further information required by SO																																		
B2597851	DDA - 4th Sub	0			0		05-Jun-21	◆ DDA - 4th Sub																																		
B2597861	DDA - 4th Review by SO	0			35	06-Jun-21	10-Jul-21	■ DDA - 4th Review by SO																																		
B263211	DDA - SO Consent for Construction	0		01-Mar-21	0		10-Jul-21	◆ DDA - SO Consent for Construction																																		
[STE] DDA Hoi Bun Road Junction - Roadworks and Street Furniture		0	01-Mar-21	01-Mar-21	89	20-Jan-21 A	13-May-21 A	[STE] DDA Hoi Bun Road Junction - Roadworks and Street Furniture																																		
B2596711	DDA - 3rd Sub	0			0		20-Jan-21 A	◆ DDA - 3rd Sub																																		

Page 8 of 26 Data Date: 29-May-21	<ul style="list-style-type: none"> ◆ Milestone ▬ Planned Bar ▬ Critical Activity ◆ Actual Milestone ▬ Actual Work ◆ Baseline Milestone ▬ Baseline Bar 	<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme (May-21)</h3>		<table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>05-Nov-19</td> <td>00V0</td> <td>WYu</td> <td></td> </tr> <tr> <td>18-Dec-19</td> <td>00V1</td> <td>WYu</td> <td></td> </tr> <tr> <td>22-Feb-20</td> <td>01V0</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Apr-20</td> <td>01V1</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>17-Jul-20</td> <td>01V2</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Oct-20</td> <td>01V3</td> <td>SPa/LLo</td> <td>WYu</td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																													
05-Nov-19	00V0	WYu																														
18-Dec-19	00V1	WYu																														
22-Feb-20	01V0	SPa/LLo	WYu																													
09-Apr-20	01V1	SPa/LLo	WYu																													
17-Jul-20	01V2	SPa/LLo	WYu																													
09-Oct-20	01V3	SPa/LLo	WYu																													

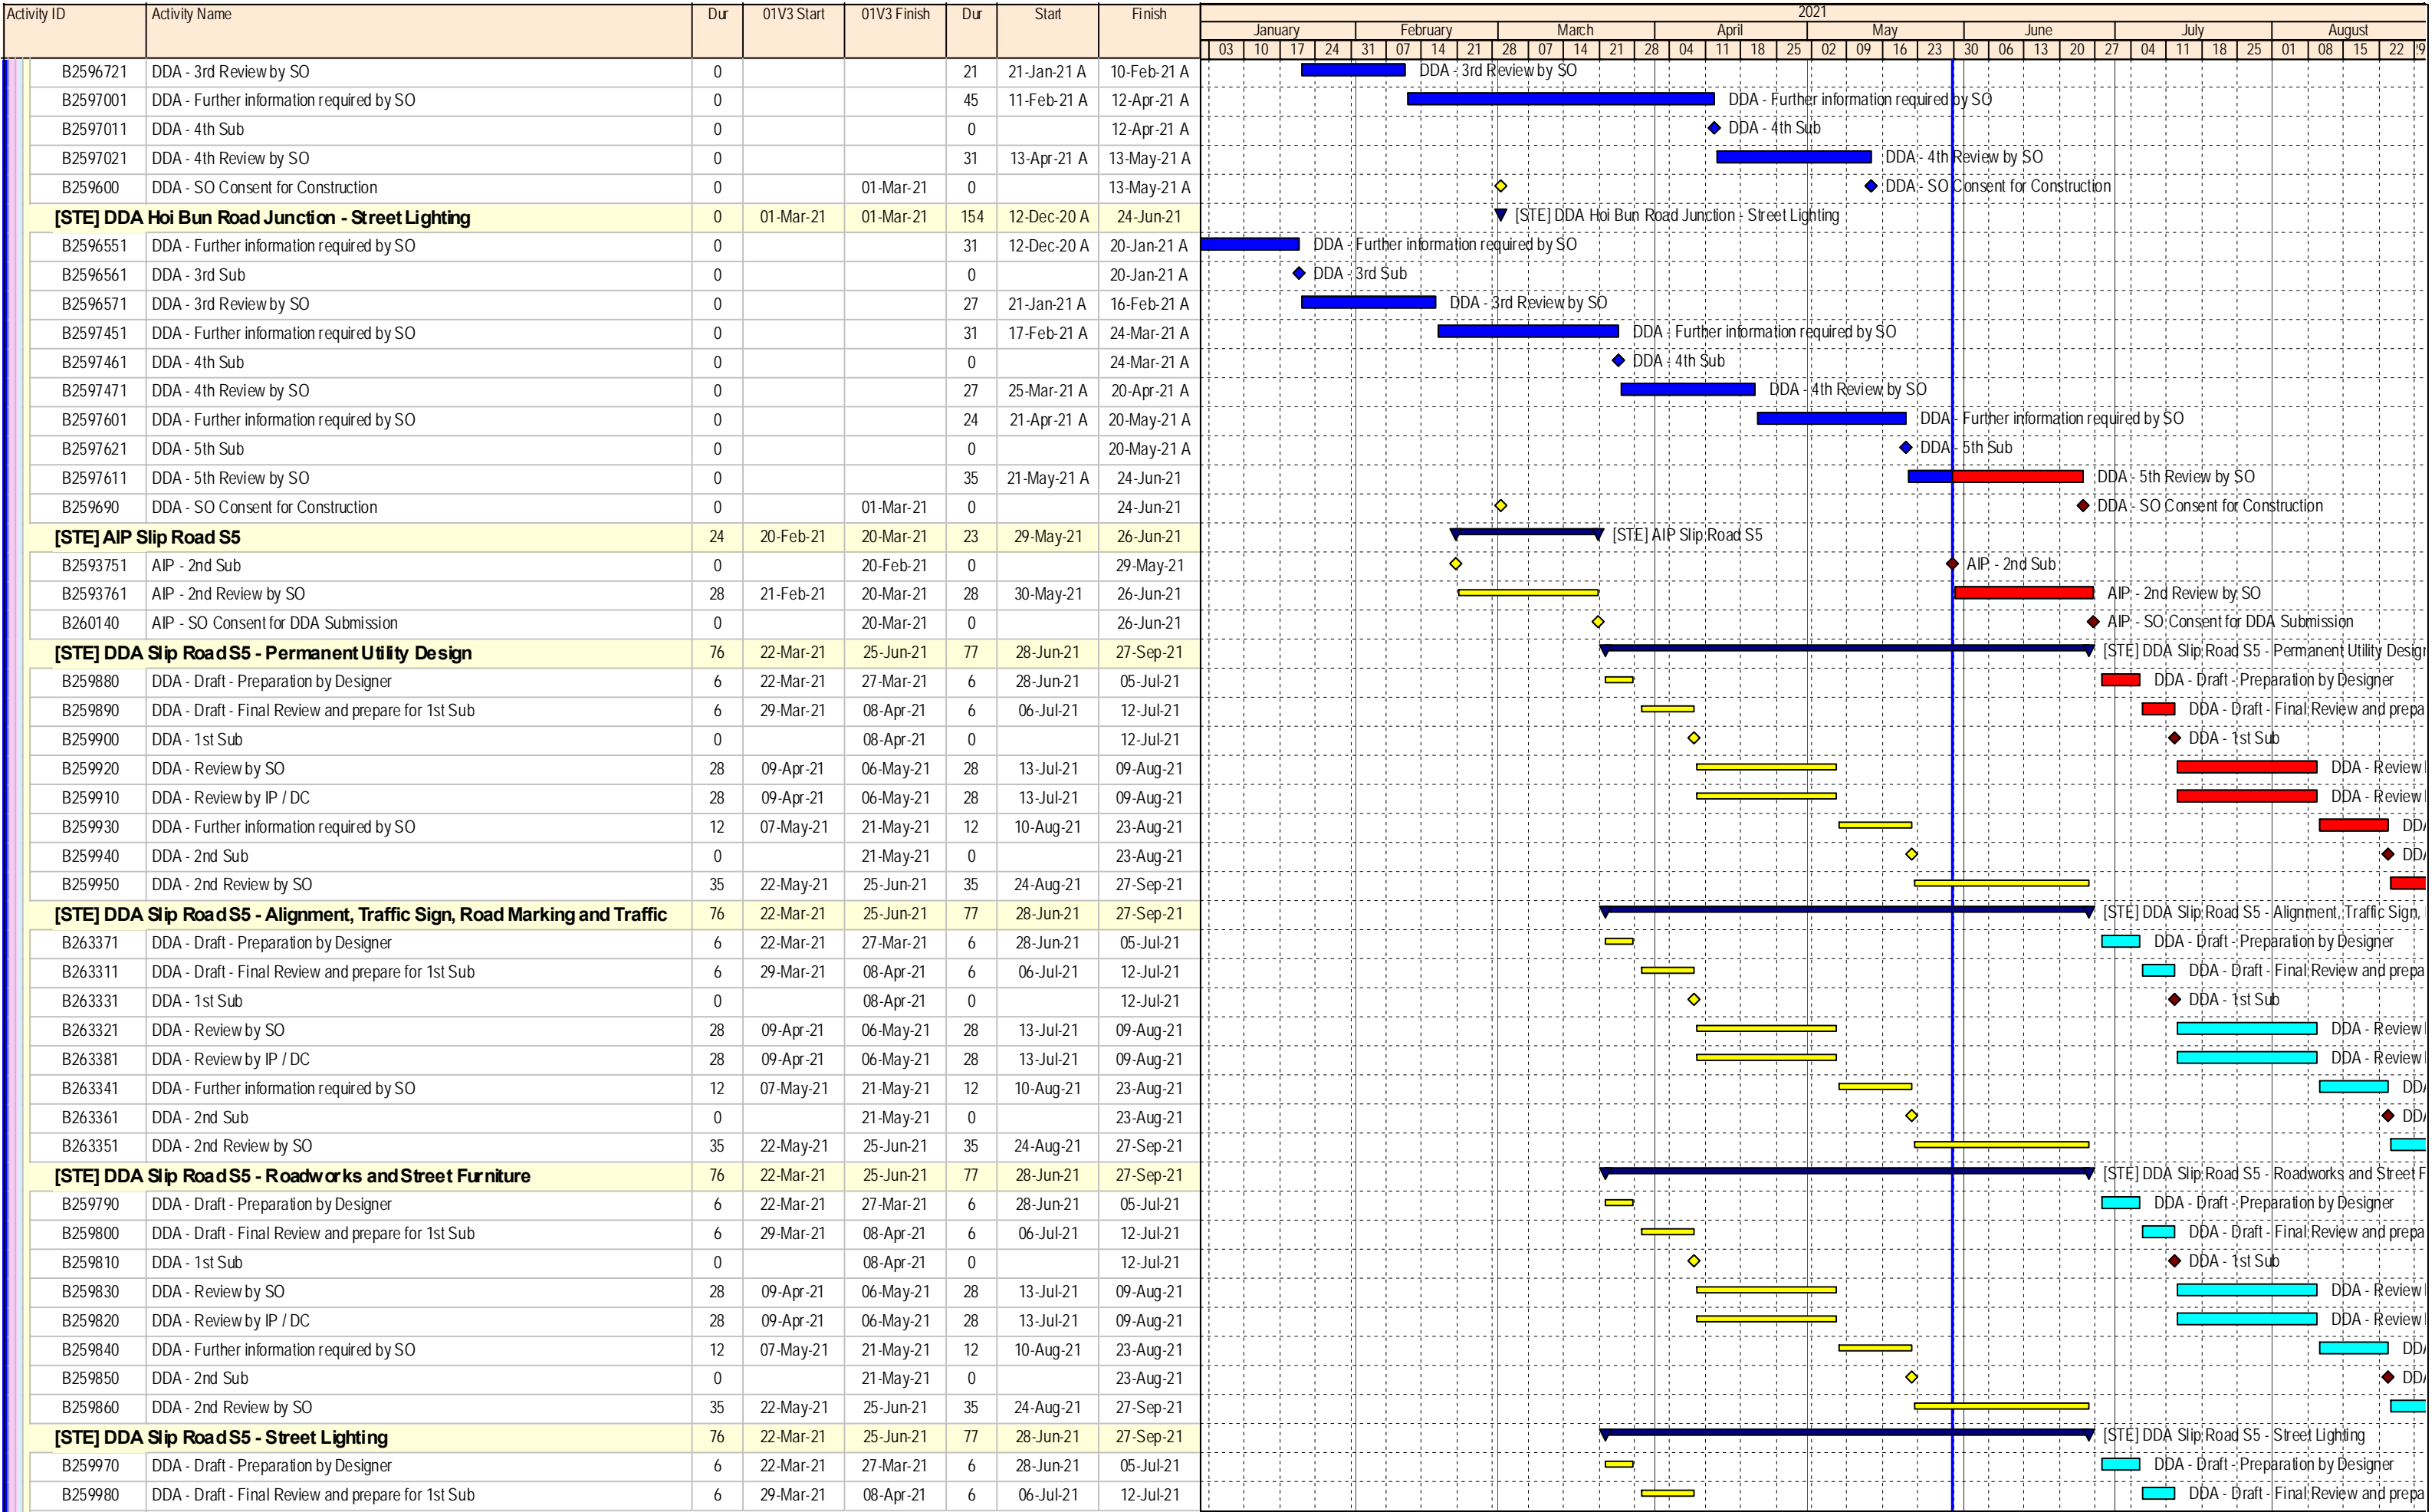


Page 9 of 26
 Data Date: 29-May-21



- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ▬ Actual Work
- ▬ Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

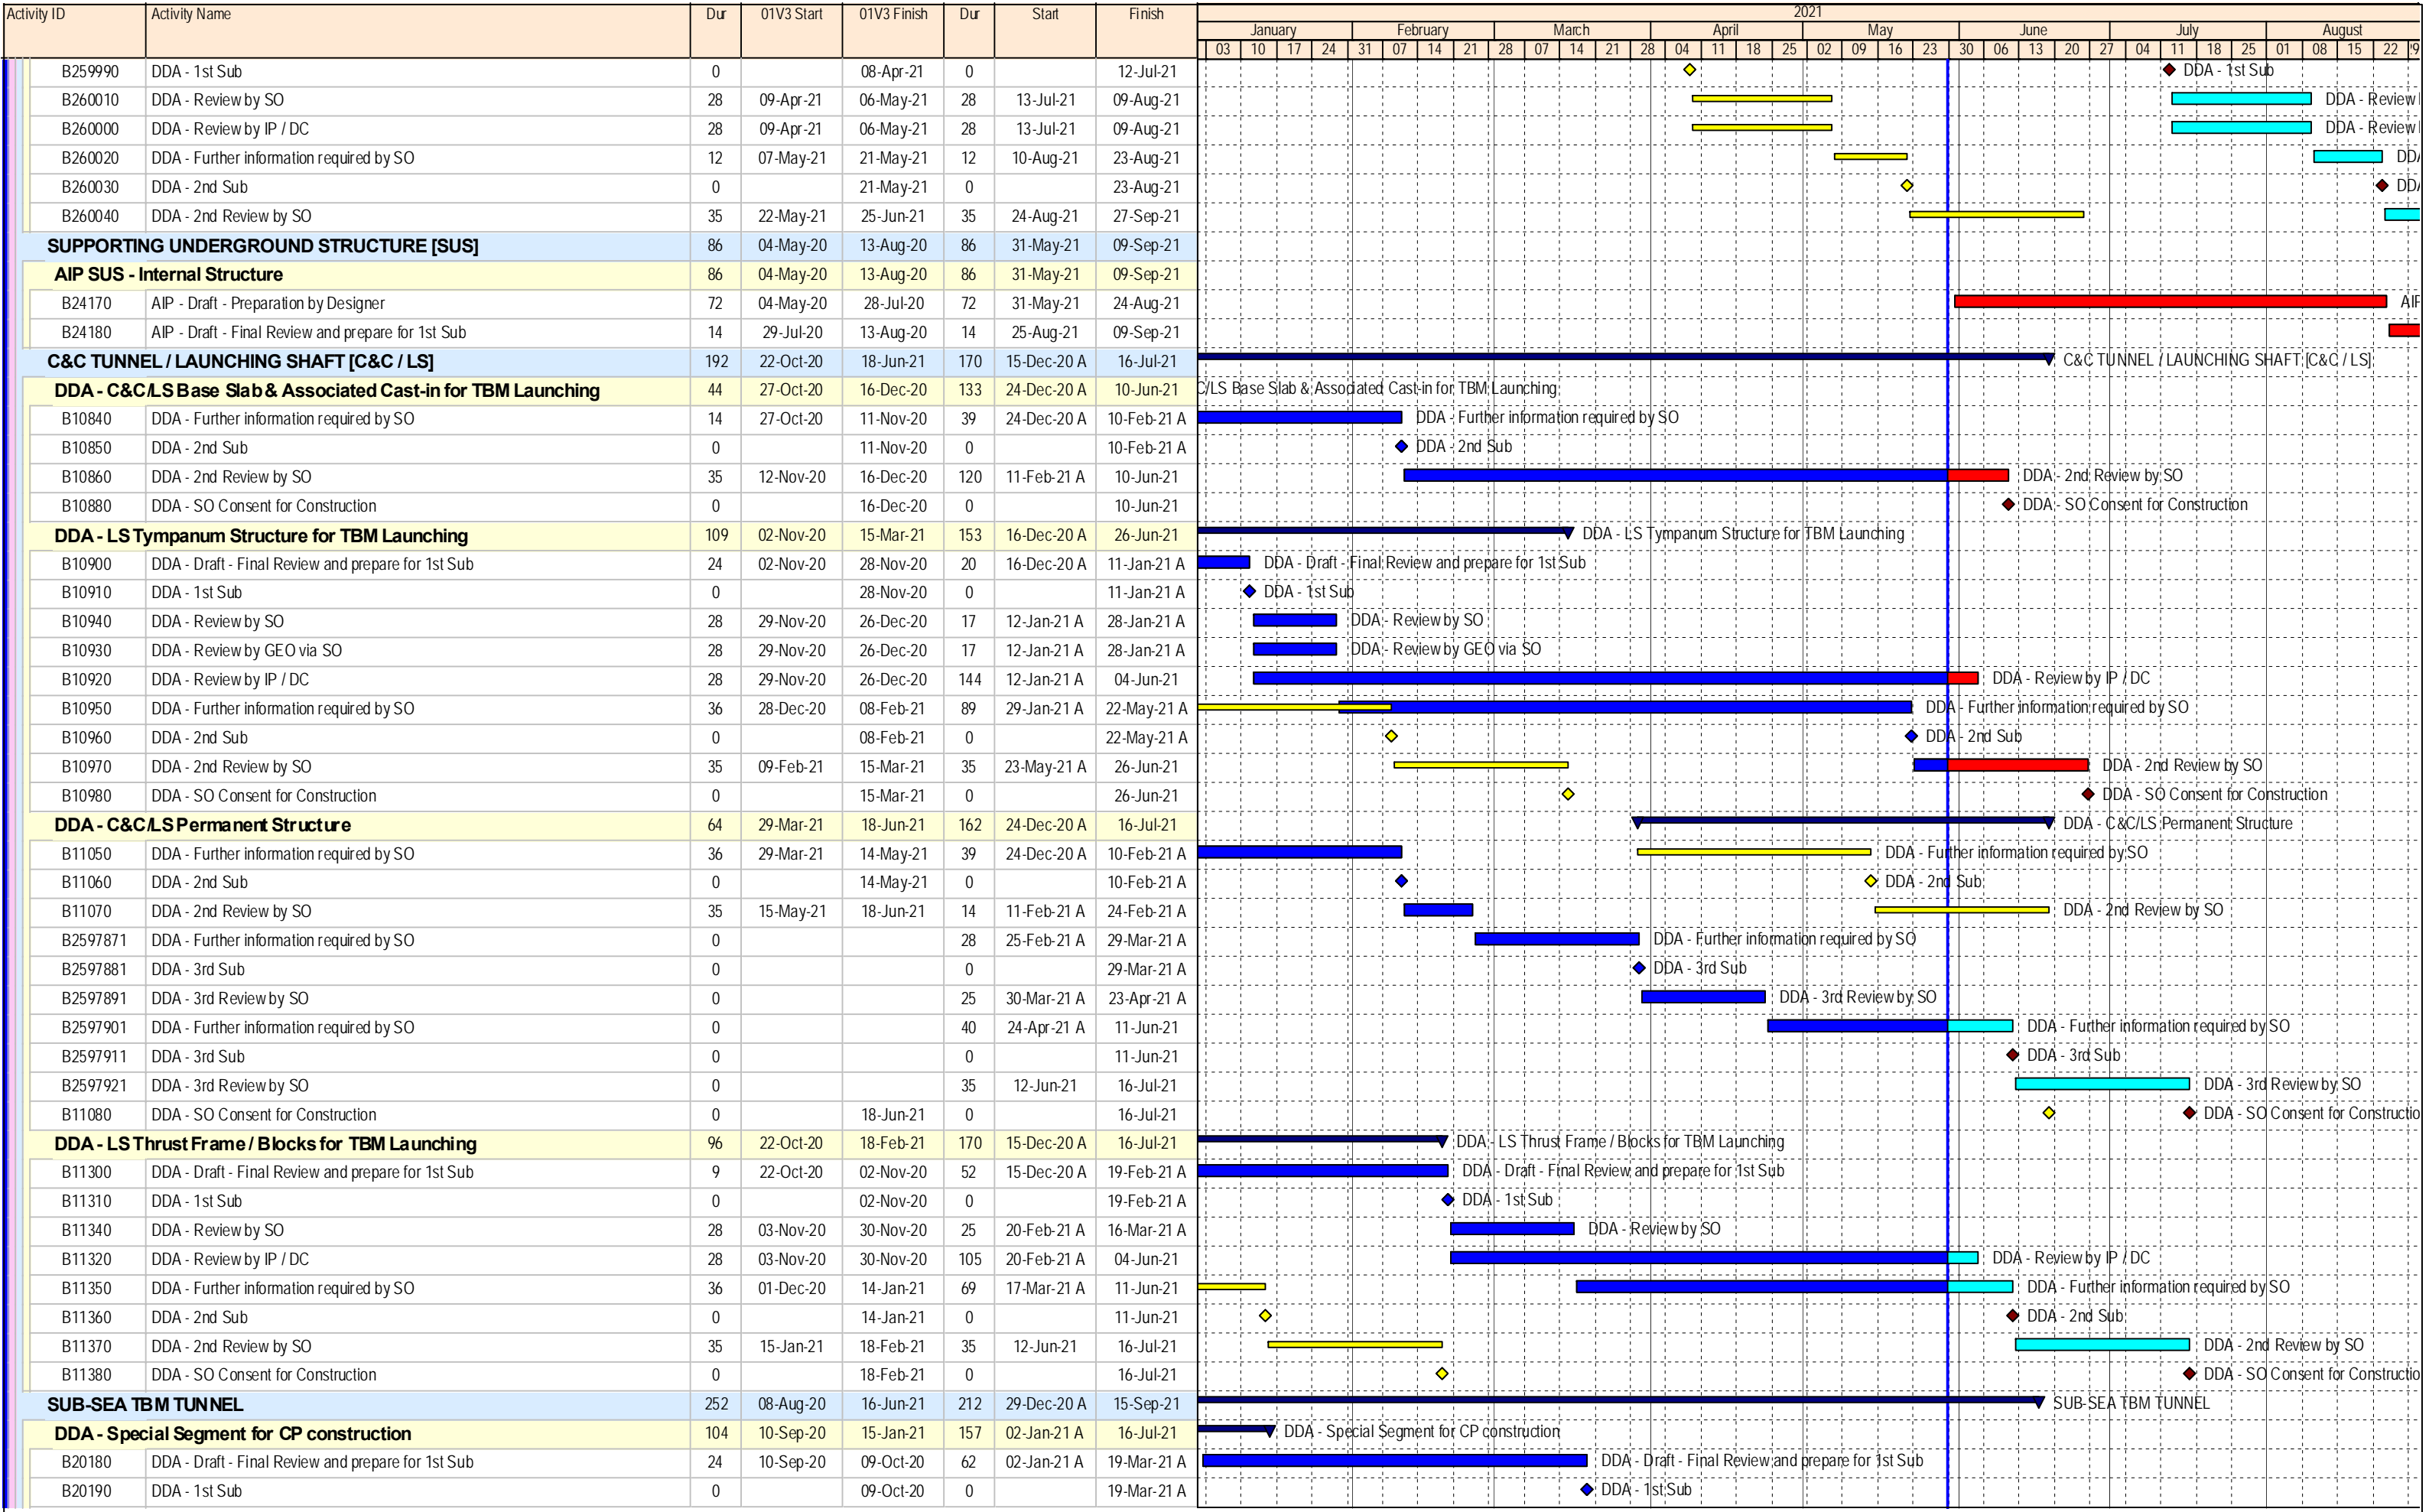


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

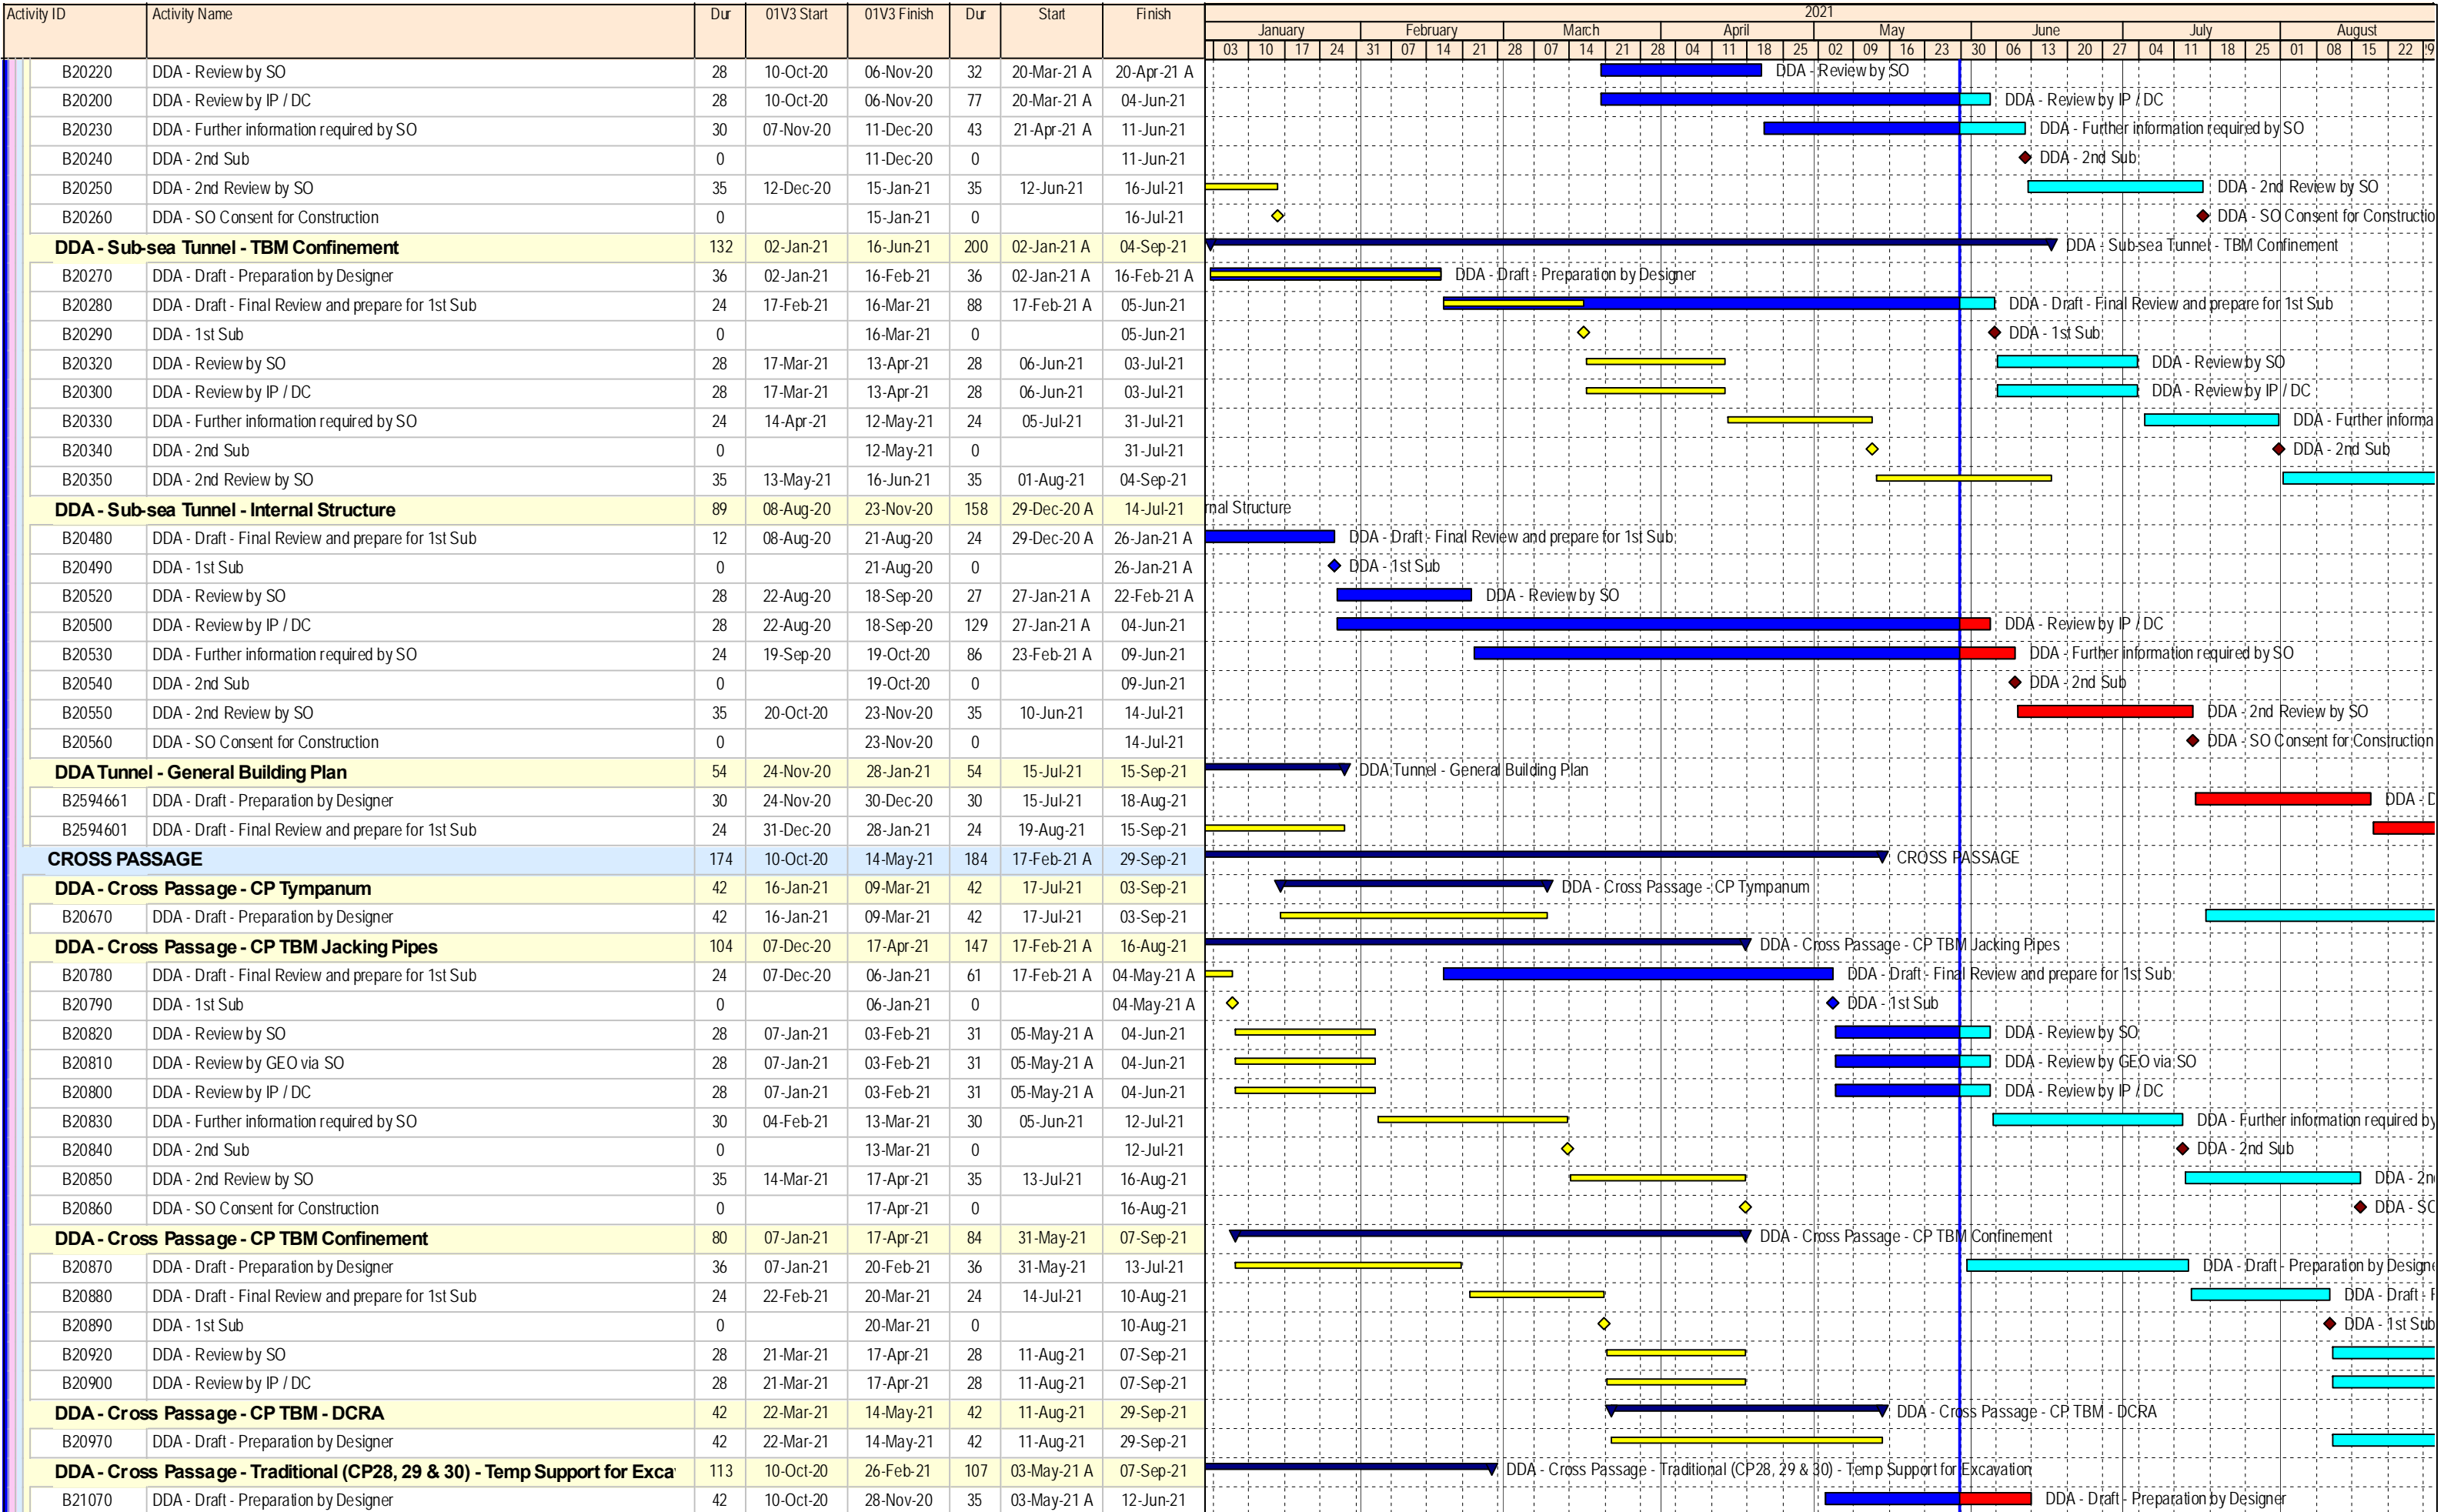


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu

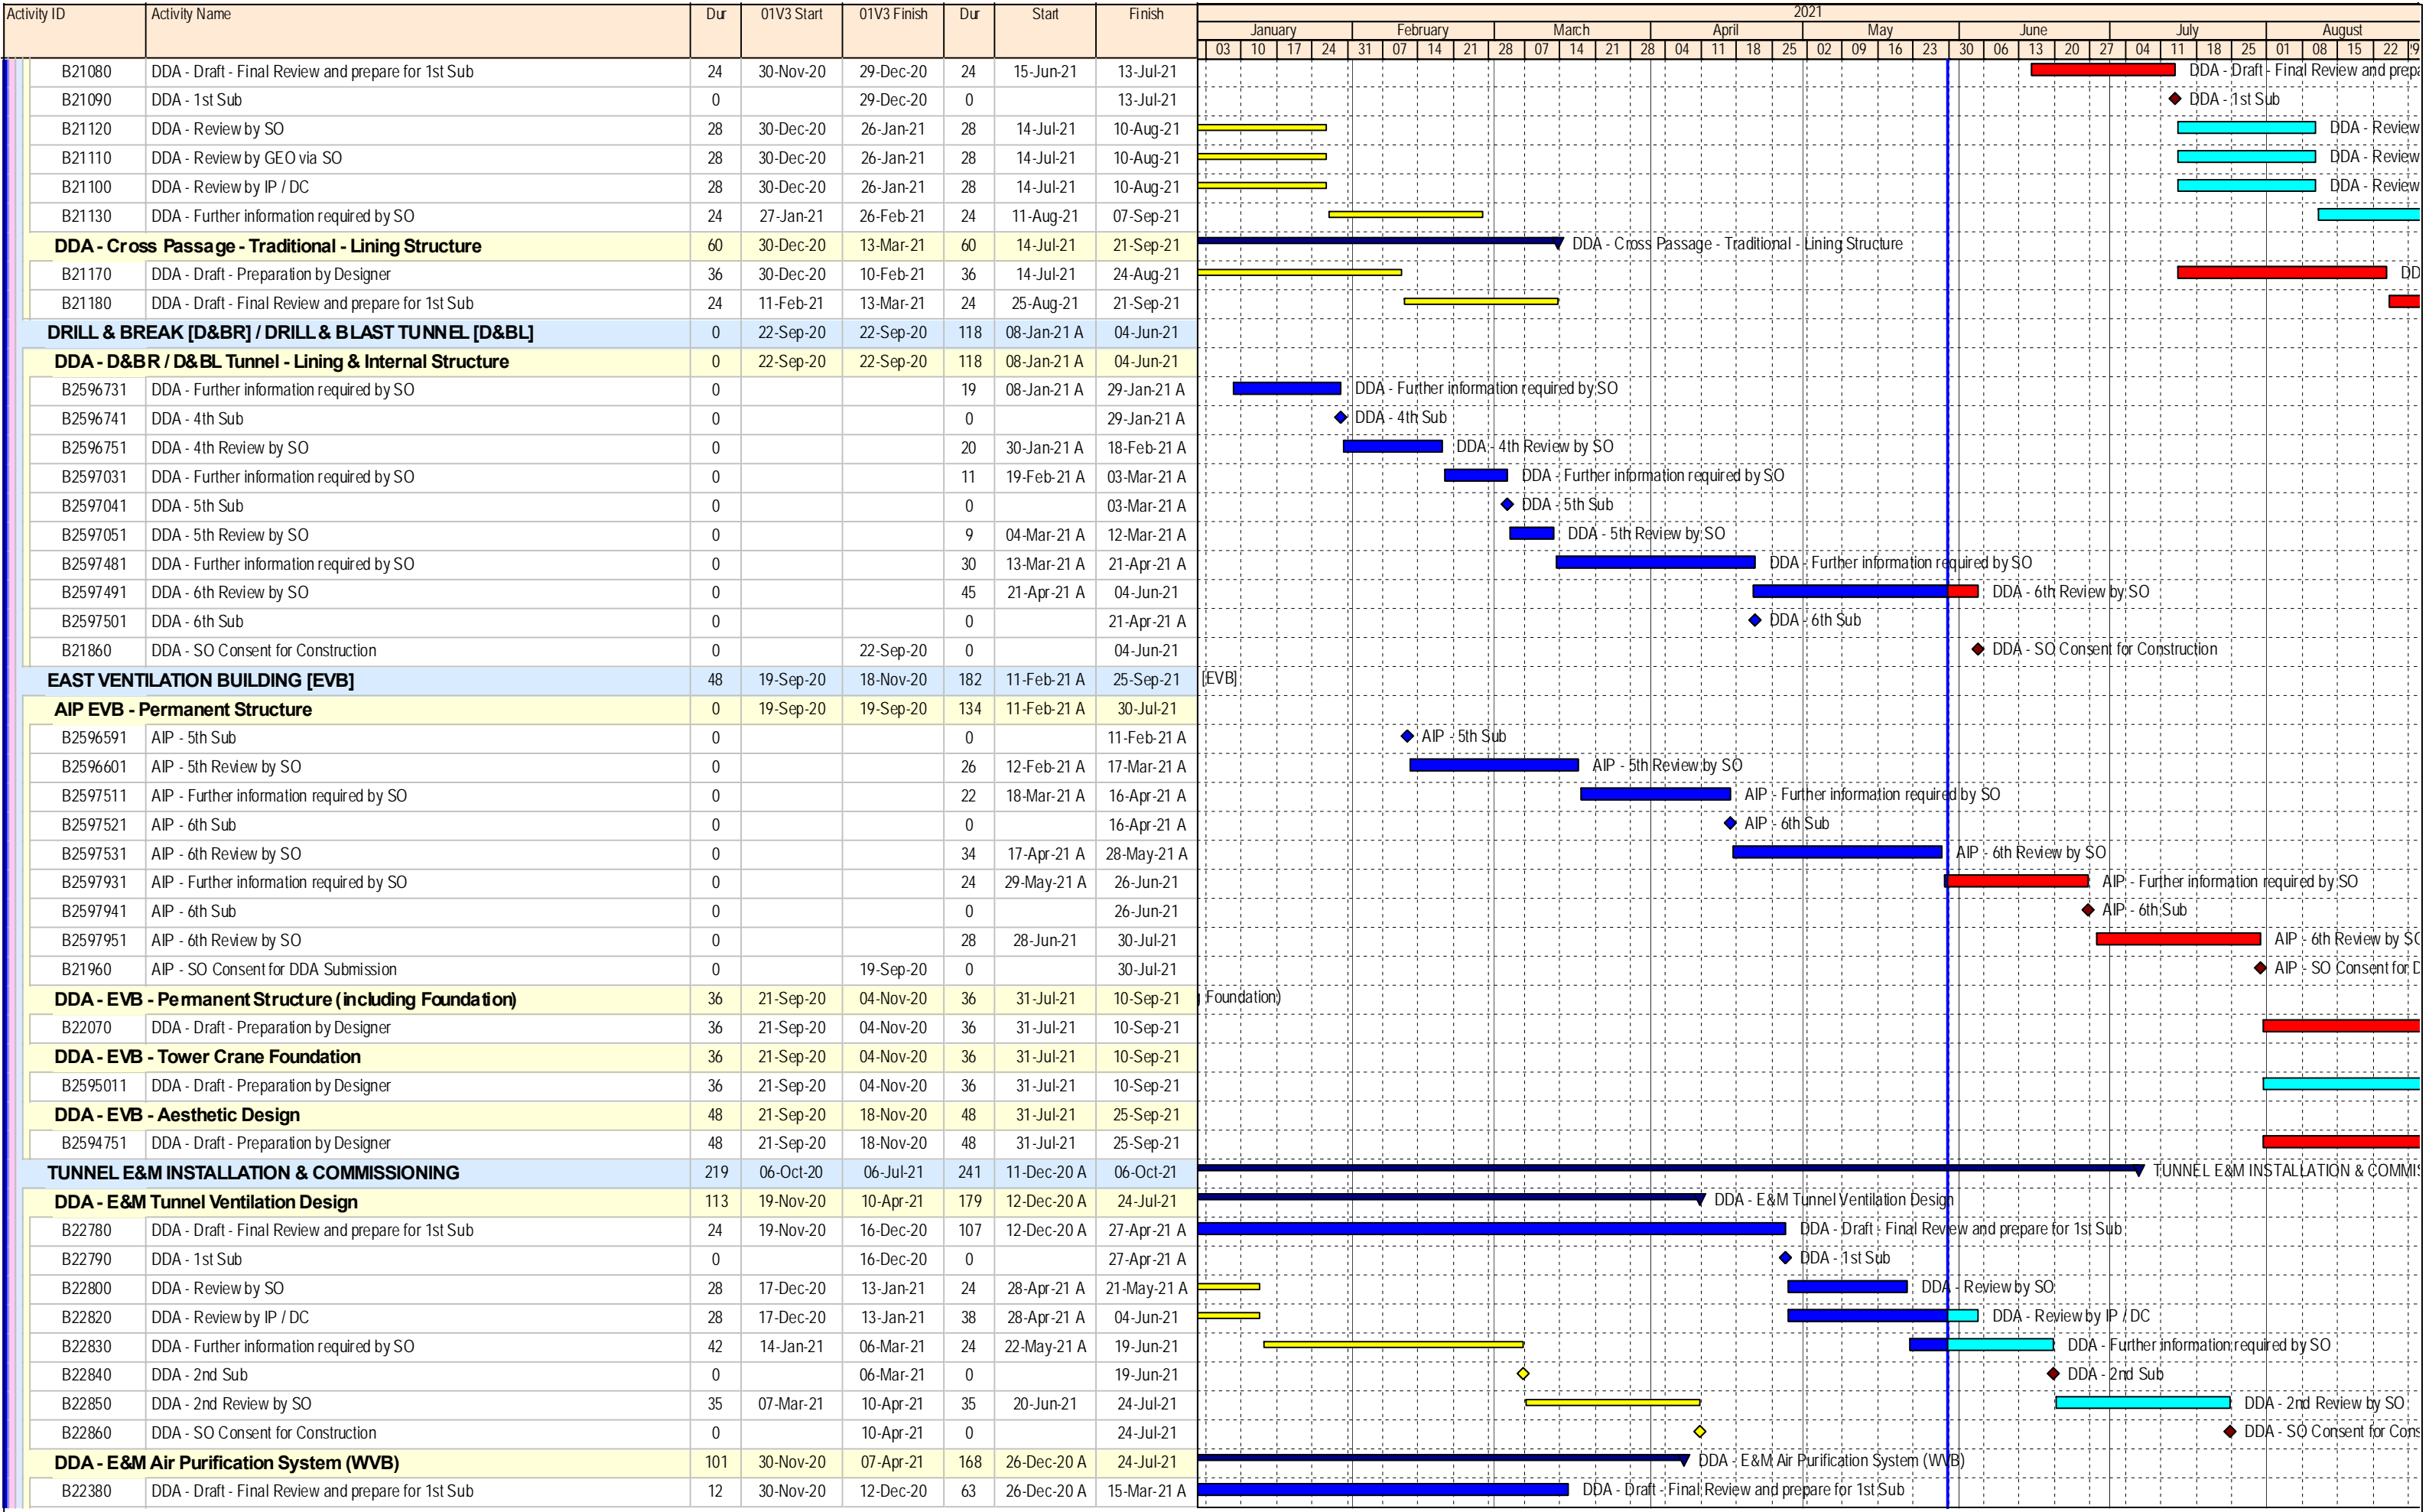


Page 12 of 26
Data Date: 29-May-21

- Milestone
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary
- Planned Bar

**ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (May-21)**



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

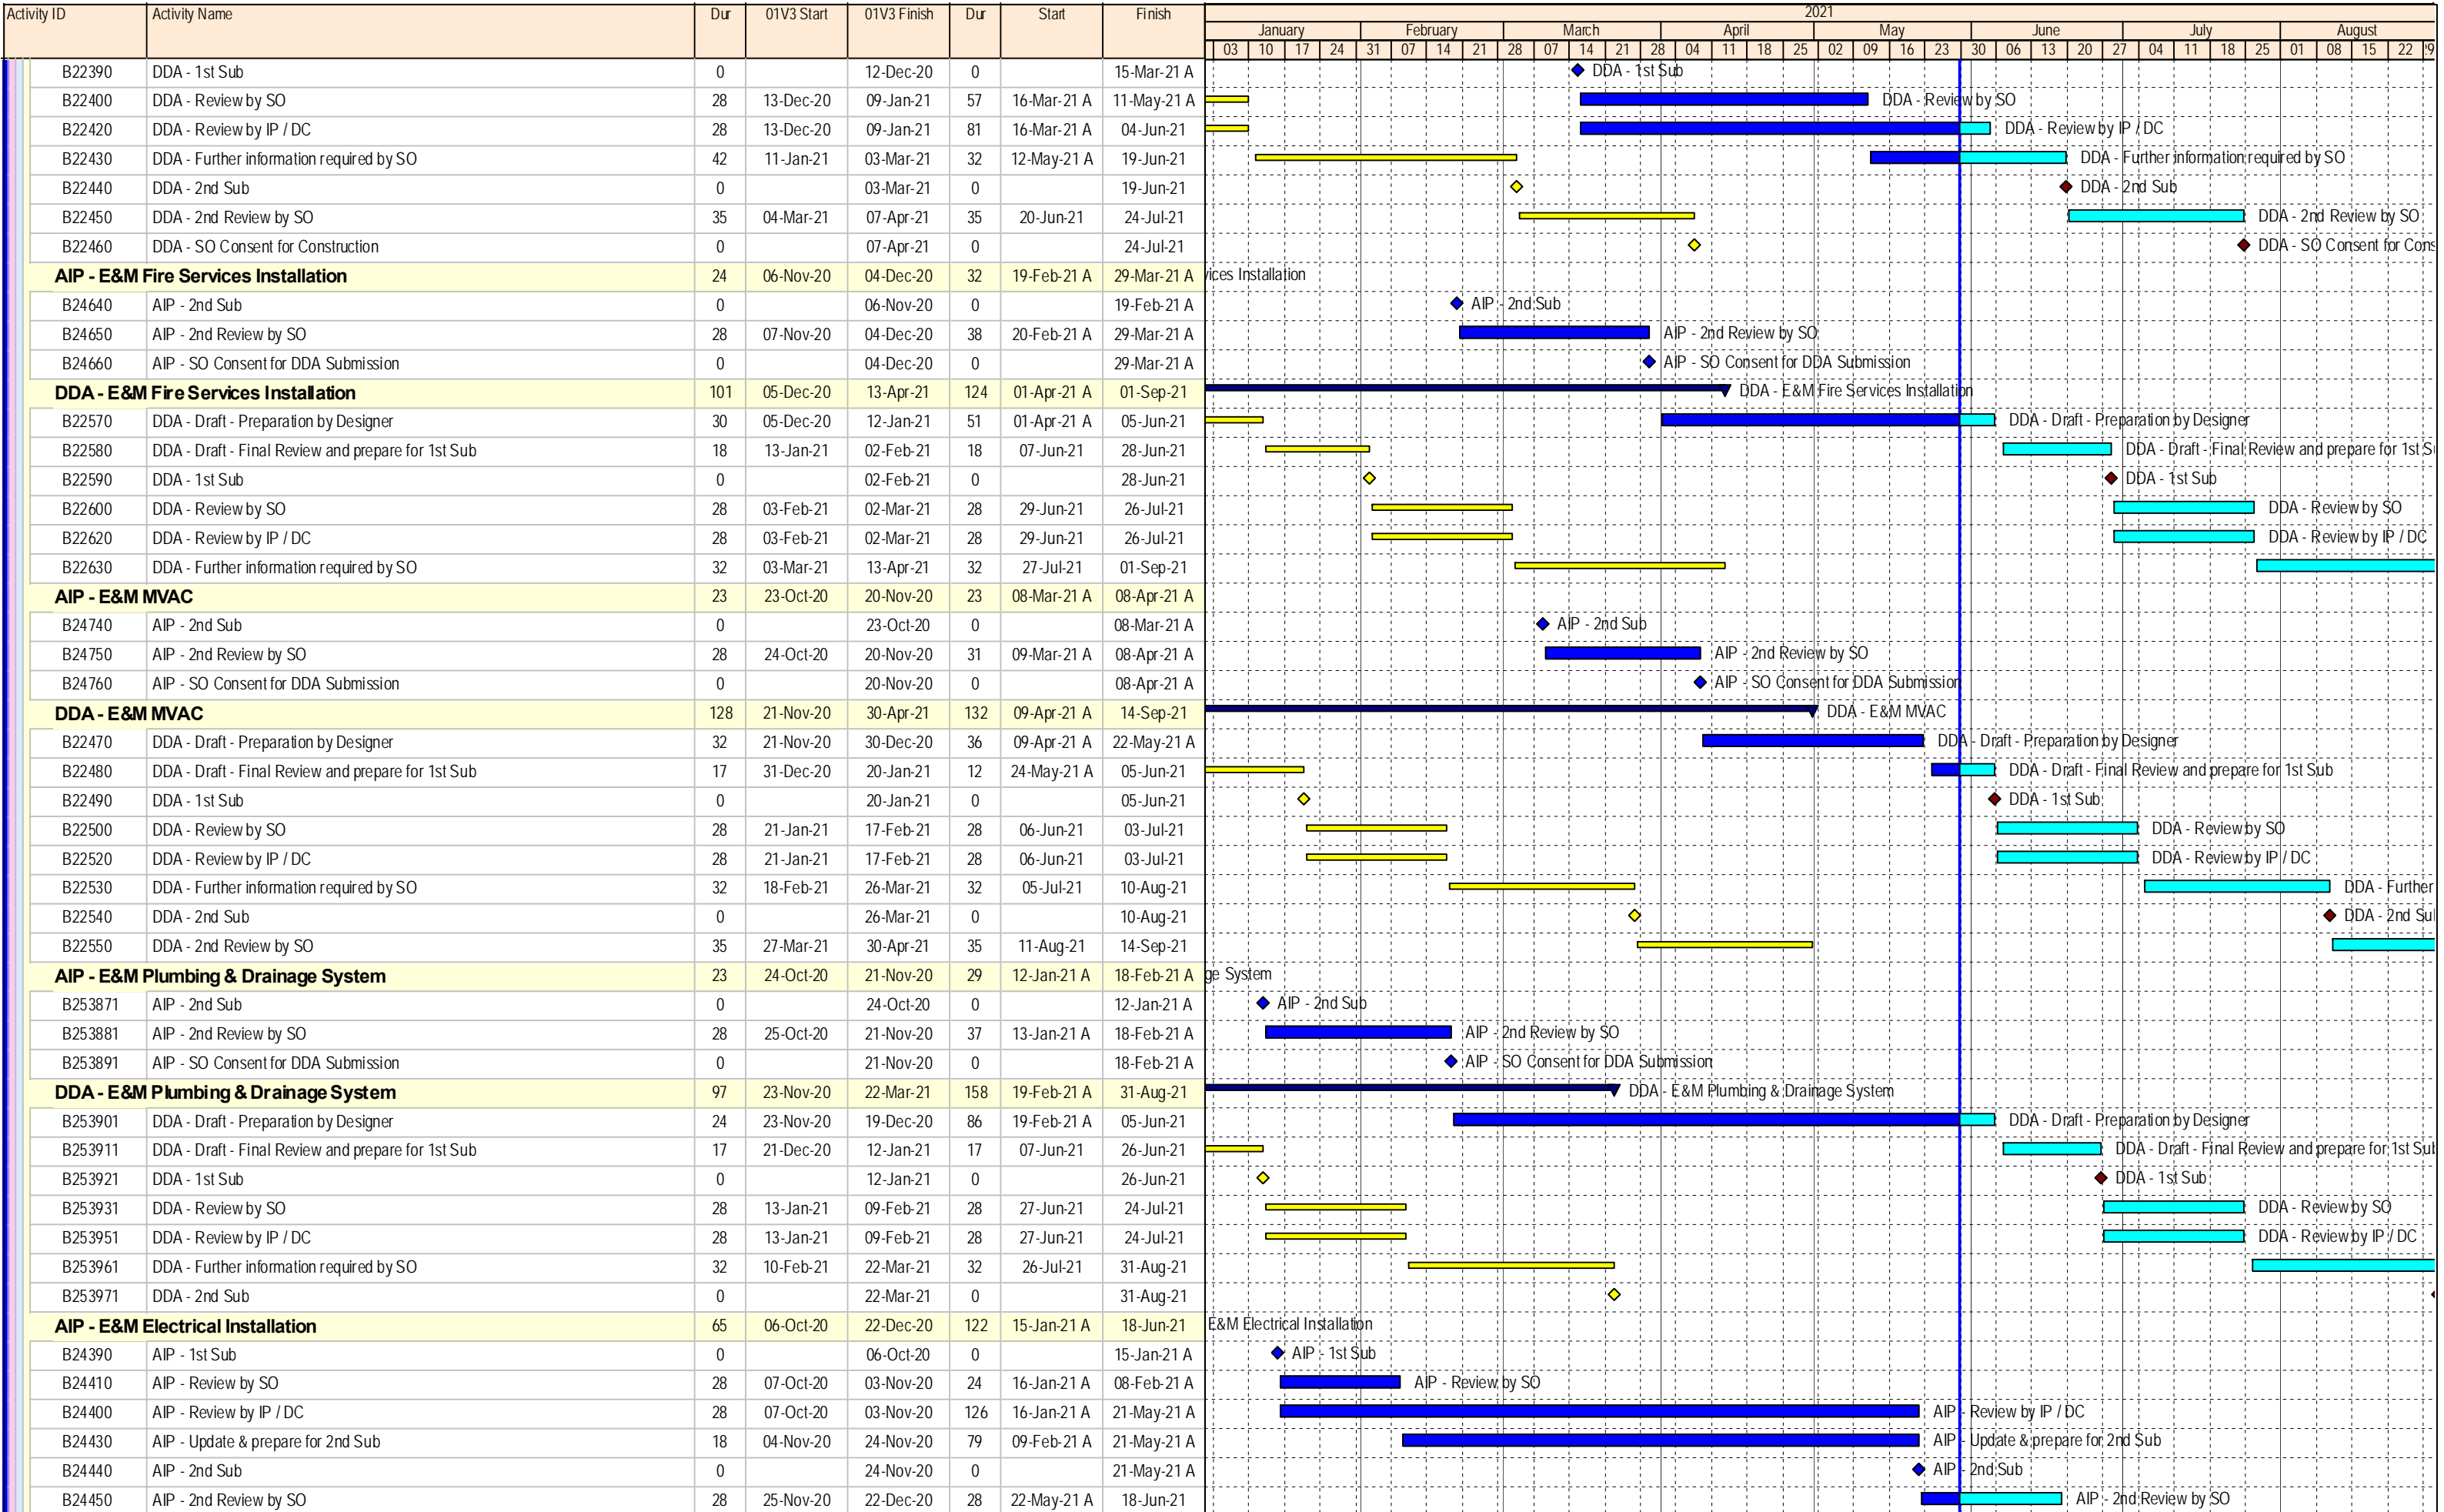


	Milestone
	Planned Bar
	Critical Activity
	Actual Milestone
	Actual Work
	Baseline Milestone
	Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

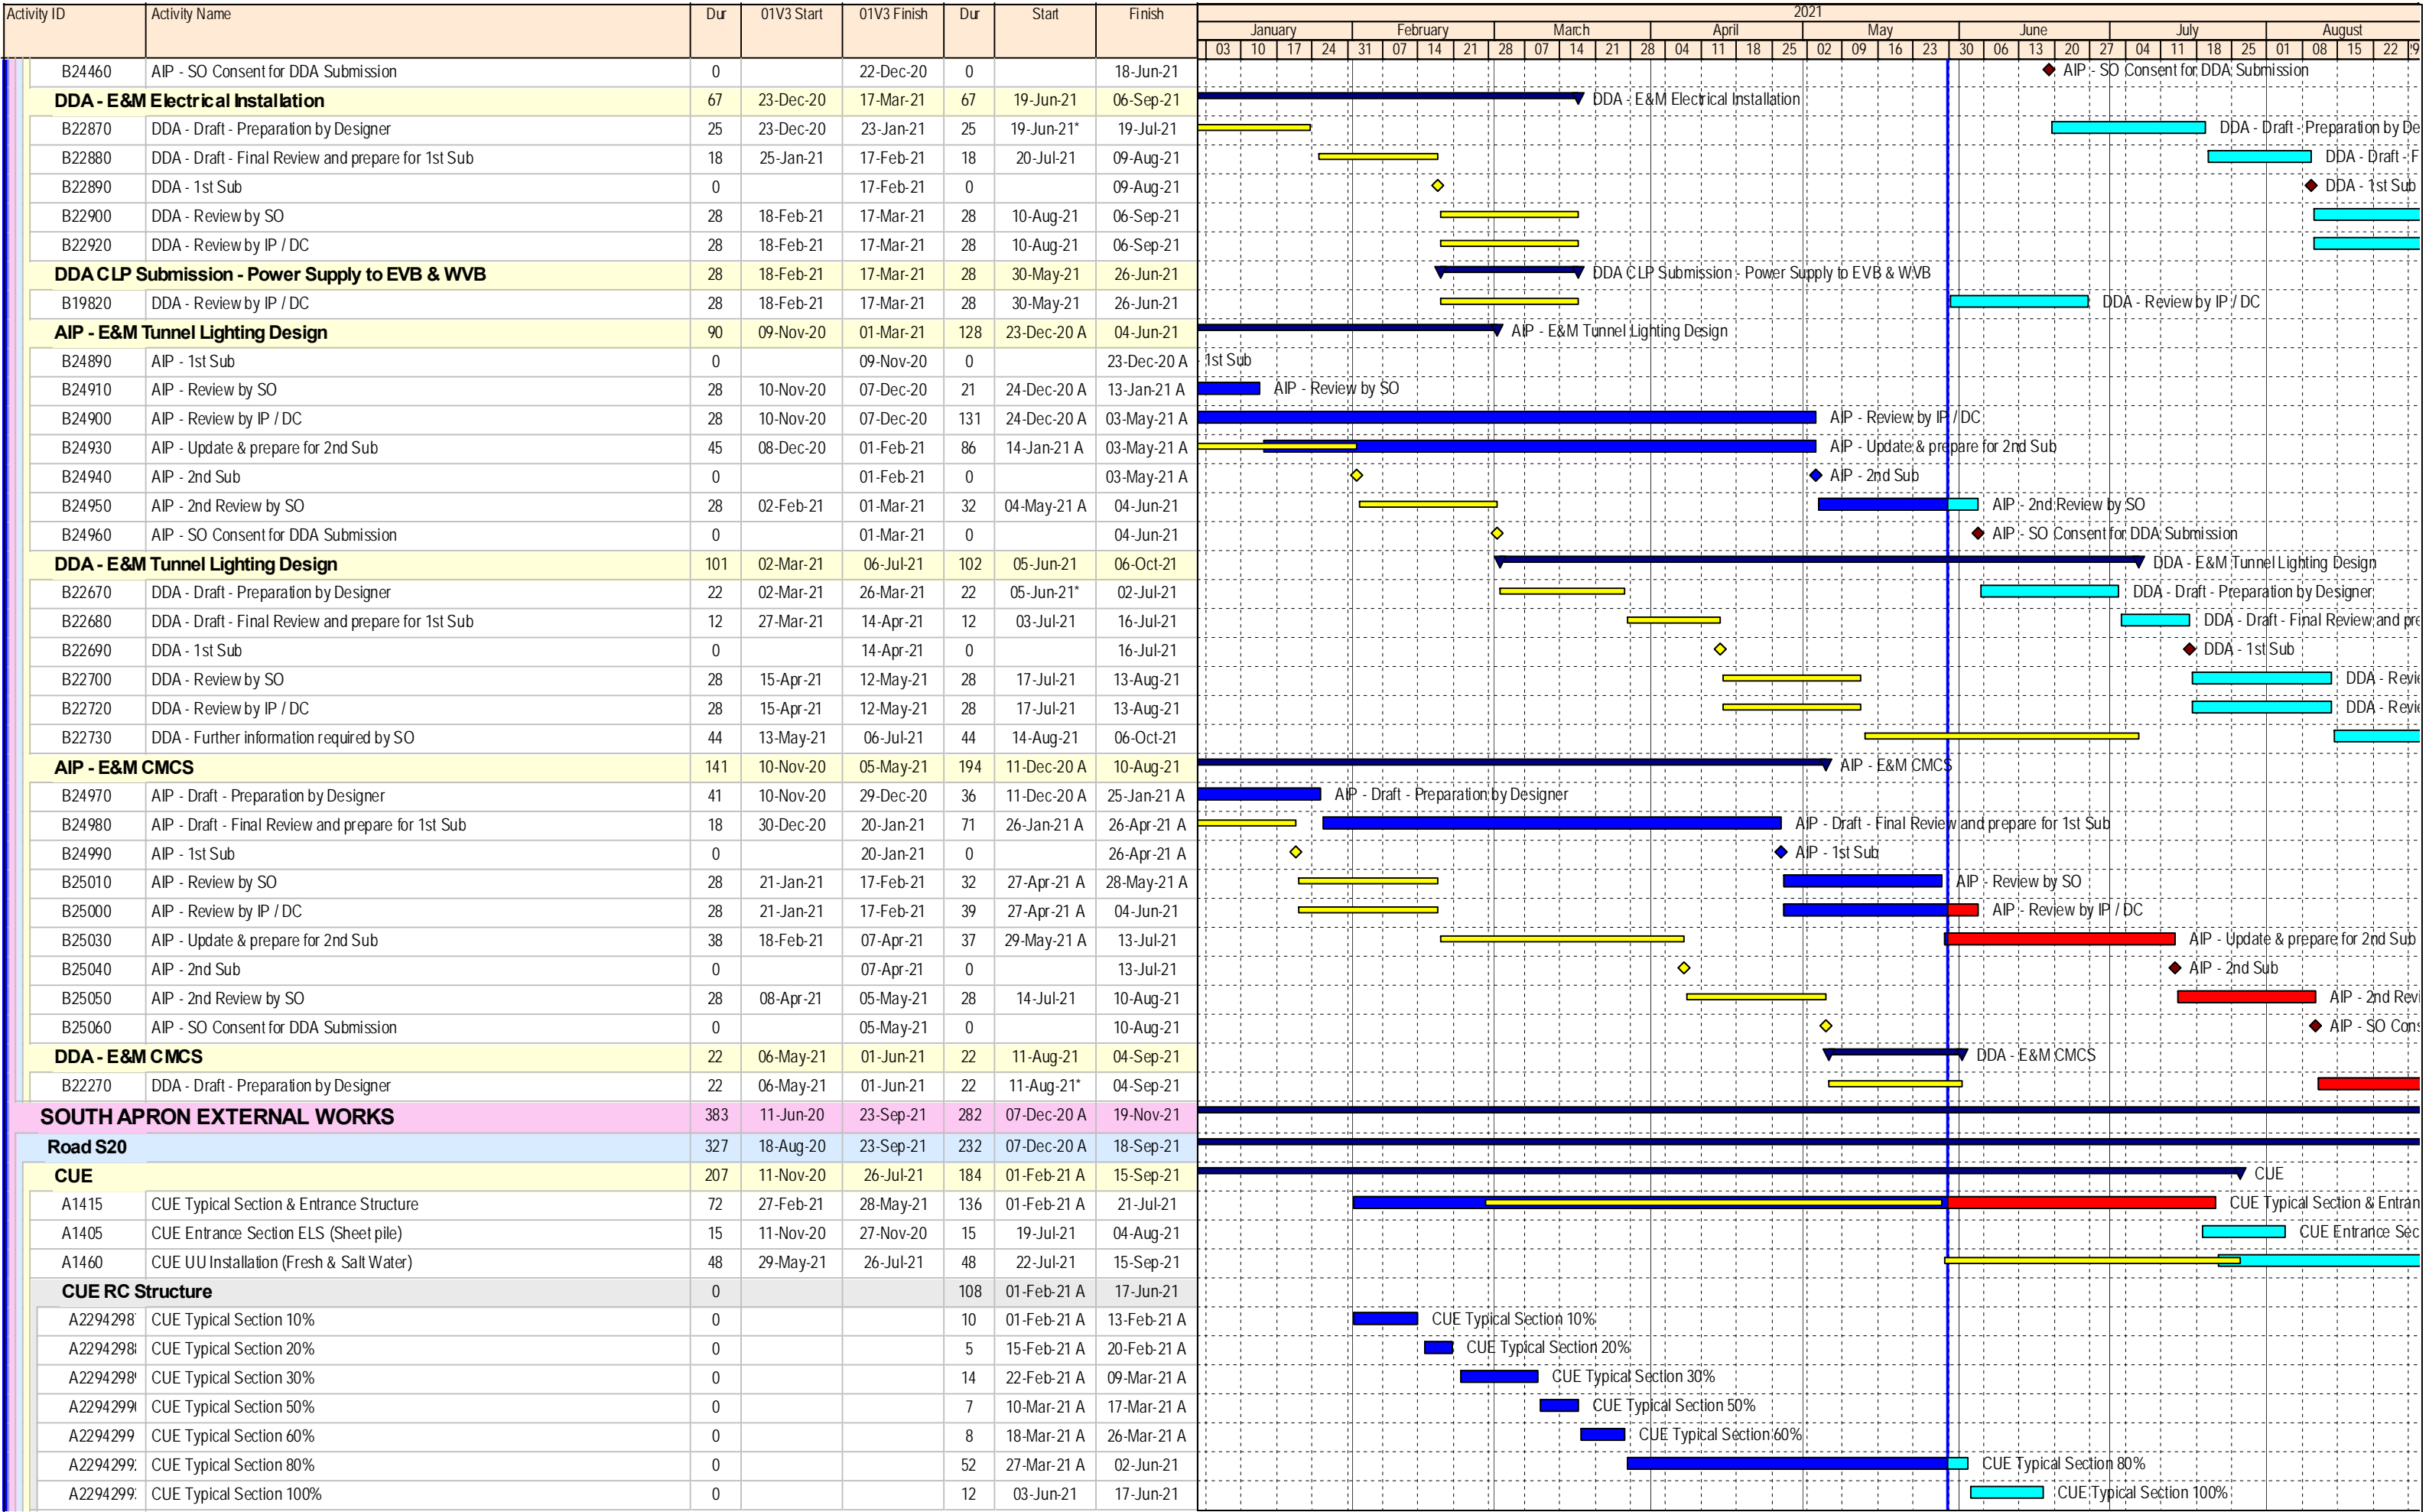


Page 14 of 26
Data Date: 29-May-21


- ◆ Milestone
- ▶ Summary
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

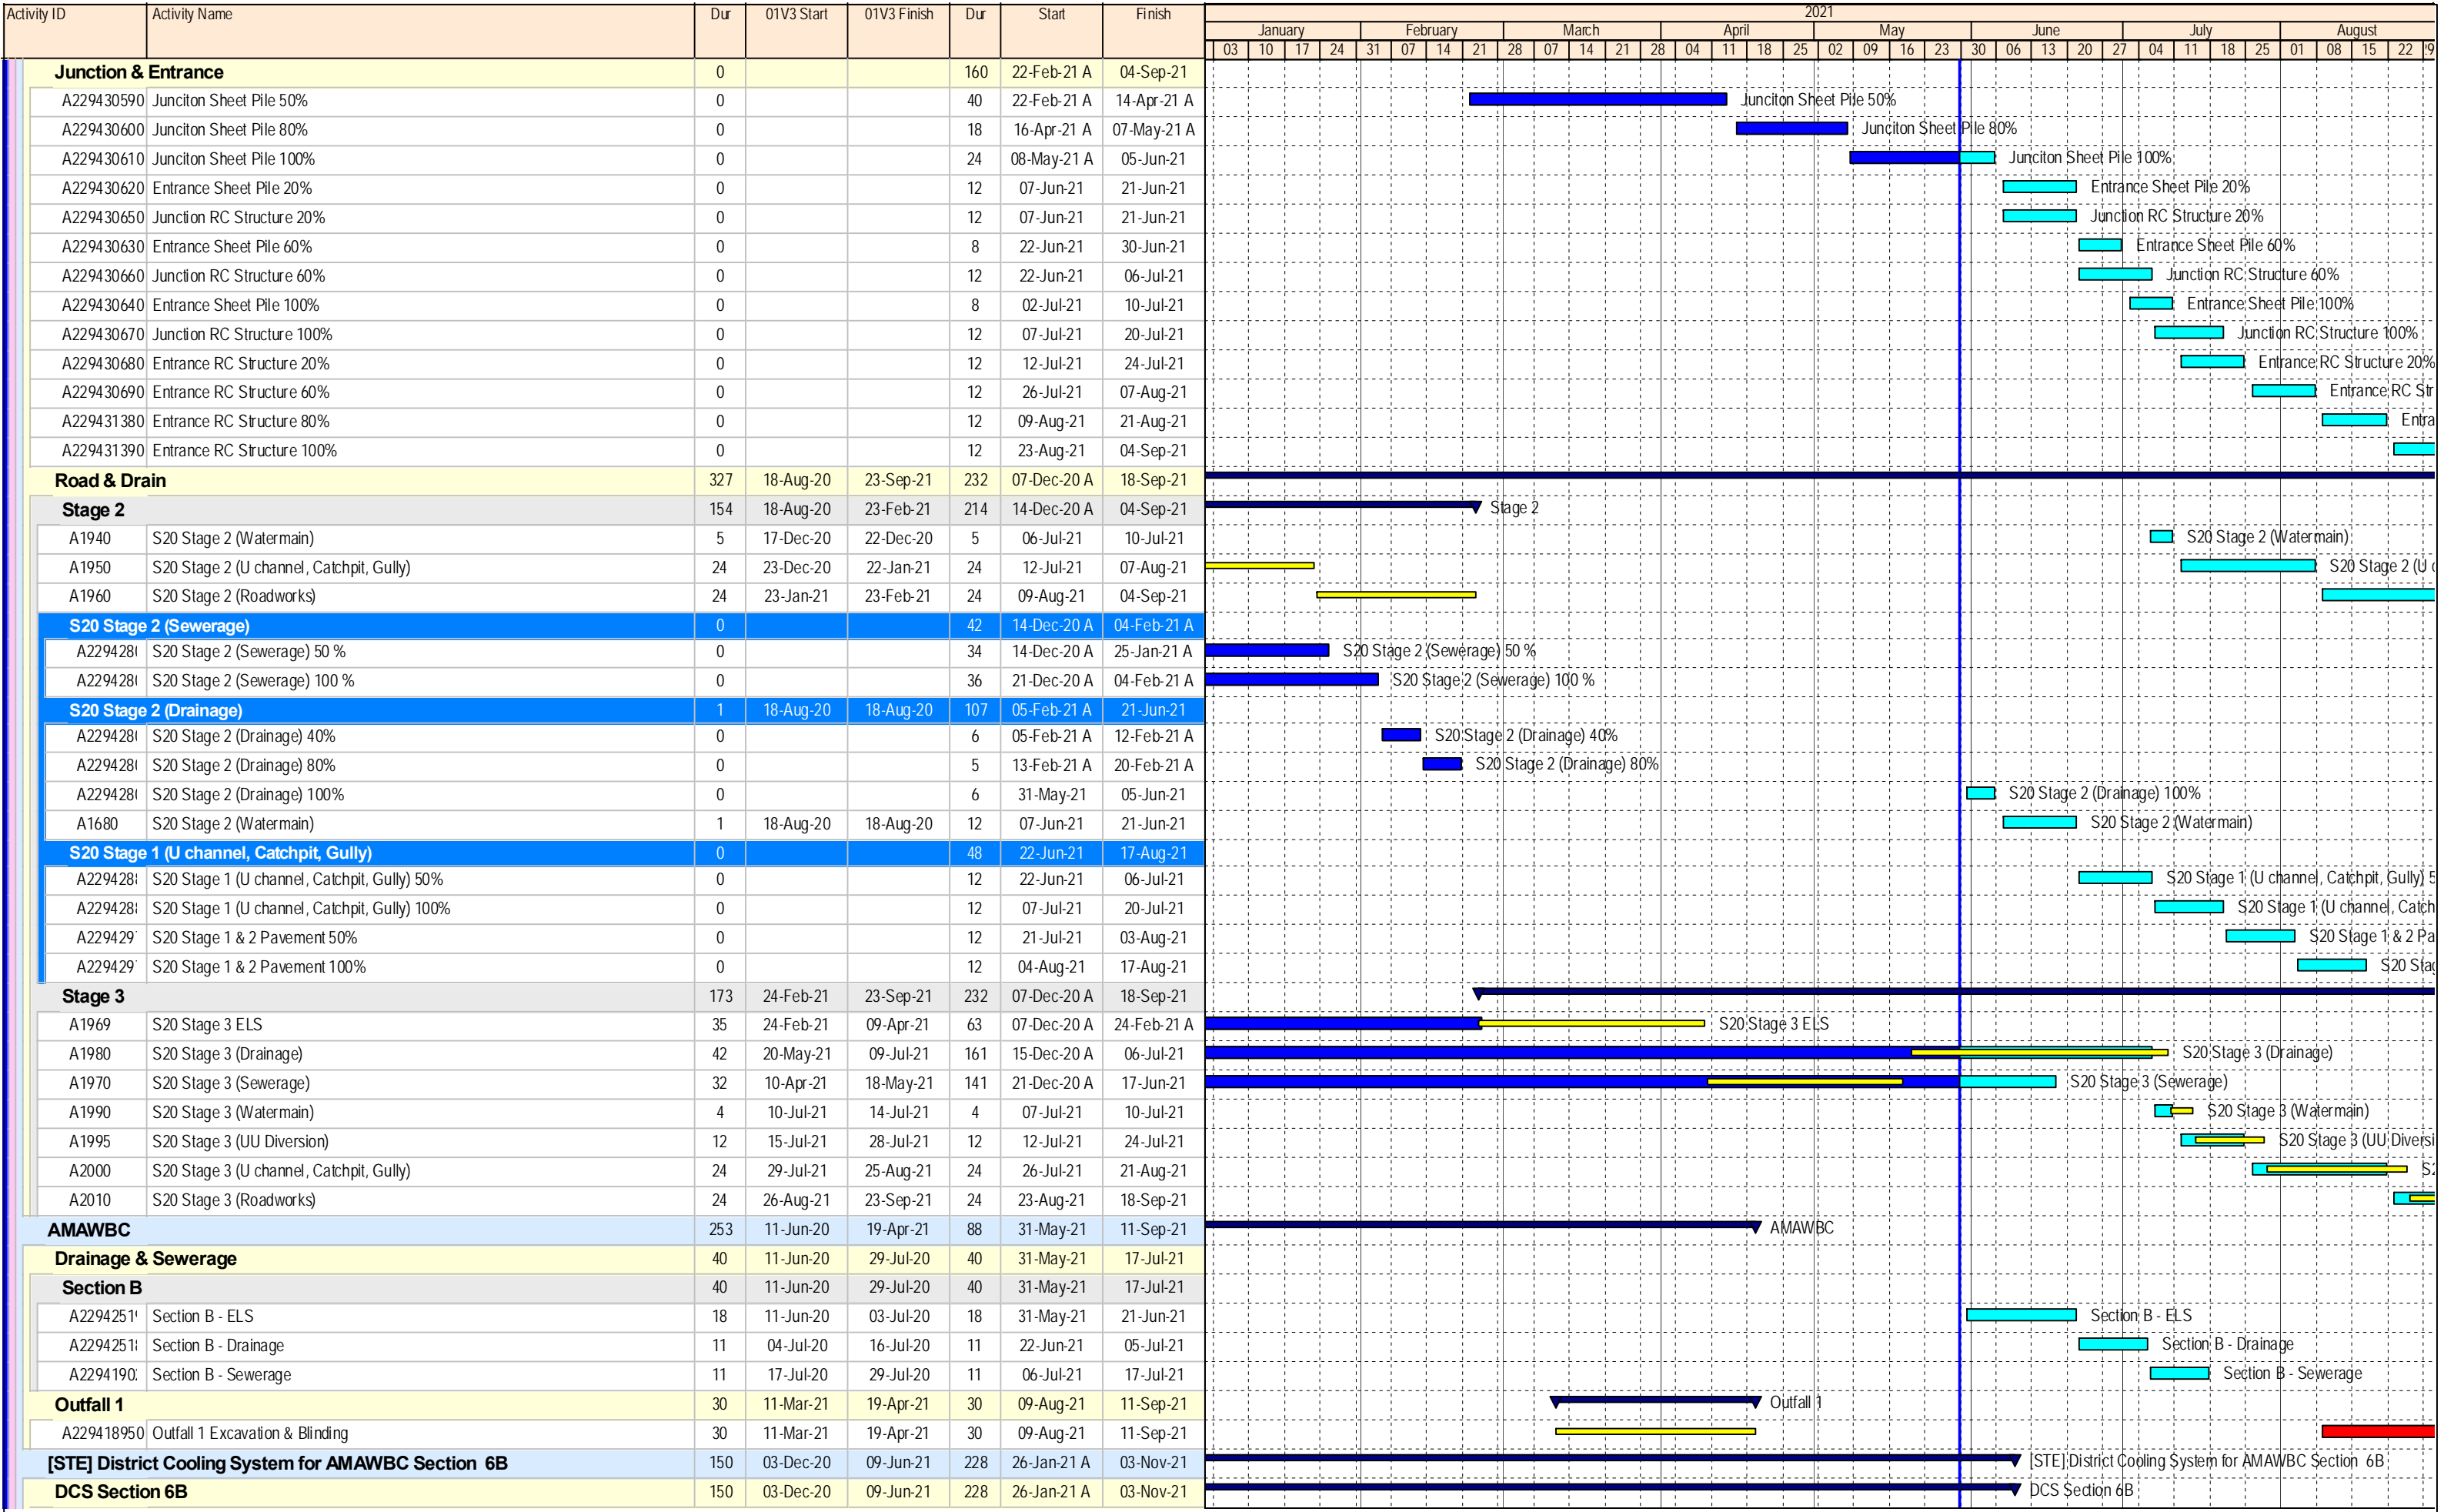


Page 15 of 26
Data Date: 29-May-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

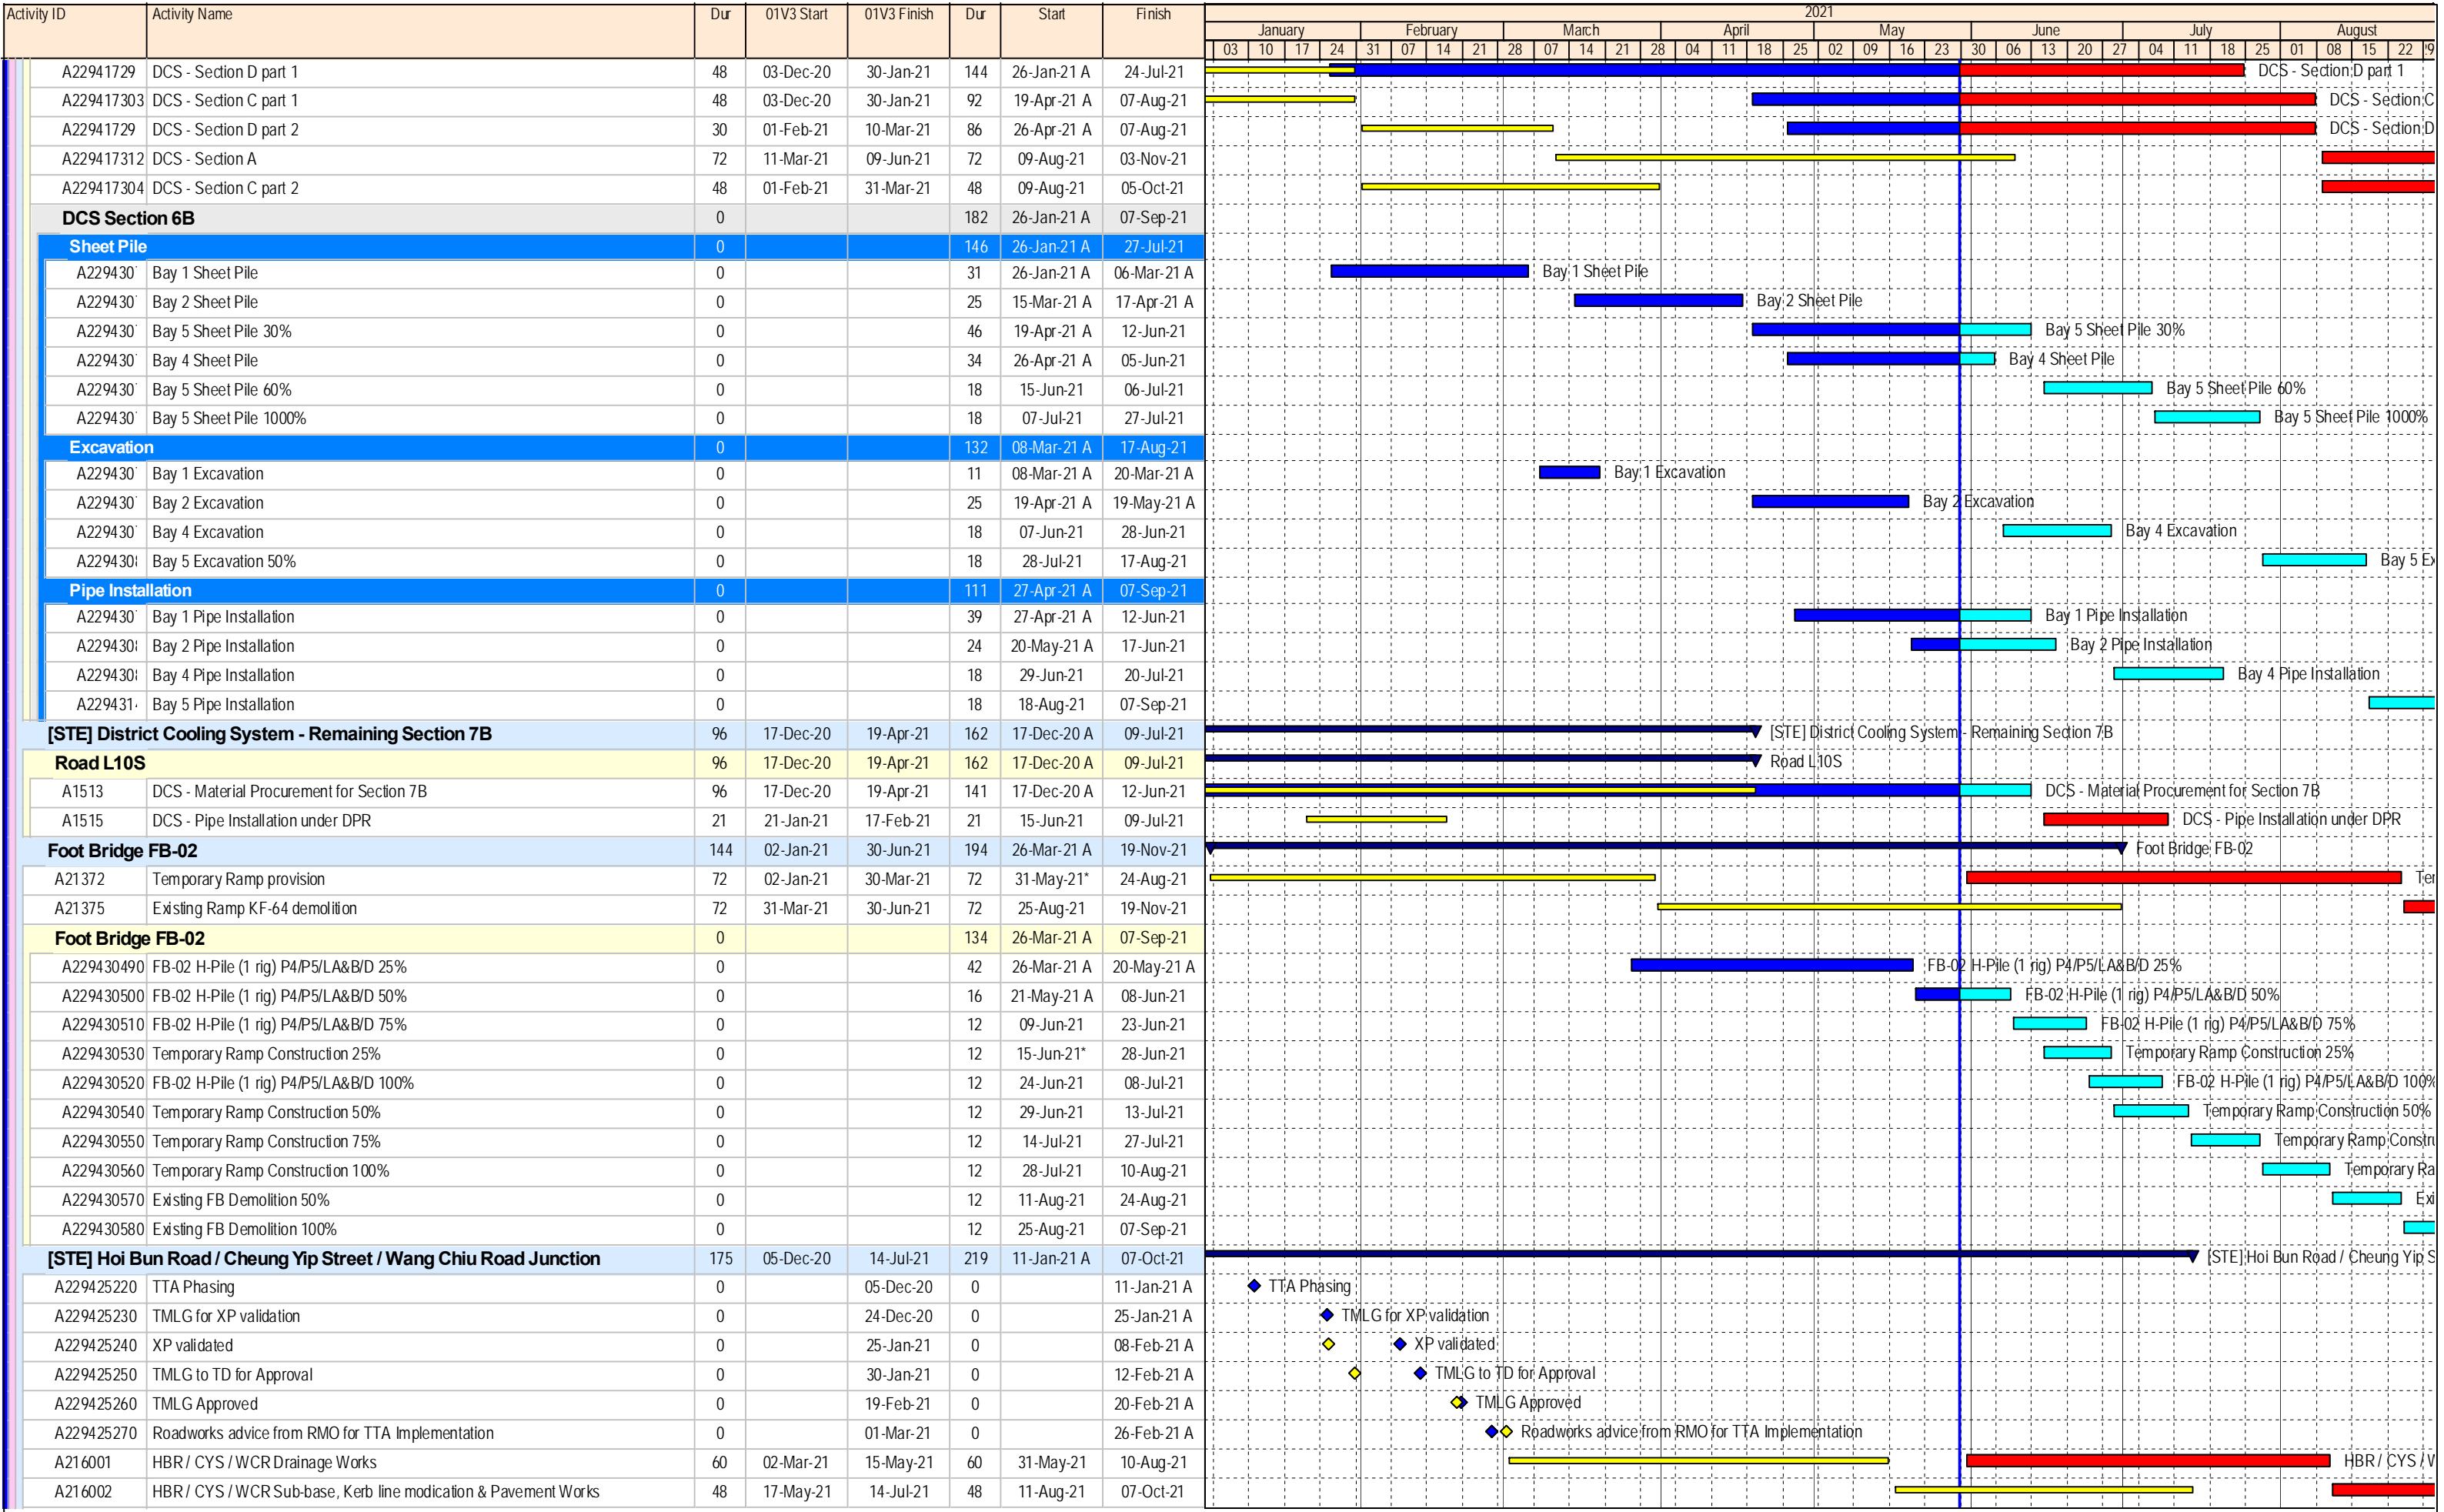

Page 16 of 26
Data Date: 29-May-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

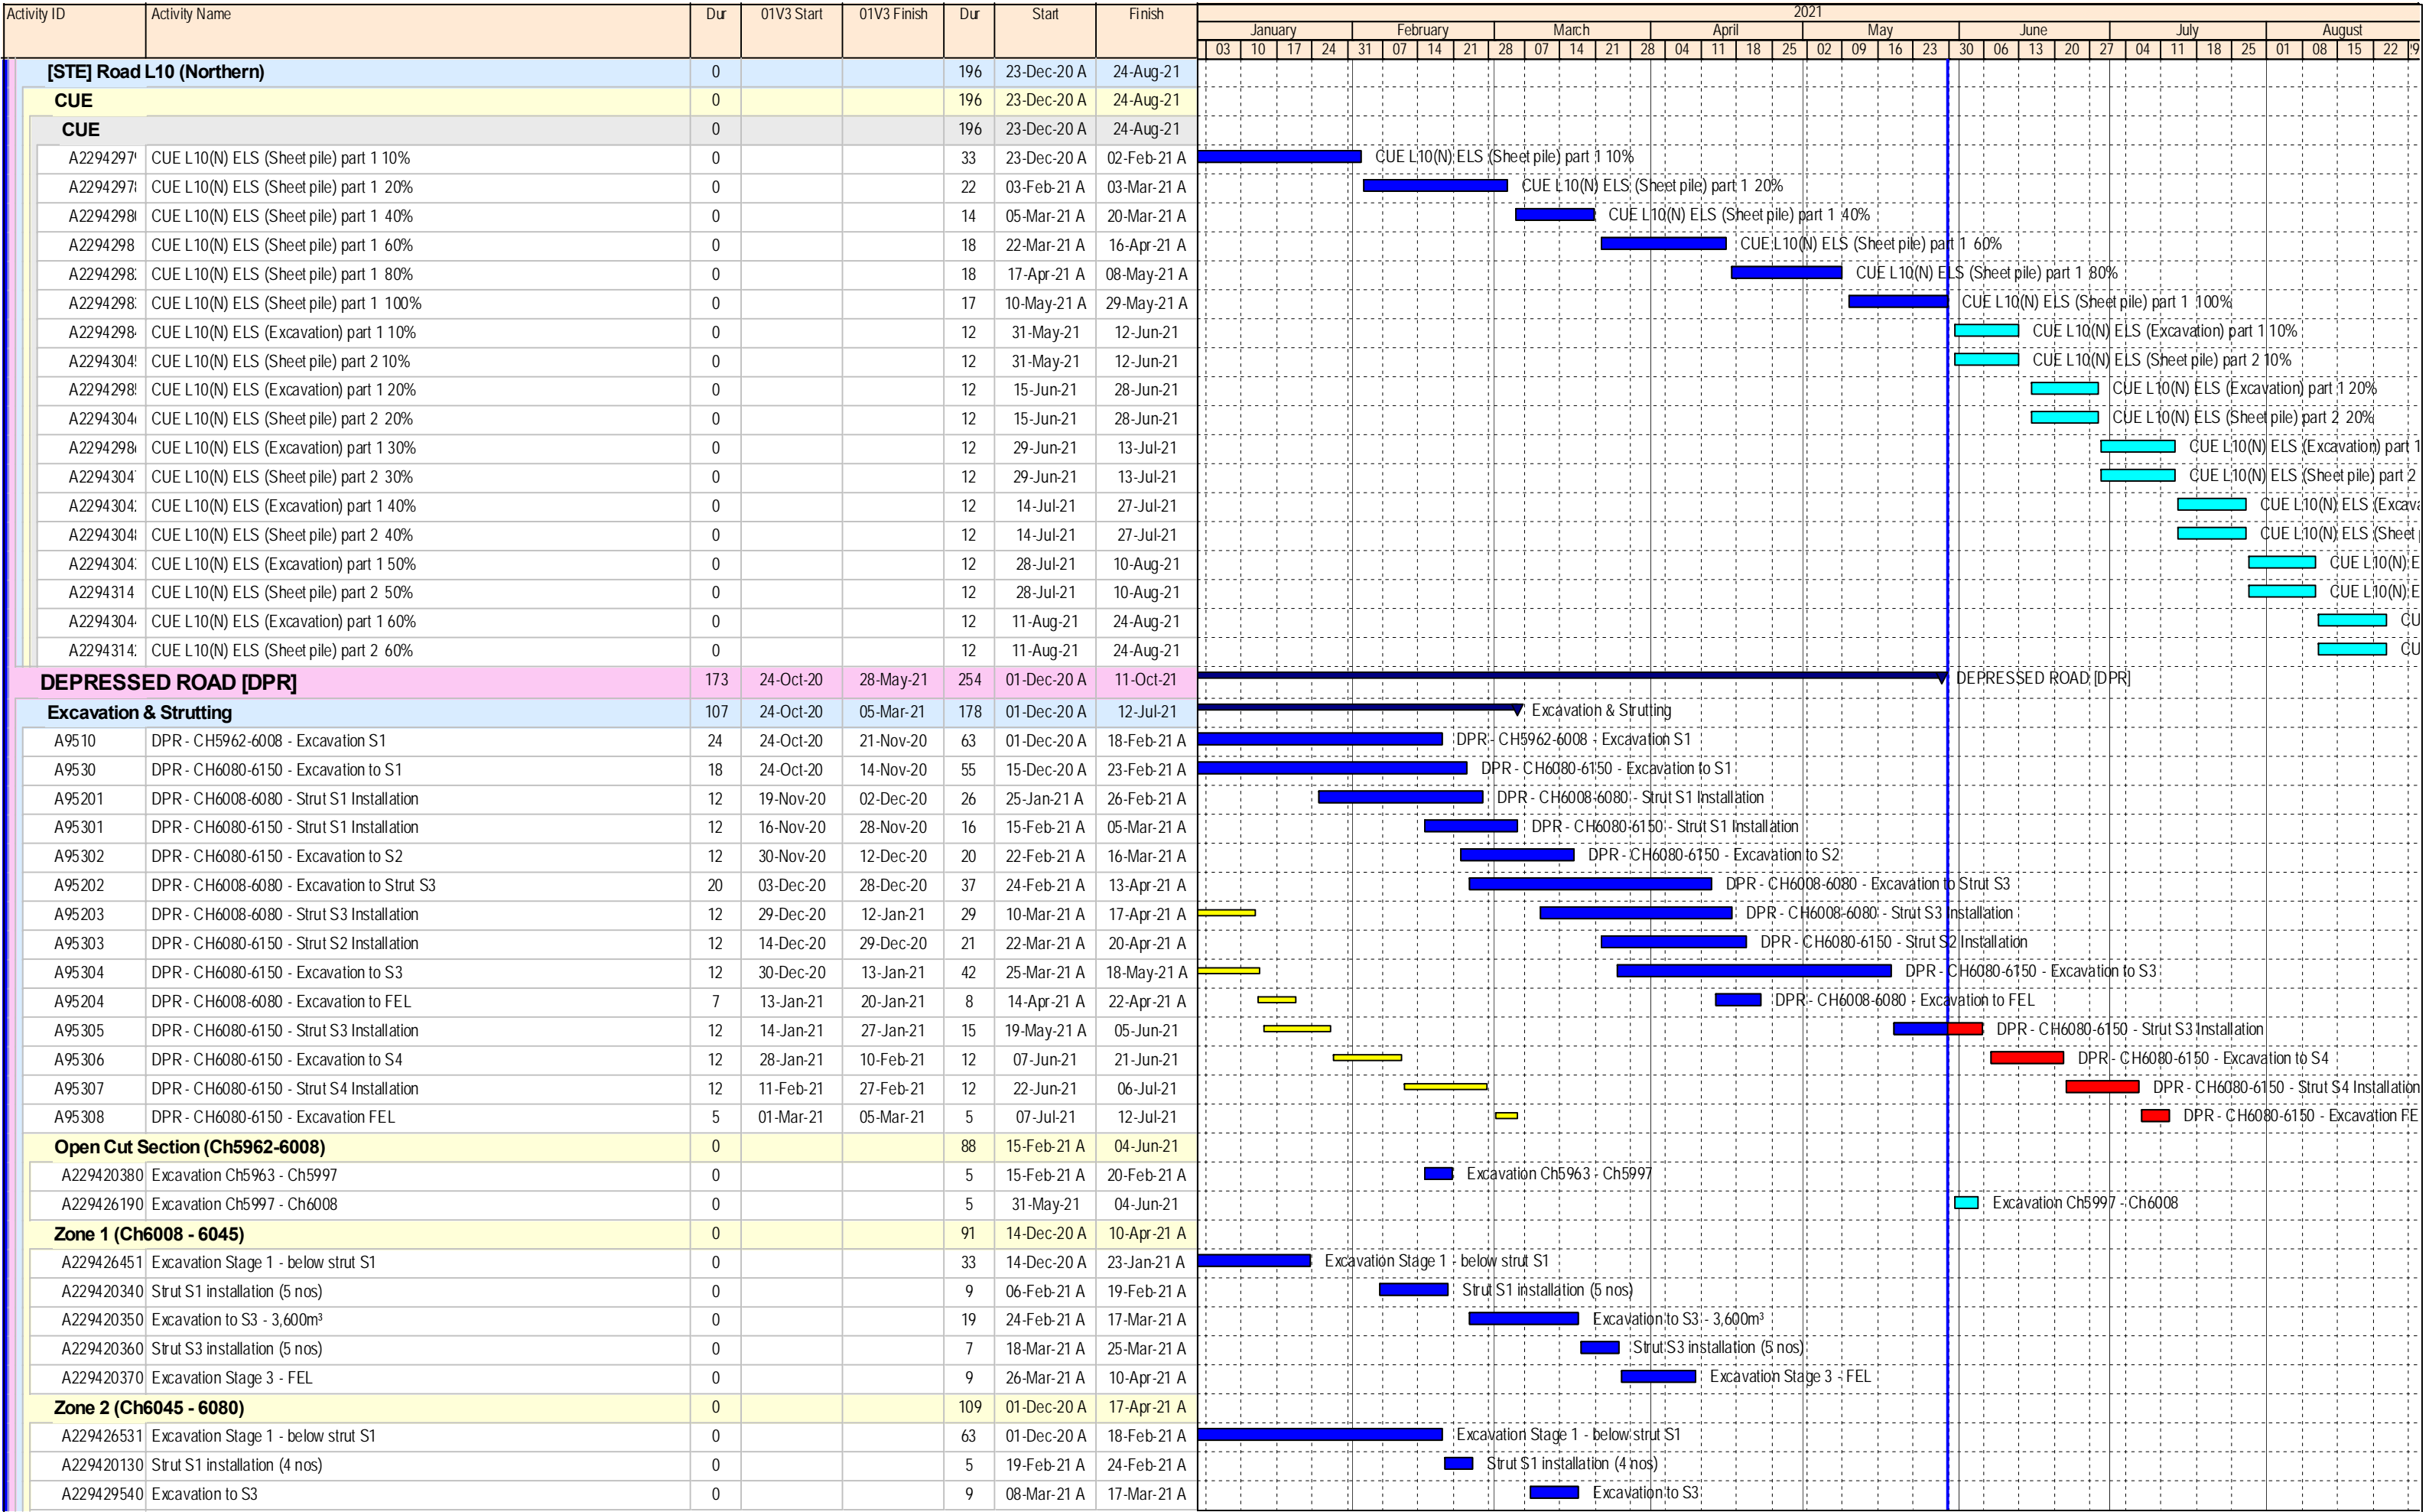

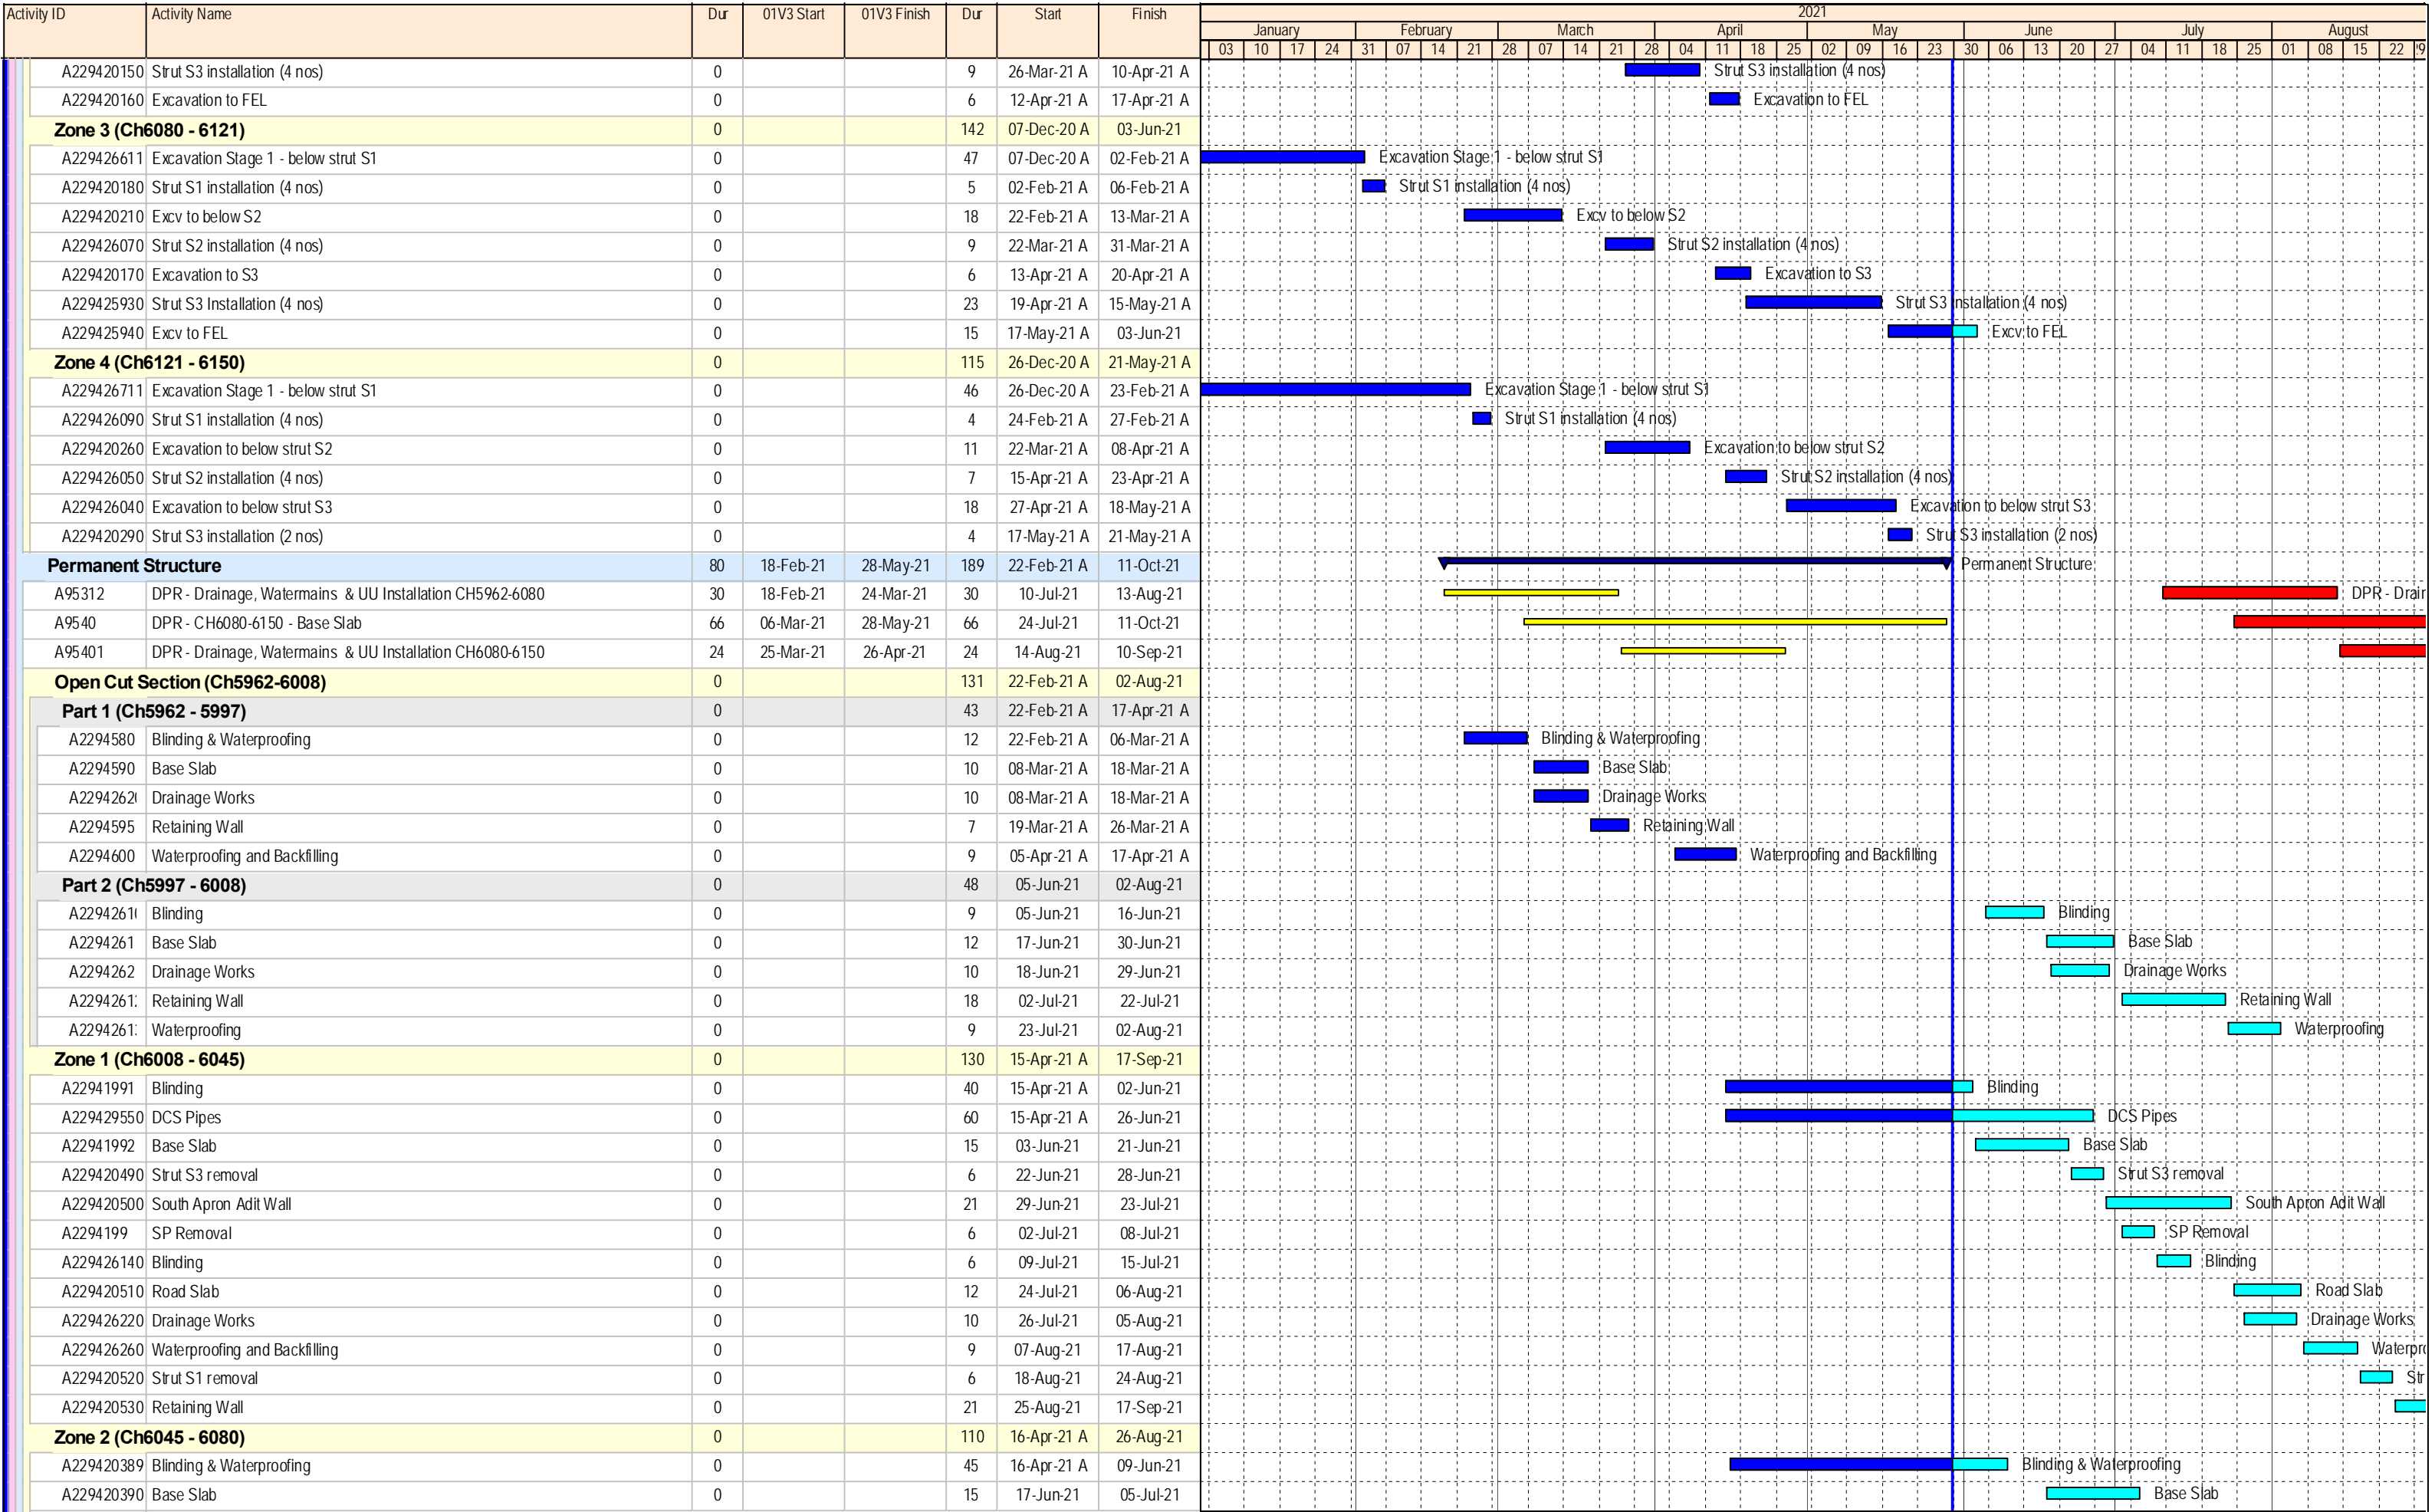

Page 18 of 26 Data Date: 29-May-21		<h2>ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3>Three Months Rolling Programme (May-21)</h3>		Date	Revision	Checked	Approved
				05-Nov-19	00V0	WYu	
				18-Dec-19	00V1	WYu	
				22-Feb-20	01V0	SPa/LLo	WYu
				09-Apr-20	01V1	SPa/LLo	WYu
				17-Jul-20	01V2	SPa/LLo	WYu
				09-Oct-20	01V3	SPa/LLo	WYu

Activity ID	Activity Name	Dur	01V3 Start	01V3 Finish	Dur	Start	Finish	2021																																						
								January				February				March				April				May				June				July				August										
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29				
A114071	Steel Fixing for Capping Beam & Strutting Slab	0			4	01-Dec-20 A	04-Dec-20 A																																							
A114101	Pour 1 Concreting	0			1	07-Dec-20 A	07-Dec-20 A																																							
A114111	Formwork removal & CJ cleaning	0			1	08-Dec-20 A	08-Dec-20 A																																							
Pour 2 (Gantry Beam)		0			19	10-Dec-20 A	04-Jan-21 A																																							
North		0			14	11-Dec-20 A	29-Dec-20 A																																							
A114171	Gantry Beam & Y2N formation works (SAMMON)	0			8	11-Dec-20 A	18-Dec-20 A																																							
A114191	Blinding Concrete (WKK)	0			1	19-Dec-20 A	19-Dec-20 A																																							
A114201	Steel Fixing of Gantry Beam (BP)	0			4	21-Dec-20 A	26-Dec-20 A																																							
A114221	Formworks erection of Gantry Beam (WKK)	0			6	21-Dec-20 A	29-Dec-20 A																																							
South		0			17	10-Dec-20 A	31-Dec-20 A																																							
A114151	ELS Walling & Struts Installation (BTP)	0			4	10-Dec-20 A	14-Dec-20 A																																							
A114182	GW removal & Excavation to Gantry Beam soffit (BTP)	0			2	15-Dec-20 A	16-Dec-20 A																																							
A114181	Gantry Beam & Y2S formation works (SAMMON)	0			5	17-Dec-20 A	22-Dec-20 A																																							
A114183	Blinding Concrete (WKK)	0			1	22-Dec-20 A	22-Dec-20 A																																							
A114231	Steel Fixing of Gantry Beam (BP)	0			8	23-Dec-20 A	30-Dec-20 A																																							
A114241	Formworks erection of Gantry Beam (WKK)	0			4	28-Dec-20 A	31-Dec-20 A																																							
Overall		0			2	02-Jan-21 A	04-Jan-21 A																																							
A114251	Pour 2 Concreting (WKK)	0			1	02-Jan-21 A	02-Jan-21 A																																							
A114261	Pour 2 Formworks removal & CJ Cleaning (WKK & BTP)	0			1	04-Jan-21 A	04-Jan-21 A																																							
Pour 3 (Capping Beam & Strutting Slab S1) Part 2		0			14	05-Jan-21 A	21-Jan-21 A																																							
South		0			2	05-Jan-21 A	06-Jan-21 A																																							
A114433	ELS Removal at Zone C (DARWIN)	0			2	05-Jan-21 A	06-Jan-21 A																																							
Overall		0			13	06-Jan-21 A	21-Jan-21 A																																							
A114281	Blinding Concrete (WKK)	0			2	06-Jan-21 A	07-Jan-21 A																																							
A229428	Backfilling & Formation	0			2	08-Jan-21 A	09-Jan-21 A																																							
A114291	Steel Fixing Pour 3 (BP)	0			4	11-Jan-21 A	14-Jan-21 A																																							
A114311	Pour 3 Concreting (WKK)	0			1	15-Jan-21 A	15-Jan-21 A																																							
A114441	Concrete Strength Gain	0			3	16-Jan-21 A	18-Jan-21 A																																							
A114451	Cut & Cover Bulk Excavation Start	0			0	21-Jan-21 A																																								
Cut & Cover Bulk Excavation		0			180	21-Jan-21 A	31-Aug-21																																							
A2294283	Excavation to below S2	0			15	21-Jan-21 A	04-Feb-21 A																																							
A2294283	Strut S2 Construction	0			9	05-Feb-21 A	13-Feb-21 A																																							
A2294283	Excavation to below S3	0			8	16-Feb-21 A	23-Feb-21 A																																							
A2294283	Strut S3 Construction	0			10	24-Feb-21 A	05-Mar-21 A																																							
A2294283	Excavation to below S4	0			10	09-Mar-21 A	19-Mar-21 A																																							
A2294286	Permanent Strutting Slab S4	0			20	20-Mar-21 A	17-Apr-21 A																																							
A2294289	Excavation to below S5	0			16	20-Apr-21 A	08-May-21 A																																							
A2294289	Steel Strut S5	0			17	10-May-21 A	29-May-21 A																																							
A2294289	Excavation to below S6	0			9	31-May-21	09-Jun-21																																							
A2294295	Steel Strut S6	0			12	10-Jun-21	24-Jun-21																																							
A2294295	Excavation to FEL	0			12	25-Jun-21	09-Jul-21																																							
A2294301	Barrette Trimming	0			9	10-Jul-21	20-Jul-21																																							
A2294313	Drainage, Blinding & Waterproofing	0			12	21-Jul-21	03-Aug-21																																							
A2294301	Base Slab Construction 40%	0			12	04-Aug-21	17-Aug-21																																							
A2294313	Base Slab Construction 80%	0			12	18-Aug-21	31-Aug-21																																							
Launching Shaft ELS		0			165	02-Dec-20 A	26-Jun-21																																							
Capping Beam		0			59	02-Dec-20 A	12-Feb-21 A																																							
Cell 2		0			49	02-Dec-20 A	31-Jan-21 A																																							
Pour 4 (South)		<																																												


Activity ID	Activity Name	Dur	01V3 Start	01V3 Finish	Dur	Start	Finish	2021																																		
								January				February				March				April				May				June				July				August						
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29
Civil Works for TBM Assembly								99	07-Jun-21	04-Oct-21	72	28-Jun-21	20-Sep-21																													
A2370	Cell 2 WB Base slab	24	07-Jun-21	06-Jul-21	24	28-Jun-21	26-Jul-21	Cell 2 WB Base slab																																		
A2380	Cell 1 WB Tympanum	36	07-Jun-21	20-Jul-21	36	28-Jun-21	09-Aug-21	Cell 1 WB Tympanum																																		
A2425	C&C Dwal Removal Lead time	12	17-Jul-21	30-Jul-21	12	02-Jul-21	15-Jul-21	C&C Dwal Removal Lead time																																		
A2470	C&C Shaft - Base Slab	36	31-Jul-21	10-Sep-21	36	16-Jul-21	26-Aug-21	C&C Shaft - Base Slab																																		
A2390	Cell 1 WB Base Slab	24	07-Jul-21	03-Aug-21	24	27-Jul-21	23-Aug-21	Cell 1 WB Base Slab																																		
A2400	Cell 2 EB Base slab	24	07-Jul-21	03-Aug-21	24	27-Jul-21	23-Aug-21	Cell 2 EB Base slab																																		
A2410	Cell 1 EB Tympanum	36	21-Jul-21	31-Aug-21	36	10-Aug-21	20-Sep-21	Cell 1 EB Tympanum																																		
A2420	Cell 1 EB Base Slab	24	04-Aug-21	31-Aug-21	24	24-Aug-21	20-Sep-21	Cell 1 EB Base Slab																																		
A2520	C&C Strut removal for G2 Shifting	18	11-Sep-21	04-Oct-21	18	27-Aug-21	16-Sep-21	C&C Strut removal for G2 Shifting																																		
Launching Shaft RC Structure								0			63	28-Jun-21	09-Sep-21																													
Base Slab								0			63	28-Jun-21	09-Sep-21																													
A2294309	Blinding & Waterproofing	0			9	28-Jun-21	08-Jul-21	Blinding & Waterproofing																																		
A2294296	Base Slab Cell 2 30%	0			12	09-Jul-21	22-Jul-21	Base Slab Cell 2 30%																																		
A2294301	Base Slab Cell 2 80%	0			12	23-Jul-21	05-Aug-21	Base Slab Cell 2 80%																																		
A2294301	Base Slab Cell 2 100%	0			6	06-Aug-21	12-Aug-21	Base Slab Cell 2 100%																																		
A2294302	Base Slab Cell 1 25%	0			12	13-Aug-21	26-Aug-21	Base Slab Cell 1 25%																																		
A2294309	Base Slab Cell 1 50%	0			12	27-Aug-21	09-Sep-21	Base Slab Cell 1 50%																																		
Tympanum								0			57	28-Jun-21	02-Sep-21																													
A2294309	Blinding & Waterproofing	0			9	28-Jun-21	08-Jul-21	Blinding & Waterproofing																																		
A2294296	Tympanum Pour 1	0			12	09-Jul-21	22-Jul-21	Tympanum Pour 1																																		
A2294301	Tympanum Pour 2	0			6	23-Jul-21	29-Jul-21	Tympanum Pour 2																																		
A2294301	Tympanum Pour 3	0			10	30-Jul-21	10-Aug-21	Tympanum Pour 3																																		
A2294301	Tympanum Pour 4	0			10	11-Aug-21	21-Aug-21	Tympanum Pour 4																																		
A2294301	Tympanum Pour 5	0			10	23-Aug-21	02-Sep-21	Tympanum Pour 5																																		
SUB-SEA TBM TUNNEL - WESTBOUND								351	23-Oct-20	29-Dec-21	251	01-Dec-20 A	07-Oct-21																													
Precast Fabrication								216	12-Apr-21	29-Dec-21	234	21-Dec-20 A	07-Oct-21																													
TBM Precast Segments								216	12-Apr-21	29-Dec-21	234	21-Dec-20 A	07-Oct-21																													
A9440-020	Precast TBM Segment - 10%	36	12-Apr-21	25-May-21	20	21-Dec-20 A	15-Jan-21 A	Precast TBM Segment - 10%																																		
A9440-030	Precast TBM Segment - 20%	36	26-May-21	08-Jul-21	58	16-Jan-21 A	27-Mar-21 A	Precast TBM Segment - 20%																																		
A9440-040	Precast TBM Segment - 30%	36	09-Jul-21	19-Aug-21	48	29-Mar-21 A	29-May-21 A	Precast TBM Segment - 30%																																		
A9440-050	Precast TBM Segment - 40%	36	20-Aug-21	02-Oct-21	36	31-May-21	13-Jul-21	Precast TBM Segment - 40%																																		
A9440-060	Precast TBM Segment - 50%	36	04-Oct-21	15-Nov-21	36	14-Jul-21	24-Aug-21	Precast TBM Segment - 50%																																		
A9440-070	Precast TBM Segment - 60%	36	16-Nov-21	29-Dec-21	36	25-Aug-21	07-Oct-21	Precast TBM Segment - 60%																																		
Site Establishment								275	23-Oct-20	27-Sep-21	243	01-Dec-20 A	27-Sep-21																													
Precast Elements Storage Yard								0			143	22-Mar-21 A	13-Sep-21																													
Segment Yard								0			143	22-Mar-21 A	13-Sep-21																													
A2294285	Foundation civil works part 1	0			59	22-Mar-21 A	04-Jun-21	Foundation civil works part 1																																		
A2294290	RC Beam & Rail Installation 50% part 1	0			12	05-Jun-21	19-Jun-21	RC Beam & Rail Installation 50% part 1																																		
A2294290	RC Beam & Rail Installation 100% part 1	0			12	21-Jun-21	05-Jul-21	RC Beam & Rail Installation 100% part 1																																		
A2294290	Gantry Crane Assembly part 1 50%	0			12	06-Jul-21	19-Jul-21	Gantry Crane Assembly part 1 50%																																		
A2294290	Gantry Crane Assembly part 1 100%	0			12	20-Jul-21	02-Aug-21	Gantry Crane Assembly part 1 100%																																		
A2294309	Foundation civil works part 2	0			12	03-Aug-21*	16-Aug-21	Foundation civil works part 2																																		
A2294309	RC Beam & Rail Installation 50% part 2	0			12	17-Aug-21	30-Aug-21	RC Beam & Rail Installation 50% part 2																																		
A2294309	RC Beam & Rail Installation 100% part 2	0			12	31-Aug-21	13-Sep-21	RC Beam & Rail Installation 100% part 2																																		
Gantry Crane Setup for TBM Assembly								66	13-Apr-21	02-Jul-21	99	22-Mar-21 A	23-Jul-21																													
A229020	Gantry Crane - Ground Beam Construction	24	13-Apr-21	11-May-21	69	22-Mar-21 A	17-Jun-21	Gantry Crane - Ground Beam Construction																																		
A229030	Gantry Crane - Delivery & Assembly	36	12-May-21	24-Jun-21	24	18-Jun-21	16-Jul-21	Gantry Crane - Delivery & Assembly																																		
A229040	Gantry Crane - Commissioning & Load Test	6	25-Jun-21	02-Jul-21	6	17-Jul-21	23-Jul-21	Gantry Crane - Commissioning & Load Test																																		
Slurry Treatment Plant								96	12-May-21	03-Sep-21	183	25-Jan-21 A	07-Sep-21																													

Page 22 of 26
Data Date: 29-May-21


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

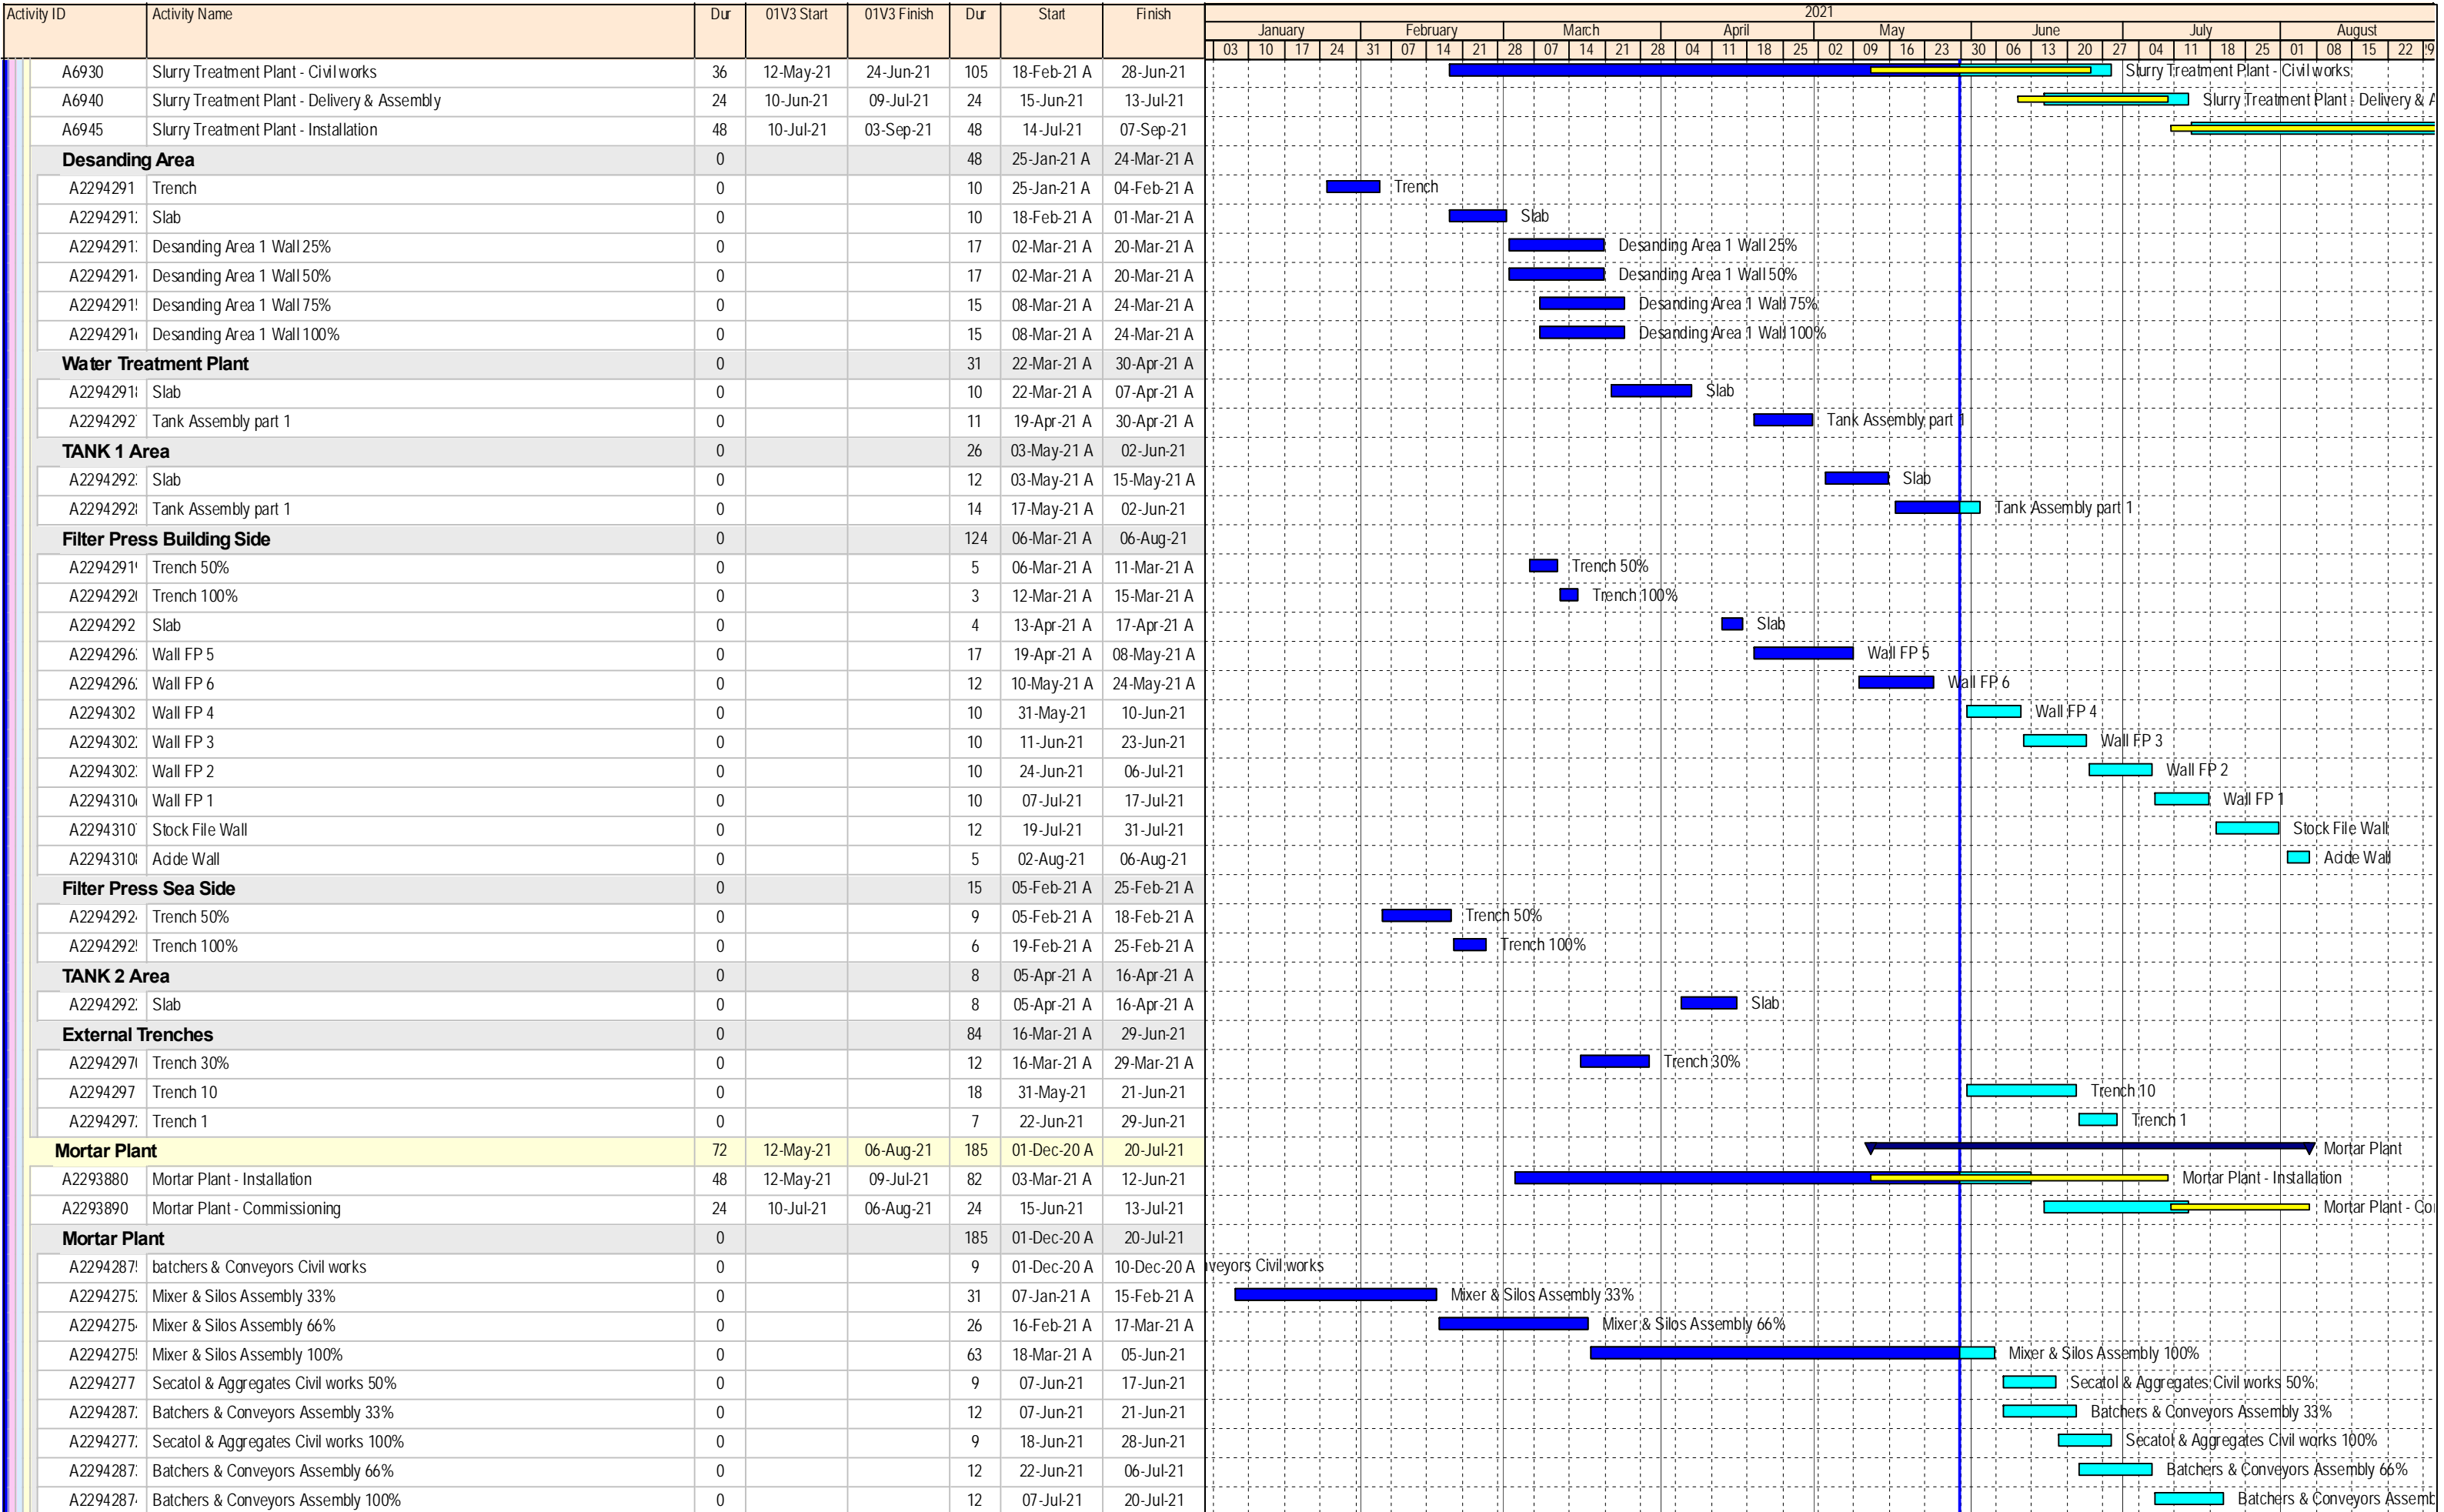

Page 23 of 26 Data Date: 29-May-21	<ul style="list-style-type: none"> ◆ Milestone ▬ Planned Bar ▬ Critical Activity ◆ Actual Milestone ▬ Actual Work ◆ Baseline Milestone ▬ Baseline Bar 	<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme (May-21)</h3>		Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																												
05-Nov-19	00V0	WYu																													
18-Dec-19	00V1	WYu																													
22-Feb-20	01V0	SPa/LLo	WYu																												
09-Apr-20	01V1	SPa/LLo	WYu																												
17-Jul-20	01V2	SPa/LLo	WYu																												
09-Oct-20	01V3	SPa/LLo	WYu																												

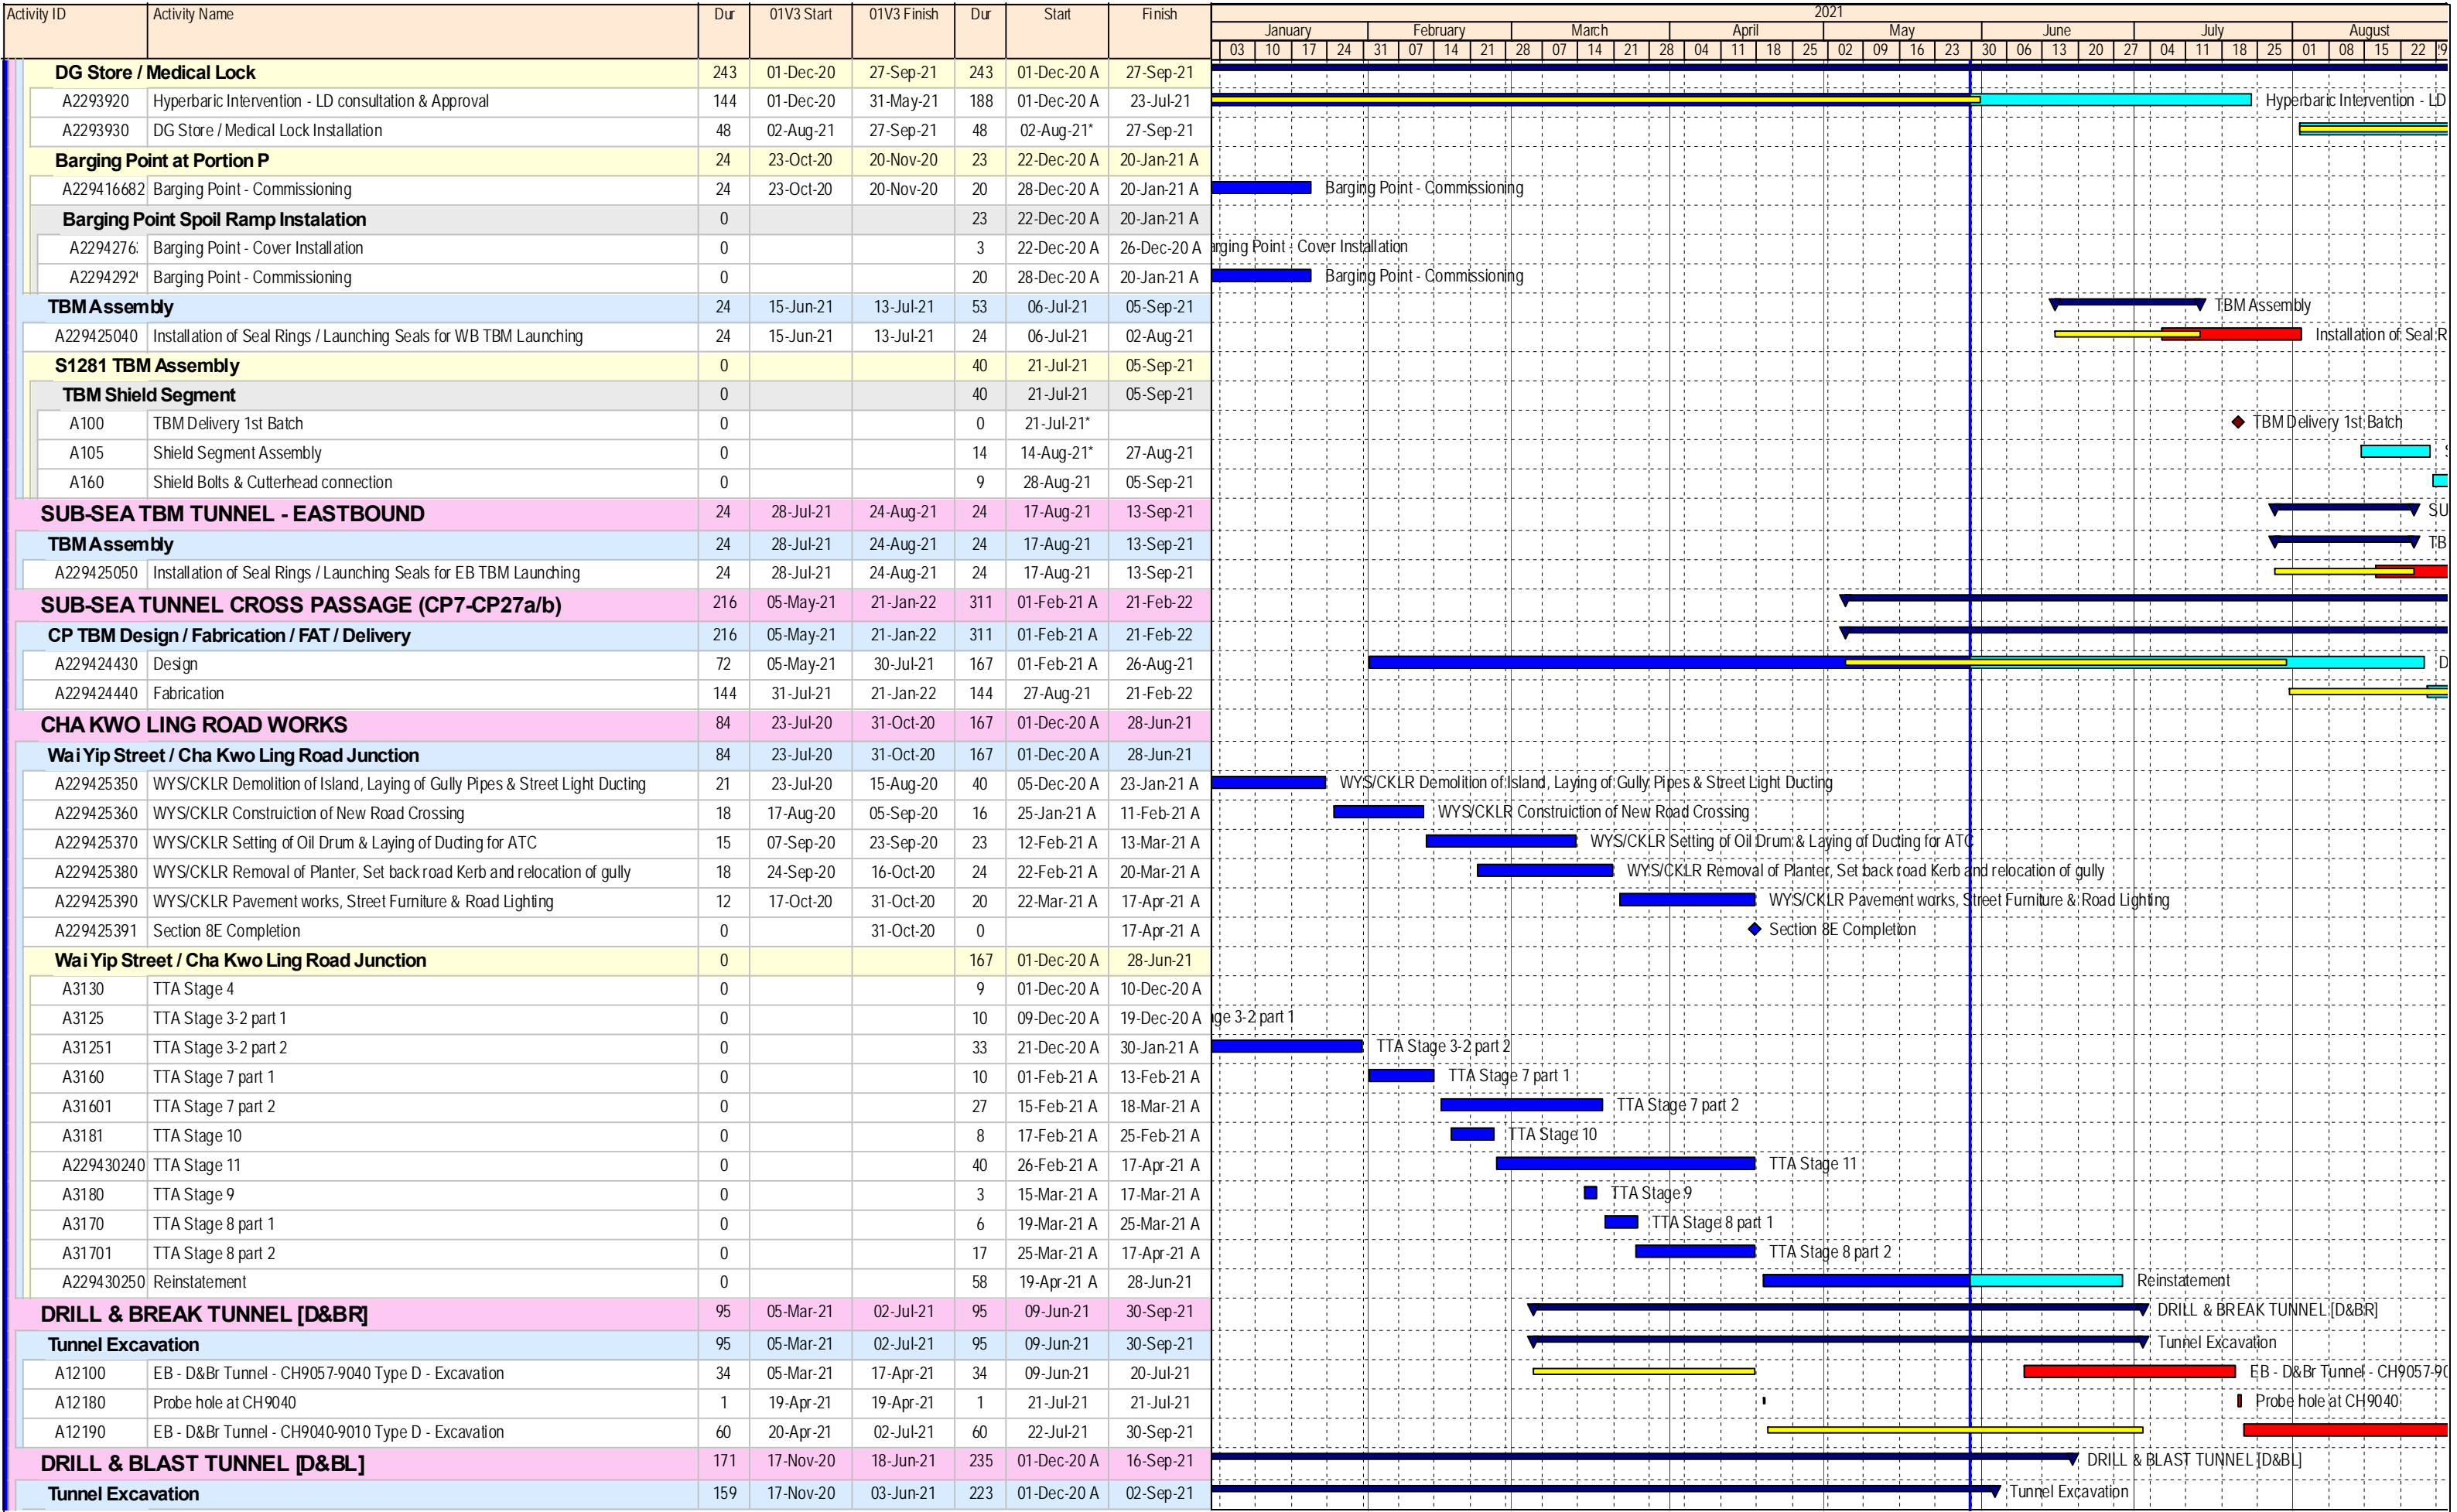


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

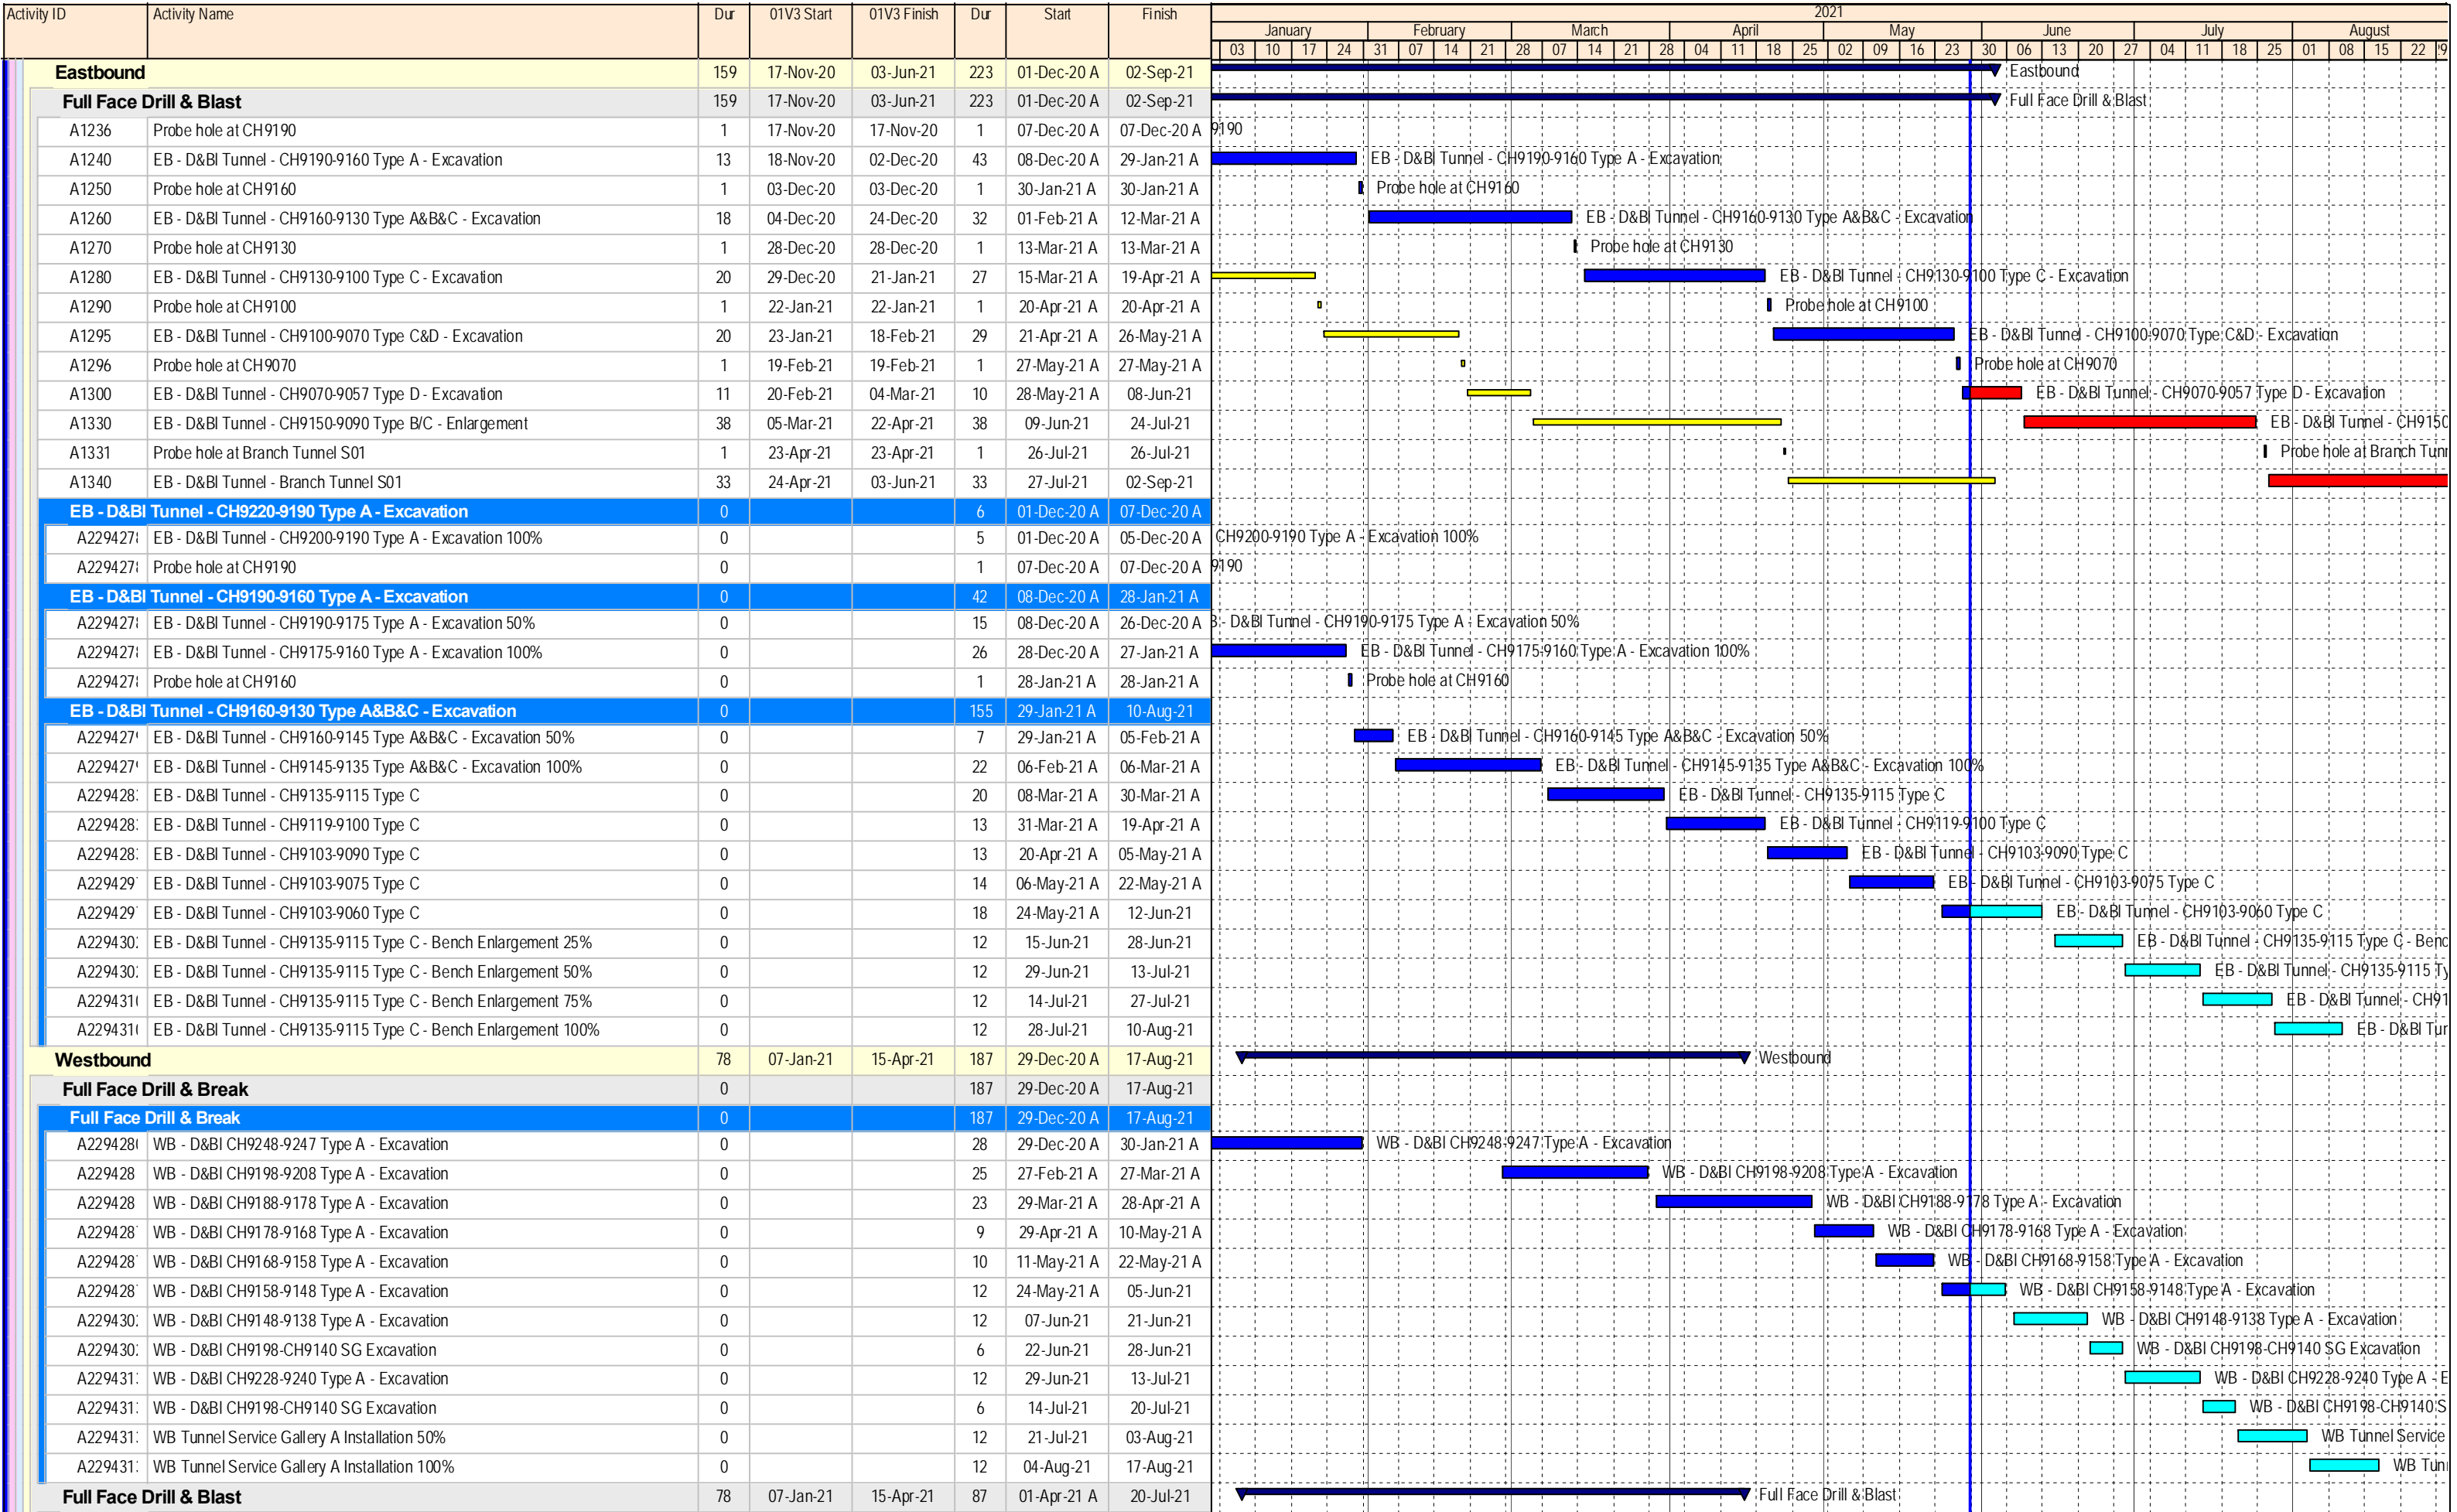

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

