

Page 1 of 24  
Data Date: 28-Nov-20


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

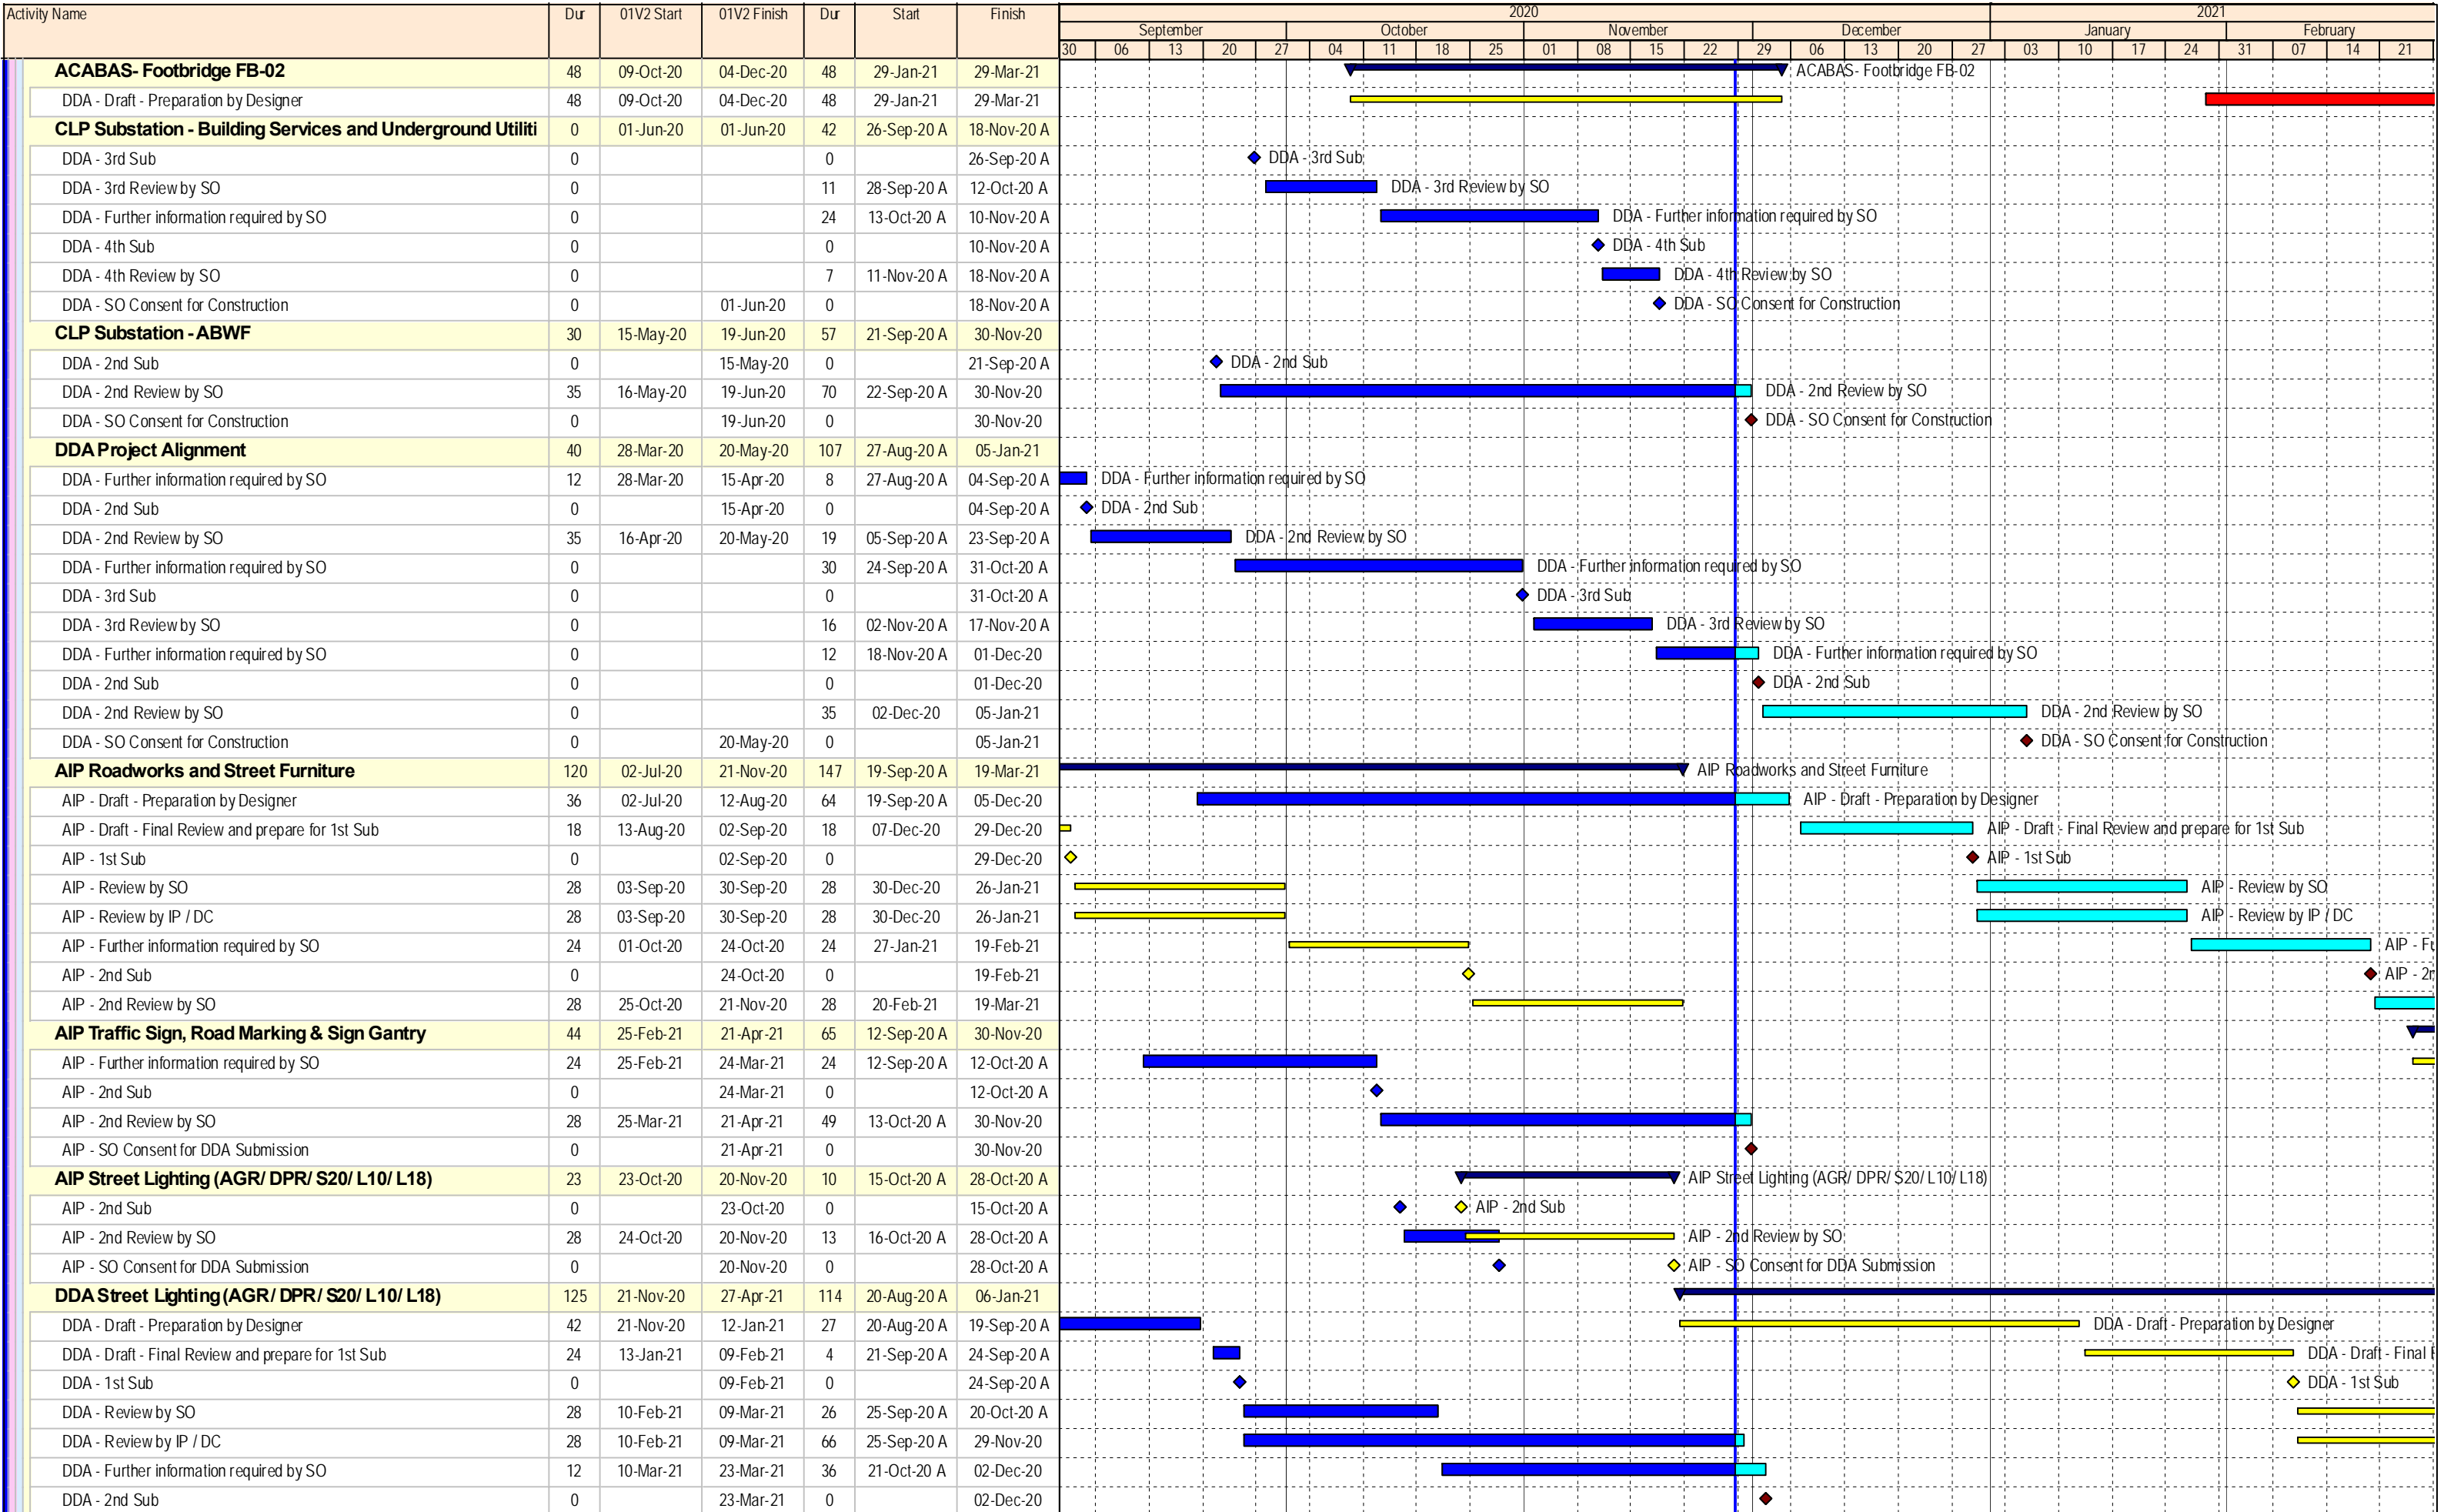


Page 2 of 24  
Data Date: 28-Nov-20


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

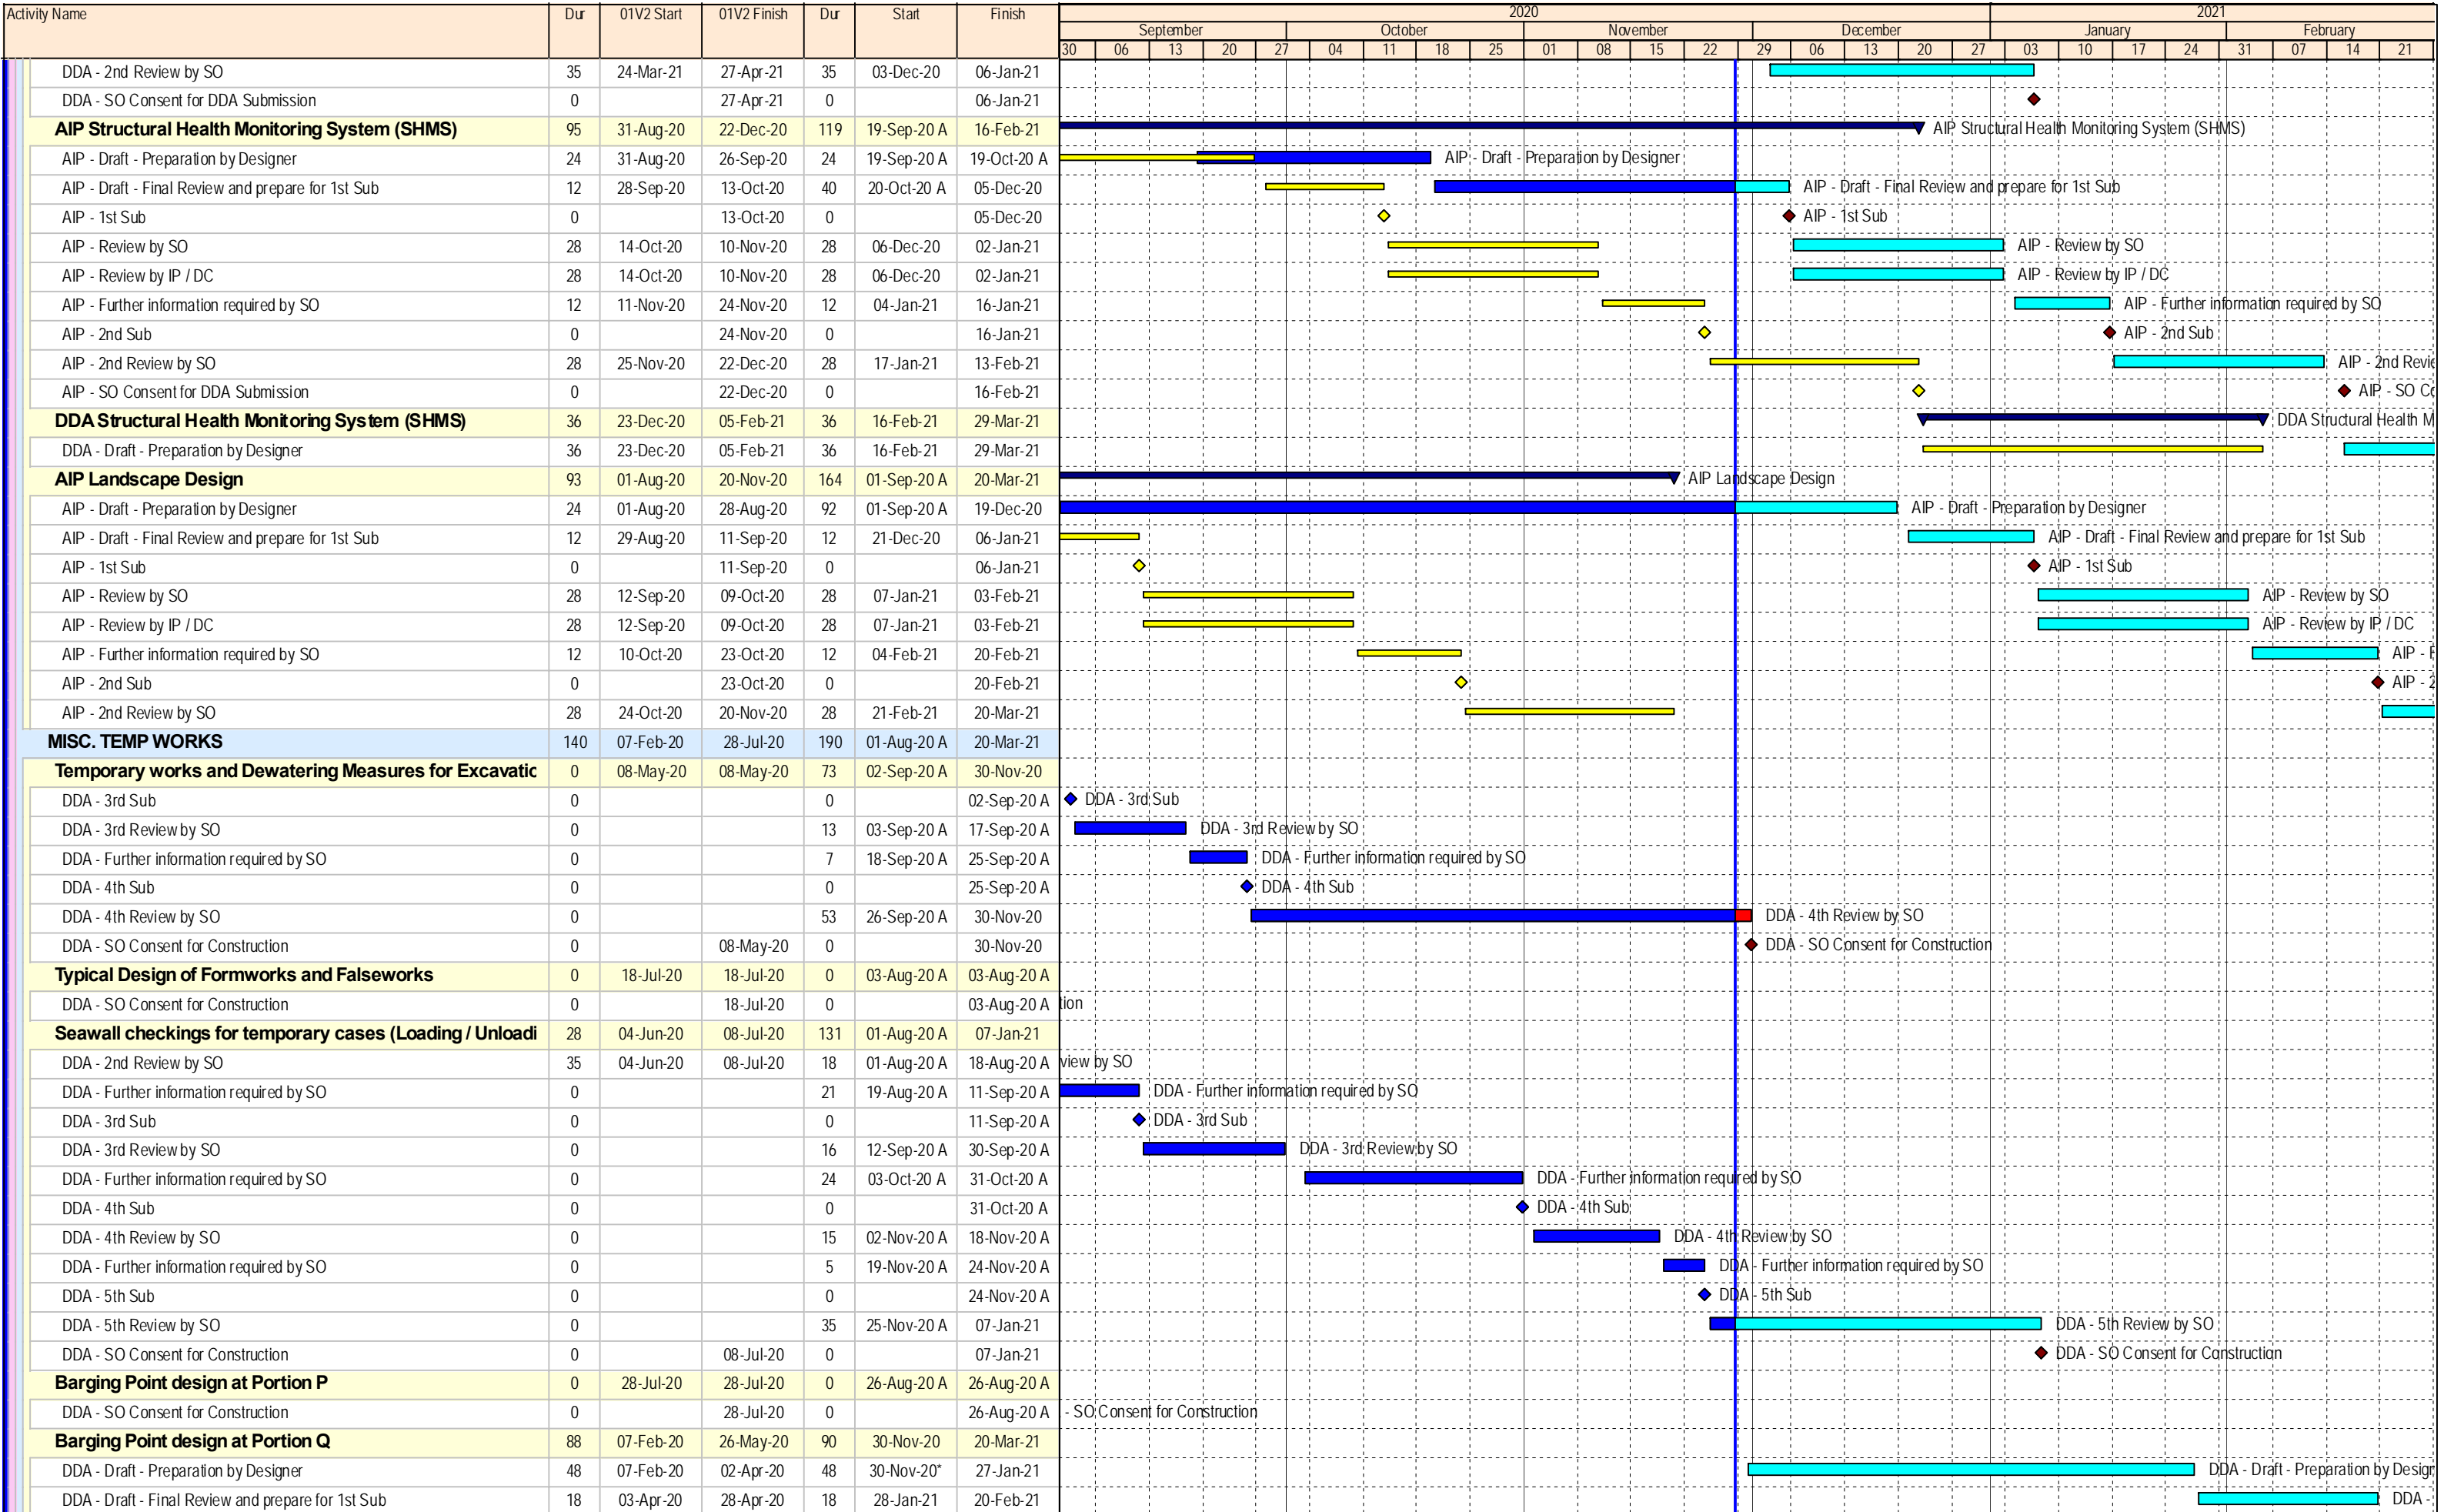


Page 3 of 24  
Data Date: 28-Nov-20


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

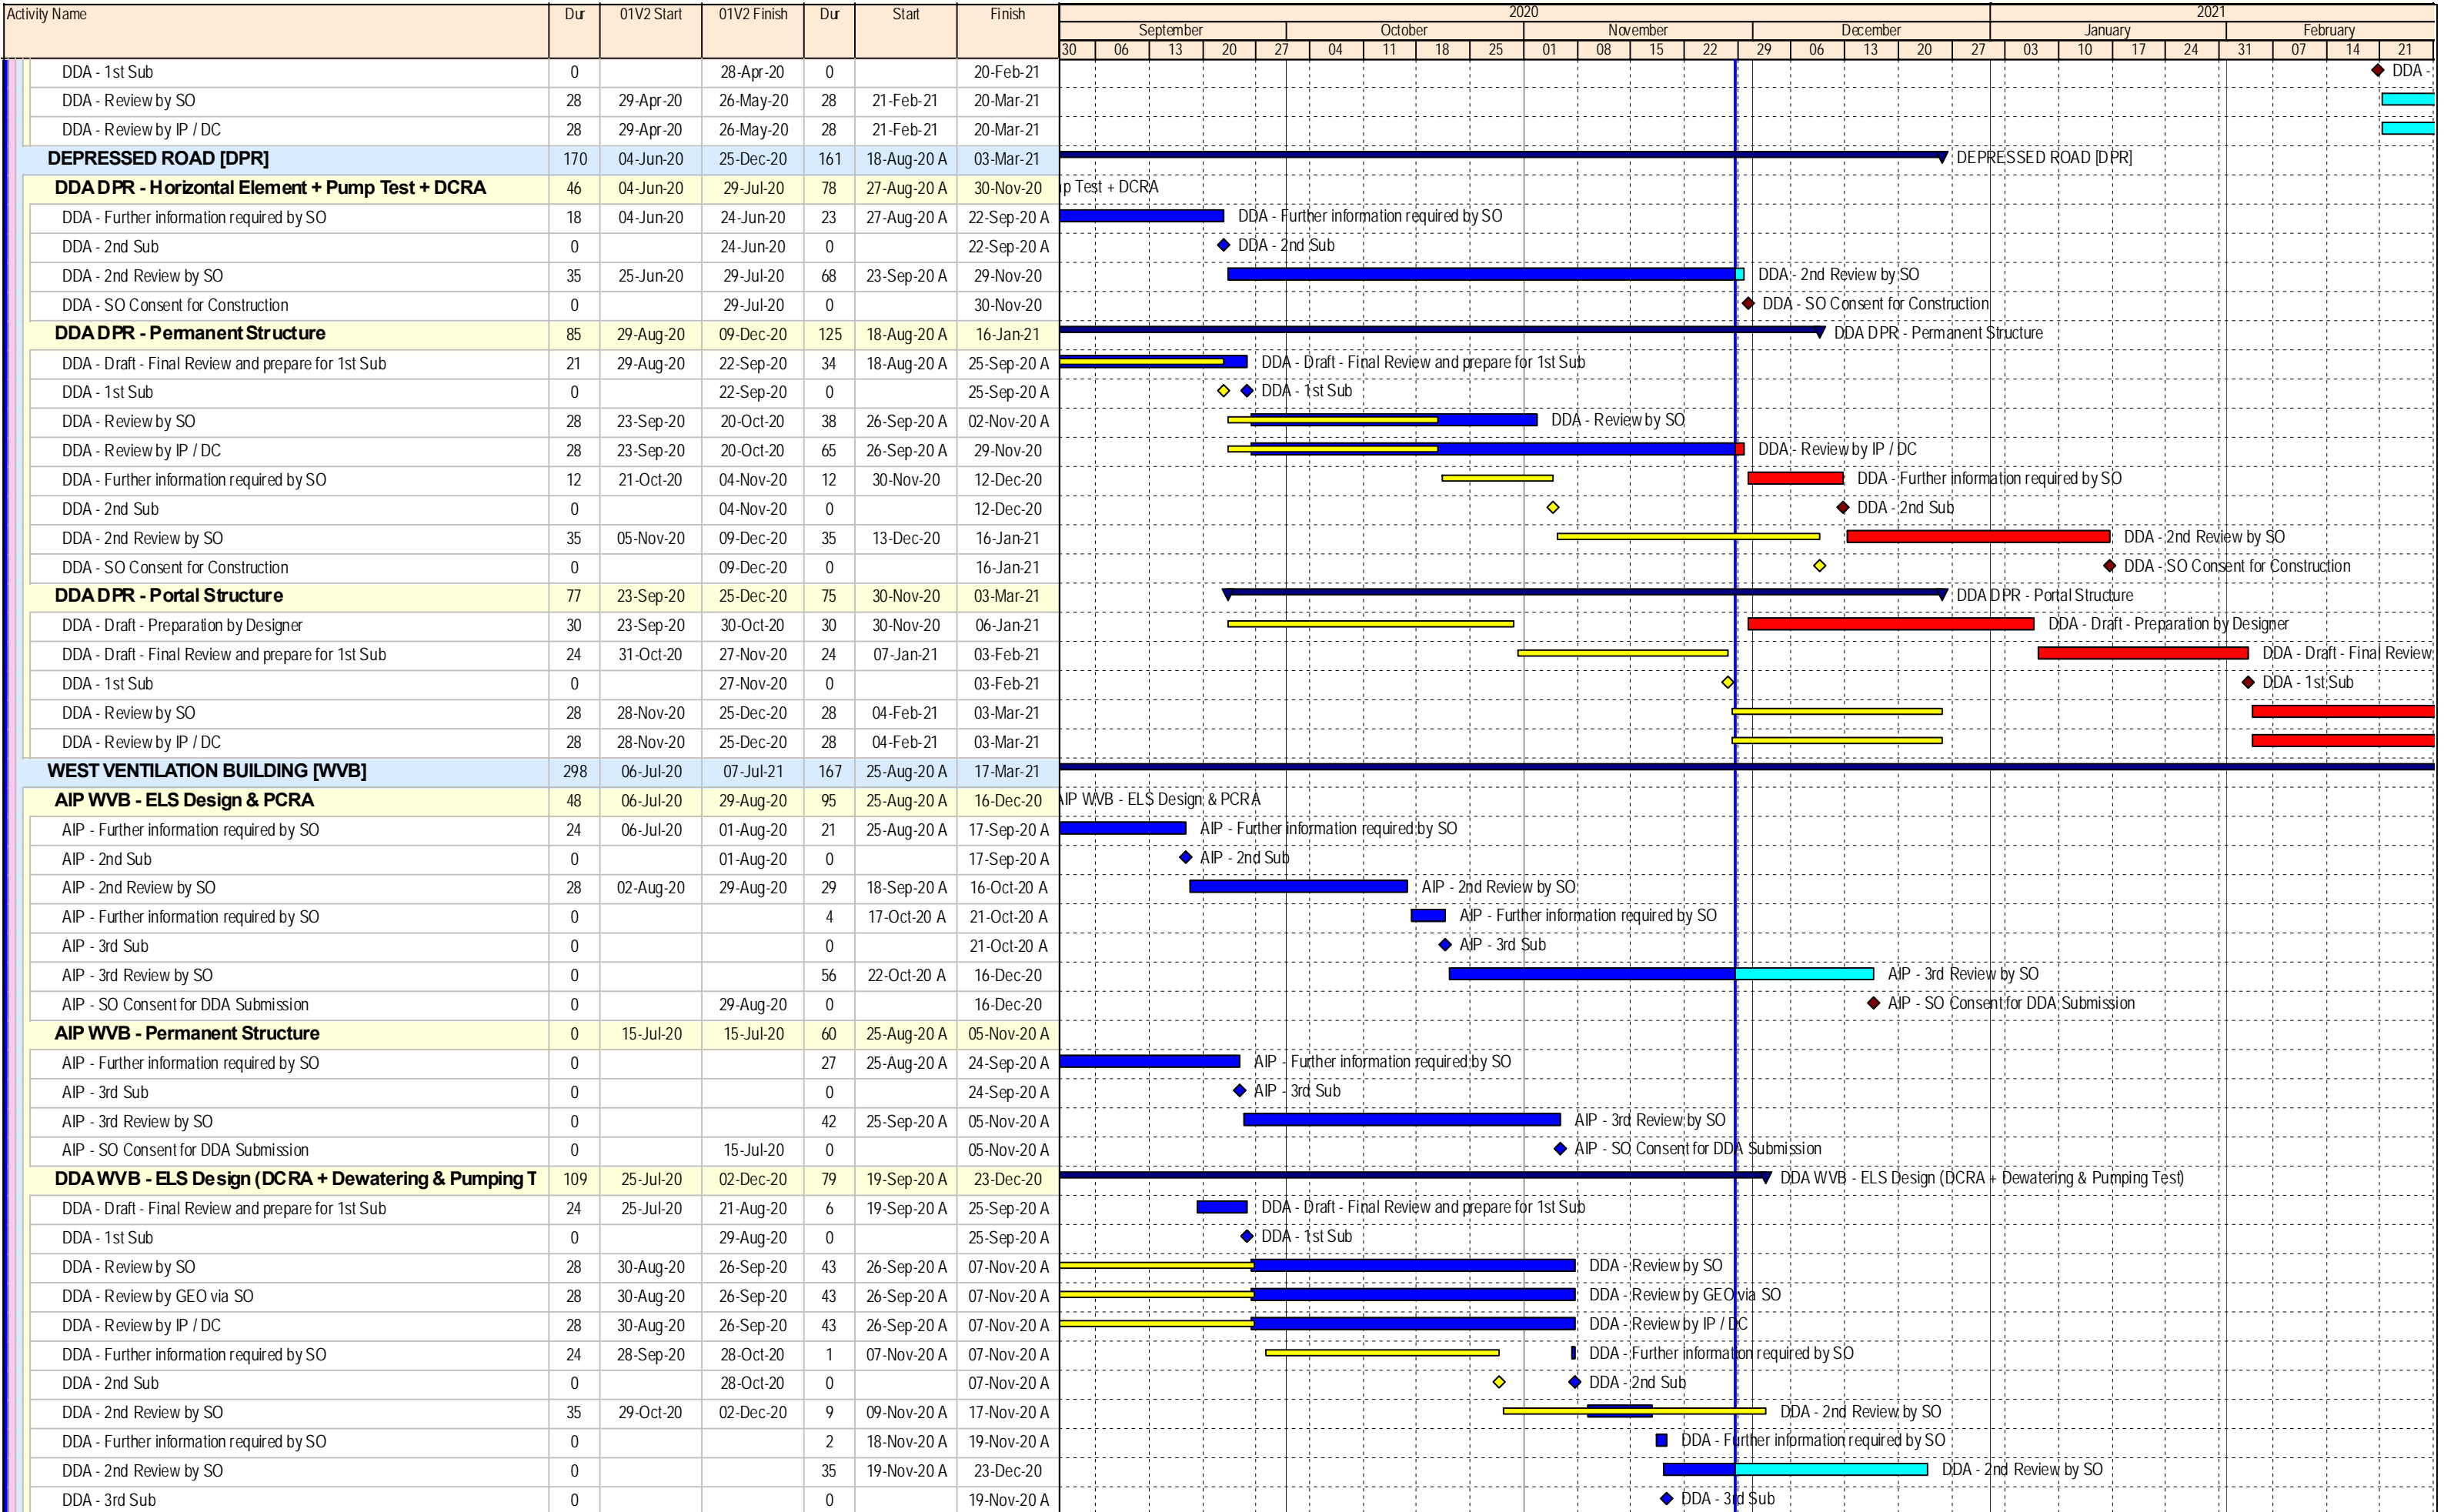


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

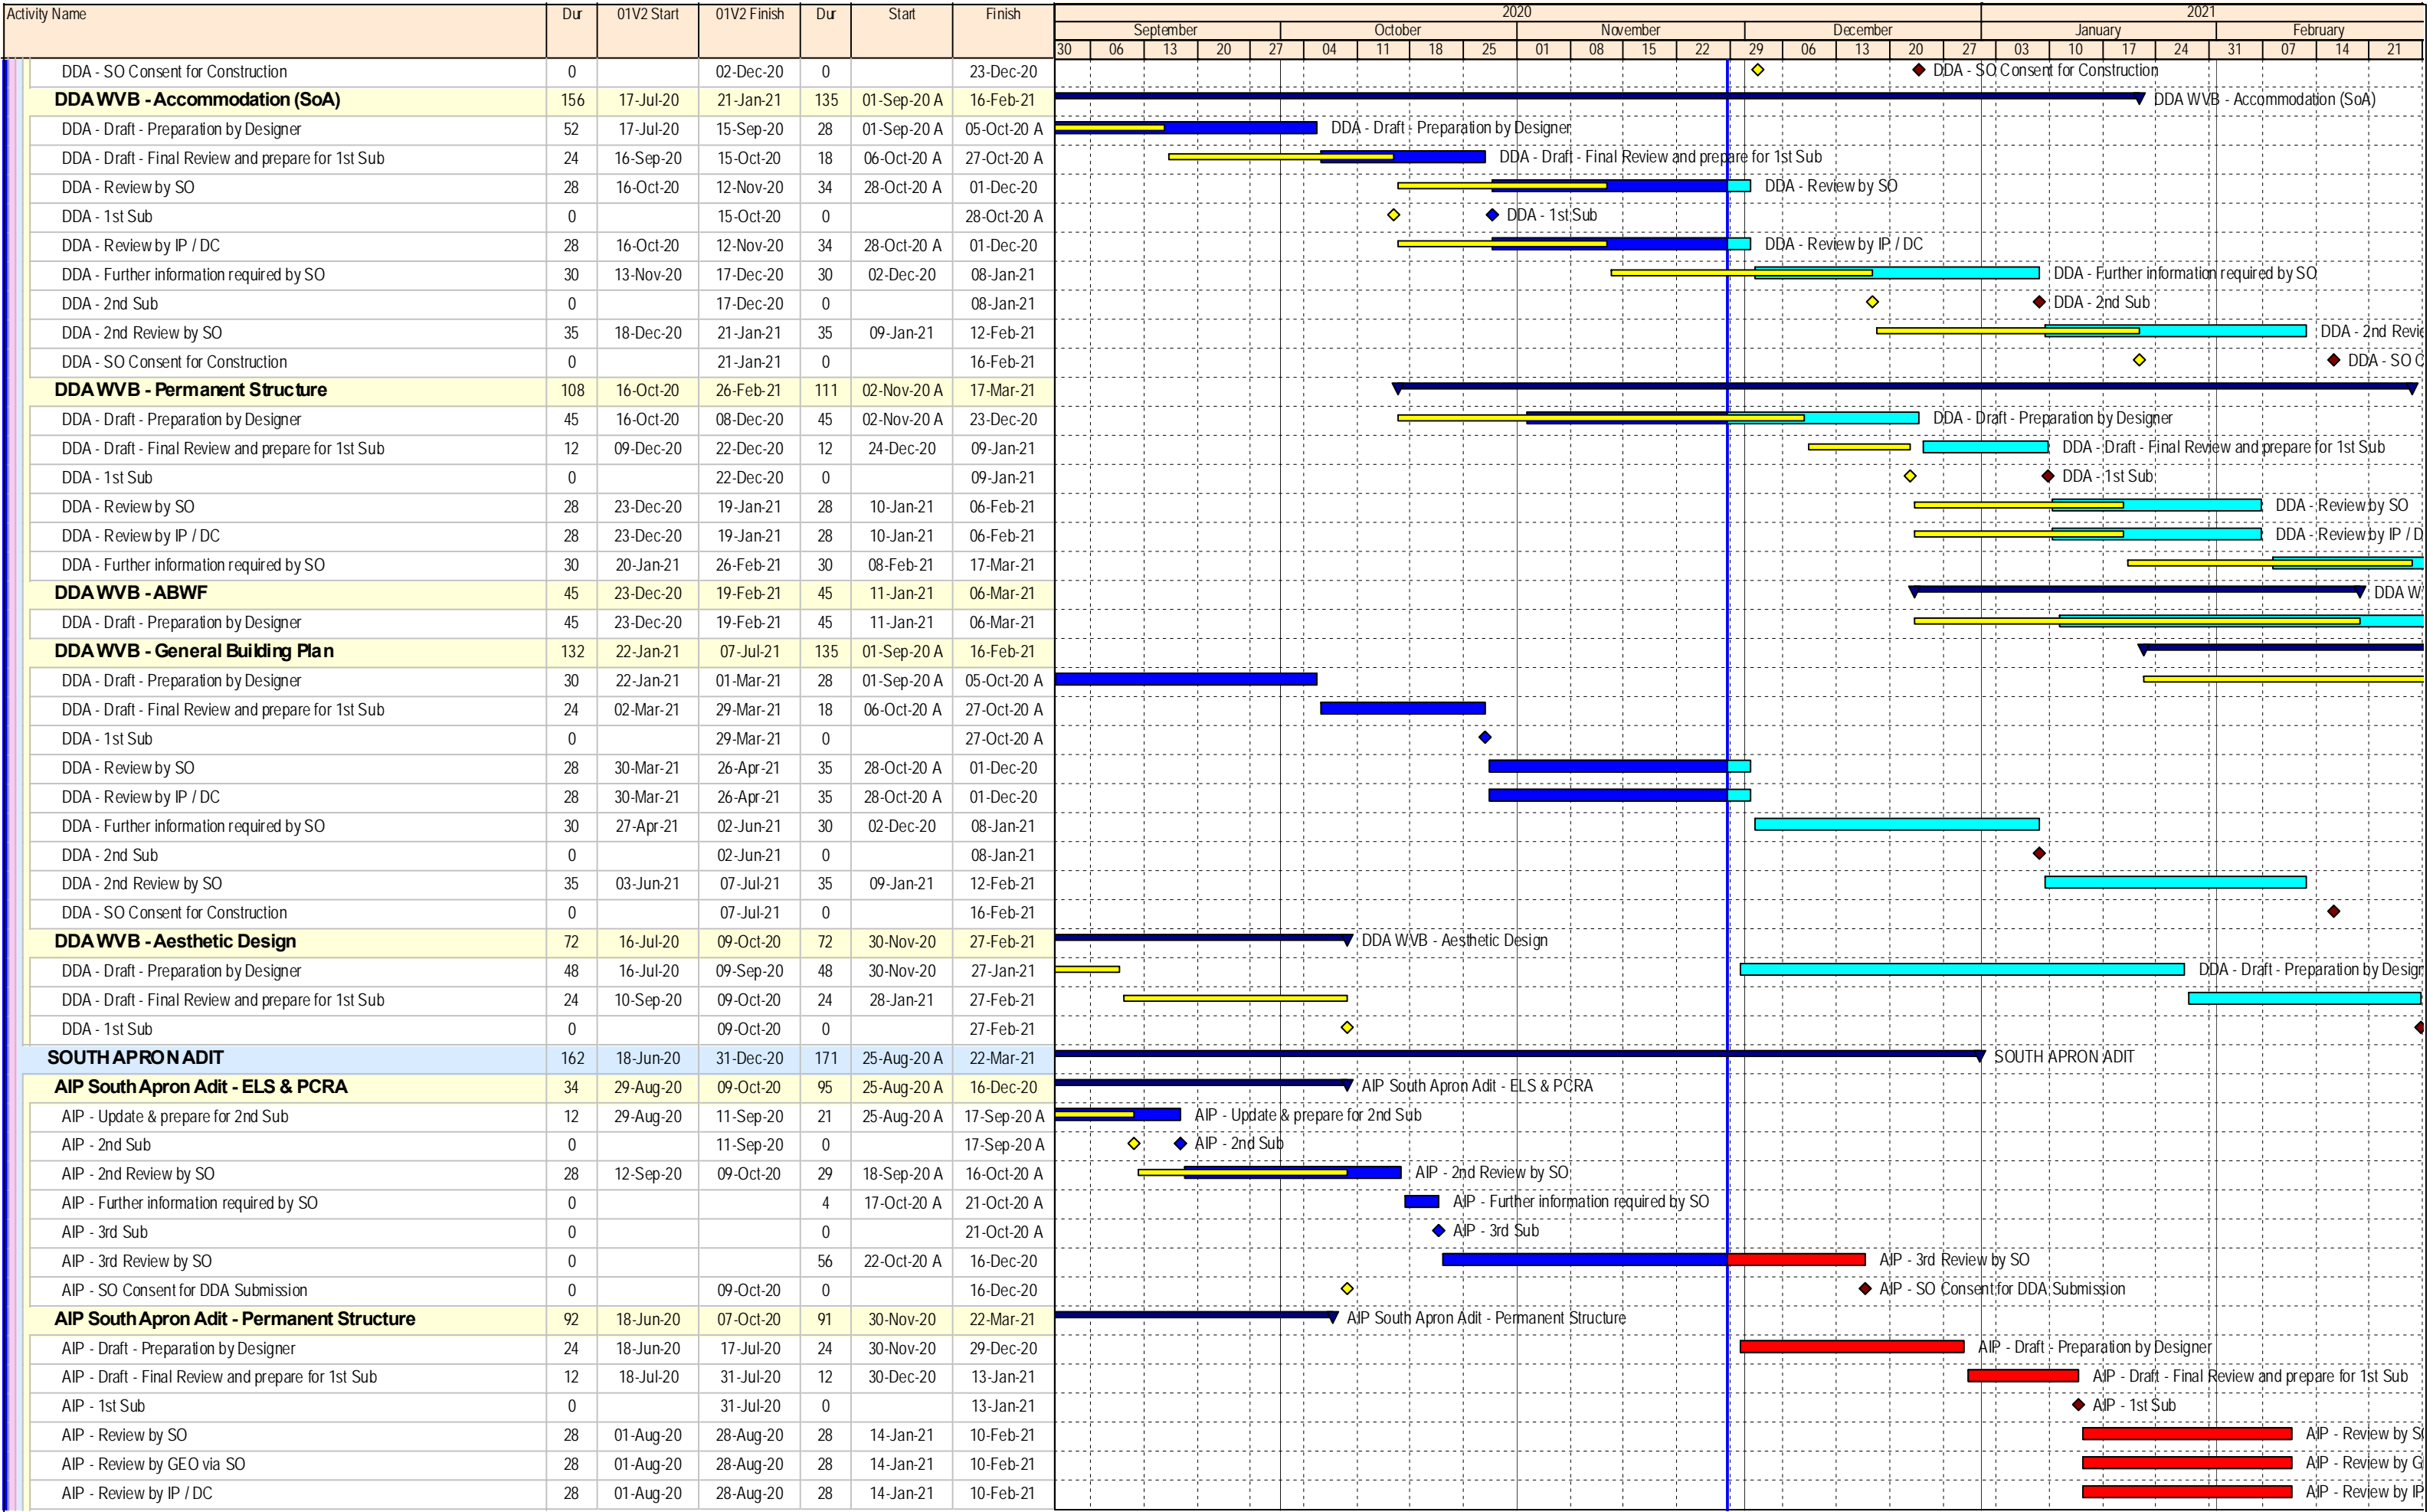


◆ Milestone  
 ◆ Actual Milestone  
 ◆ Baseline Milestone  
 ▶ Summary  
 ▶ Planned Bar  
 ▶ Critical Activity  
 ▶ Actual Work  
 ▶ Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

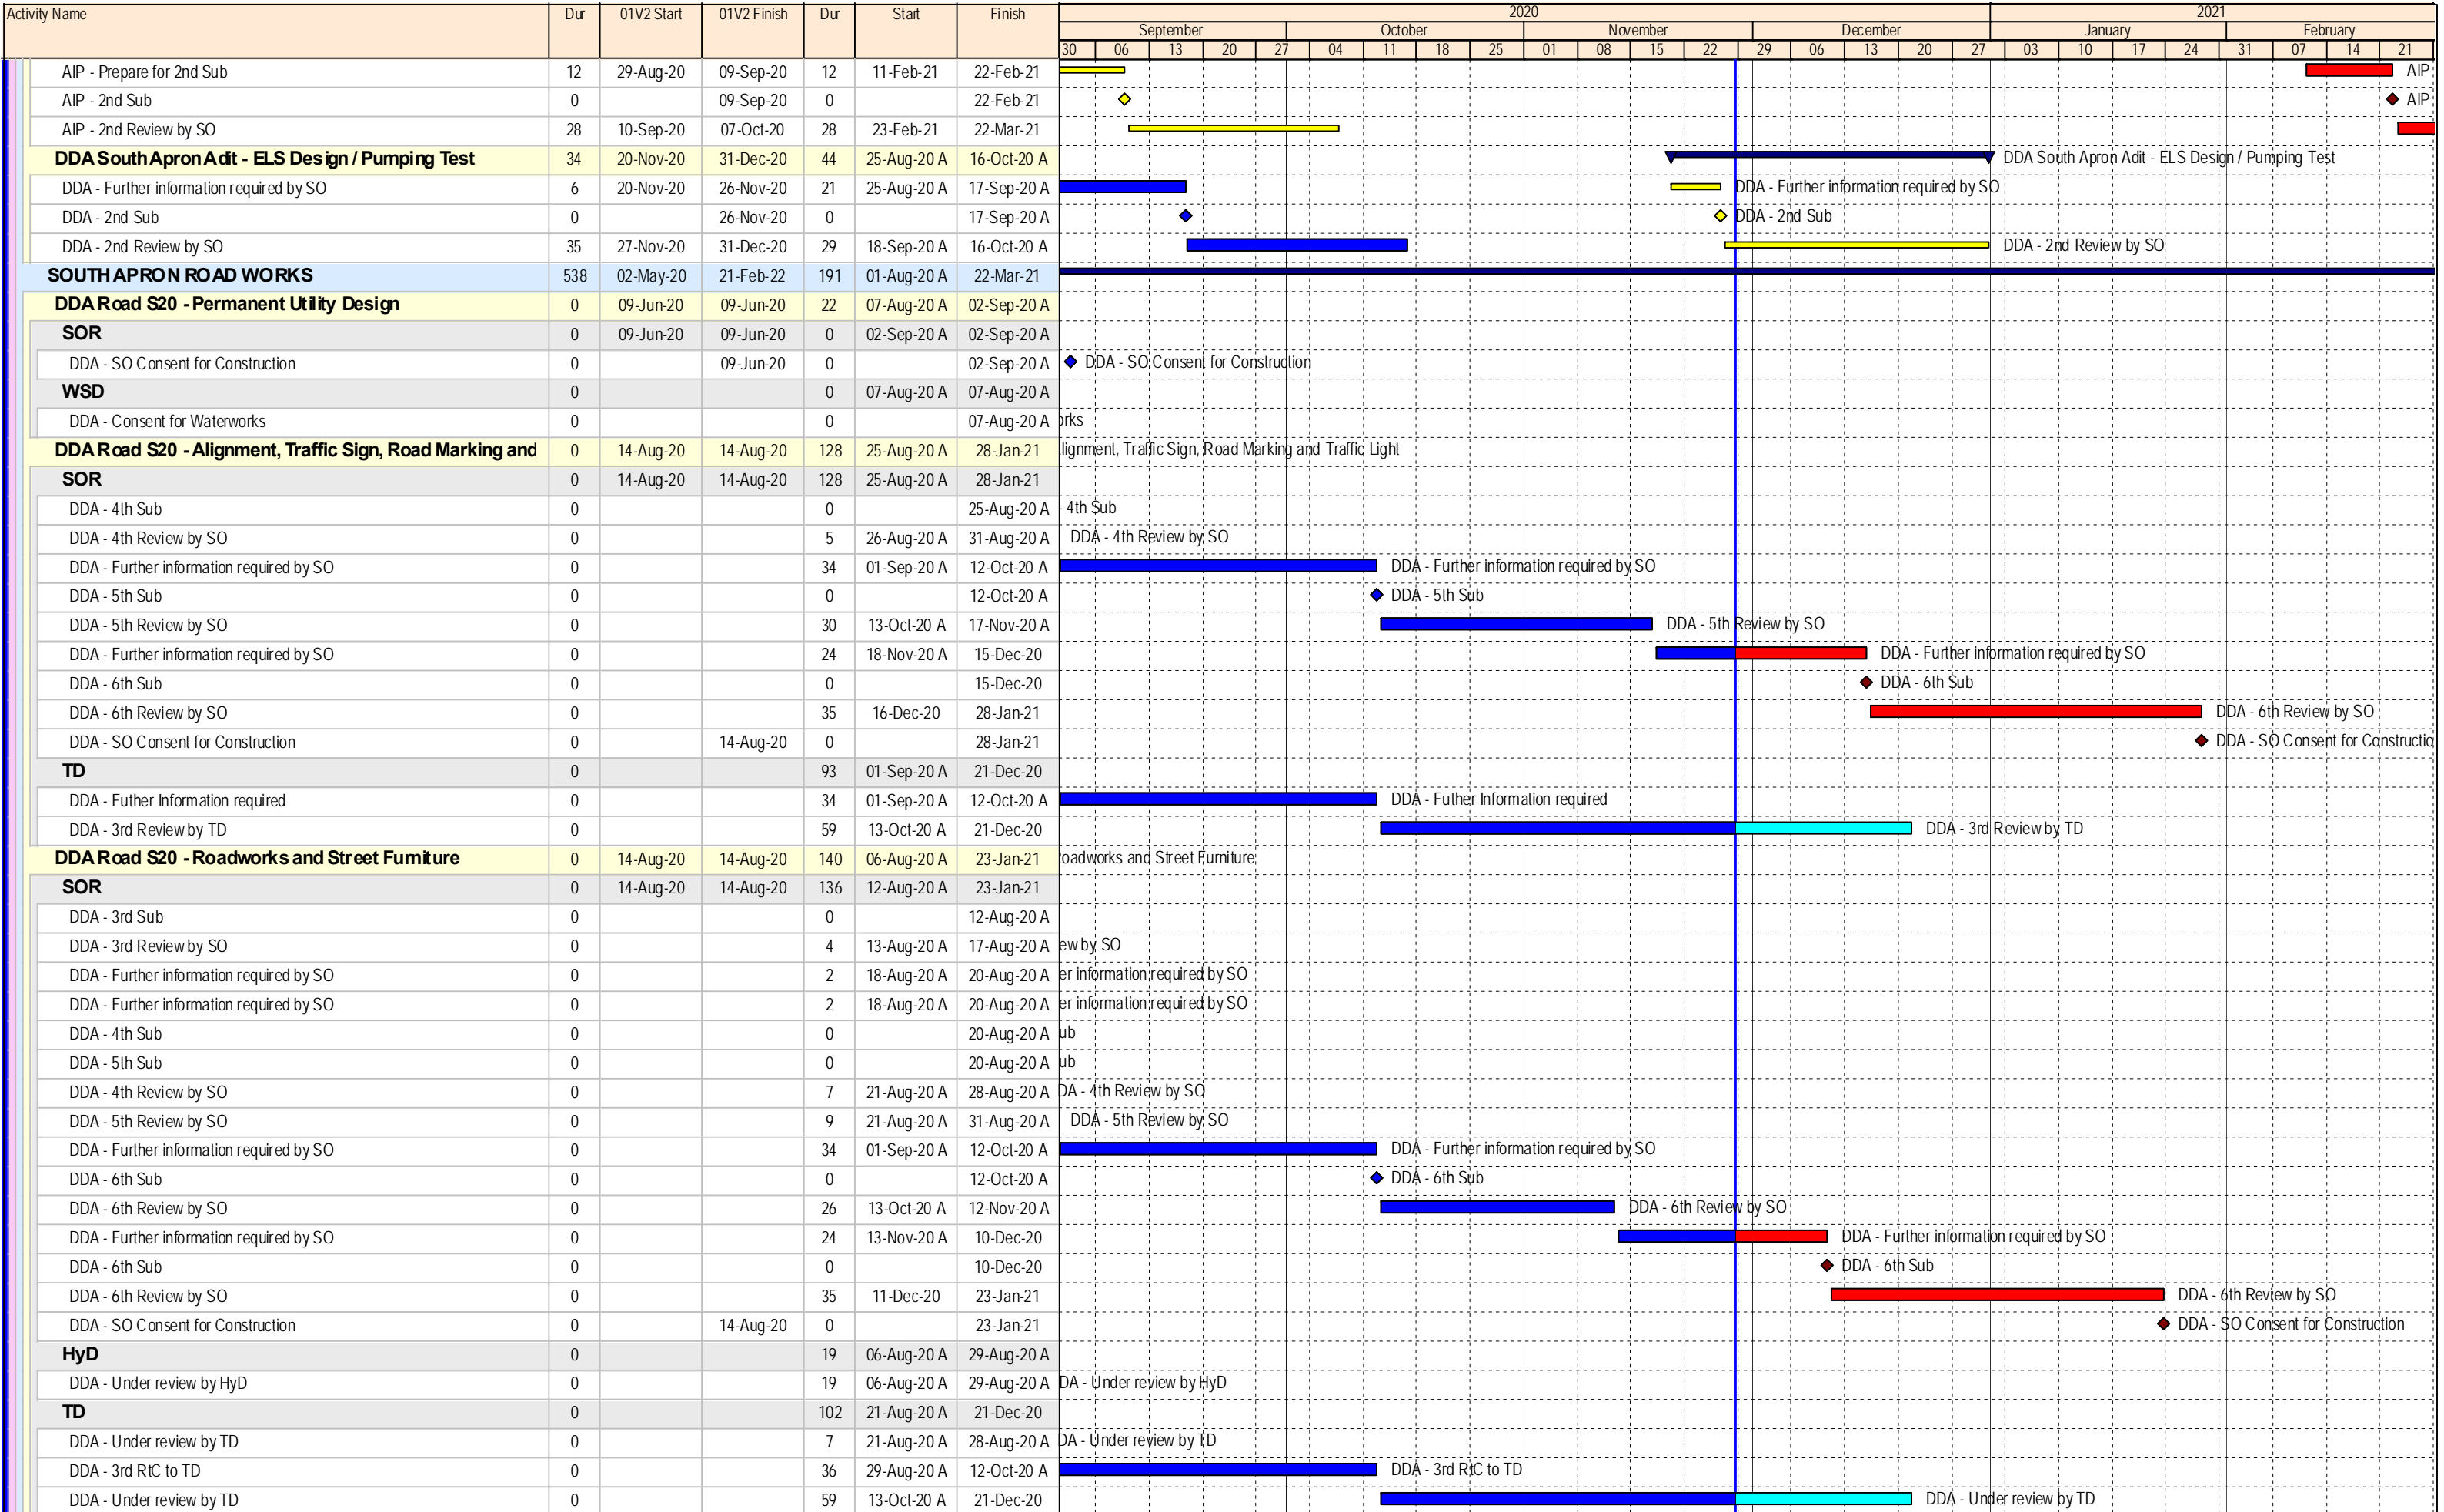


Page 6 of 24  
Data Date: 28-Nov-20


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

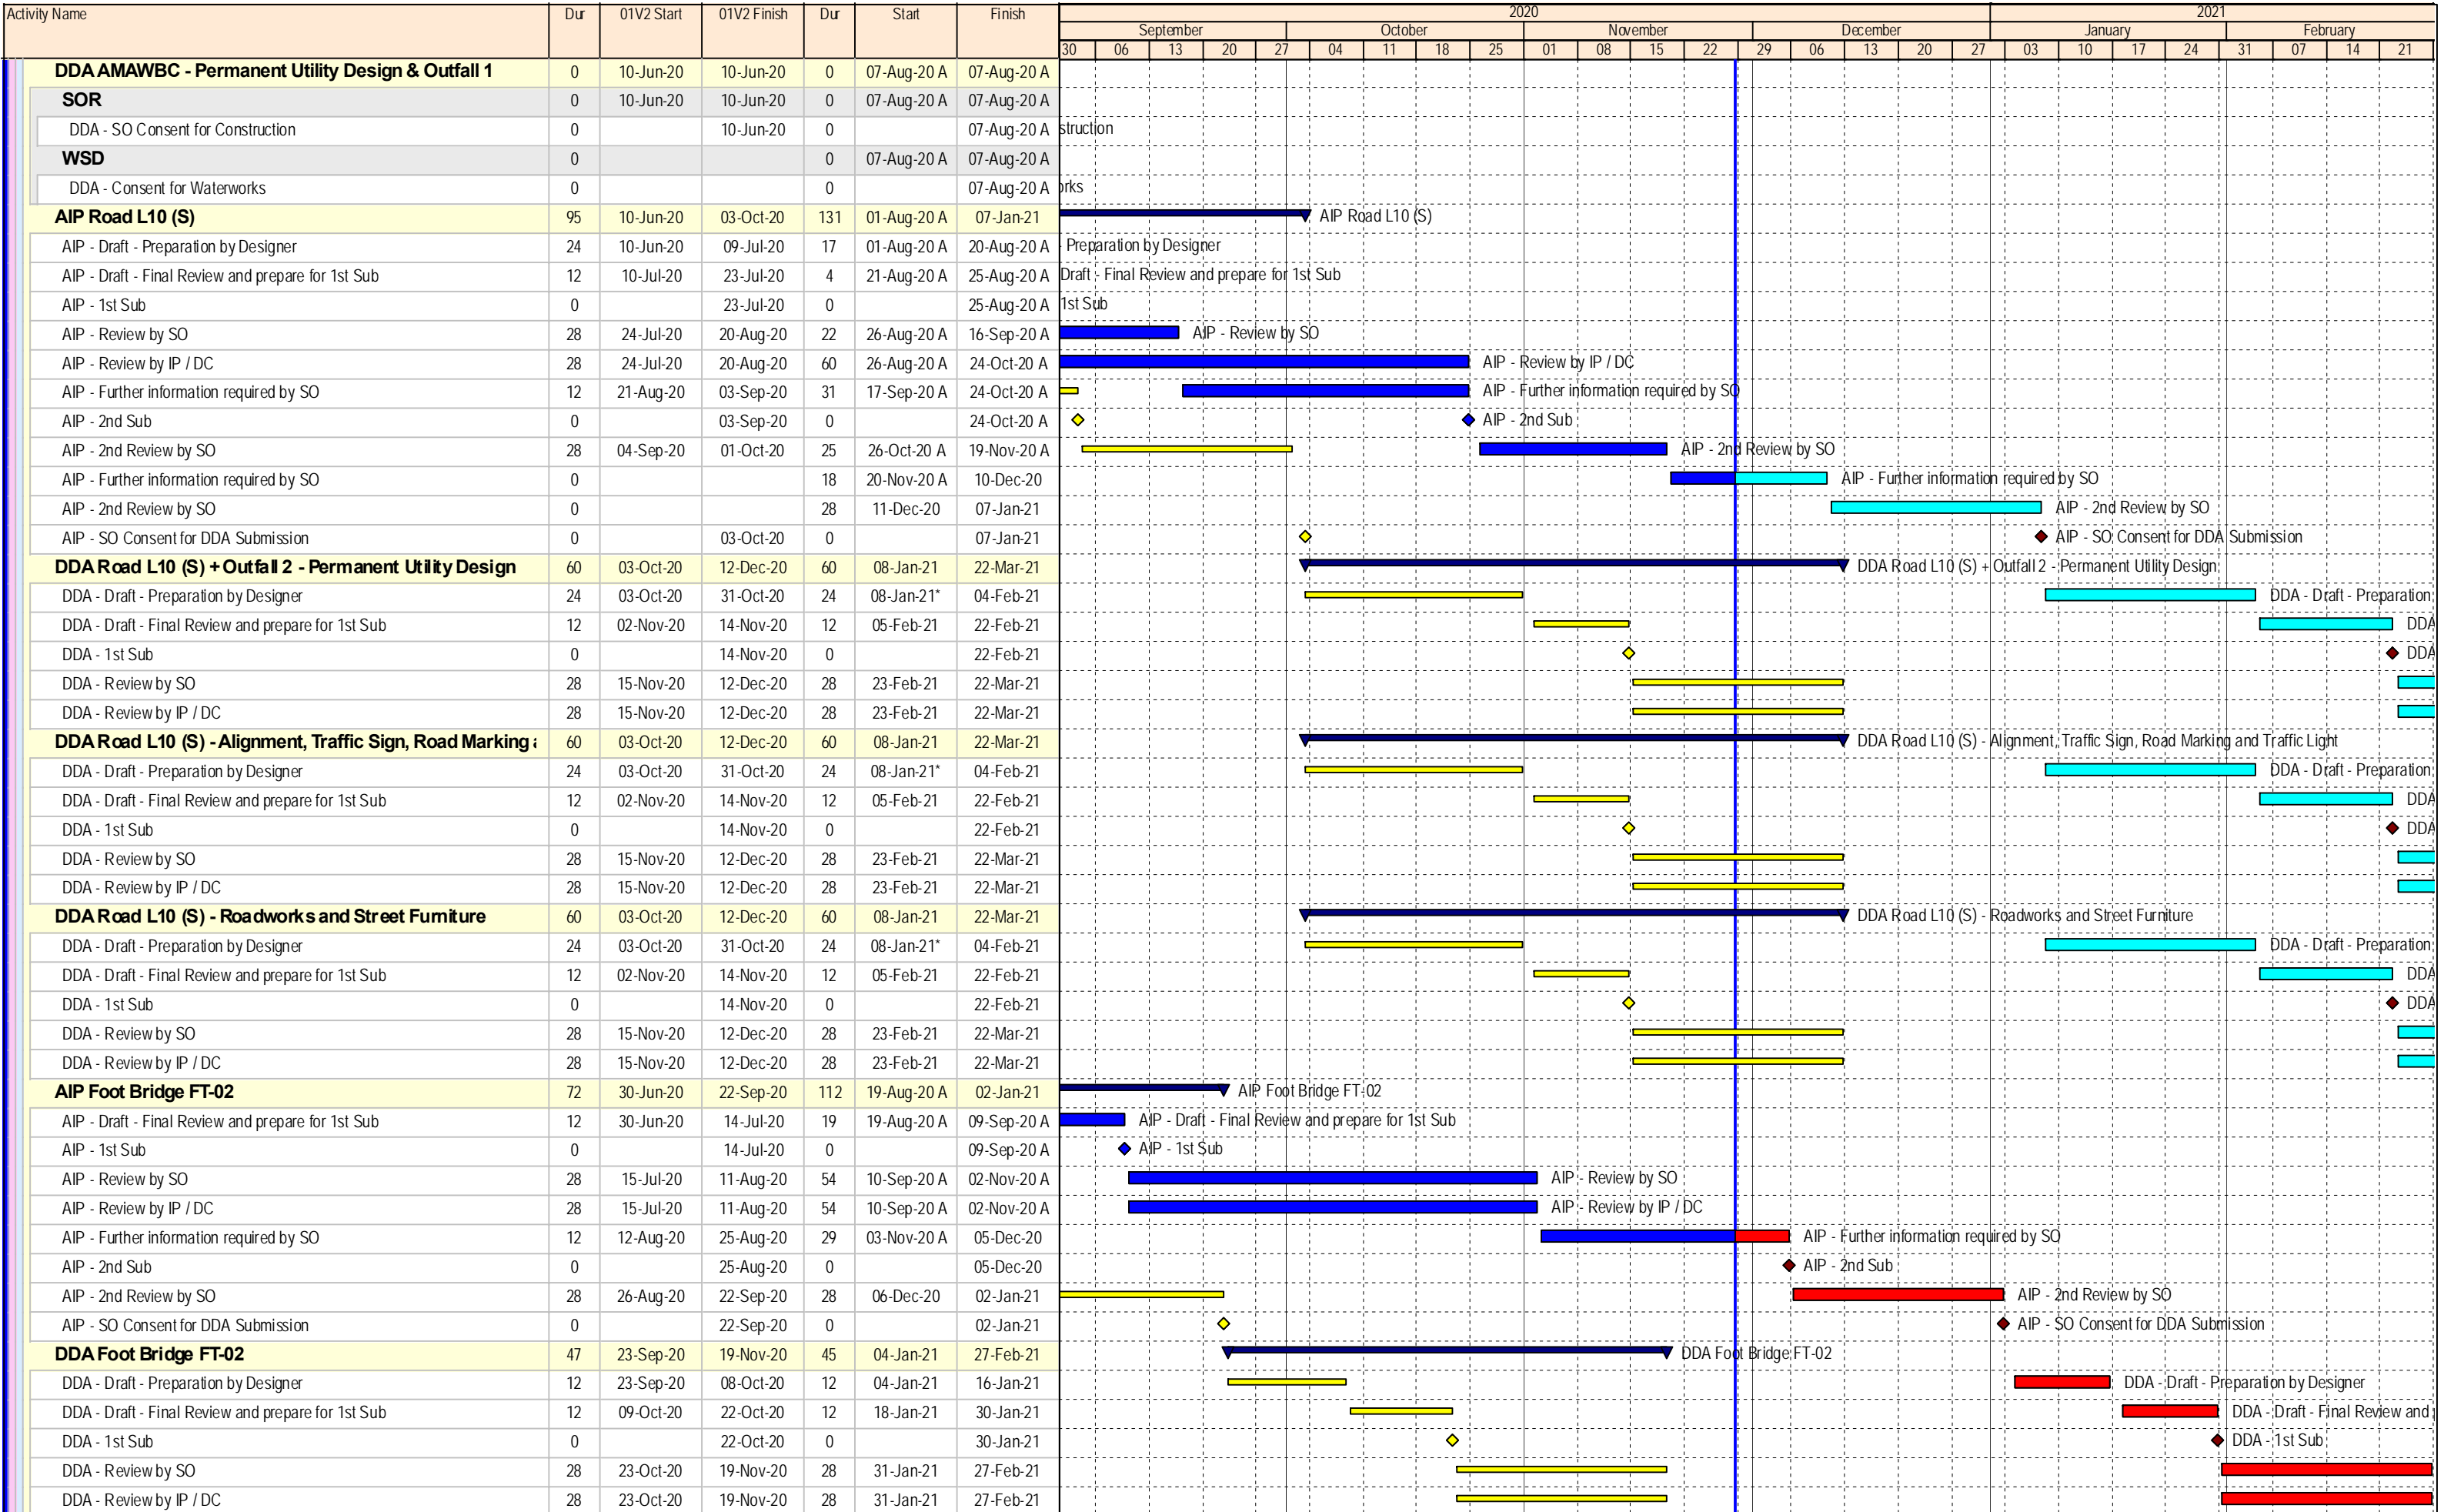


Page 7 of 24  
Data Date: 28-Nov-20

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar


Summary ▬

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

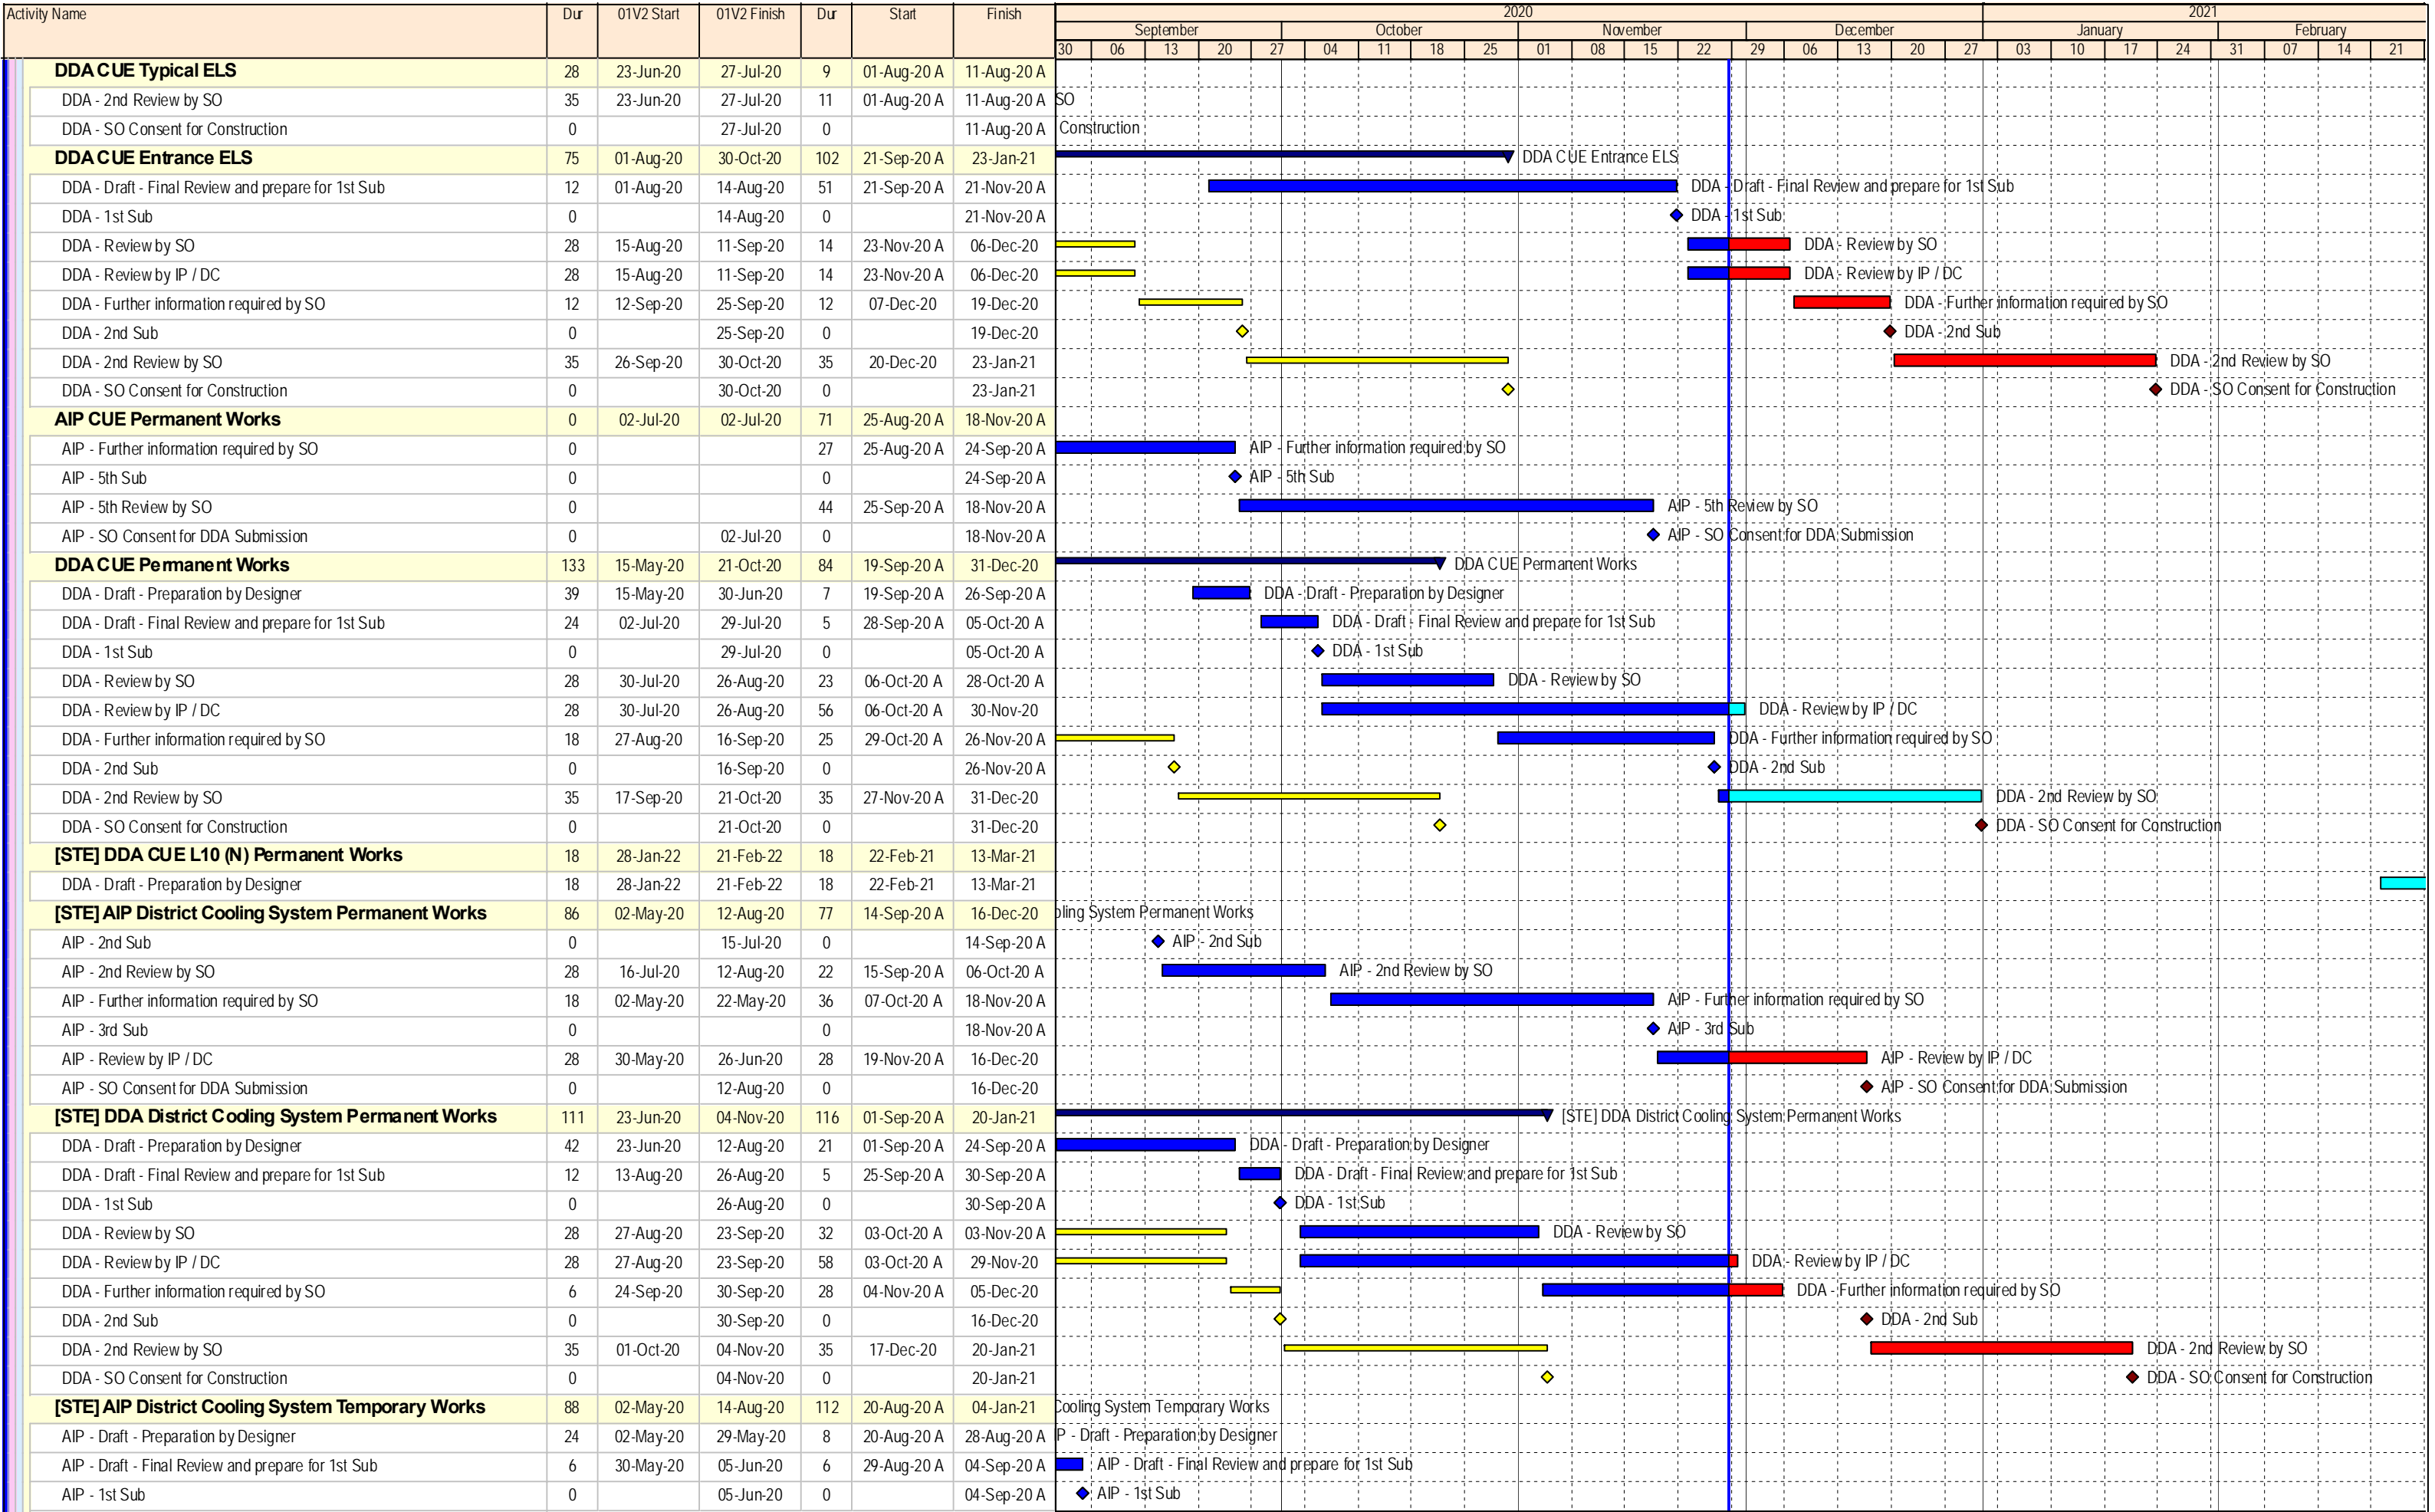

Page 8 of 24  
Data Date: 28-Nov-20

- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ▬ Actual Work
- ▬ Baseline Bar
- ▬ Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu



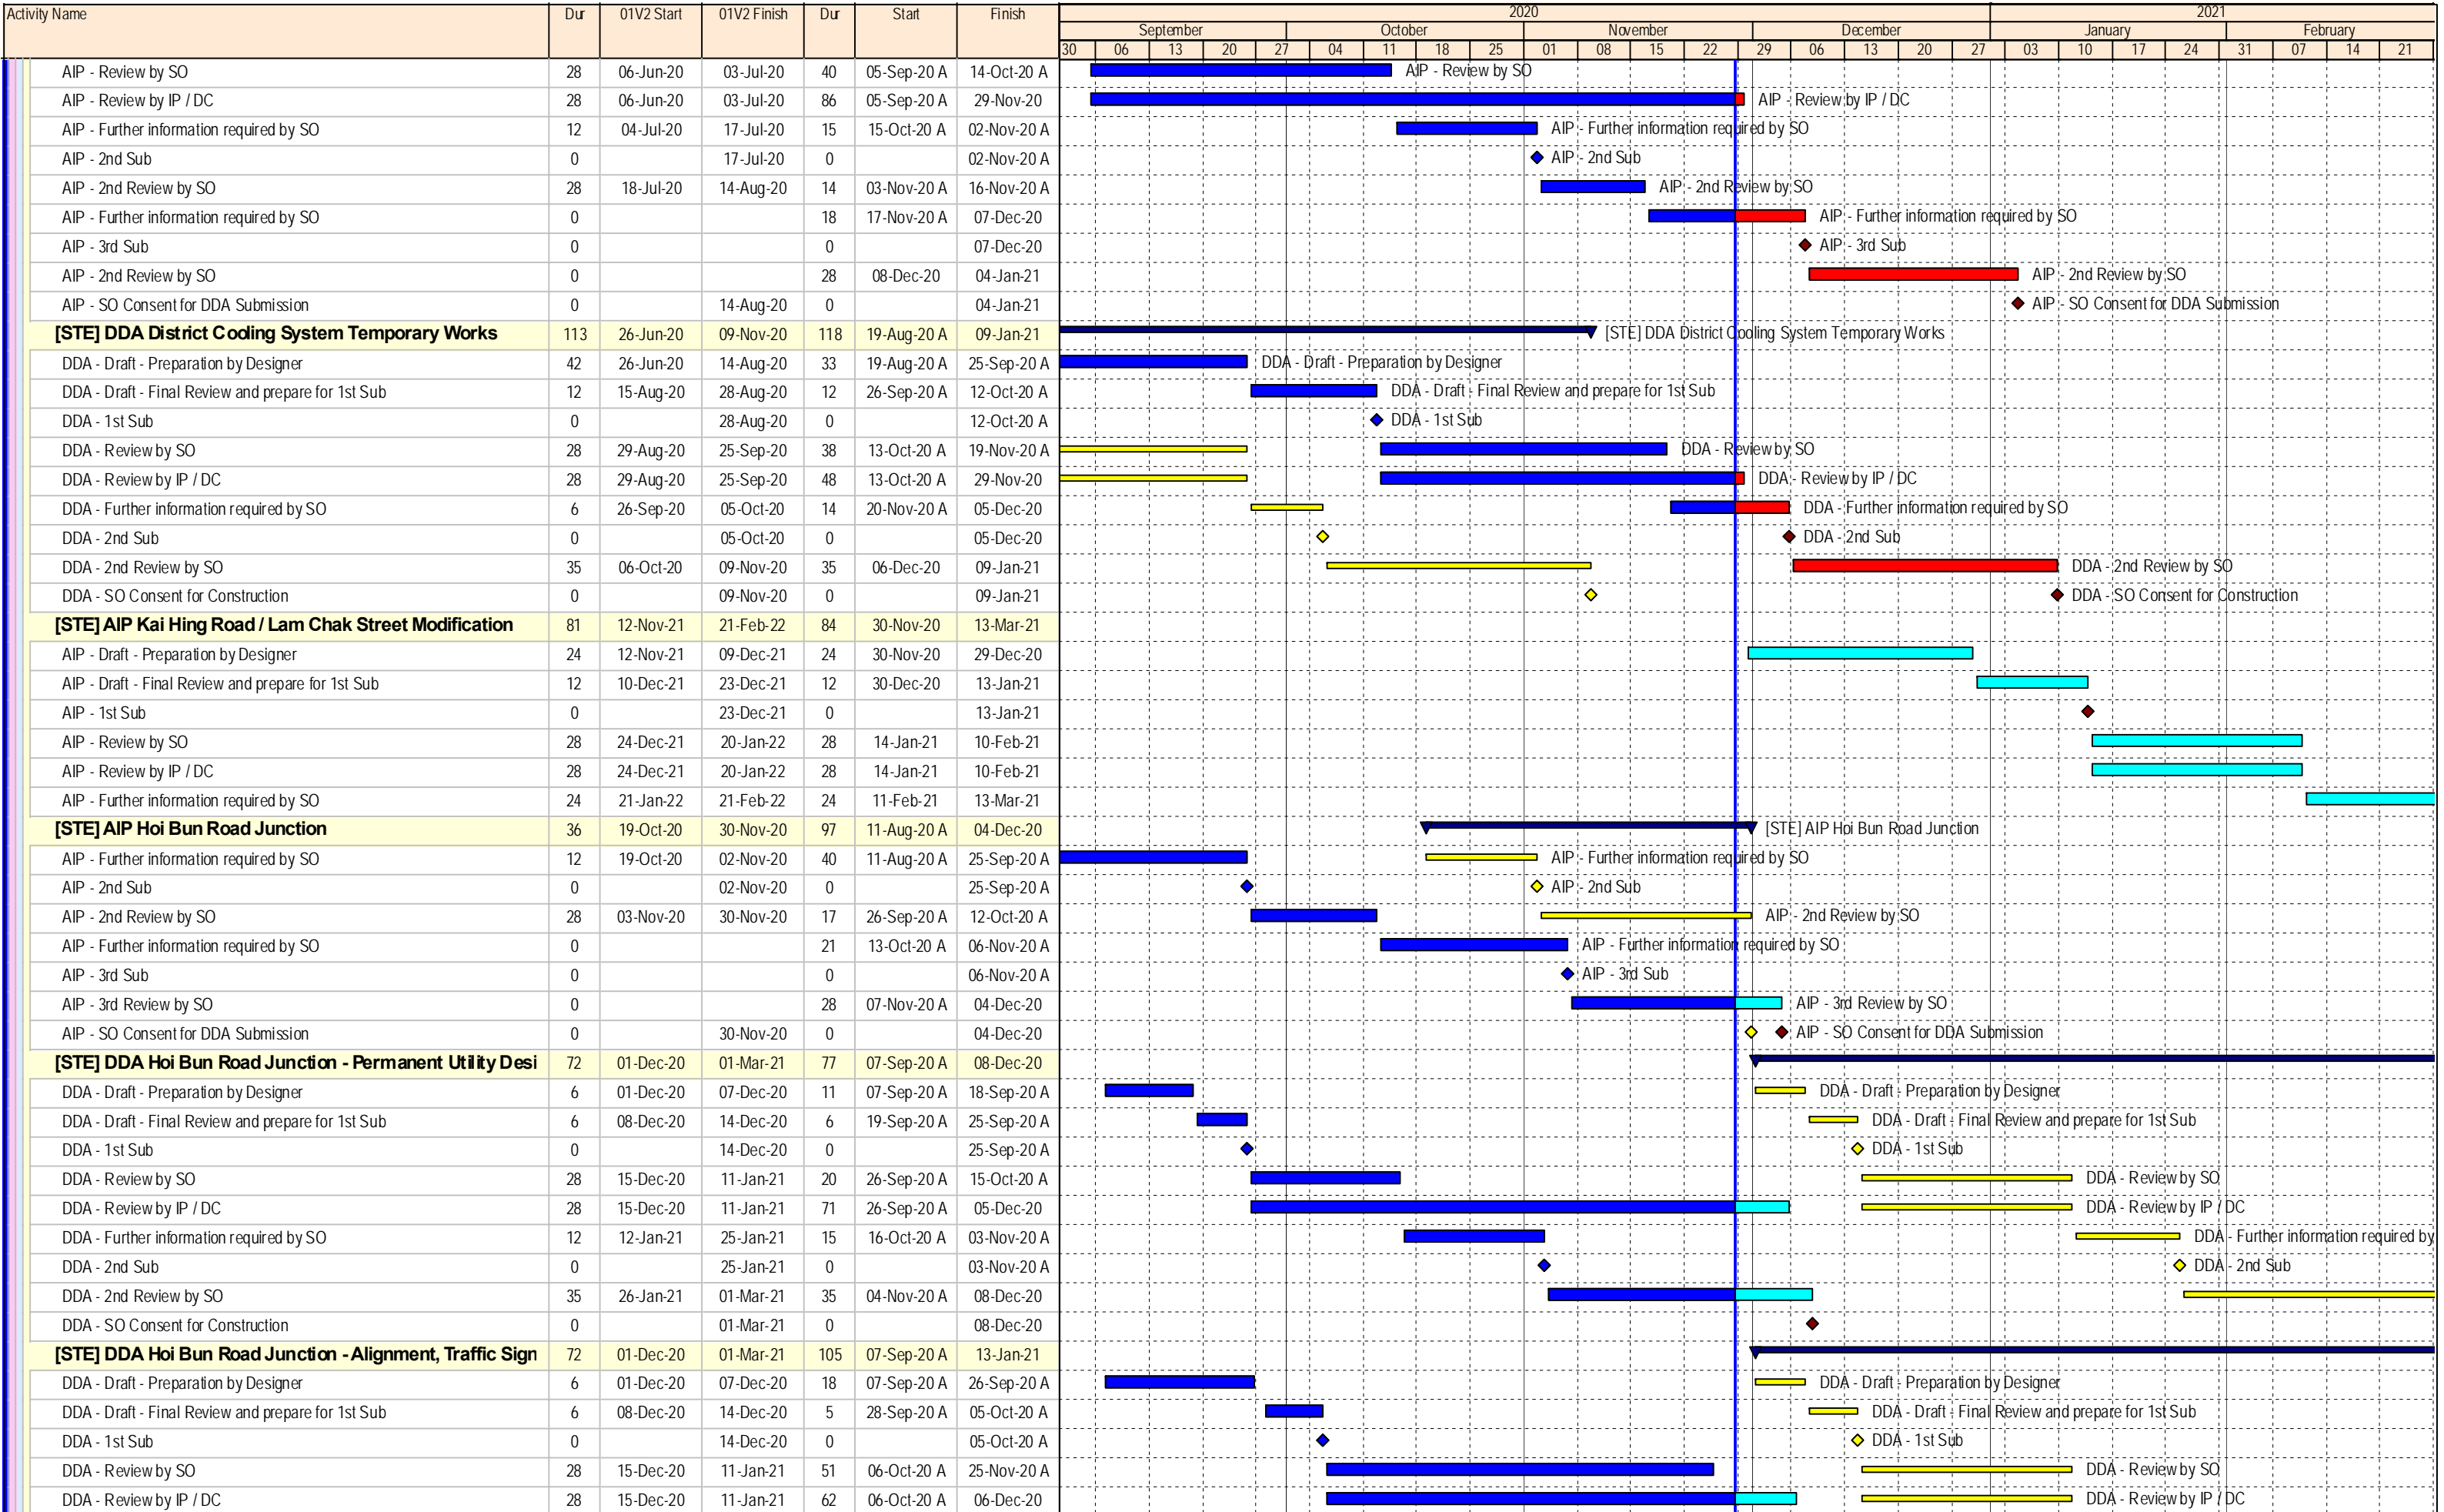


Page 9 of 24  
Data Date: 28-Nov-20

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

Summary ▬


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu



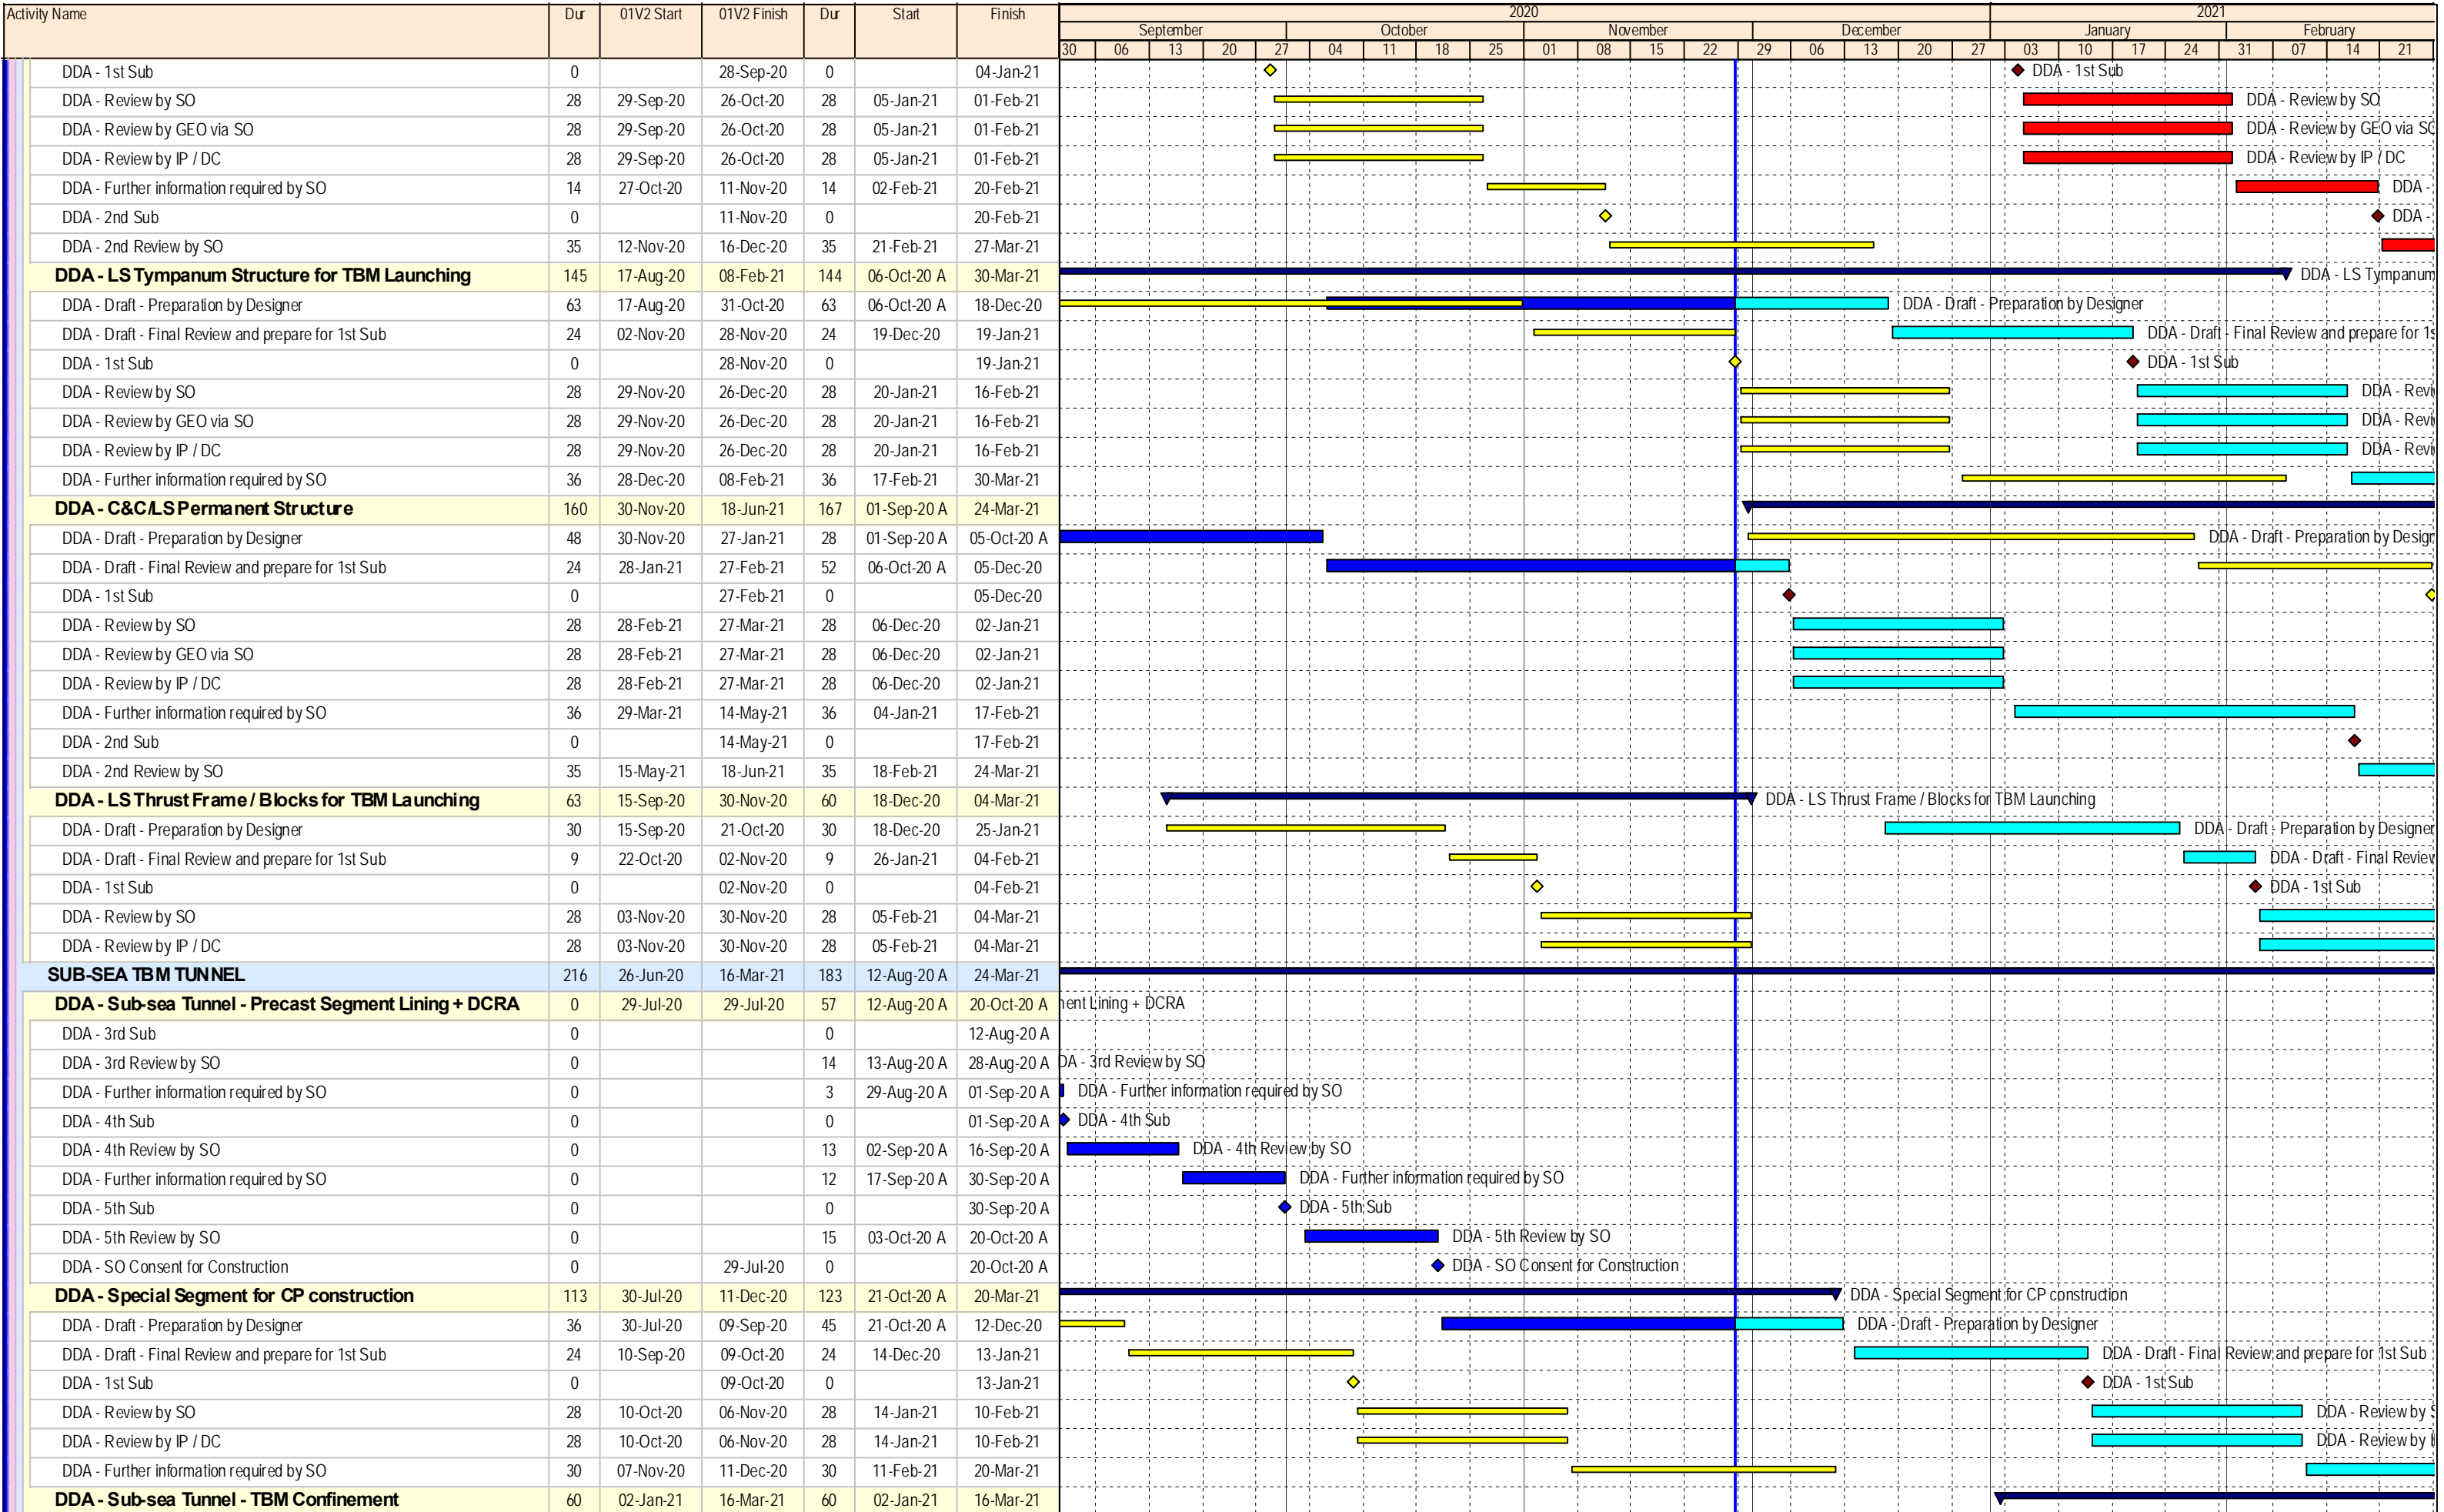


Page 11 of 24  
Data Date: 28-Nov-20

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar


Summary ▬

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

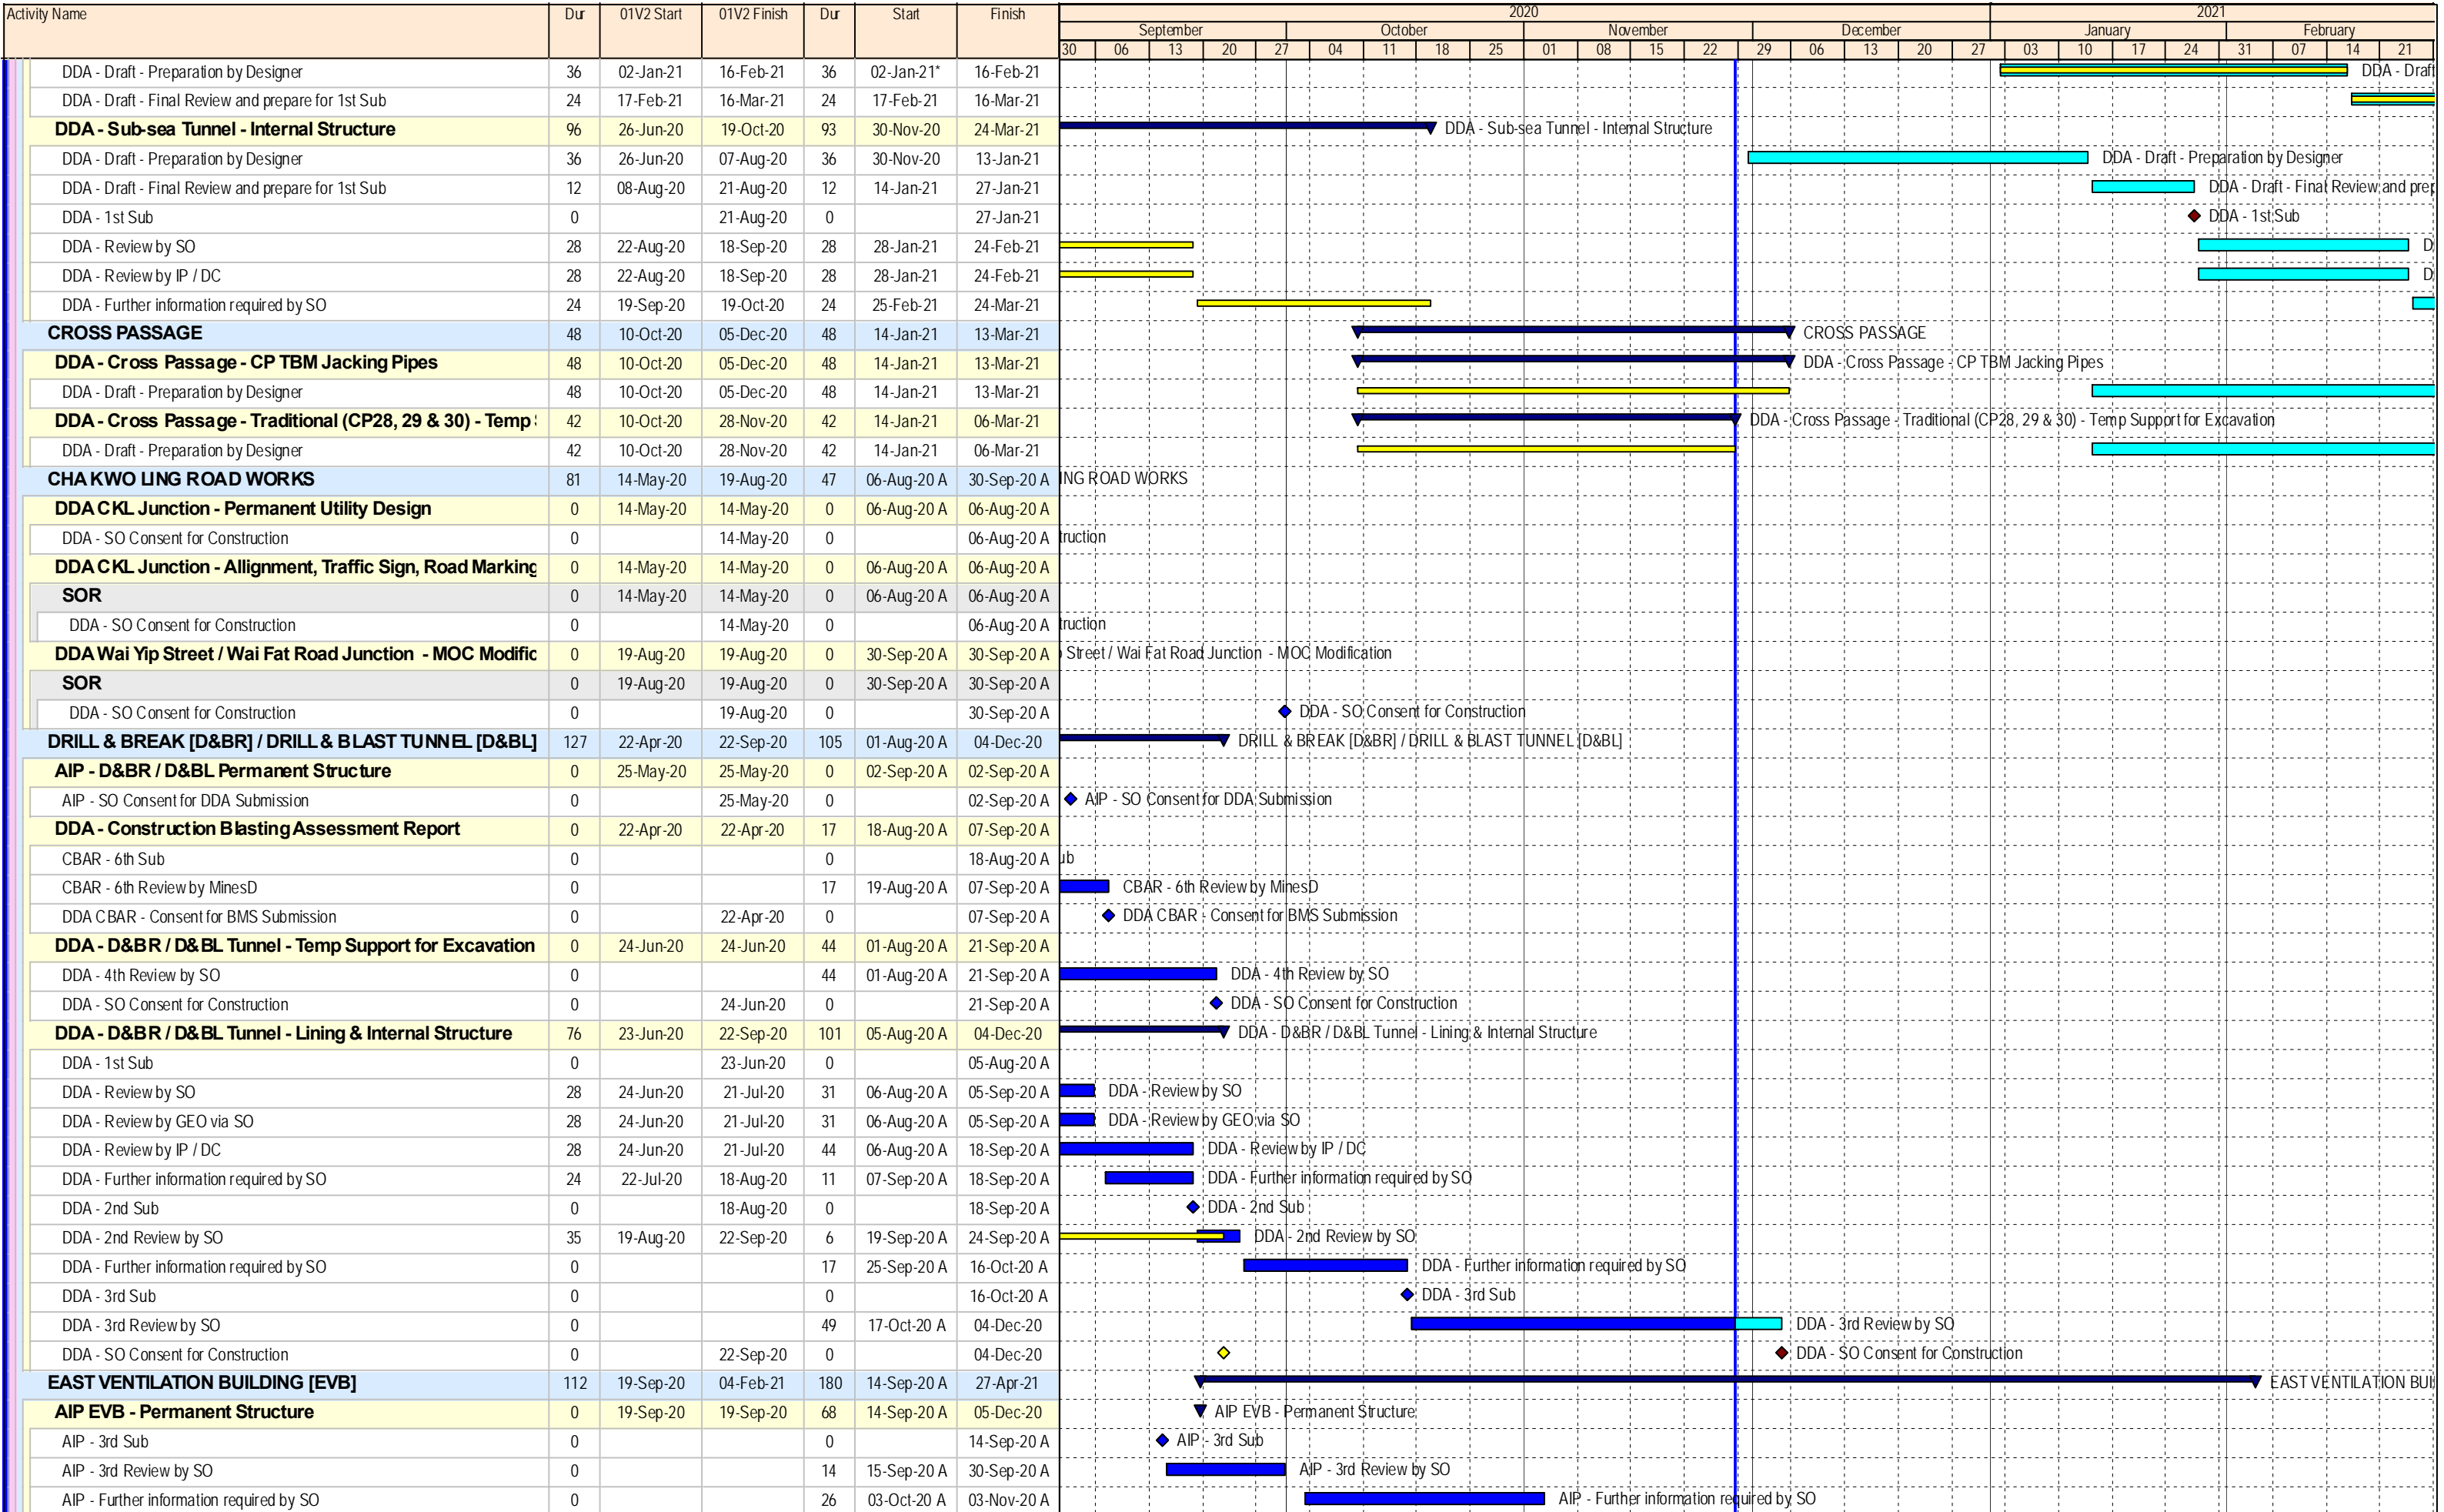


Page 12 of 24  
Data Date: 28-Nov-20

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu



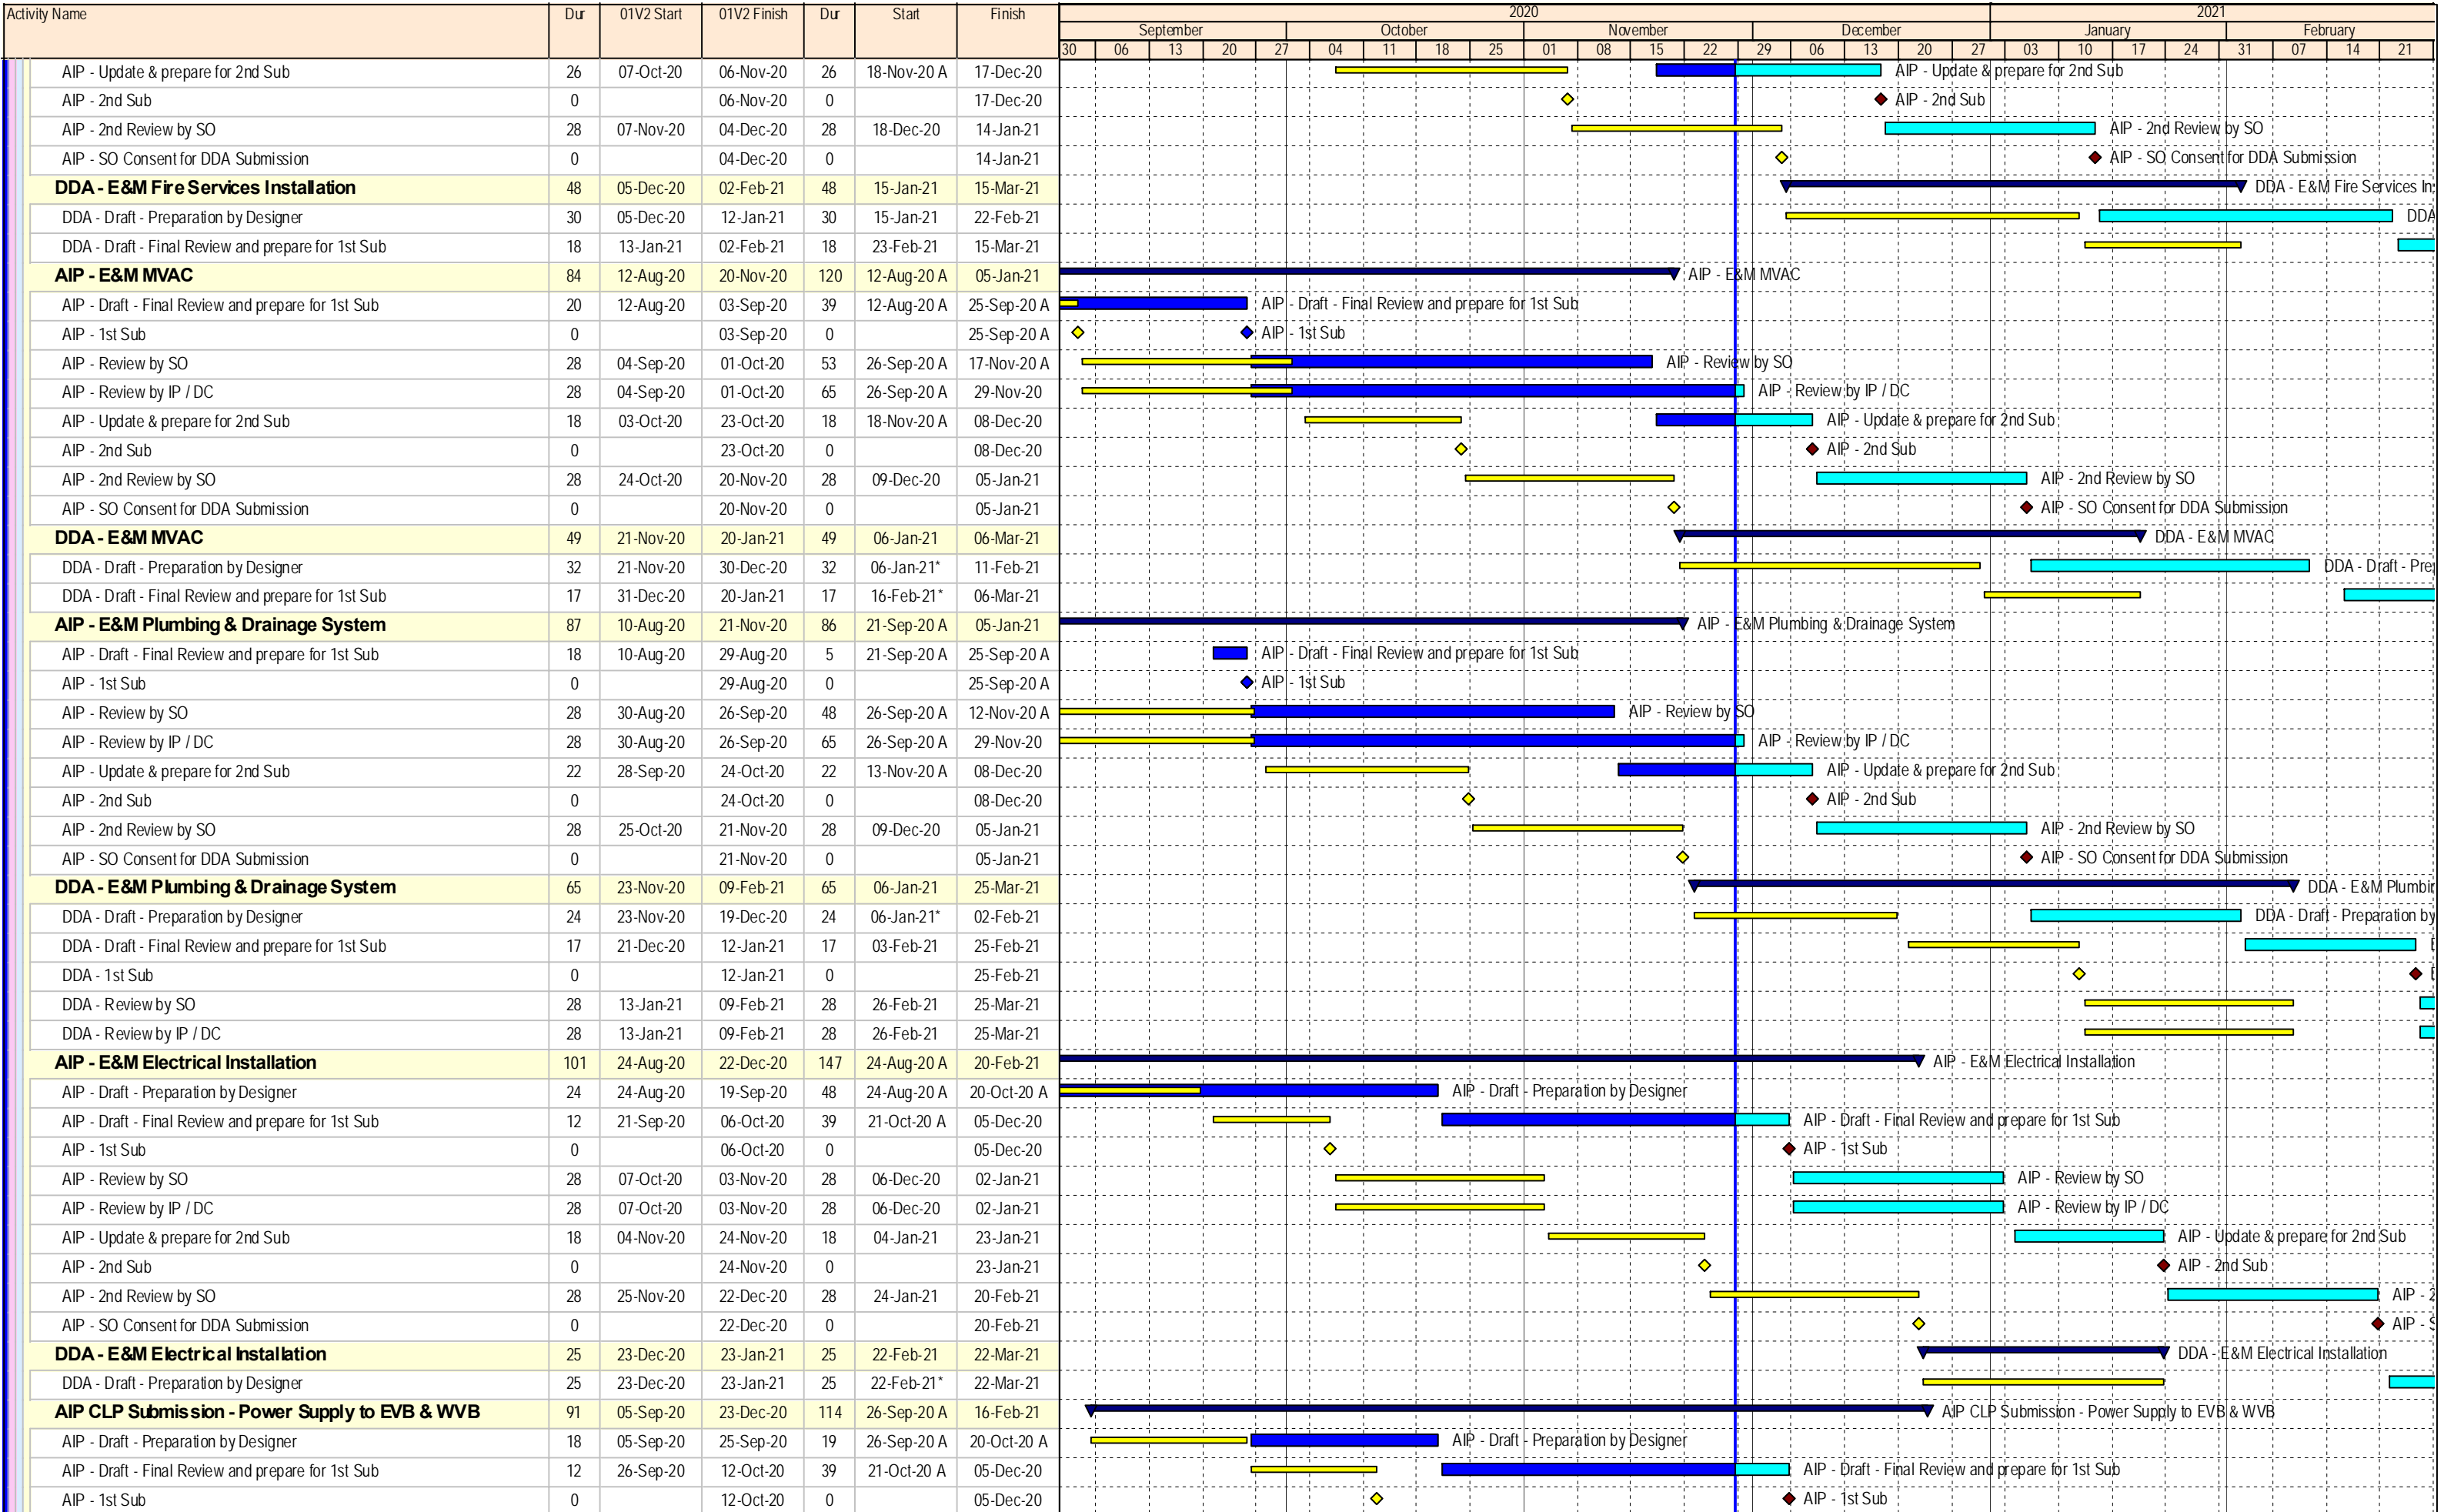


Page 14 of 24  
Data Date: 28-Nov-20

- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu



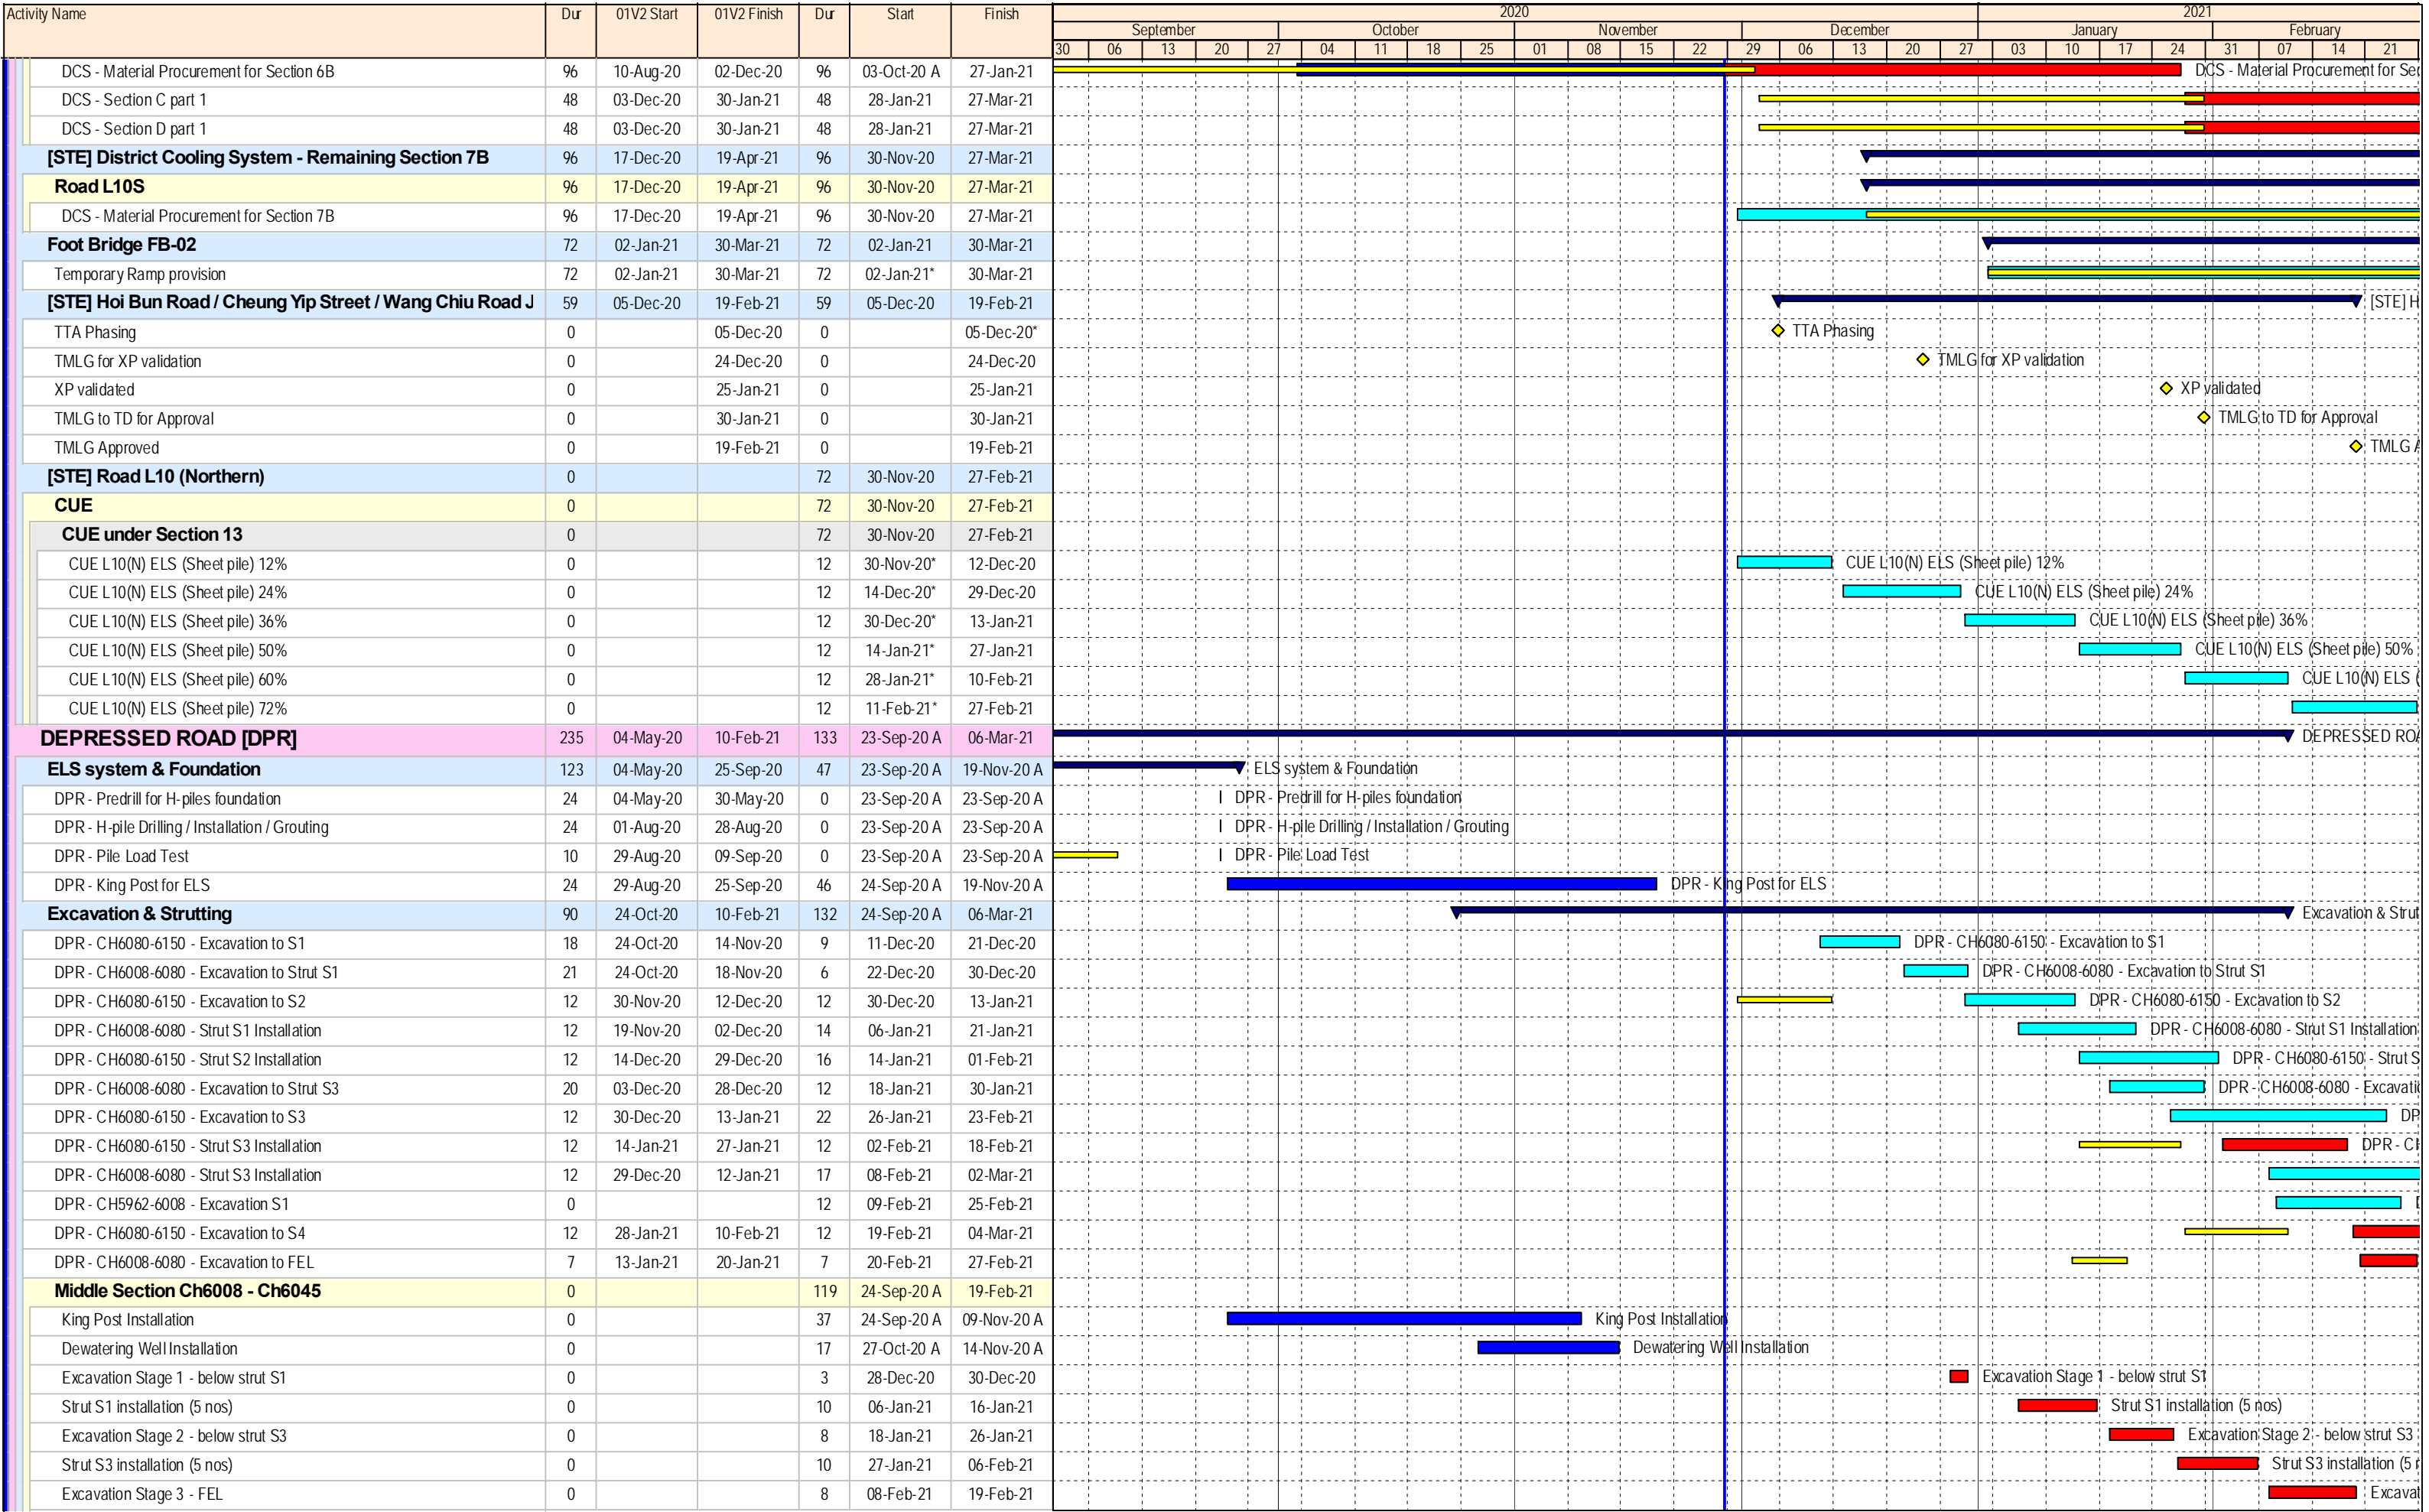


Page 16 of 24  
Data Date: 28-Nov-20

	Milestone		Summary
	Planned Bar		
	Critical Activity		
	Actual Milestone		
	Actual Work		
	Baseline Milestone		
	Baseline Bar		


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu



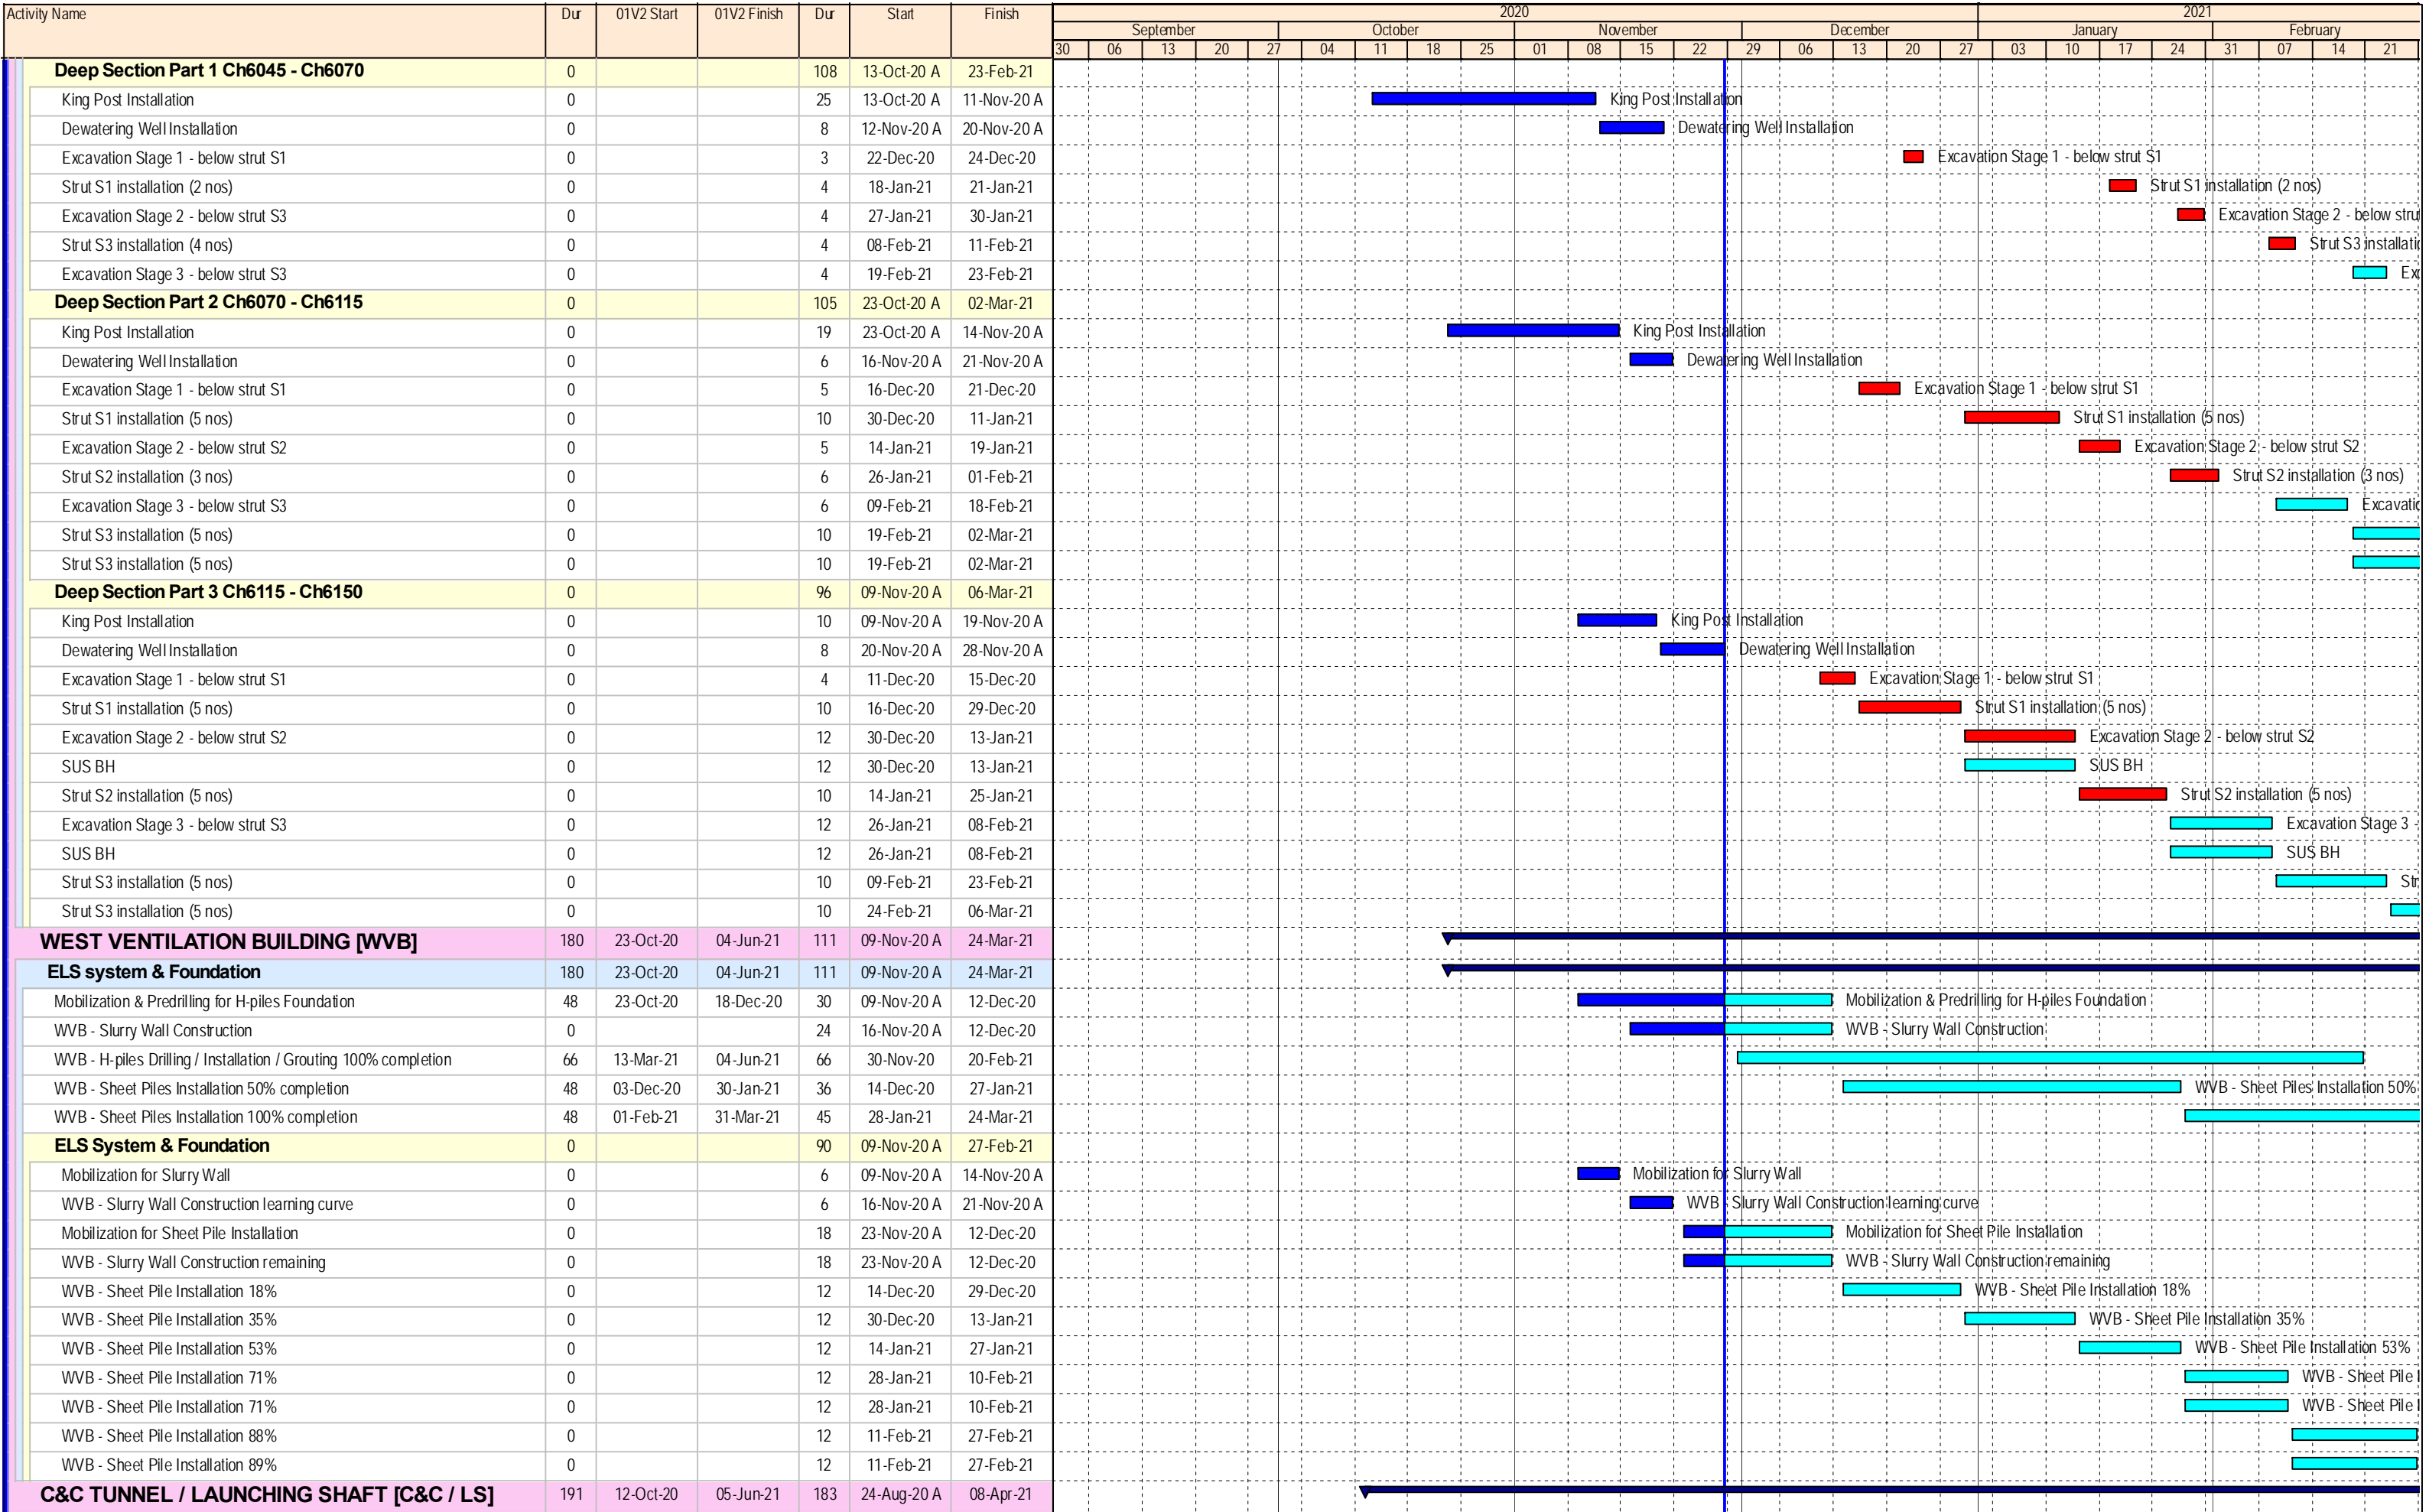


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu

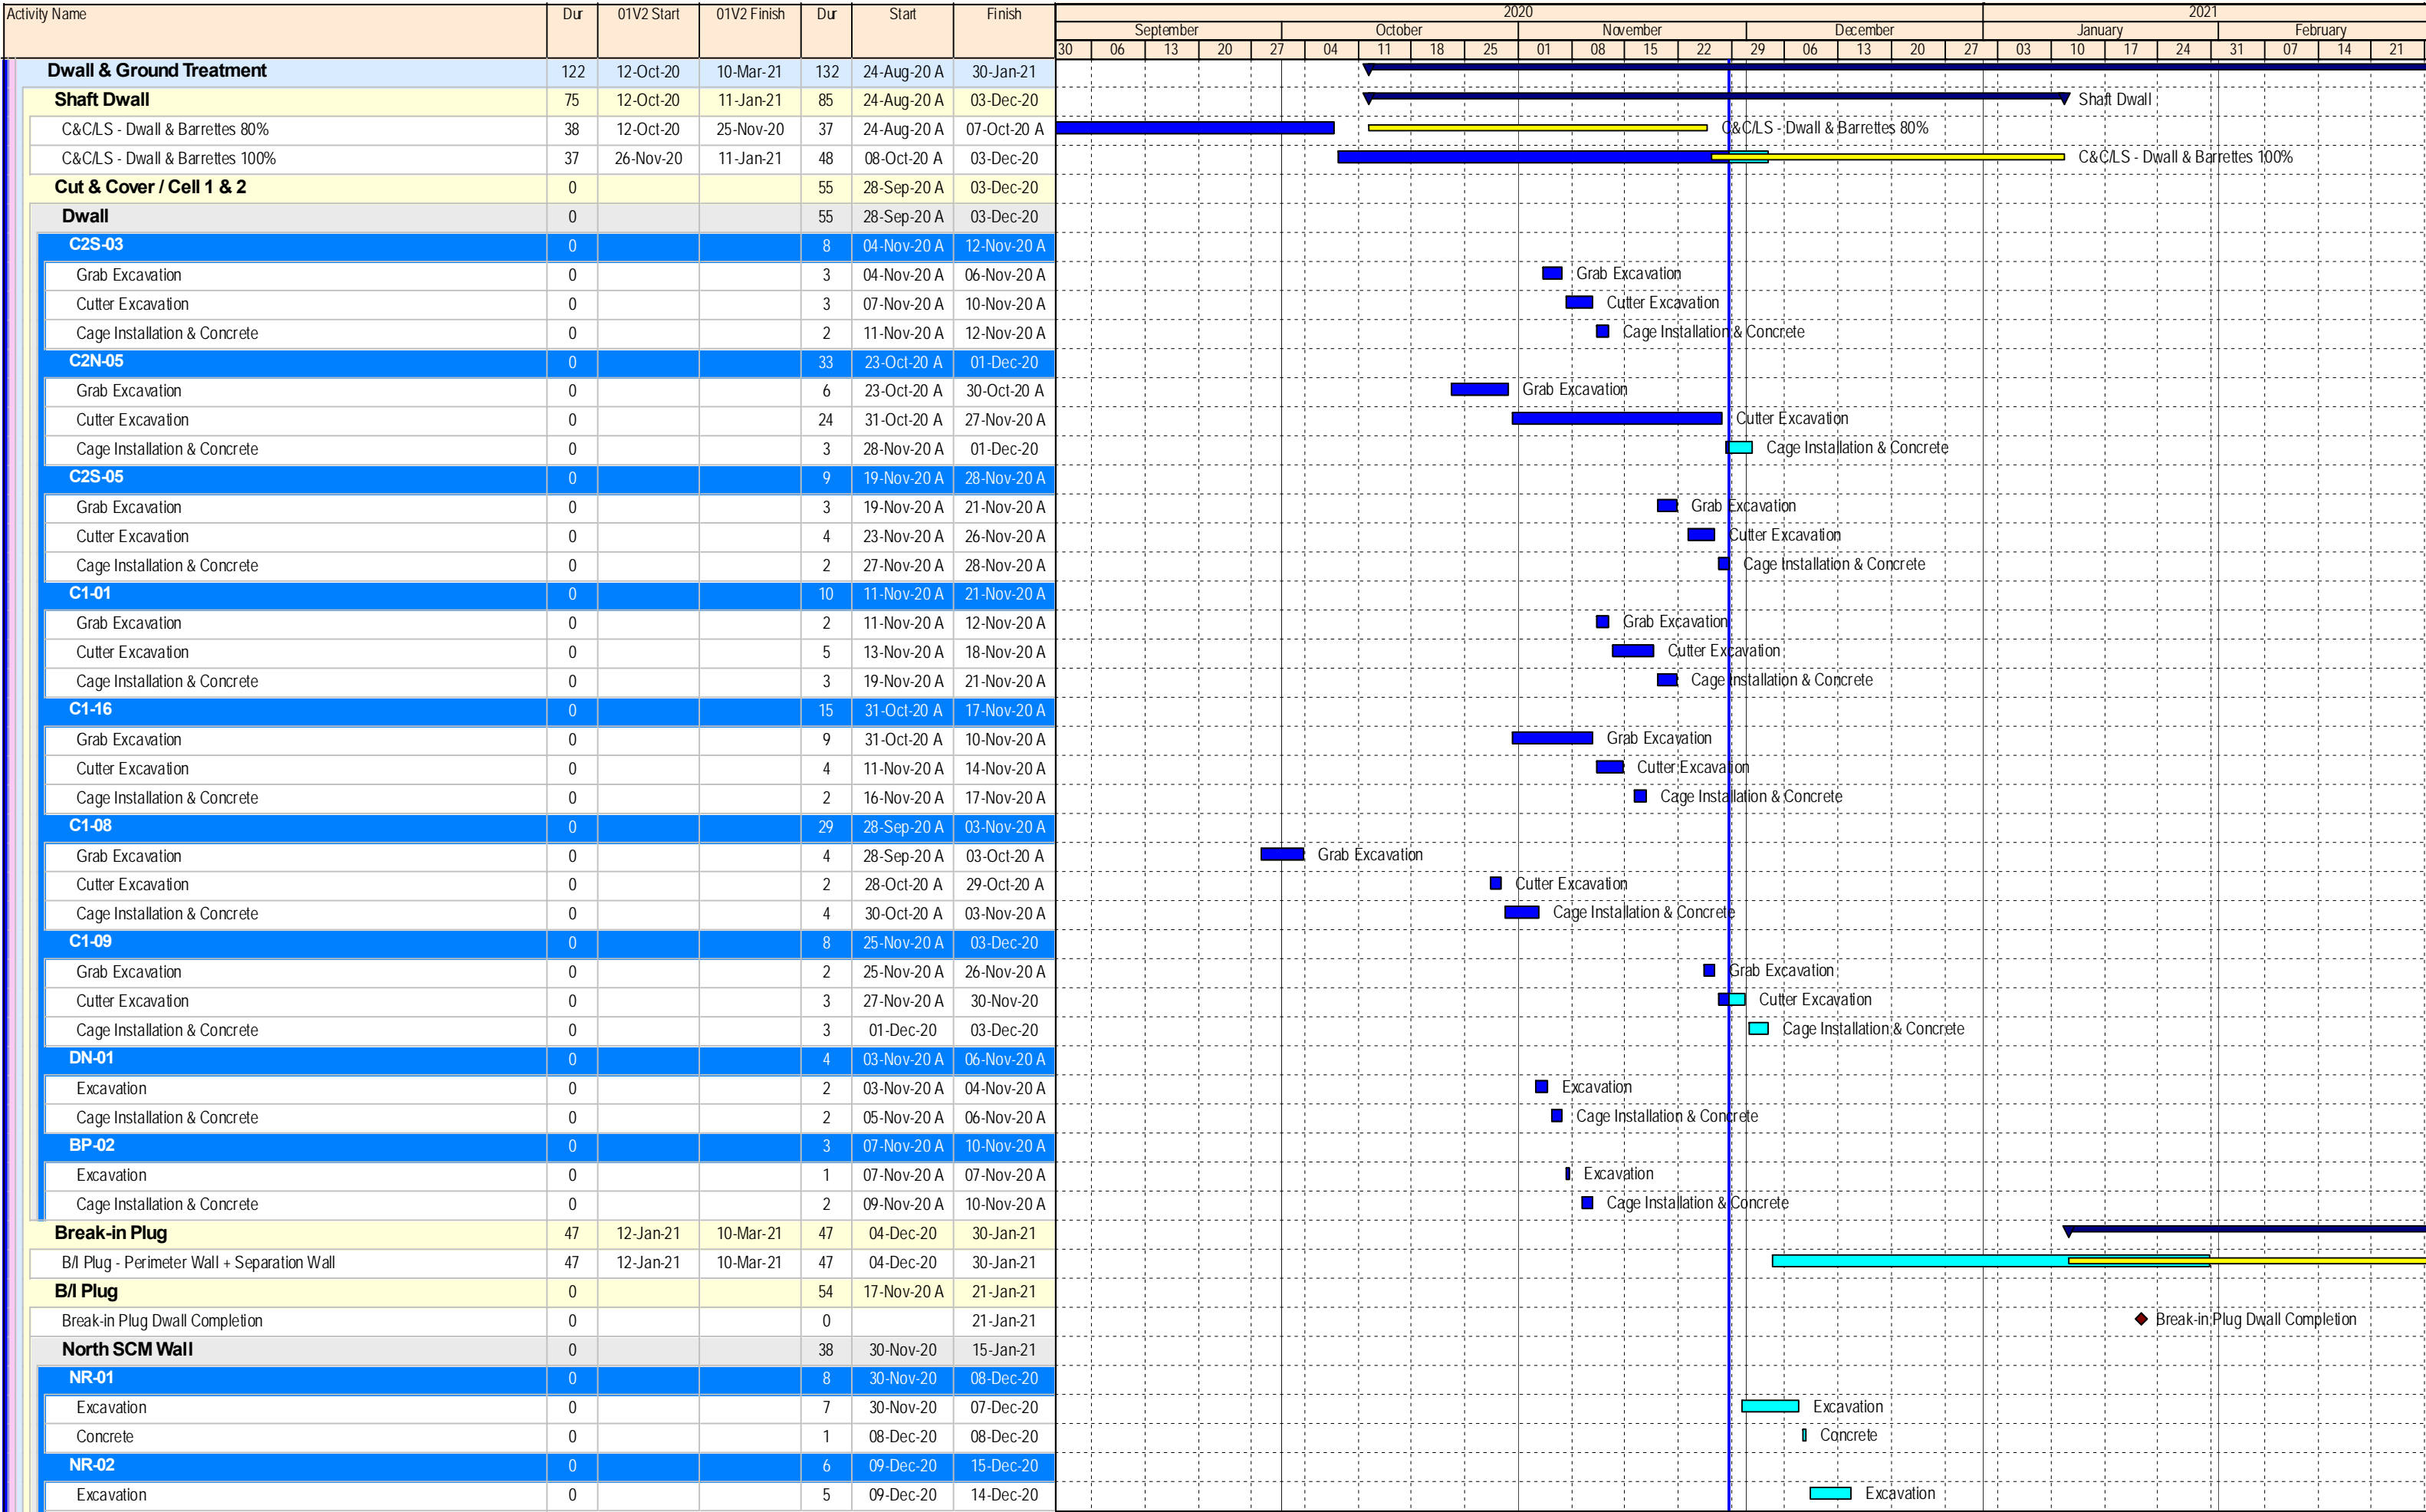

Page 18 of 24  
Data Date: 28-Nov-20


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

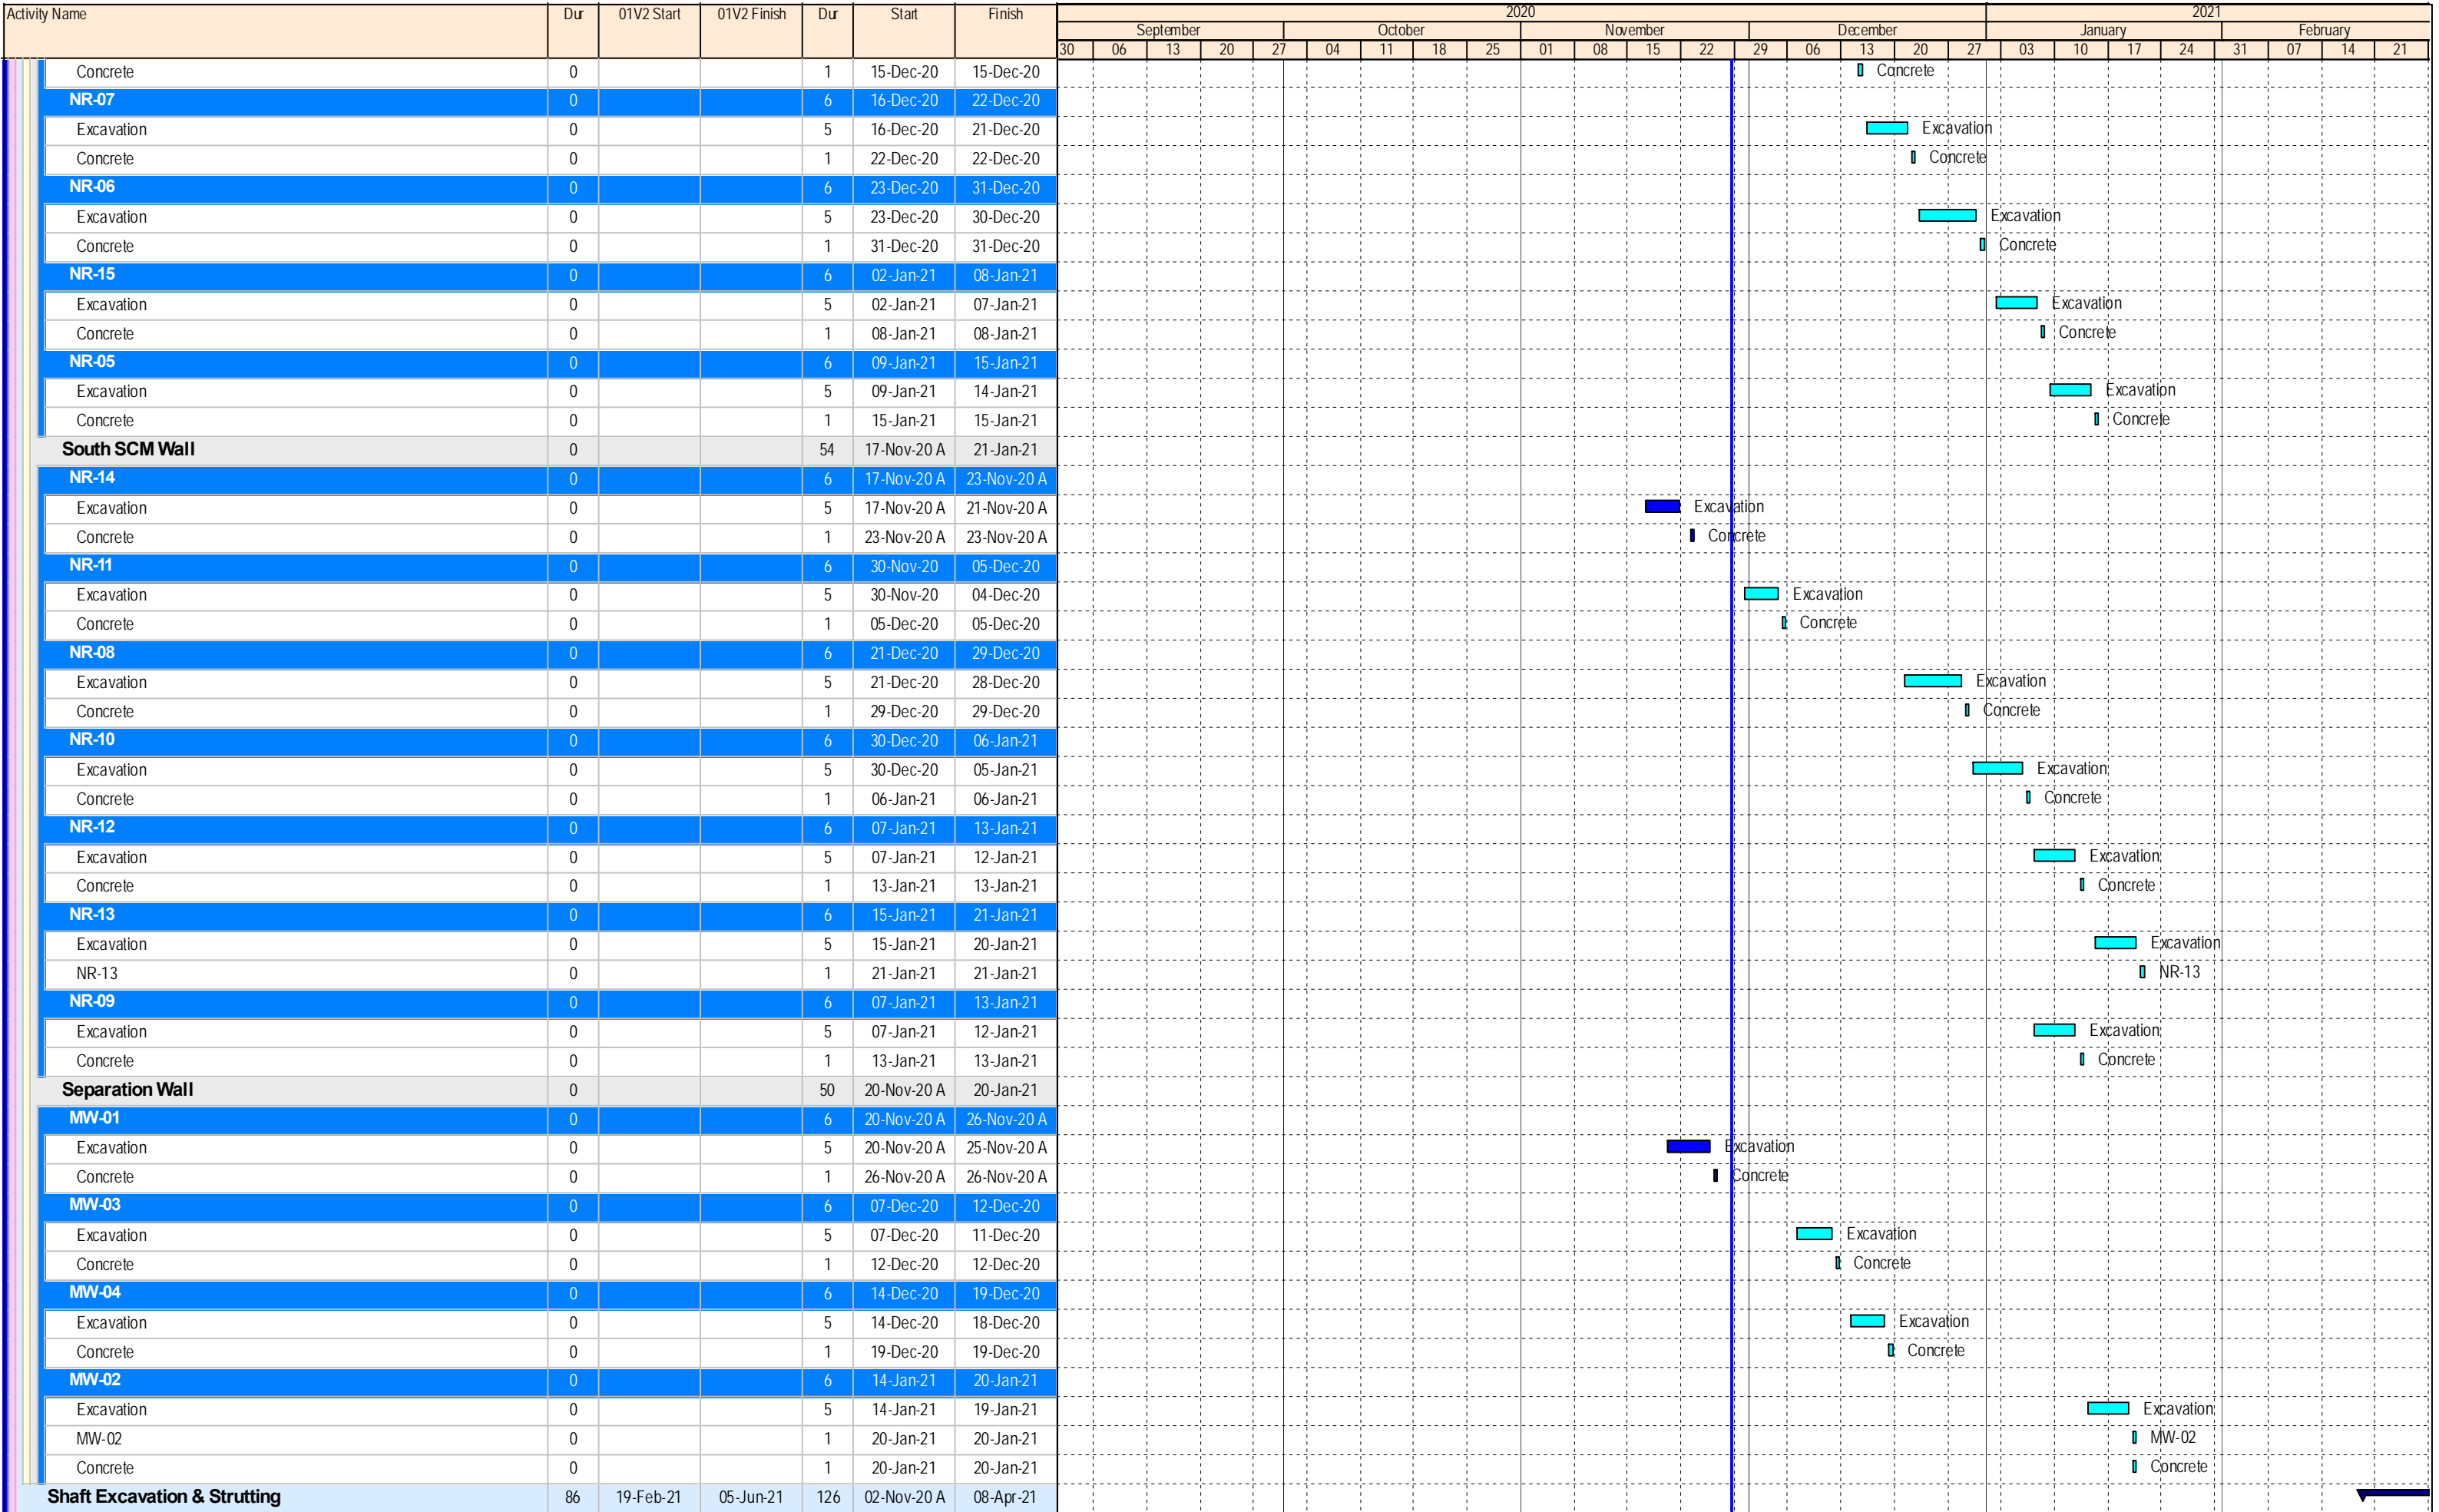


Page 19 of 24  
Data Date: 28-Nov-20

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

Summary

**ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron**


**Three Months Rolling Programme (Nov-20)**



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu






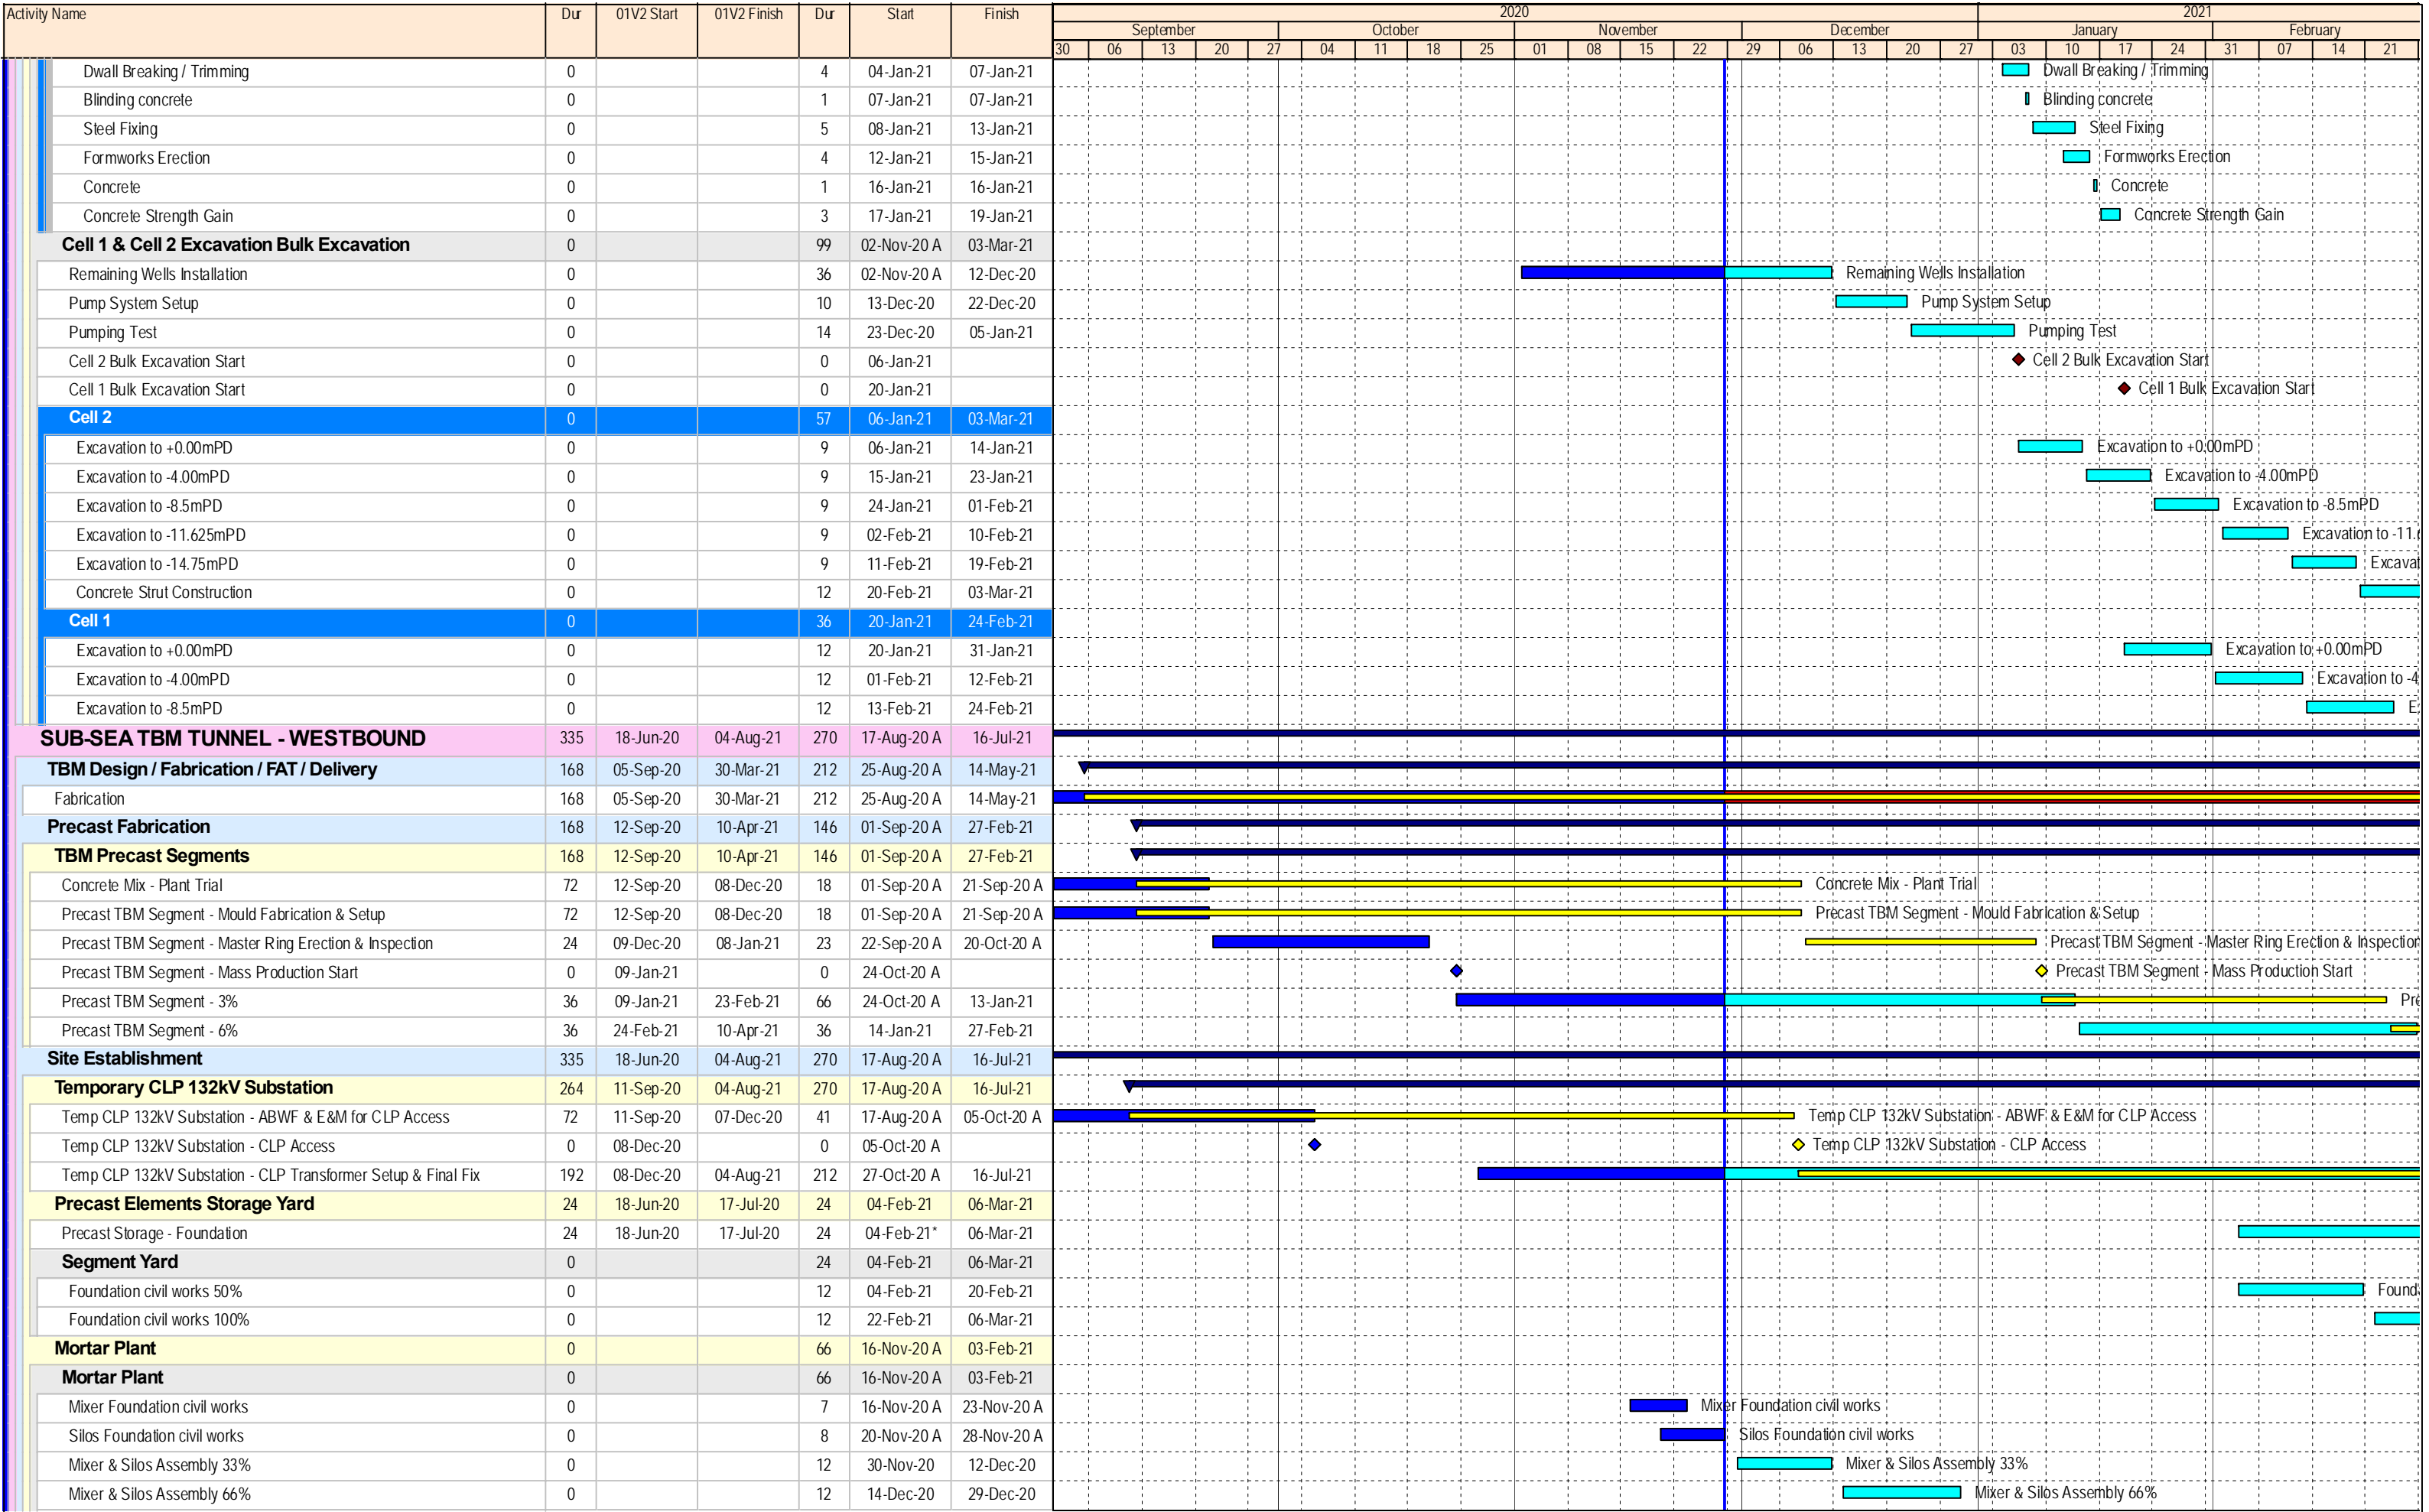


Page 22 of 24	◆ Milestone	▶ Summary
Data Date: 28-Nov-20	▬ Planned Bar	
	▬ Critical Activity	
	◆ Actual Milestone	
	▬ Actual Work	
	◆ Baseline Milestone	
	▬ Baseline Bar	

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

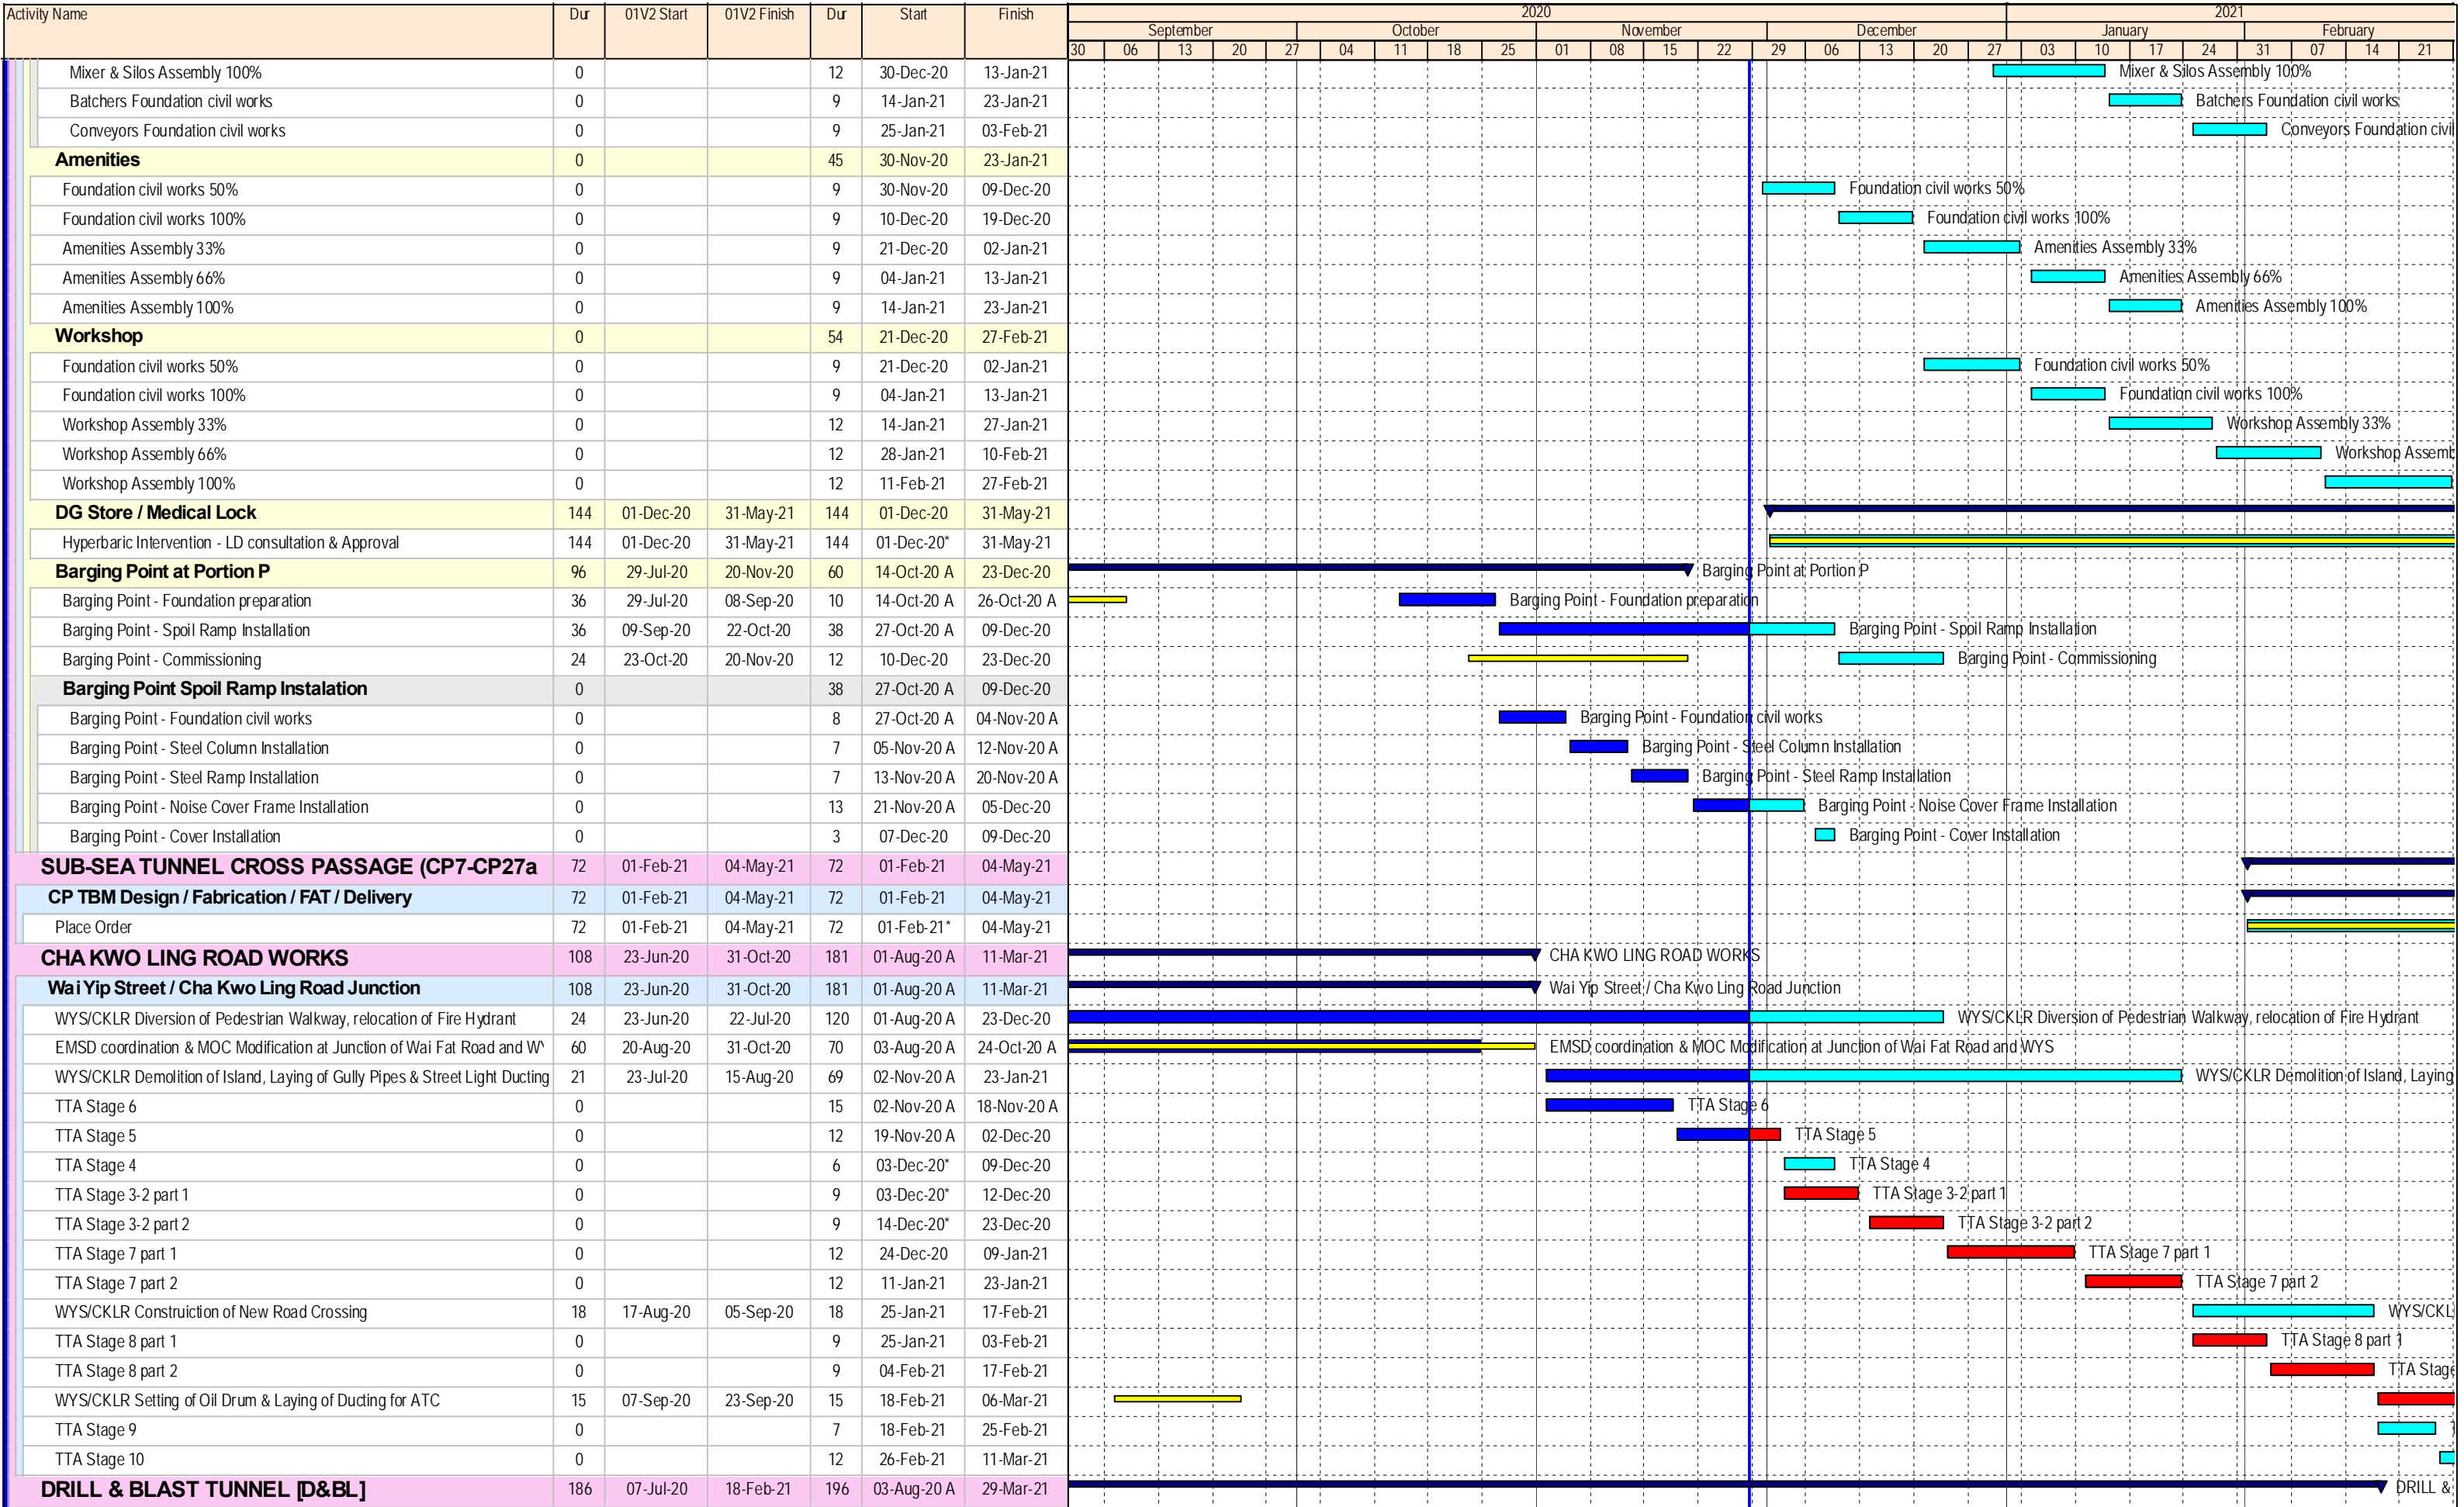


Page 23 of 24  
Data Date: 28-Nov-20

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2020							2021													
							30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17
<b>Tunnel Excavation</b>	186	07-Jul-20	18-Feb-21	196	03-Aug-20 A	29-Mar-21																					
<b>Eastbound</b>	156	10-Aug-20	18-Feb-21	177	10-Aug-20 A	13-Mar-21																					
EB - Noise Measurement & CNP	0		10-Aug-20	0		10-Aug-20 A																					
<b>Full Face Drill &amp; Blast</b>	148	20-Aug-20	18-Feb-21	153	07-Sep-20 A	13-Mar-21																					
EB - D&BI Tunnel - CH9240-9220 Type A - Excavation	30	20-Aug-20	23-Sep-20	46	07-Sep-20 A	02-Nov-20 A																					
Probe hole at CH9220	1	24-Sep-20	24-Sep-20	1	03-Nov-20 A	03-Nov-20 A																					
EB - D&BI Tunnel - CH9220-9190 Type A - Excavation	42	25-Sep-20	16-Nov-20	30	04-Nov-20 A	08-Dec-20																					
Probe hole at CH9190	1	17-Nov-20	17-Nov-20	1	10-Dec-20	10-Dec-20																					
EB - D&BI Tunnel - CH9190-9160 Type A - Excavation	13	18-Nov-20	02-Dec-20	13	11-Dec-20	28-Dec-20																					
Probe hole at CH9160	1	03-Dec-20	03-Dec-20	1	29-Dec-20	29-Dec-20																					
EB - D&BI Tunnel - CH9160-9130 Type A&B&C - Excavation	18	04-Dec-20	24-Dec-20	18	30-Dec-20	20-Jan-21																					
Probe hole at CH9130	1	28-Dec-20	28-Dec-20	1	21-Jan-21	21-Jan-21																					
EB - D&BI Tunnel - CH9130-9100 Type C - Excavation	20	29-Dec-20	21-Jan-21	20	22-Jan-21	17-Feb-21																					
Probe hole at CH9100	1	22-Jan-21	22-Jan-21	1	18-Feb-21	18-Feb-21																					
EB - D&BI Tunnel - CH9100-9070 Type C&D - Excavation	20	23-Jan-21	18-Feb-21	20	19-Feb-21	13-Mar-21																					
<b>EB - D&amp;BI Tunnel - CH9220-9190 Type A - Excavation</b>	0			31	04-Nov-20 A	09-Dec-20																					
EB - D&BI Tunnel - CH9220-9210 Type A - Excavation 40%	0			12	04-Nov-20 A	17-Nov-20 A																					
EB - D&BI Tunnel - CH9210-9200 Type A - Excavation 80%	0			12	18-Nov-20 A	01-Dec-20																					
EB - D&BI Tunnel - CH9200-9190 Type A - Excavation 100%	0			6	02-Dec-20	08-Dec-20																					
Probe hole at CH9190	0			1	09-Dec-20	09-Dec-20																					
<b>EB - D&amp;BI Tunnel - CH9190-9160 Type A - Excavation</b>	0			14	11-Dec-20	29-Dec-20																					
EB - D&BI Tunnel - CH9190-9175 Type A - Excavation 50%	0			7	11-Dec-20	18-Dec-20																					
EB - D&BI Tunnel - CH9175-9160 Type A - Excavation 100%	0			6	19-Dec-20	28-Dec-20																					
Probe hole at CH9160	0			1	29-Dec-20	29-Dec-20																					
<b>EB - D&amp;BI Tunnel - CH9160-9130 Type A&amp;B&amp;C - Excavation</b>	0			54	30-Dec-20	06-Mar-21																					
EB - D&BI Tunnel - CH9160-9145 Type A&B&C - Excavation 50%	0			9	30-Dec-20	09-Jan-21																					
EB - D&BI Tunnel - CH9145-9135 Type A&B&C - Excavation 100%	0			9	11-Jan-21	20-Jan-21																					
EB - D&BI Tunnel - CH9135-9119 Type C - Bench Enlargement	0			12	21-Jan-21	03-Feb-21																					
EB - D&BI Tunnel - CH9119-9103 Type C - Bench Enlargement	0			12	04-Feb-21	20-Feb-21																					
EB - D&BI Tunnel - CH9103-9087 Type C - Bench Enlargement	0			12	22-Feb-21	06-Mar-21																					
<b>Westbound</b>	117	07-Jul-20	23-Nov-20	196	03-Aug-20 A	29-Mar-21																					
<b>Full Face Drill &amp; Break</b>	62	07-Jul-20	16-Sep-20	141	03-Aug-20 A	20-Jan-21																					
WB - Install 1st arch rib	6	07-Jul-20	13-Jul-20	4	03-Aug-20 A	06-Aug-20 A																					
WB - D&Br & Install arch rib (2nd - 5th)	28	14-Jul-20	14-Aug-20	36	07-Aug-20 A	17-Sep-20 A																					
WB - D&Br CH9257-9250 Type A - Excavation	28	15-Aug-20	16-Sep-20	34	18-Sep-20 A	31-Oct-20 A																					
<b>Full Face Drill &amp; Break</b>	0			66	02-Nov-20 A	20-Jan-21																					
WB - D&Br CH9250-9249 Type A - Excavation	0			18	02-Nov-20 A	21-Nov-20 A																					
WB - D&Br CH9249-9248 Type A - Excavation	0			12	23-Nov-20 A	05-Dec-20																					
WB - D&Br CH9248-9247 Type A - Excavation	0			12	07-Dec-20	19-Dec-20																					
WB - D&Br CH9247-9246 Type A - Excavation	0			12	21-Dec-20	06-Jan-21																					
WB - D&Br CH9246-9245 Type A - Excavation	0			12	07-Jan-21	20-Jan-21																					
<b>Full Face Drill &amp; Blast</b>	55	17-Sep-20	23-Nov-20	55	21-Jan-21	29-Mar-21																					
WB- Blast Door Installation	24	17-Sep-20	16-Oct-20	24	21-Jan-21	20-Feb-21																					
WB- D&BI start	0		16-Oct-20	0		20-Feb-21																					
WB - D&BI Tunnel - CH9250-9230 Type A - Excavation	31	17-Oct-20	23-Nov-20	31	22-Feb-21	29-Mar-21																					
<b>Blast Door Installation</b>	0			24	21-Jan-21	20-Feb-21																					
WB- Blast Door Installation 50%	0			12	21-Jan-21	03-Feb-21																					
WB- Blast Door Installation 100%	0			12	04-Feb-21	20-Feb-21																					

Page 24 of 24  
Data Date: 28-Nov-20

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Nov-20)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
