

| #  | Activity Name   | Dur | Start      | Finish     | 2024  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
|----|---|-----|------------|------------|---|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|
|    |   |     |            |            | Jan-24  | 14 | 21 | 28 | 04 | 11 | 18 | 25 | 03 | 10 | 17 | 24 | 31 | 07 | 14 | 21 | 28 | 05 | 12 | 19 | 26 | 02 | 09 | 16 | 23 | 30 | 07 | 14 |
| 1  | <b>ED/2018/04 TRUNK ROAD T2</b>                               | 145 | 02-Jan-24  | 29-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 2  | <b>WEST VENTILATION BUILDING [WVB]</b>                        | 134 | 02-Jan-24  | 17-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 3  | <b>WVB Construction</b>                                       | 122 | 16-Jan-24  | 17-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 4  | GBP resubmission and approval                                 | 37  | 16-Jan-24* | 01-Mar-24  | GBP resubmission and approval                                 |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 5  | <b>E&amp;M</b>  | 107 | 17-Jan-24  | 30-May-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 6  | WVB - E&M works (G/F)   | 83  | 17-Jan-24* | 30-Apr-24  | WVB - E&M works (G/F)   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 7  | WVB - E&M works (1/F)   | 84  | 16-Feb-24* | 30-May-24  | WVB - E&M works (1/F)   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 8  | <b>External Works / EVA</b>                                   | 96  | 19-Feb-24  | 17-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 9  | UU works and Backfilling                                      | 36  | 19-Feb-24  | 03-Apr-24  | UU works and Backfilling                                      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 10 | Access Road Construction                                      | 36  | 05-Apr-24  | 18-May-24  | Access Road Construction                                      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 11 | Fire Hydrants confirmation from FSD for FSI inspection        | 0   |            | 01-Jun-24  | ◆ Fire Hydrants confirmation from FSD for FSI inspection      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 12 | EVA Construction  | 24  | 20-May-24  | 17-Jun-24  | EVA Construction  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 13 | <b>Essential Criteria for FSI</b>                             | 133 | 02-Jan-24  | 15-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 14 | <b>Power Engerization</b>                                     | 90  | 05-Feb-24  | 30-May-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 15 | CLP Final Inspection / CLP Tx Rm - Handover to CLP            | 0   |            | 05-Feb-24  | ◆ CLP Final Inspection / CLP Tx Rm - Handover to CLP          |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 16 | CLP Mobilization  | 45  | 06-Feb-24  | 05-Apr-24  | CLP Mobilization  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 17 | CLP Installation  | 45  | 06-Apr-24  | 30-May-24  | CLP Installation  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 18 | CLP Tx Rm - Power On  | 0   |            | 30-May-24  | ◆ CLP Tx Rm - Power On  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 19 | <b>Dangerous Goods Licenses</b>                               | 133 | 02-Jan-24  | 15-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 20 | Emergency Generator Room - ABWF works                         | 34  | 02-Jan-24* | 09-Feb-24  | Emergency Generator Room - ABWF works                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 21 | WVB - Genset & Oil Tank delivery on site                      | 0   |            | 01-Mar-24  | ◆ WVB - Genset & Oil Tank delivery on site                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 22 | WVB - Genset & Oil Tank Installation and T&C                  | 48  | 02-Mar-24  | 02-May-24  | WVB - Genset & Oil Tank Installation and T&C                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 23 | Receipt of report of compliance                               | 0   |            | 10-May-24  | ◆ Receipt of report of compliance                             |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 24 | Submission of Application                                     | 7   | 03-May-24  | 10-May-24  | Submission of Application                                     |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 25 | DG Licenses Inspection (Vent) by FSD                          | 0   |            | 20-May-24  | ◆ DG Licenses Inspection (Vent) by FSD                        |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 26 | DG Licenses Inspection (Layout) by FSD                        | 0   |            | 07-Jun-24  | ◆ DG Licenses Inspection (Layout) by FSD                      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 27 | Issuance of Certificate from FSD                              | 0   |            | 15-Jun-24  | ◆ Issuance of Certificate from FSD                            |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 28 | <b>Fireman Lift</b>   | 87  | 06-Feb-24  | 27-May-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 29 | Lift Installation (by OTIS)                                   | 51  | 06-Feb-24  | 12-Apr-24  | Lift Installation (by OTIS)                                   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 30 | T&C (by OTIS) & Issue WR1 / Submisison of LE5                 | 24  | 13-Apr-24  | 11-May-24  | T&C (by OTIS) & Issue WR1 / Submisison of LE5                 |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 31 | EMSD Inspection   | 12  | 13-May-24  | 27-May-24  | EMSD Inspection   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 32 | Issuance of Permit by EMSD                                    | 0   |            | 27-May-24  | ◆ Issuance of Permit by EMSD                                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 33 | <b>Water Supply</b>   | 121 | 15-Jan-24  | 15-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 34 | <b>FS Water (Inside WVB)</b>                                  | 109 | 30-Jan-24  | 15-Jun-24  |   |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 35 | 542 Approval from WSD   | 0   |            | 30-Jan-24* | ◆ 542 Approval from WSD                                       |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 36 | Submission WW046 part 1                                       | 0   |            | 01-Feb-24  | ◆ Submission WW046 part 1                                     |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 37 | Submission of WW046 Part IV for FS Water                      | 0   |            | 30-Apr-24  | ◆ Submission of WW046 Part IV for FS Water                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 38 | Inspection for FS Water & Issuance of WW046 part V (a) by WSD | 12  | 17-May-24  | 30-May-24  | Inspection for FS Water & Issuance of WW046 part V (a) by WSD |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 39 | Pipe Sterilization & Water Sampling                           | 6   | 31-May-24  | 06-Jun-24  | Pipe Sterilization & Water Sampling                           |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 40 | Water Sample Testing  | 3   | 07-Jun-24  | 11-Jun-24  | Water Sample Testing  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 41 | Issuance of WW046 Part V(b) from WSD                          | 0   |            | 11-Jun-24  | ◆ Issuance of WW046 Part V(b) from WSD                        |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |


Appendix A

Page 1 of 8

- ◆ Milestone
- Planned Bar
- Critical Bar

**ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron**

Three Months Rolling Programme (Feb-24)



| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 31-Jan-24 | Rev. A   | SPa     |          |





| #   | Activity Name   | Dur | Start      | Finish    | 2024    |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
|-----|---|-----|------------|-----------|---------|----|----|----|----------|----|----|----|----|-------|----|----|----|-------|----|----|----|-----|----|----|----|----|------|----|----|----|------|----|----|--|--|--|--|
|     |   |     |            |           | January |    |    |    | February |    |    |    |    | March |    |    |    | April |    |    |    | May |    |    |    |    | June |    |    |    | July |    |    |  |  |  |  |
|     |   |     |            |           | 14      | 21 | 28 | 04 | 11       | 18 | 25 | 03 | 10 | 17    | 24 | 31 | 07 | 14    | 21 | 28 | 05 | 12  | 19 | 26 | 02 | 09 | 16   | 23 | 30 | 07 | 14   | 21 | 28 |  |  |  |  |
| 83  | Pipe relocation - R0347-R0392                                 | 12  | 05-Apr-24  | 18-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 84  | Pipe relocation - R0393-R0437                                 | 12  | 19-Apr-24  | 03-May-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 85  | Pipe relocation - R0438-R0483                                 | 12  | 04-May-24  | 18-May-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 86  | Pipe relocation - R0484-R0528                                 | 12  | 20-May-24  | 05-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 87  | Pipe relocation - R0529-R0573                                 | 12  | 07-Jun-24  | 21-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 88  | <b>SUB-SEA TUNNEL CROSS PASSAGE [CP]</b>                      | 60  | 16-Mar-24  | 04-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 89  | <b>Tympanum Civil Works</b>                                   | 60  | 16-Mar-24  | 04-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 90  | <b>Eastbound</b>  | 24  | 16-Mar-24  | 17-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 91  | CP25 - EB - Tympanum Civil works CH8489                       | 24  | 16-Mar-24  | 17-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 92  | <b>Westbound</b>  | 28  | 27-Apr-24  | 04-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 93  | CP25 - WB - Tympanum Civil works CH8499                       | 28  | 27-Apr-24  | 04-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 94  | <b>INTERNAL STRUCTURES</b>                                    | 133 | 04-Jan-24  | 18-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 95  | <b>Service Gallery B</b>                                      | 42  | 15-Feb-24  | 09-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 96  | <b>Eastbound</b>  | 0   | 15-Feb-24  | 15-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 97  | EB ISIG re-start at SG0820E                                   | 0   | 15-Feb-24  |           |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 98  | <b>Westbound</b>  | 0   | 09-Apr-24  | 09-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 99  | WB ISIG re-start at SG0808W                                   | 0   | 09-Apr-24  |           |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 100 | <b>Corbel</b>   | 84  | 29-Feb-24  | 18-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 101 | <b>Eastbound</b>  | 84  | 29-Feb-24  | 18-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 102 | EB Corbel re-start  | 0   | 29-Feb-24  |           |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 103 | EB Corbel construction CH8444-8573 129m                       | 84  | 29-Feb-24  | 18-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 104 | <b>Westbound</b>  | 0   | 23-Apr-24  | 23-Apr-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 105 | WB Corbel re-start  | 0   | 23-Apr-24  |           |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 106 | <b>Thermal Barrier</b>  | 113 | 18-Jan-24  | 07-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 107 | <b>Crown</b>  | 12  | 22-Jan-24  | 03-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 108 | <b>Westbound @ 7.5 R/day</b>                                  | 12  | 22-Jan-24  | 03-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 109 | EB Crown Fire Board transfer to WB                            | 12  | 22-Jan-24  | 03-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 110 | <b>Road Level</b>   | 113 | 18-Jan-24  | 07-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 111 | <b>Eastbound</b>  | 83  | 18-Jan-24  | 02-May-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 112 | <b>OHVD Soffit</b>  | 83  | 18-Jan-24  | 02-May-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 113 | Road level Fire Board installation CH6642 to CP21 1,458m @ 13 | 83  | 18-Jan-24* | 02-May-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 114 | <b>NCPS</b>   | 38  | 22-Jan-24  | 08-Mar-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 115 | Road level Fire Board installation CH6642 to CH8976 2,334m @  | 38  | 22-Jan-24* | 08-Mar-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 116 | <b>Westbound</b>  | 95  | 08-Feb-24  | 07-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 117 | <b>NCPS</b>   | 95  | 08-Feb-24  | 07-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 118 | WB NCP Fire Board @ 13.2m/d CH6703-7109 (406m) up to CP11     | 31  | 08-Feb-24  | 18-Mar-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 119 | WB NCP Fire Board @ 13.2m/d CH7109-7607 (498m) up to CP16     | 38  | 23-Apr-24  | 07-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 120 | <b>OHVD Slab</b>  | 12  | 31-Jan-24  | 16-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 121 | <b>Eastbound</b>  | 12  | 31-Jan-24  | 16-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 122 | ISIG Transfer to WB   | 12  | 31-Jan-24  | 16-Feb-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |
| 123 | <b>Parapet Installation</b>                                   | 131 | 04-Jan-24  | 15-Jun-24 |         |    |    |    |          |    |    |    |    |       |    |    |    |       |    |    |    |     |    |    |    |    |      |    |    |    |      |    |    |  |  |  |  |

- ◆ Milestone
- Planned Bar
- Critical Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron

Three Months Rolling Programme (Feb-24)



| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 31-Jan-24 | Rev. A   | SPa     |          |

| #   | Activity Name   | Dur | Start      | Finish    | 2024  |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
|-----|---|-----|------------|-----------|---|----------|-------|-------|-----|------|------|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|
|     |   |     |            |           | January   | February | March | April | May | June | July | 14 | 21 | 28 | 04 | 11 | 18 | 25 | 03 | 10 | 17 | 24 | 31 | 07 | 14 | 21 | 28 | 05 | 12 | 19 | 26 | 02 | 09 | 16 | 23 |
| 124 | <b>Eastbound</b>  | 139 | 07-Jan-24  | 26-May-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 125 | EB CH 8609-8738 - Parapet installation 129m                     | 92  | 07-Jan-24  | 07-Apr-24 | EB CH 8609-8738 - Parapet installation 129m                     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 126 | EB CH 8738-8832 - Parapet installation 94m                      | 47  | 08-Apr-24  | 26-May-24 | EB CH 8738-8832 - Parapet installation 94m                      |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 127 | <b>Westbound</b>  | 127 | 04-Jan-24  | 15-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 128 | <b>NCPS</b>   | 127 | 04-Jan-24  | 15-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 129 | Parapet installation - R0301-R074 (44 parapets) up to CP8       | 19  | 04-Jan-24  | 25-Jan-24 | Parapet installation - R0301-R074 (44 parapets) up to CP8       |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 130 | Parapet installation - R075-R0120 (46 parapets) up to CP9       | 19  | 18-Jan-24  | 08-Feb-24 | Parapet installation - R075-R0120 (46 parapets) up to CP9       |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 131 | Parapet installation - R021-R0164 (44 parapets) up to CP10      | 19  | 01-Feb-24  | 26-Feb-24 | Parapet installation - R021-R0164 (44 parapets) up to CP10      |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 132 | Parapet installation - R0165-R0209 (45 parapets) up to CP11     | 19  | 19-Feb-24  | 11-Mar-24 | Parapet installation - R0165-R0209 (45 parapets) up to CP11     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 133 | Parapet installation - R0210-R0255 (46 parapets) up to CP12     | 19  | 04-Mar-24  | 25-Mar-24 | Parapet installation - R0210-R0255 (46 parapets) up to CP12     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 134 | Parapet installation - R0711-R0756 (46 parapets) up to CP13     | 19  | 18-Mar-24  | 12-Apr-24 | Parapet installation - R0711-R0756 (46 parapets) up to CP13     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 135 | Parapet installation - R0026-R0300 (45 parapets) up to CP14     | 19  | 05-Apr-24  | 26-Apr-24 | Parapet installation - R0026-R0300 (45 parapets) up to CP14     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 136 | Parapet installation - R0301-R0346 (46 parapets) up to CP15     | 19  | 19-Apr-24  | 11-May-24 | Parapet installation - R0301-R0346 (46 parapets) up to CP15     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 137 | Parapet installation - R0347-R0392 (46 parapets) up to CP16     | 19  | 04-May-24  | 29-May-24 | Parapet installation - R0347-R0392 (46 parapets) up to CP16     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 138 | Parapet installation - R0393-R0437 (45 parapets) up to CP17     | 19  | 20-May-24  | 15-Jun-24 | Parapet installation - R0393-R0437 (45 parapets) up to CP17     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 139 | <b>CKL Pilot Tunnel</b>   | 96  | 15-Feb-24  | 13-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 140 | <b>Westbound</b>  | 96  | 15-Feb-24  | 13-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 141 | WB Pilot TBM bulkhead construction 1st bulkhead + water filling | 48  | 15-Feb-24* | 15-Apr-24 | WB Pilot TBM bulkhead construction 1st bulkhead + water filling |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 142 | WB Pilot TBM bulkhead construction 2nd bulkhead (alap)          | 48  | 16-Apr-24  | 13-Jun-24 | WB Pilot TBM bulkhead construction 2nd bulkhead (alap)          |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 143 | <b>CHA KWO LING TUNNEL</b>                                      | 133 | 11-Jan-24  | 25-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 144 | <b>Eastbound</b>  | 92  | 11-Jan-24  | 06-May-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 145 | <b>Type A2</b>  | 40  | 27-Jan-24  | 16-Mar-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 146 | EB D&Br Dismantling Cavern excv + overbreak                     | 40  | 27-Jan-24  | 16-Mar-24 | EB D&Br Dismantling Cavern excv + overbreak                     |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 147 | <b>Type A1</b>  | 92  | 11-Jan-24  | 06-May-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 148 | EB Type A1 Crown (10bays, 6d/bay)                               | 60  | 11-Jan-24  | 23-Mar-24 | EB Type A1 Crown (10bays, 6d/bay)                               |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 149 | EB Type A1 to C1-C2 fwks adjustment 1st stage                   | 16  | 25-Mar-24  | 16-Apr-24 | EB Type A1 to C1-C2 fwks adjustment 1st stage                   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 150 | EB Type A1 to C1-C2 fwks adjustment 2nd stage                   | 8   | 26-Apr-24  | 06-May-24 | EB Type A1 to C1-C2 fwks adjustment 2nd stage                   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 151 | <b>Type A</b>   | 24  | 16-Feb-24  | 14-Mar-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 152 | <b>OHVD</b>   | 24  | 16-Feb-24  | 14-Mar-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 153 | EB Type A OHVD Slab fwk dismantling                             | 24  | 16-Feb-24  | 14-Mar-24 | EB Type A OHVD Slab fwk dismantling                             |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 154 | <b>Type C</b>   | 8   | 17-Apr-24  | 25-Apr-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 155 | EB Type C1 Crown (1 bay 8d/bay)                                 | 8   | 17-Apr-24  | 25-Apr-24 | EB Type C1 Crown (1 bay 8d/bay)                                 |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 156 | <b>Westbound</b>  | 97  | 02-Feb-24  | 04-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 157 | <b>Type A2</b>  | 95  | 02-Feb-24  | 01-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 158 | WB Type A2 Crown (4 bays @ 4d/bay)                              | 16  | 02-Feb-24  | 23-Feb-24 | WB Type A2 Crown (4 bays @ 4d/bay)                              |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 159 | WB Type A2 Crown Fwks dismantling                               | 12  | 24-Feb-24  | 08-Mar-24 | WB Type A2 Crown Fwks dismantling                               |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 160 | WB 1st bulkhead   | 36  | 15-Feb-24* | 27-Mar-24 | WB 1st bulkhead   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 161 | WB 1st bulkhead water filling                                   | 12  | 28-Mar-24* | 15-Apr-24 | WB 1st bulkhead water filling                                   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 162 | WB 2nd bulkhead   | 36  | 16-Apr-24  | 01-Jun-24 | WB 2nd bulkhead   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 163 | <b>Type A1</b>  | 69  | 09-Mar-24  | 04-Jun-24 |   |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 164 | WB Type A1 OHVD Fwk assembly                                    | 24  | 09-Mar-24  | 10-Apr-24 | WB Type A1 OHVD Fwk assembly                                    |          |       |       |     |      |      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Bar


ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron

Three Months Rolling Programme (Feb-24)



| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 31-Jan-24 | Rev. A   | SPa     |          |




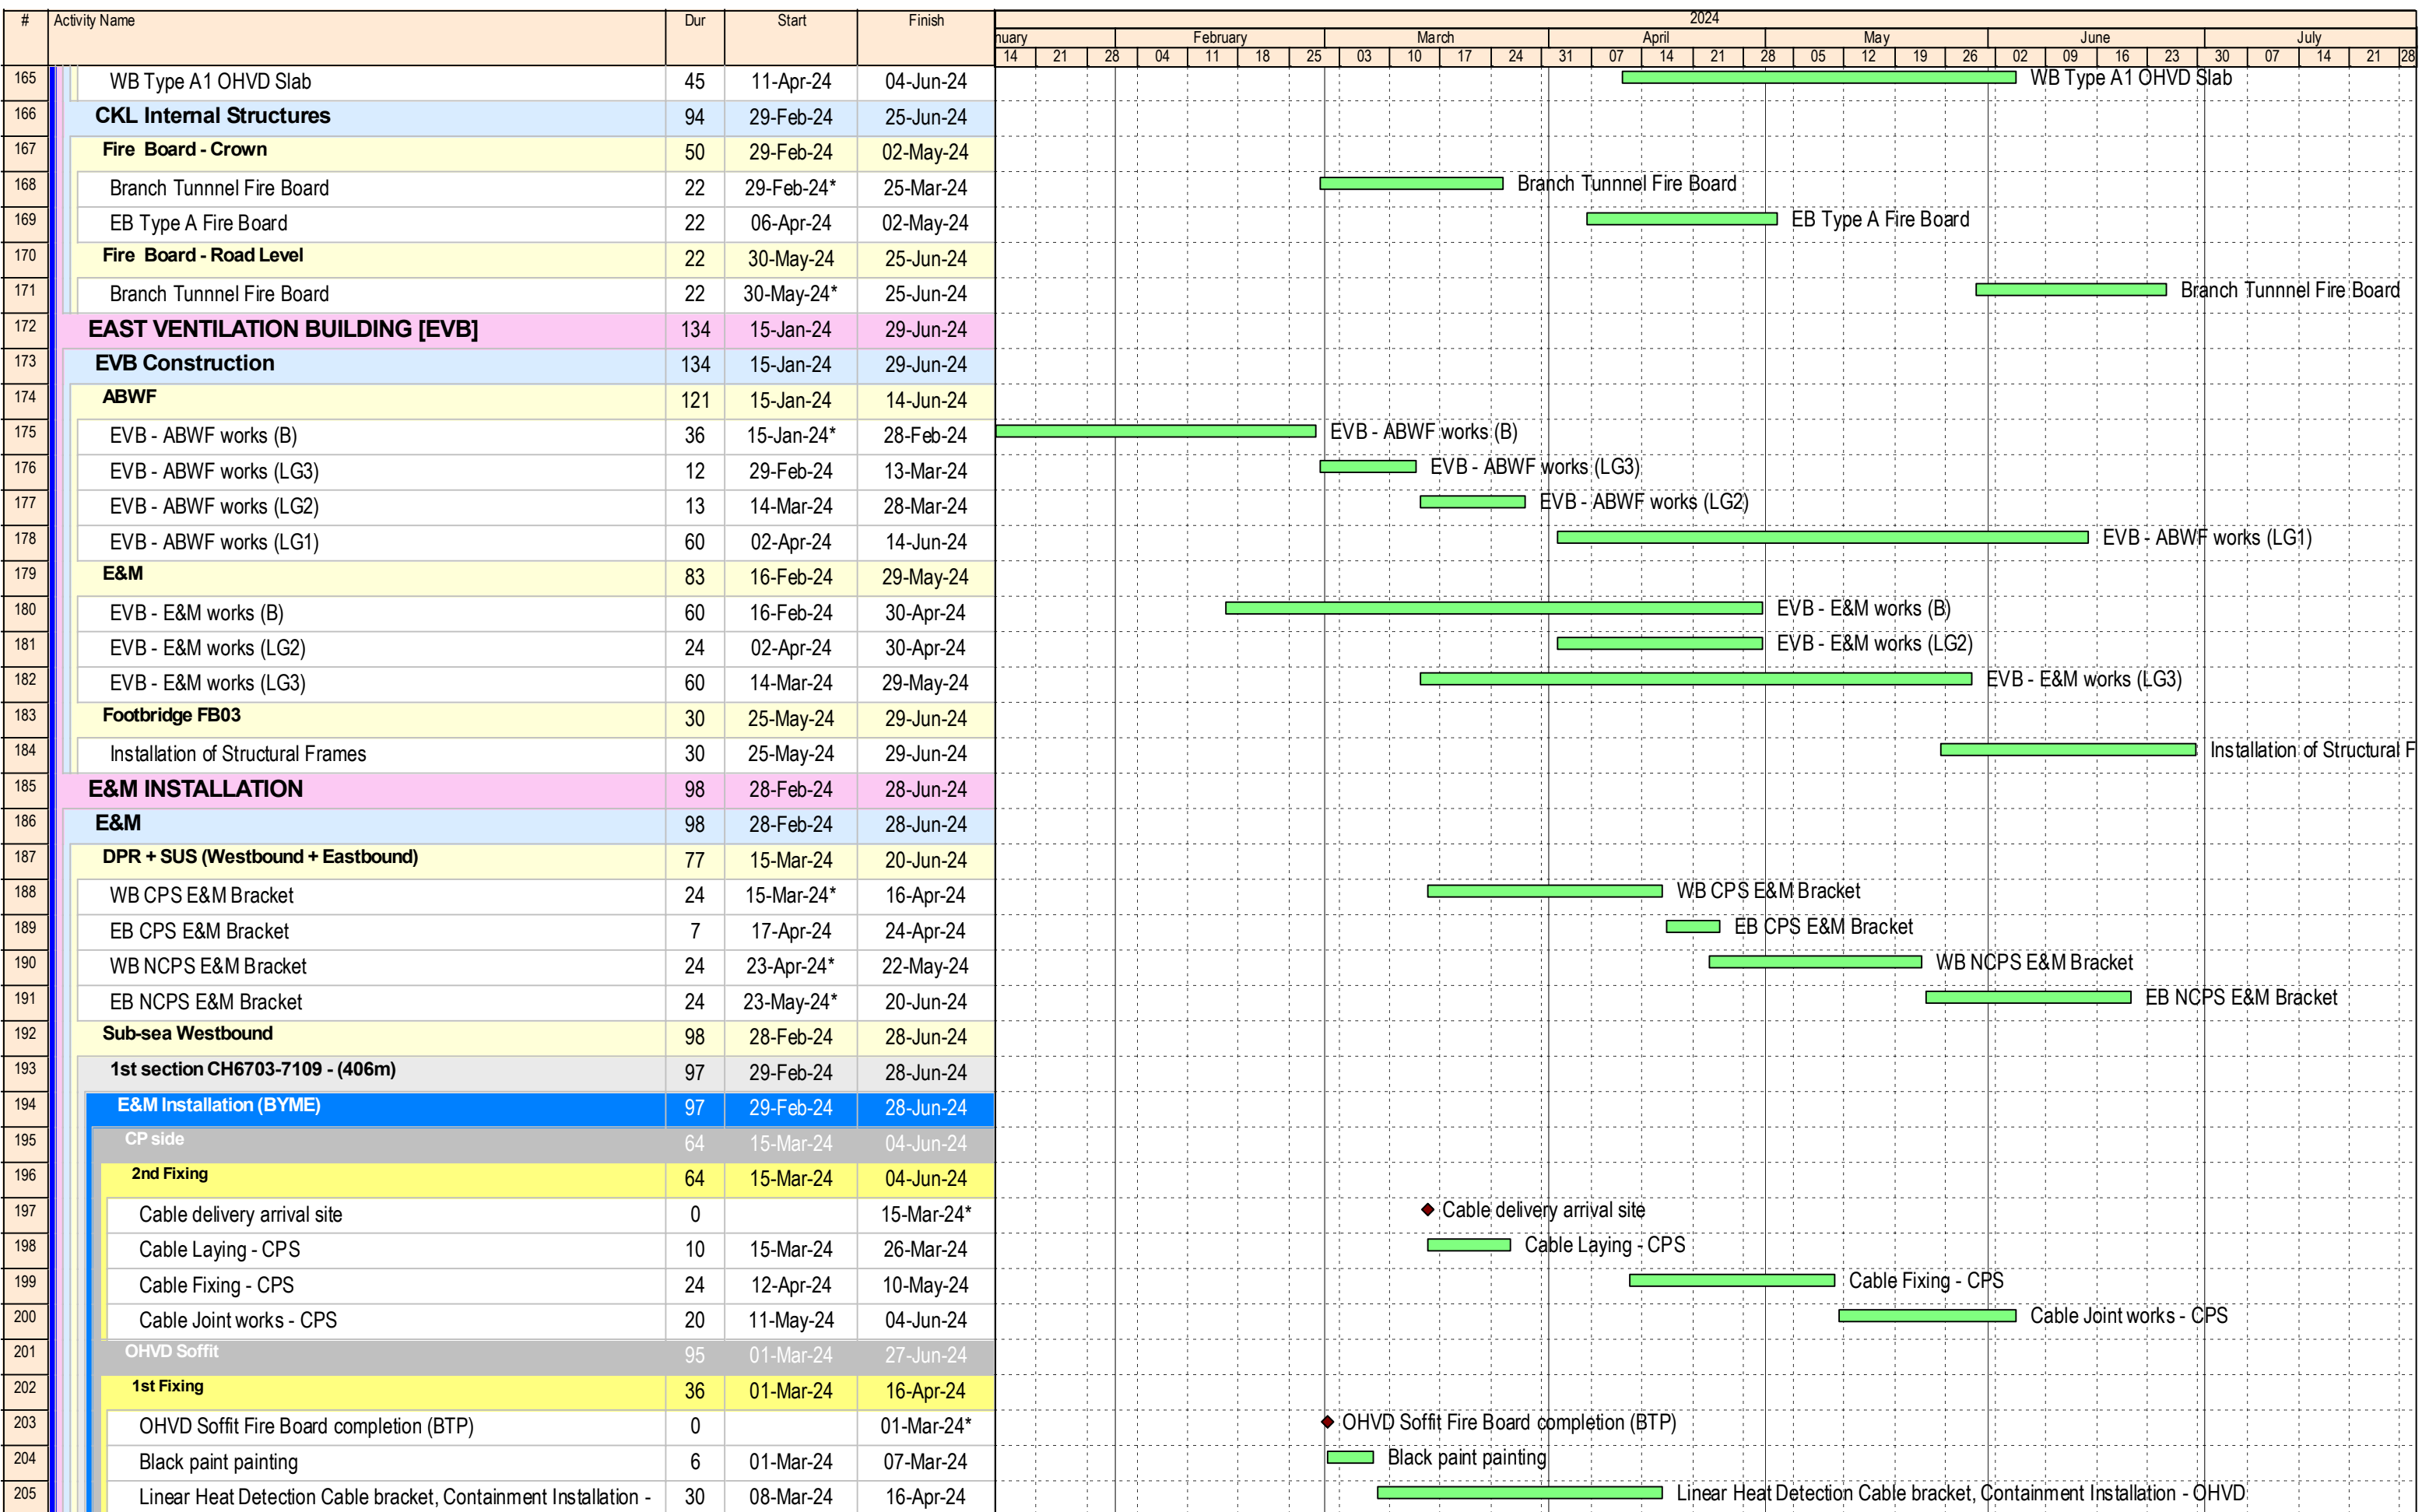

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron

Three Months Rolling Programme (Feb-24)




| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 31-Jan-24 | Rev. A   | SPa     |          |

| #   | Activity Name  | Dur | Start      | Finish     | 2024   |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
|-----|--|-----|------------|------------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|--------|
|     |  |     |            |            | Jan-14 | Jan-21 | Jan-28 | Feb-04 | Feb-11 | Feb-18 | Feb-25 | Mar-03 | Mar-10 | Mar-17 | Mar-24 | Mar-31 | Apr-07 | Apr-14 | Apr-21 | Apr-28 | May-05 | May-12 | May-19 | May-26 | Jun-02 | Jun-09 | Jun-16 | Jun-23 | Jun-30 | Jul-07 | Jul-14 | Jul-21 |
| 206 | <b>2nd Fixing</b>  | 39  | 11-May-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 207 | Tunnel Damper Wiring Works - OHVD                                    | 30  | 11-May-24  | 17-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 208 | Final Circuit Installation - OHVD                                    | 24  | 30-May-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 209 | Non CP side  | 97  | 29-Feb-24  | 28-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 210 | <b>1st Fixing</b>  | 24  | 12-Mar-24  | 13-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 211 | E&M Bracket  | 24  | 12-Mar-24  | 12-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 212 | NCPS Bracket completion  | 0   |            | 13-Apr-24* |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 213 | <b>2nd Fixing</b>  | 97  | 29-Feb-24  | 28-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 214 | High Voltage cable delivery arrival at site                          | 0   |            | 29-Feb-24* |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 215 | HV Cable Pulling - NCPS (Parapet location)                           | 30  | 29-Feb-24  | 08-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 216 | Cable Laying - NCPS  | 10  | 13-Apr-24  | 24-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 217 | Cable Fixing - NCPS  | 10  | 25-Apr-24  | 07-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 218 | Smartone / CSL / GOFs by others                                      | 24  | 08-May-24  | 05-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 219 | Cable Joint works - NCPS   | 20  | 05-Jun-24  | 28-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 220 | <b>2nd section CH7109-7607 - (498m)</b>                              | 98  | 28-Feb-24  | 28-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 221 | <b>E&amp;M Installation (BYME)</b>                                   | 97  | 28-Feb-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 222 | CP side  | 91  | 28-Feb-24  | 20-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 223 | <b>1st Fixing</b>  | 24  | 28-Feb-24  | 26-Mar-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 224 | E&M Bracket installation   | 24  | 28-Feb-24* | 26-Mar-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 225 | <b>2nd Fixing</b>  | 34  | 27-Mar-24  | 10-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 226 | Cable Laying - CPS   | 10  | 27-Mar-24  | 11-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 227 | Cable Fixing - CPS   | 24  | 12-Apr-24  | 10-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 228 | <b>Final Fixing</b>  | 10  | 08-Jun-24  | 20-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 229 | AQMS / CMCS Sensor Installation - CPS                                | 10  | 08-Jun-24  | 20-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 230 | OHVD Soffit  | 83  | 15-Mar-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 231 | <b>1st Fixing</b>  | 36  | 15-Mar-24  | 30-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 232 | OHVD Soffit Fire Board completion (BTP)                              | 0   |            | 15-Mar-24* |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 233 | Black paint painting   | 6   | 15-Mar-24  | 21-Mar-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 234 | Linear Heat Detection Cable bracket, Containment Installation - OHVD | 30  | 22-Mar-24  | 30-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 235 | <b>2nd Fixing</b>  | 39  | 11-May-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 236 | Tunnel Damper Wiring Works - OHVD                                    | 30  | 11-May-24  | 17-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 237 | Final Circuit Installation - OHVD                                    | 24  | 30-May-24  | 27-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 238 | Non CP side  | 77  | 29-Feb-24  | 04-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 239 | <b>1st Fixing</b>  | 24  | 12-Apr-24  | 11-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 240 | E&M Bracket  | 24  | 12-Apr-24  | 10-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 241 | NCPS Bracket completion  | 0   |            | 11-May-24* |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 242 | <b>2nd Fixing</b>  | 77  | 29-Feb-24  | 04-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 243 | NCPS Parapet completion  | 0   |            | 29-Feb-24* |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 244 | HV Cable Pulling - NCPS (Parapet location)                           | 30  | 29-Feb-24  | 08-Apr-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 245 | Cable Laying - NCPS  | 10  | 11-May-24  | 23-May-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |
| 246 | Cable Fixing - NCPS  | 10  | 24-May-24  | 04-Jun-24  |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |        |

- Milestone
- Planned Bar
- Critical Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works  
for Developments at South Apron

Three Months Rolling Programme (Feb-24)



|           |          |         |          |
|-----------|----------|---------|----------|
| Date      | Revision | Checked | Approved |
| 31-Jan-24 | Rev. A   | SPa     |          |










| Activity ID   | Activity Name                                       | Original Duration | Early Start | Early Finish | Late Start | Late Finish | 2023 |           |           |           |           |     |     |    |    |     |    |    | 2024 |    |    |     |    |     |     |    |    |     |    |    | 2025 |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|---|---|-------------------|-------------|--------------|------------|-------------|------|-----------|-----------|-----------|-----------|-----|-----|----|----|-----|----|----|------|----|----|-----|----|-----|-----|----|----|-----|----|----|------|----|----|-----|----|-----|-----|-----|----|-----|----|-----|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|   |   |                   |             |              |            |             | Jan  | F         | M         | Apr       | M         | Jun | Jul | A  | S  | Oct | N  | D  | Jan  | F  | M  | Apr | M  | Jun | Jul | A  | S  | Oct | N  | D  | Jan  | F  | M  | Apr | M  | Jun | Jul | Aug | S  | Oct | N  | Dec |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|   |   |                   |             |              |            |             | 13   | 14        | 15        | 16        | 17        | 18  | 19  | 20 | 21 | 22  | 23 | 24 | 25   | 26 | 27 | 28  | 29 | 30  | 31  | 32 | 33 | 34  | 35 | 36 | 37   | 38 | 39 | 40  | 41 | 42  | 43  | 44  | 45 | 46  | 47 | 48  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Trunk Road T2 - Traffic Control &amp; Surveillance System &amp; Associated Works</b> |   |                   |             |              |            |             | 665  | 17-Jul-23 | 29-Sep-25 | 23-May-24 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Site Installation and Testing &amp; Commissioning</b>                                |   |                   |             |              |            |             | 665  | 17-Jul-23 | 29-Sep-25 | 23-May-24 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation &amp; Testing Related to Stage 2 of Works</b>                           |   |                   |             |              |            |             | 493  | 21-Aug-23 | 11-Apr-25 | 28-Jun-24 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation</b>   |   |                   |             |              |            |             | 451  | 21-Aug-23 | 20-Feb-25 | 28-Jun-24 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Portion 4 - TKO-LTT (LT Interchange)</b>   |   |                   |             |              |            |             | 300  | 21-Aug-23 | 19-Aug-24 | 28-Jun-24 | 16-Jan-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1930  | Install Cable Containments                          | 48                | 21-Aug-23   | 17-Oct-23    | 28-Jun-24  | 23-Aug-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1960  | Install Equipment in Kiosk C                        | 12                | 25-Mar-24   | 08-Apr-24    | 06-Nov-24  | 19-Nov-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1940  | Install CCTV Camera                                 | 36                | 03-Apr-24   | 17-May-24    | 04-Dec-24  | 16-Jan-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1980  | Laying of Leaky Cable                               | 48                | 16-Apr-24   | 13-Jun-24    | 16-Oct-24  | 10-Dec-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1950  | Laying of Signal Cable - the 1st Section            | 48                | 25-Apr-24   | 22-Jun-24    | 23-Sep-24  | 19-Nov-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1990  | Laying of Signal Cable - the 3rd Section            | 50                | 21-Jun-24   | 19-Aug-24    | 18-Nov-24  | 16-Jan-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1970  | Laying of Signal Cable - the 2nd Section            | 48                | 24-Jun-24   | 19-Aug-24    | 20-Nov-24  | 16-Jan-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Portion 1 - South Apron Up to SUS</b>  |   |                   |             |              |            |             | 217  | 01-Dec-23 | 21-Aug-24 | 03-Jul-24 | 17-Feb-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2000  | Install Cable Containments - the 1st Section        | 48                | 01-Dec-23   | 27-Jan-24    | 03-Jul-24  | 27-Aug-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2050  | Install Cable Containments - the 2nd Section        | 24                | 29-Jan-24   | 28-Feb-24    | 07-Oct-24  | 04-Nov-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2060  | Laying of Leaky Cable                               | 48                | 27-Feb-24   | 23-Apr-24    | 02-Nov-24  | 28-Dec-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2010  | Install CCTV Camera                                 | 24                | 03-Apr-24   | 02-May-24    | 21-Aug-24  | 17-Sep-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2020  | Signal Cable Laying - the 1st Section               | 48                | 27-Apr-24   | 25-Jun-24    | 04-Sep-24  | 01-Nov-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2030  | Install Equipment in Kiosk F                        | 12                | 13-May-24   | 27-May-24    | 04-Feb-25  | 17-Feb-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2040  | Install Radio Antenna                               | 10                | 13-May-24   | 24-May-24    | 06-Jan-25  | 16-Jan-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2070  | Signal Cable Laying - the 2nd Section               | 48                | 26-Jun-24   | 21-Aug-24    | 02-Nov-24  | 28-Dec-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Portion 2 - Tunnel Section, Service Gallery, WVB &amp; EVB</b>                       |   |                   |             |              |            |             | 287  | 08-Mar-24 | 20-Feb-25 | 09-Sep-24 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2080  | Install Cable Containments                          | 229               | 08-Mar-24   | 09-Dec-24    | 09-Sep-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2090  | Install CCTV Camera                                 | 224               | 13-Apr-24   | 09-Jan-25    | 17-Oct-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2100  | Install ET  | 224               | 20-Apr-24   | 16-Jan-25    | 28-Dec-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2110  | Install Radio System in Service Gallery             | 218               | 06-May-24   | 23-Jan-25    | 24-Oct-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2120  | Signal Cable Laying                                 | 188               | 08-Jul-24   | 20-Feb-25    | 13-Nov-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2130  | Laying of Leaky Cable                               | 58                | 10-Dec-24   | 20-Feb-25    | 16-Dec-24  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Portion 3 - CKL Branch Tunnel in TKO-LTT Site</b>                                    |   |                   |             |              |            |             | 80   | 08-Mar-24 | 13-Jun-24 | 28-Jan-25 | 22-Apr-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2230  | Install Cable Containments                          | 36                | 08-Mar-24   | 19-Apr-24    | 07-Feb-25  | 20-Mar-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2220  | Install CCTV Camera                                 | 29                | 03-Apr-24   | 08-May-24    | 28-Jan-25  | 05-Mar-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2250  | Signal Cable Laying                                 | 36                | 20-Apr-24   | 03-Jun-24    | 11-Mar-25  | 22-Apr-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2240  | Laying of Leaky Cable                               | 36                | 30-Apr-24   | 13-Jun-24    | 14-Feb-25  | 27-Mar-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Underpass S21</b>  |   |                   |             |              |            |             | 30   | 05-Apr-24 | 10-May-24 | 26-Apr-25 | 03-Jun-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2260  | Install Cable Containment                           | 14                | 05-Apr-24   | 20-Apr-24    | 26-Apr-25  | 14-May-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2280  | Laying of Leaky Cable                               | 30                | 05-Apr-24   | 10-May-24    | 26-Apr-25  | 03-Jun-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2290  | Laying of Power Cable From TCCS Cabinet in T2 Area  | 14                | 13-Apr-24   | 29-Apr-24    | 17-May-25  | 03-Jun-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2270  | Install YAGI Antenna                                | 7                 | 22-Apr-24   | 29-Apr-24    | 26-May-25  | 03-Jun-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Testing</b>  |   |                   |             |              |            |             | 265  | 25-May-24 | 11-Apr-25 | 06-Jan-25 | 31-Oct-26 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| TC1590  | Testing of FS-related TCCS Equipment                | 265               | 25-May-24   | 11-Apr-25    | 06-Jan-25  | 31-Oct-26   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| TC1610  | Issue Notice of Stage 2 Completion to the Engineer  | 0                 |             | 11-Apr-25    |            | 19-Jun-25   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Portion 4 - TKO-LTT (LT Interchange)</b>   |   |                   |             |              |            |             | 443  | 17-Jul-23 | 03-Jan-25 | 23-May-24 | 19-Jun-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1020  | Inspect Civil Provisions & Submit Inspection Report | 12                | 17-Jul-23   | 29-Jul-23    | 23-May-24  | 05-Jun-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1030  | Rectify Civil Provision Defects by Others           | 18                | 31-Jul-23   | 19-Aug-23    | 06-Jun-24  | 27-Jun-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation Works</b>   |   |                   |             |              |            |             | 300  | 21-Aug-23 | 19-Aug-24 | 28-Jun-24 | 16-Jan-25 |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1040  | Install Cable Containments                          | 48                | 21-Aug-23   | 17-Oct-23    | 28-Jun-24  | 23-Aug-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1050  | Install Equipment Racks                             | 24                | 21-Aug-23   | 16-Sep-23    | 07-Sep-24  | 07-Oct-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1110  | Install Traffic Control Devices                     | 48                | 19-Feb-24   | 15-Apr-24    | 17-Aug-24  | 15-Oct-24   |      |           |           |           |           |     |     |    |    |     |    |    |      |    |    |     |    |     |     |    |    |     |    |    |      |    |    |     |    |     |     |     |    |     |    |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

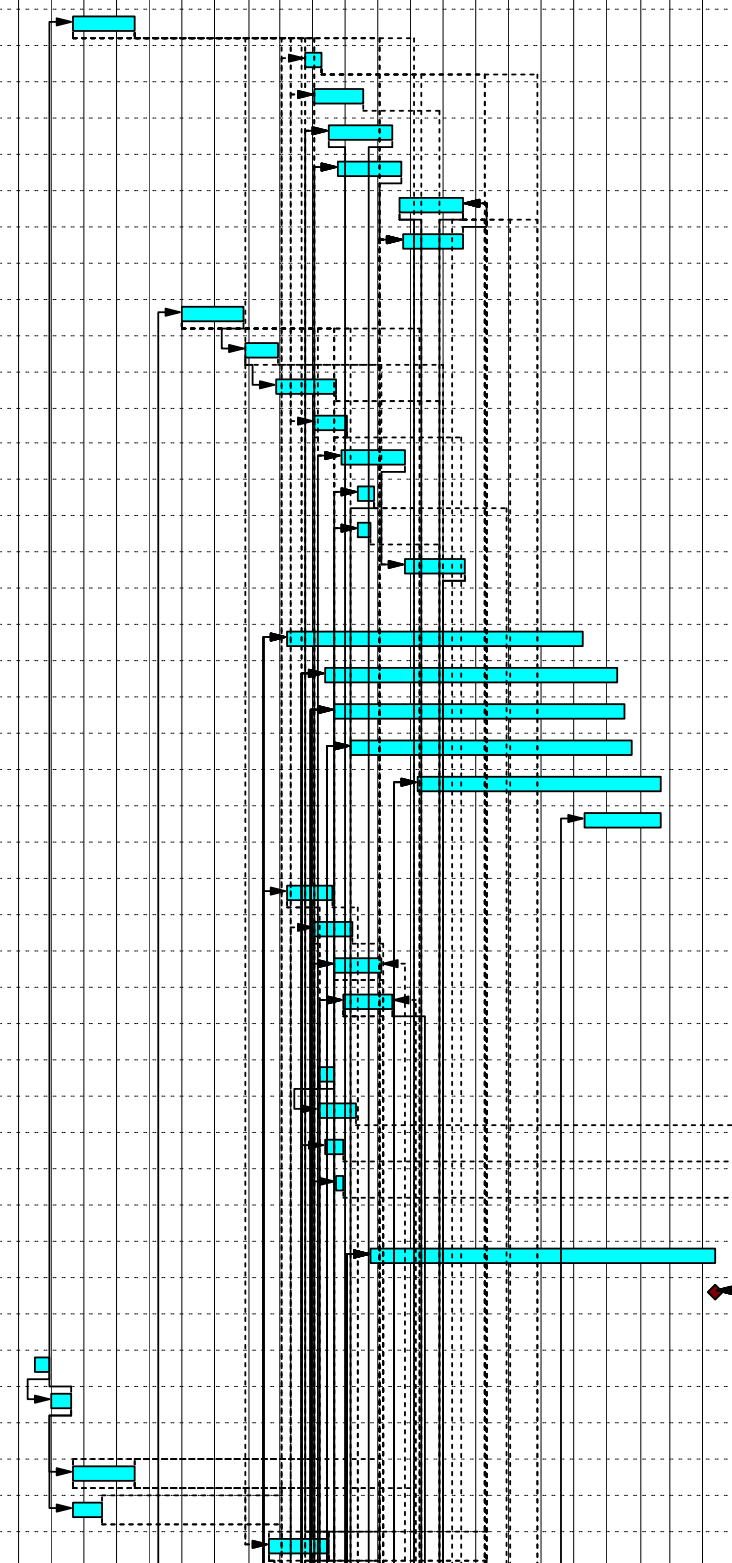

| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 18-Apr-23 | Rev. D   | FC      |          |
| 10-May-23 | Rev. E   | FC      |          |
| 07-Jul-23 | Rev. F   | MY      |          |









| Activity ID                                  | Activity Name  | Original Duration | Early Start | Early Finish | Late Start | Late Finish | 2023       |   |   |     |   |     |     |   |   |     |   |   | 2024 |   |   |     |   |     |     |   |   |     |   |   | 2025 |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
|--|--|-------------------|-------------|--------------|------------|-------------|------------|---|---|-----|---|-----|-----|---|---|-----|---|---|------|---|---|-----|---|-----|-----|---|---|-----|---|---|------|---|---|-----|---|-----|-----|---|---|-----|---|---|--|--|--|--|--|--|--|--|--|--|--|--|
|  |  |                   |             |              |            |             | Jan        | F | M | Apr | M | Jun | Jul | A | S | Oct | N | D | Jan  | F | M | Apr | M | Jun | Jul | A | S | Oct | N | D | Jan  | F | M | Apr | M | Jun | Jul | A | S | Oct | N | D |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation Works</b>                    |  |                   |             |              |            |             | <b>54</b>  |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2510                                       | Install Cable Containment                                  | 24                | 07-Jun-24   | 10-Aug-24    | 25-Oct-24  | 17-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2520                                       | Install VLSL   | 18                | 22-Jun-24   | 13-Jul-24    | 28-Nov-24  | 18-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2530                                       | Install PA in Service Gallery                              | 24                | 22-Jun-24   | 20-Jul-24    | 15-Nov-24  | 12-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2540                                       | Install Traffic Control Devices                            | 24                | 29-Jun-24   | 27-Jul-24    | 29-Nov-24  | 27-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2550                                       | Install CCTV Camera  | 18                | 08-Jul-24   | 27-Jul-24    | 12-Dec-24  | 03-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2560                                       | Install PABX in Service Gallery                            | 24                | 08-Jul-24   | 03-Aug-24    | 29-Nov-24  | 27-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2570                                       | Install Radio System in Service Gallery                    | 24                | 15-Jul-24   | 10-Aug-24    | 06-Dec-24  | 04-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2580                                       | Install Detection Camera                                   | 18                | 22-Jul-24   | 10-Aug-24    | 27-Dec-24  | 17-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2590                                       | Install ET   | 12                | 29-Jul-24   | 10-Aug-24    | 28-Dec-24  | 11-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Tunnel Section - CH 8+100 to CH 8+750</b> |  |                   |             |              |            |             | <b>78</b>  |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2920                                       | Inspect Civil Provisions & Submit Inspection Report        | 3                 | 13-Aug-24   | 15-Aug-24    | 04-Oct-24  | 07-Oct-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2930                                       | Rectify Civil Provision Defects by Others                  | 6                 | 16-Aug-24   | 22-Aug-24    | 08-Oct-24  | 15-Oct-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation Works</b>                    |  |                   |             |              |            |             | <b>69</b>  |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2600                                       | Install Cable Containment                                  | 24                | 23-Aug-24   | 20-Sep-24    | 16-Oct-24  | 12-Nov-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2610                                       | Install VLSL   | 18                | 06-Sep-24   | 27-Sep-24    | 28-Nov-24  | 18-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2620                                       | Install PA in Service Gallery                              | 24                | 06-Sep-24   | 05-Oct-24    | 15-Nov-24  | 12-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2630                                       | Install Traffic Control Devices                            | 24                | 13-Sep-24   | 14-Oct-24    | 29-Nov-24  | 27-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2640                                       | Install CCTV Camera  | 18                | 21-Sep-24   | 14-Oct-24    | 12-Dec-24  | 03-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2650                                       | Install PABX in Service Gallery                            | 24                | 21-Sep-24   | 21-Oct-24    | 29-Nov-24  | 27-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2700                                       | Install GOFS (CH 7+600 to CH 8+750)                        | 45                | 21-Sep-24   | 14-Nov-24    | 06-Mar-25  | 28-Apr-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2710                                       | Signal Cable Laying and Termination (CH 7+600 to CH 8+750) | 45                | 21-Sep-24   | 14-Nov-24    | 13-Nov-24  | 06-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2660                                       | Install Radio System in Service Gallery                    | 24                | 28-Sep-24   | 28-Oct-24    | 06-Dec-24  | 04-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2670                                       | Install Detection Camera                                   | 18                | 07-Oct-24   | 28-Oct-24    | 27-Dec-24  | 17-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2680                                       | Install ET   | 12                | 15-Oct-24   | 28-Oct-24    | 28-Dec-24  | 11-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2690                                       | Install SEC Camera   | 18                | 22-Oct-24   | 11-Nov-24    | 03-Mar-25  | 22-Mar-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Tunnel Section - CH 8+750 to CH 9+250</b> |  |                   |             |              |            |             | <b>86</b>  |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2940                                       | Inspect Civil Provisions & Submit Inspection Report        | 1                 | 07-Nov-24   | 07-Nov-24    | 07-Nov-24  | 07-Nov-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2950                                       | Rectify Civil Provision Defects by Others                  | 4                 | 08-Nov-24   | 12-Nov-24    | 08-Nov-24  | 12-Nov-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation Works</b>                    |  |                   |             |              |            |             | <b>81</b>  |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2720                                       | Install Cable Containment                                  | 23                | 13-Nov-24   | 09-Dec-24    | 13-Nov-24  | 09-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2730                                       | Install VLSL   | 13                | 10-Dec-24   | 24-Dec-24    | 02-Jan-25  | 16-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2740                                       | Install PA in Service Gallery                              | 19                | 10-Dec-24   | 02-Jan-25    | 04-Jan-25  | 25-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2750                                       | Install Traffic Control Devices                            | 19                | 10-Dec-24   | 02-Jan-25    | 11-Jan-25  | 05-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2780                                       | Install GOFS (CH 7+600 to CH 8+750)                        | 58                | 10-Dec-24   | 20-Feb-25    | 19-Feb-25  | 28-Apr-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2790                                       | Signal Cable Laying and Termination (CH 7+600 to CH 8+750) | 58                | 10-Dec-24   | 20-Feb-25    | 10-Dec-24  | 20-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2850                                       | Laying of Leaky Cable                                      | 58                | 10-Dec-24   | 20-Feb-25    | 16-Dec-24  | 26-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2760                                       | Install CCTV Camera  | 18                | 18-Dec-24   | 09-Jan-25    | 10-Jan-25  | 03-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2770                                       | Install PABX in Service Gallery                            | 22                | 20-Dec-24   | 16-Jan-25    | 15-Jan-25  | 12-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2800                                       | Install Radio System in Service Gallery                    | 22                | 28-Dec-24   | 23-Jan-25    | 22-Jan-25  | 19-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2810                                       | Install Detection Camera                                   | 18                | 03-Jan-25   | 23-Jan-25    | 12-Feb-25  | 04-Mar-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2820                                       | Install ET   | 12                | 03-Jan-25   | 16-Jan-25    | 06-Feb-25  | 19-Feb-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2830                                       | Install SEC Camera   | 18                | 10-Jan-25   | 03-Feb-25    | 15-Apr-25  | 07-May-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW2840                                       | Install PVMS   | 12                | 17-Jan-25   | 03-Feb-25    | 22-Apr-25  | 07-May-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>West Ventilation Building</b>             |  |                   |             |              |            |             | <b>279</b> |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1360                                       | Inspect Civil Provisions & Submit Inspection Report        | 12                | 04-Sep-23   | 16-Sep-23    | 07-Sep-24  | 21-Sep-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1370                                       | Rectify Civil Provision Defects by Others                  | 18                | 18-Sep-23   | 10-Oct-23    | 23-Sep-24  | 15-Oct-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| <b>Installation Works</b>                    |  |                   |             |              |            |             | <b>249</b> |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1650                                       | Install Cable Containments                                 | 24                | 11-Oct-23   | 08-Nov-23    | 16-Oct-24  | 12-Nov-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1660                                       | Position Equipment Rack                                    | 12                | 09-Nov-23   | 22-Nov-23    | 23-Nov-24  | 06-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1690                                       | Install PABX Equipment                                     | 20                | 10-Nov-23   | 02-Dec-23    | 06-Nov-24  | 28-Nov-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1670                                       | Install Network Equipment                                  | 36                | 25-Mar-24   | 07-May-24    | 07-Dec-24  | 20-Jan-25   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |
| SW1710                                       | Install Radio Equipment                                    | 12                | 13-Apr-24   | 26-Apr-24    | 29-Nov-24  | 12-Dec-24   |            |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |      |   |   |     |   |     |     |   |   |     |   |   |  |  |  |  |  |  |  |  |  |  |  |  |



■ Planned Activities
 ■ Actual Work
 ■ Critical Activity
 ◆ Milestone

| Date      | Revision | Checked | Approved |
|-----------|----------|---------|----------|
| 18-Apr-23 | Rev. D   | FC      |          |
| 10-May-23 | Rev. E   | FC      |          |
| 07-Jul-23 | Rev. F   | MY      |          |





