

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																																	
								January				February				March				April				May				June				July									
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25				
WORKS PROGRAMME (01V3)								672	02-Mar-20	11-Jun-22	321	22-Sep-20 A	23-Oct-21																												
DESIGN SUBMISSION & APPROVAL								672	02-Mar-20	11-Jun-22	293	22-Sep-20 A	17-Sep-21																												
GENERAL								340	02-Mar-20	27-Apr-21	261	22-Sep-20 A	11-Aug-21	GENERAL																											
Design Memorandum								0	02-Mar-20	02-Mar-20	102	08-Jan-21 A	15-May-21																												
A229426091	Design Memorandum - 3th Review	0			5	08-Jan-21 A	13-Jan-21 A	Design Memorandum - 3th Review																																	
A229428882	Design Memorandum - 4th Sub	0			5	14-Jan-21 A	19-Jan-21 A	Design Memorandum - 4th Sub																																	
A229428892	Design Memorandum - 4th Review	0			23	20-Jan-21 A	18-Feb-21 A	Design Memorandum - 4th Review																																	
A229429360	Design Memorandum - 5th Sub	0			29	19-Feb-21 A	24-Mar-21 A	Design Memorandum - 5th Sub																																	
A229429370	Design Memorandum - 5th Review	0			19	25-Mar-21 A	20-Apr-21 A	Design Memorandum - 5th Review																																	
A229431000	Design Memorandum - 5th Sub	0			21	21-Apr-21 A	15-May-21	Design Memorandum - 5th Sub																																	
A22690	Design Memorandum - Approval	0		02-Mar-20	0		15-May-21	Design Memorandum - Approval																																	
Construction Traffic Impact Assessment - Kai Tak Area								0	10-Jun-20	10-Jun-20	115	12-Dec-20 A	07-May-21																												
A229426161	CTIA Kai Tak Area - Resubmission	0			33	12-Dec-20 A	22-Jan-21 A	CTIA Kai Tak Area - Resubmission																																	
A229426171	CTIA Kai Tak Area - 4th Sub	0			0		22-Jan-21 A	CTIA Kai Tak Area - 4th Sub																																	
A229426181	CTIA Kai Tak Area - 4th Review	0			20	23-Jan-21 A	11-Feb-21 A	CTIA Kai Tak Area - 4th Review																																	
A229429380	CTIA Kai Tak Area - Resubmission	0			32	12-Feb-21 A	24-Mar-21 A	CTIA Kai Tak Area - Resubmission																																	
A229429390	CTIA Kai Tak Area - 5th Sub	0			0		24-Mar-21 A	CTIA Kai Tak Area - 5th Sub																																	
A229429400	CTIA Kai Tak Area - 5th Review	0			44	25-Mar-21 A	07-May-21	CTIA Kai Tak Area - 5th Review																																	
A22720	CTIA Kai Tak Area - Approval	0		10-Jun-20	0		07-May-21	CTIA Kai Tak Area - Approval																																	
Durability Assessment Report								0	07-May-20	07-May-20	94	19-Jan-21 A	18-May-21																												
A229426141	Durability Assessment Report - 5th Sub	0			0		19-Jan-21 A	Durability Assessment Report - 5th Sub																																	
A229426151	Durability Assessment Report - 5th Review	0			29	20-Jan-21 A	25-Feb-21 A	Durability Assessment Report - 5th Review																																	
A229431010	Durability Assessment Report - Resubmission	0			30	26-Feb-21 A	01-Apr-21 A	Durability Assessment Report - Resubmission																																	
A229431020	Durability Assessment Report - 5th Sub	0			0		01-Apr-21 A	Durability Assessment Report - 5th Sub																																	
A229431030	Durability Assessment Report - 5th Review	0			35	02-Apr-21 A	18-May-21	Durability Assessment Report - 5th Review																																	
A22730	Durability Assessment Report - Approval	0		07-May-20	0		18-May-21	Durability Assessment Report - Approval																																	
ACABAS - Western Tunnel Portal and Concrete Finishes for Retaining Struc								50	10-Aug-20	08-Oct-20	113	16-Dec-20 A	08-May-21	structure																											
B18010	DDA - Further information required by SO	22	10-Aug-20	03-Sep-20	56	16-Dec-20 A	25-Feb-21 A	DDA - Further information required by SO																																	
B18020	DDA - 2nd Sub	0		03-Sep-20	0		25-Feb-21 A	DDA - 2nd Sub																																	
B18030	DDA - 2nd Review by SO	35	04-Sep-20	08-Oct-20	72	26-Feb-21 A	08-May-21	DDA - 2nd Review by SO																																	
B18040	DDA - SO Consent for Construction	0		08-Oct-20	0		08-May-21	DDA - SO Consent for Construction																																	
ACABAS- Footbridge FB-02								78	09-Oct-20	12-Jan-21	78	10-May-21	11-Aug-21	ACABAS- Footbridge FB-02																											
B266491	DDA - Draft - Preparation by Designer	48	09-Oct-20	04-Dec-20	48	10-May-21	07-Jul-21	DDA - Draft - Prep																																	
B266421	DDA - Draft - Final Review and prepare for 1st Sub	30	05-Dec-20	12-Jan-21	30	08-Jul-21	11-Aug-21	DDA - Draft - Prep																																	
CLP Substation - Building Services and Underground Utilities Design								0	01-Jun-20	01-Jun-20	143	11-Nov-20 A	08-May-21																												
B2595251	DDA - 4th Review by SO	0			143	11-Nov-20 A	08-May-21	DDA - 4th Review by SO																																	
B266841	DDA - SO Consent for Construction	0		01-Jun-20	0		08-May-21	DDA - SO Consent for Construction																																	
CLP Substation - ABWF								30	16-May-20	19-Jun-20	182	22-Sep-20 A	07-May-21																												
B266911	DDA - 2nd Review by SO	35	16-May-20	19-Jun-20	228	22-Sep-20 A	07-May-21	DDA - 2nd Review by SO																																	
B266931	DDA - SO Consent for Construction	0		19-Jun-20	0		07-May-21	DDA - SO Consent for Construction																																	
DDA Project Alignment								0	20-May-20	20-May-20	71	11-Dec-20 A	11-Mar-21 A																												
B2596021	DDA - 3rd Sub	0			0		11-Dec-20 A	DDA - 3rd Review by SO																																	
B2596031	DDA - 3rd Review by SO	0			35	12-Dec-20 A	15-Jan-21 A	DDA - 3rd Review by SO																																	
B2596611	DDA - Further information required by SO	0			11	16-Jan-21 A	28-Jan-21 A	DDA - Further information required by SO																																	
B2596621	DDA - 4th Sub	0			0		28-Jan-21 A	DDA - 4th Sub																																	
B2596631	DDA - 4th Review by SO	0			42	29-Jan-21 A	11-Mar-21 A	DDA - 4th Review by SO																																	
B11680	DDA - SO Consent for Construction	0		20-May-20	0		11-Mar-21 A	DDA - SO Consent for Construction																																	
AIP Roadworks and Street Furniture								42	01-Oct-20	21-Nov-20	117	10-Dec-20 A	07-May-21	ure																											
B267091	AIP - Further information required by SO	24	01-Oct-20	24-Oct-20	45	10-Dec-20 A	23-Jan-21 A	AIP - Further information required by SO																																	

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																													
								January				February				March				April				May				June				July					
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25
B267111	AIP - 2nd Sub	0		24-Oct-20	0		23-Jan-21 A	◆ AIP - 2nd Sub																													
B267101	AIP - 2nd Review by SO	28	25-Oct-20	21-Nov-20	30	25-Jan-21 A	23-Feb-21 A	■ AIP - 2nd Review by SO																													
B2597061	AIP - Further information required by SO	0			34	24-Feb-21 A	29-Mar-21 A	■ AIP - Further information required by SO																													
B2597071	AIP - 3rd Sub	0			0		29-Mar-21 A	◆ AIP - 3rd Sub																													
B2597081	AIP - 3rd Review by SO	0			37	01-Apr-21 A	07-May-21	■ AIP - 3rd Review by SO																													
B267121	AIP - SO Consent for DDA Submission	0		21-Nov-20	0		07-May-21	◆ AIP - SO Consent for DDA Submission																													
DDA Roadworks and Street Furniture		75	23-Nov-20	24-Feb-21	78	08-May-21	10-Aug-21	■ DDA Roadworks and Street Furniture																													
B11690	DDA - Draft - Preparation by Designer	36	23-Nov-20	06-Jan-21	36	08-May-21	21-Jun-21	■ DDA - Draft - Preparation by Designer																													
B11700	DDA - Draft - Final Review and prepare for 1st Sub	18	07-Jan-21	27-Jan-21	18	22-Jun-21	13-Jul-21	■ DDA - Draft - Final Review and prepare for 1st Sub																													
B11710	DDA - 1st Sub	0		27-Jan-21	0		13-Jul-21	◆ DDA - 1st Sub																													
B11730	DDA - Review by SO	28	28-Jan-21	24-Feb-21	28	14-Jul-21	10-Aug-21	■ DDA - Review by SO																													
B11720	DDA - Review by IP / DC	28	28-Jan-21	24-Feb-21	28	14-Jul-21	10-Aug-21	■ DDA - Review by IP / DC																													
AIP Traffic Sign, Road Marking & Sign Gantry		0	21-Apr-21	21-Apr-21	53	01-Dec-20 A	03-Feb-21 A	◆ AIP Traffic Sign, Road Marking & Sign Gantry																													
B2596251	AIP - Further information required by SO	0			18	01-Dec-20 A	21-Dec-20 A	■ AIP - Further information required by SO																													
B2596271	AIP - 2nd Sub	0			0		21-Dec-20 A	◆ AIP - 2nd Sub																													
B2596261	AIP - 2nd Review by SO	0			44	22-Dec-20 A	03-Feb-21 A	■ AIP - 2nd Review by SO																													
B267201	AIP - SO Consent for DDA Submission	0		21-Apr-21	0		03-Feb-21 A	◆ AIP - SO Consent for DDA Submission																													
DDA Street Lighting (AGR/ DPR/ S20/ L10/ L18)		26	23-Mar-21	27-Apr-21	114	20-Jan-21 A	12-Jun-21	■ DDA Street Lighting (AGR/ DPR/ S20/ L10/ L18)																													
B267641	DDA - 2nd Sub	0		23-Mar-21	0		20-Jan-21 A	◆ DDA - 2nd Sub																													
B267631	DDA - 2nd Review by SO	35	24-Mar-21	27-Apr-21	19	21-Jan-21 A	08-Feb-21 A	■ DDA - 2nd Review by SO																													
B2596791	DDA - Further information required by SO	0			26	09-Feb-21 A	13-Mar-21 A	■ DDA - Further information required by SO																													
B2596811	DDA - 3rd Sub	0			0		13-Mar-21 A	◆ DDA - 3rd Sub																													
B2596801	DDA - 3rd Review by SO	0			32	15-Mar-21 A	15-Apr-21 A	■ DDA - 3rd Review by SO																													
B2597541	DDA - Further information required by SO	0			19	16-Apr-21 A	08-May-21	■ DDA - Further information required by SO																													
B2597561	DDA - 3rd Sub	0			0		08-May-21	◆ DDA - 3rd Sub																													
B2597551	DDA - 3rd Review by SO	0			35	09-May-21	12-Jun-21	■ DDA - 3rd Review by SO																													
B267651	DDA - SO Consent for DDA Submission	0		27-Apr-21	0		12-Jun-21	◆ DDA - SO Consent for DDA Submission																													
AIP Structural Health Monitoring System (SHMS)		59	13-Oct-20	22-Dec-20	48	21-Jan-21 A	22-Mar-21 A	◆ AIP Structural Health Monitoring System (SHMS)																													
B267431	AIP - 1st Sub	0		13-Oct-20	0		21-Jan-21 A	◆ AIP - 1st Sub																													
B267421	AIP - Review by SO	28	14-Oct-20	10-Nov-20	15	22-Jan-21 A	05-Feb-21 A	■ AIP - Review by SO																													
B267491	AIP - Review by IP / DC	28	14-Oct-20	10-Nov-20	19	22-Jan-21 A	09-Feb-21 A	■ AIP - Review by IP / DC																													
B267441	AIP - Further information required by SO	12	11-Nov-20	24-Nov-20	25	06-Feb-21 A	10-Mar-21 A	■ AIP - Further information required by SO																													
B267461	AIP - 2nd Sub	0		24-Nov-20	0		10-Mar-21 A	◆ AIP - 2nd Sub																													
B267451	AIP - 2nd Review by SO	28	25-Nov-20	22-Dec-20	12	11-Mar-21 A	22-Mar-21 A	■ AIP - 2nd Review by SO																													
B267471	AIP - SO Consent for DDA Submission	0		22-Dec-20	0		22-Mar-21 A	◆ AIP - SO Consent for DDA Submission																													
DDA Structural Health Monitoring System (SHMS)		80	23-Dec-20	06-Apr-21	105	23-Mar-21 A	31-Jul-21	■ DDA Structural Health Monitoring System (SHMS)																													
B18150	DDA - Draft - Preparation by Designer	36	23-Dec-20	05-Feb-21	57	23-Mar-21 A	03-Jun-21	■ DDA - Draft - Preparation by Designer																													
B18160	DDA - Draft - Final Review and prepare for 1st Sub	24	06-Feb-21	09-Mar-21	24	04-Jun-21	03-Jul-21	■ DDA - Draft - Final Review and prepare for 1st Sub																													
B18170	DDA - 1st Sub	0		09-Mar-21	0		03-Jul-21	◆ DDA - 1st Sub																													
B18200	DDA - Review by SO	28	10-Mar-21	06-Apr-21	28	04-Jul-21	31-Jul-21	■ DDA - Review by SO																													
B18180	DDA - Review by IP / DC	28	10-Mar-21	06-Apr-21	28	04-Jul-21	31-Jul-21	■ DDA - Review by IP / DC																													
AIP Landscape Design		69	29-Aug-20	20-Nov-20	119	14-Dec-20 A	13-May-21	◆ AIP Landscape Design																													
B267501	AIP - Draft - Final Review and prepare for 1st Sub	12	29-Aug-20	11-Sep-20	12	14-Dec-20 A	29-Dec-20 A	■ AIP - Draft - Final Review and prepare for 1st Sub																													
B267521	AIP - 1st Sub	0		11-Sep-20	0		29-Dec-20 A	◆ AIP - 1st Sub																													
B267511	AIP - Review by SO	28	12-Sep-20	09-Oct-20	31	30-Dec-20 A	29-Jan-21 A	■ AIP - Review by SO																													
B267581	AIP - Review by IP / DC	28	12-Sep-20	09-Oct-20	129	30-Dec-20 A	07-May-21	■ AIP - Review by IP / DC																													
B267531	AIP - Further information required by SO	12	10-Oct-20	23-Oct-20	31	30-Jan-21 A	10-Mar-21 A	■ AIP - Further information required by SO																													
B267551	AIP - 2nd Sub	0		23-Oct-20	0		10-Mar-21 A	◆ AIP - 2nd Sub																													
B267541	AIP - 2nd Review by SO	28	24-Oct-20	20-Nov-20	64	11-Mar-21 A	13-May-21	■ AIP - 2nd Review by SO																													
B267561	AIP - SO Consent for Construction	0		20-Nov-20	0		13-May-21	◆ AIP - SO Consent for Construction																													

Page 2 of 25
Data Date: 01-May-21

- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar
- ▶ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu


Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																													
								January				February				March				April				May				June				July					
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25
DDA Landscape Design								DDA Landscape Design																													
B17650	DDA - Draft - Preparation by Designer	42	21-Nov-20	09-Feb-21	66	14-May-21	02-Aug-21	DDA - Draft - Prepar																													
B17660	DDA - Draft - Final Review and prepare for 1st Sub	24	13-Jan-21	09-Feb-21	24	06-Jul-21	02-Aug-21																														
MISC. TEMP WORKS																																					
Seawall checkings for temporary cases (Loading / Unloading)																																					
B17270	DDA - SO Consent for Construction	0	08-Jul-20	08-Jul-20	0	12-Jan-21 A	12-Jan-21 A	DDA - SO Consent for Construction																													
DEPRESSED ROAD [DPR]								DEPRESSED ROAD [DPR]																													
DDA DPR - Horizontal Element + Pump Test + DCRA																																					
B2596351	DDA - 4th Sub	0			0		17-Dec-20 A	Sub																													
B2596361	DDA - 4th Review by SO	0			54	18-Dec-20 A	09-Feb-21 A	DDA - 4th Review by SO																													
B15740	DDA - SO Consent for Construction	0		29-Jul-20	0		09-Feb-21 A	DDA - SO Consent for Construction																													
DDA DPR - Permanent Structure								Permanent Structure																													
B15820	DDA - 2nd Sub	0	04-Nov-20	09-Dec-20	97	11-Dec-20 A	15-Apr-21 A																														
B15830	DDA - 2nd Review by SO	35	05-Nov-20	09-Dec-20	20	12-Dec-20 A	31-Dec-20 A	DDA - 2nd Review by SO																													
B2596371	DDA - Further information required by SO	0			34	02-Jan-21 A	10-Feb-21 A	DDA - Further information required by SO																													
B2596381	DDA - 3rd Sub	0			0		10-Feb-21 A	DDA - 3rd Sub																													
B2596391	DDA - 2nd Review by SO	0			64	11-Feb-21 A	15-Apr-21 A	DDA - 2nd Review by SO																													
B15850	DDA - SO Consent for Construction	0		09-Dec-20	0		15-Apr-21 A	DDA - SO Consent for Construction																													
DDA DPR - Portal Structure								DDA DPR - Portal Structure																													
B15860	DDA - Draft - Preparation by Designer	30	23-Sep-20	30-Oct-20	24	24-Dec-20 A	23-Jan-21 A	DDA - Draft - Preparation by Designer																													
B15870	DDA - Draft - Final Review and prepare for 1st Sub	24	31-Oct-20	27-Nov-20	82	25-Jan-21 A	08-May-21	DDA - Draft - Final Review and prepare for 1st Sub																													
B15880	DDA - 1st Sub	0		27-Nov-20	0		08-May-21	DDA - 1st Sub																													
B15910	DDA - Review by SO	28	28-Nov-20	25-Dec-20	28	09-May-21	05-Jun-21	DDA - Review by SO																													
B15890	DDA - Review by IP / DC	28	28-Nov-20	25-Dec-20	28	09-May-21	05-Jun-21	DDA - Review by IP / DC																													
B15920	DDA - Further information required by SO	12	28-Dec-20	11-Jan-21	12	07-Jun-21	21-Jun-21	DDA - Further information requir																													
B15930	DDA - 2nd Sub	0		11-Jan-21	0		21-Jun-21	DDA - 2nd Sub																													
B15940	DDA - 2nd Review by SO	35	12-Jan-21	15-Feb-21	35	22-Jun-21	26-Jul-21	D																													
B15960	DDA - SO Consent for Construction	0		16-Feb-21	0		26-Jul-21	D																													
WEST VENTILATION BUILDING [WVB]								WEST VENTILATI																													
DDA WVB - ELS Design (DCRA + Dewatering & Pumping Test)								n (DCRA + Dewatering & Pumping Test)																													
B2596111	DDA - 3rd Sub	0			0		28-Dec-20 A	DDA - 3rd Sub																													
B2596121	DDA - 3rd Review by SO	0			14	29-Dec-20 A	11-Jan-21 A	DDA - 3rd Review by SO																													
B2597091	DDA - Further information required by SO	0			93	12-Jan-21 A	08-May-21	DDA - Further information required by SO																													
B2597111	DDA - 4th Sub	0			0		08-May-21	DDA - 4th Sub																													
B2597101	DDA - 4th Review by SO	0			35	09-May-21	12-Jun-21	DDA - 4th Review by SO																													
B13900	DDA - SO Consent for Construction	0		02-Dec-20	0		12-Jun-21	DDA - SO Consent for Construction																													
DDA WVB - Accommodation (SoA)								DDA WVB - Accommodation (SoA)																													
B14380	DDA - Further information required by SO	30	13-Nov-20	17-Dec-20	40	30-Dec-20 A	18-Feb-21 A	DDA - Further information required by SO																													
B14390	DDA - 2nd Sub	0		17-Dec-20	0		18-Feb-21 A	DDA - 2nd Sub																													
B14400	DDA - 2nd Review by SO	35	18-Dec-20	21-Jan-21	18	19-Feb-21 A	08-Mar-21 A	DDA - 2nd Review by SO																													
B2597121	DDA - Further information required by SO	0			50	09-Mar-21 A	11-May-21	DDA - Further information required by SO																													
B2597131	DDA - 3rd Sub	0			0		11-May-21	DDA - 3rd Sub																													
B2597141	DDA - 3rd Review by SO	0			35	12-May-21	15-Jun-21	DDA - 3rd Review by SO																													
B14410	DDA - SO Consent for Construction	0		21-Jan-21	0		15-Jun-21	DDA - SO Consent for Construction																													
DDA WVB - Permanent Structure								DDA WVB - Permanent Structure																													
B14430	DDA - Draft - Final Review and prepare for 1st Sub	12	09-Dec-20	22-Dec-20	33	23-Dec-20 A	02-Feb-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B14440	DDA - 1st Sub	0		22-Dec-20	0		02-Feb-21 A	DDA - 1st Sub																													
B14470	DDA - Review by SO	28	23-Dec-20	19-Jan-21	45	03-Feb-21 A	19-Mar-21 A	DDA - Review by SO																													
B14450	DDA - Review by IP / DC	28	23-Dec-20	19-Jan-21	94	03-Feb-21 A	07-May-21	DDA - Review by IP / DC																													
B14480	DDA - Further information required by SO	30	20-Jan-21	26-Feb-21	43	20-Mar-21 A	14-May-21	DDA - Further information required by SO																													

Page 3 of 25
Data Date: 01-May-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

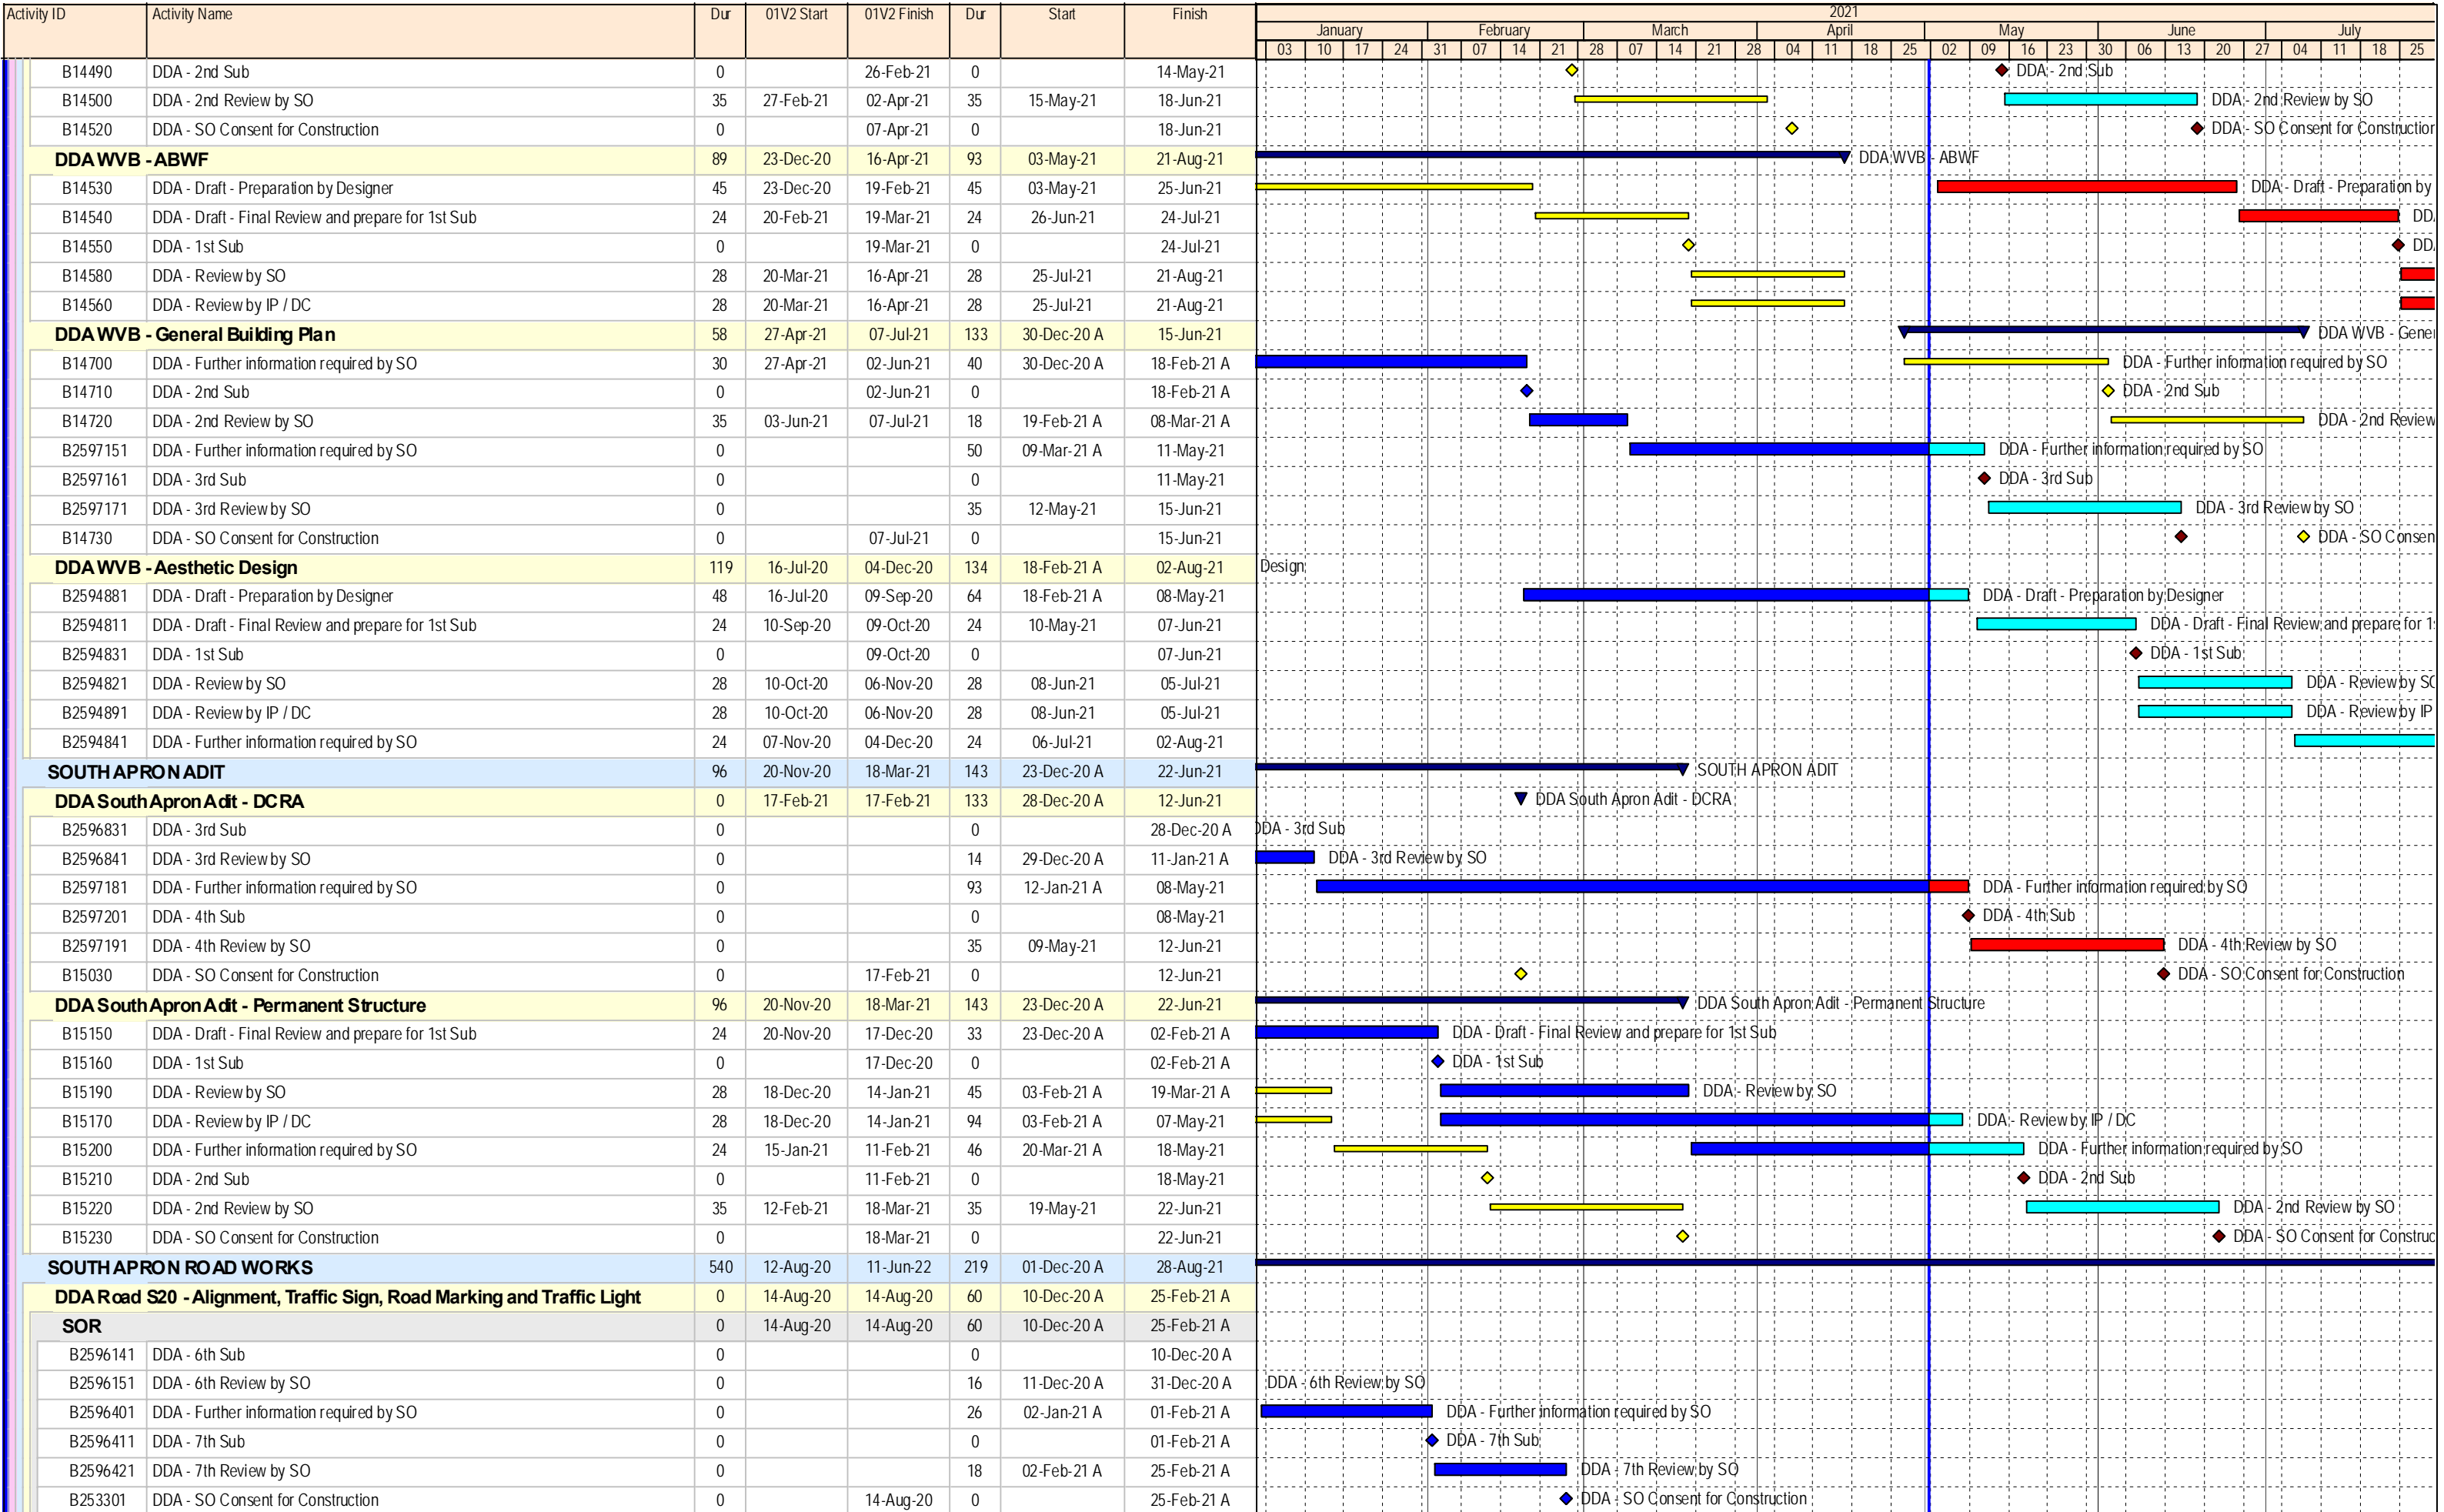

Page 4 of 25
Data Date: 01-May-21

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																																	
								January				February				March				April				May				June				July									
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25				
DDA Road S20 - Roadworks and Street Furniture								0	14-Aug-20	14-Aug-20	93	15-Dec-20 A	14-Apr-21 A																												
SOR								0	14-Aug-20	14-Aug-20	93	15-Dec-20 A	14-Apr-21 A																												
B2596171	DDA - 7th Sub	0			0		15-Dec-20 A	Sub																																	
B2596181	DDA - Further information required by SO	0			38	16-Dec-20 A	01-Feb-21 A	DDA - Further information required by SO																																	
B2596851	DDA - 7th Review by SO	0			1	01-Feb-21 A	01-Feb-21 A	DDA - 7th Review by SO																																	
B2596861	DDA - 8th Sub	0			0		01-Feb-21 A	DDA - 8th Sub																																	
B2596871	DDA - 8th Review by SO	0			18	02-Feb-21 A	25-Feb-21 A	DDA - 8th Review by SO																																	
B2597221	DDA - Further information required by SO	0			21	26-Feb-21 A	22-Mar-21 A	DDA - Further information required by SO																																	
B2597211	DDA - 9th Review by SO	0			16	23-Mar-21 A	14-Apr-21 A	DDA - 9th Review by SO																																	
B253401	DDA - SO Consent for Construction	0		14-Aug-20	0		14-Apr-21 A	DDA - SO Consent for Construction																																	
B2597231	DDA - 9th Sub	0			0		14-Apr-21 A	DDA - 9th Sub																																	
TD								0			93	16-Dec-20 A	14-Apr-21 A																												
B2595761	DDA - Under review by TD	0			93	16-Dec-20 A	14-Apr-21 A	DDA - Under review by TD																																	
AIP Road L10 (S)								0	03-Oct-20	03-Oct-20	138	01-Dec-20 A	24-May-21																												
B2596211	AIP - 2d Review by SO	0			64	01-Dec-20 A	02-Feb-21 A	AIP - 2d Review by SO																																	
B2597241	AIP - Further information required by SO	0			23	03-Feb-21 A	04-Mar-21 A	AIP - Further information required by SO																																	
B2597261	AIP - 3rd Review by SO	0			19	04-Mar-21 A	22-Mar-21 A	AIP - 3rd Review by SO																																	
B2597251	AIP - 3rd Sub	0			0		04-Mar-21 A	AIP - 3rd Sub																																	
B2597271	AIP - Further information required by SO	0			26	23-Mar-21 A	26-Apr-21 A	AIP - Further information required by SO																																	
B2597281	AIP - 4th Sub	0			0		26-Apr-21 A	AIP - 4th Sub																																	
B2597291	AIP - 4th Review by SO	0			28	27-Apr-21 A	24-May-21	AIP - 4th Review by SO																																	
B255892	AIP - SO Consent for DDA Submission	0		03-Oct-20	0		24-May-21	AIP - SO Consent for DDA Submission																																	
DDA Road L10 (S) + Outfall 2 - Permanent Utility Design								77	02-Nov-20	02-Feb-21	107	21-Dec-20 A	06-May-21	DDA Road L10 (S) + Outfall 2 - Permanent Utility Design																											
B263761	DDA - Draft - Final Review and prepare for 1st Sub	12	02-Nov-20	14-Nov-20	7	21-Dec-20 A	30-Dec-20 A	DDA - Draft - Final Review and prepare for 1st Sub																																	
B263781	DDA - 1st Sub	0		14-Nov-20	0		30-Dec-20 A	DDA - 1st Sub																																	
B263771	DDA - Review by SO	28	15-Nov-20	12-Dec-20	41	31-Dec-20 A	09-Feb-21 A	DDA - Review by SO																																	
B263831	DDA - Review by IP / DC	28	15-Nov-20	12-Dec-20	51	31-Dec-20 A	19-Feb-21 A	DDA - Review by IP / DC																																	
B263791	DDA - Further information required by SO	12	14-Dec-20	29-Dec-20	6	10-Feb-21 A	19-Feb-21 A	DDA - Further information required by SO																																	
B263811	DDA - 2nd Sub	0		29-Dec-20	0		19-Feb-21 A	DDA - 2nd Sub																																	
B263801	DDA - 2nd Review by SO	35	30-Dec-20	02-Feb-21	12	20-Feb-21 A	03-Mar-21 A	DDA - 2nd Review by SO																																	
B2597301	DDA - Further information required by SO	0			7	04-Mar-21 A	11-Mar-21 A	DDA - Further information required by SO																																	
B2597311	DDA - 3rd Sub	0			0		11-Mar-21 A	DDA - 3rd Sub																																	
B2597321	DDA - 3rd Review by SO	0			13	12-Mar-21 A	24-Mar-21 A	DDA - 3rd Review by SO																																	
B2597331	DDA - Further information required by SO	0			9	25-Mar-21 A	08-Apr-21 A	DDA - Further information required by SO																																	
B2597341	DDA - 4th Sub	0			0		08-Apr-21 A	DDA - 4th Sub																																	
B2597351	DDA - 4th Review by SO	0			28	09-Apr-21 A	06-May-21	DDA - 4th Review by SO																																	
B263751	DDA - SO Consent for Construction	0		02-Feb-21	0		06-May-21	DDA - SO Consent for Construction																																	
DDA Road L10 (S) - Alignment, Traffic Sign, Road Marking and Traffic Light								77	02-Nov-20	02-Feb-21	114	26-Dec-20 A	20-May-21	DDA Road L10 (S) - Alignment, Traffic Sign, Road Marking and Traffic Light																											
B265151	DDA - Draft - Final Review and prepare for 1st Sub	12	02-Nov-20	14-Nov-20	2	26-Dec-20 A	29-Dec-20 A	DDA - Draft - Final Review and prepare for 1st Sub																																	
B255912	DDA - 1st Sub	0		14-Nov-20	0		29-Dec-20 A	DDA - 1st Sub																																	
B265161	DDA - Review by SO	28	15-Nov-20	12-Dec-20	32	30-Dec-20 A	30-Jan-21 A	DDA - Review by SO																																	
B255913	DDA - Review by IP / DC	28	15-Nov-20	12-Dec-20	74	30-Dec-20 A	13-Mar-21 A	DDA - Review by IP / DC																																	
B265171	DDA - Further information required by SO	12	14-Dec-20	29-Dec-20	12	01-Feb-21 A	17-Feb-21 A	DDA - Further information required by SO																																	
B255942	DDA - 2nd Sub	0		29-Dec-20	0		17-Feb-21 A	DDA - 2nd Sub																																	
B265181	DDA - 2nd Review by SO	35	30-Dec-20	02-Feb-21	17	18-Feb-21 A	06-Mar-21 A	DDA - 2nd Review by SO																																	
B2597361	DDA - Further information required by SO	0			30	08-Mar-21 A	15-Apr-21 A	DDA - Further information required by SO																																	
B2597371	DDA - 3rd Sub	0			0		15-Apr-21 A	DDA - 3rd Sub																																	
B2597381	DDA - 3rd Review by SO	0			35	16-Apr-21 A	20-May-21	DDA - 3rd Review by SO																																	
B255992	DDA - SO Consent for Construction	0		02-Feb-21	0		20-May-21	DDA - SO Consent for Construction																																	
DDA Road L10 (S) - Roadworks and Street Furniture								77	02-Nov-20	02-Feb-21	138	26-Dec-20 A	18-Jun-21	DDA Road L10 (S) - Roadworks and Street Furniture																											


Page 5 of 25 Data Date: 01-May-21		<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme (Apr-21)</h3>		Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																												
05-Nov-19	00V0	WYu																													
18-Dec-19	00V1	WYu																													
22-Feb-20	01V0	SPa/LLo	WYu																												
09-Apr-20	01V1	SPa/LLo	WYu																												
17-Jul-20	01V2	SPa/LLo	WYu																												
09-Oct-20	01V3	SPa/LLo	WYu																												

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																													
								January				February				March				April				May				June				July					
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25
B263671	DDA - Draft - Final Review and prepare for 1st Sub	12	02-Nov-20	14-Nov-20	2	26-Dec-20 A	29-Dec-20 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B263691	DDA - 1st Sub	0		14-Nov-20	0		29-Dec-20 A	DDA - 1st Sub																													
B263681	DDA - Review by SO	28	15-Nov-20	12-Dec-20	28	30-Dec-20 A	26-Jan-21 A	DDA - Review by SO																													
B263741	DDA - Review by IP / DC	28	15-Nov-20	12-Dec-20	129	30-Dec-20 A	07-May-21	DDA - Review by IP / DC																													
B263701	DDA - Further information required by SO	12	14-Dec-20	29-Dec-20	85	27-Jan-21 A	14-May-21	DDA - Further information required by SO																													
B263721	DDA - 2nd Sub	0		29-Dec-20	0		14-May-21	DDA - 2nd Sub																													
B263711	DDA - 2nd Review by SO	35	30-Dec-20	02-Feb-21	35	15-May-21	18-Jun-21	DDA - 2nd Review by SO																													
B263661	DDA - SO Consent for Construction	0		02-Feb-21	0		18-Jun-21	DDA - SO Consent for Construction																													
AIP Foot Bridge FB-02		24	25-Aug-20	22-Sep-20	15	14-Dec-20 A	04-Jan-21 A																														
B256042	AIP - 2nd Sub	0		25-Aug-20	0		14-Dec-20 A	AIP - 2nd Sub																													
B265211	AIP - 2nd Review by SO	28	26-Aug-20	22-Sep-20	21	15-Dec-20 A	04-Jan-21 A	AIP - 2nd Review by SO																													
B256092	AIP - SO Consent for DDA Submission	0		22-Sep-20	0		04-Jan-21 A	AIP - SO Consent for DDA Submission																													
DDA Foot Bridge FB-02		74	09-Oct-20	07-Jan-21	128	05-Jan-21 A	12-Jun-21	DDA Foot Bridge FB-02																													
B263851	DDA - Draft - Final Review and prepare for 1st Sub	12	09-Oct-20	22-Oct-20	6	05-Jan-21 A	11-Jan-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B263871	DDA - 1st Sub	0		22-Oct-20	0		11-Jan-21 A	DDA - 1st Sub																													
B263861	DDA - Review by SO	28	23-Oct-20	19-Nov-20	45	12-Jan-21 A	25-Feb-21 A	DDA - Review by SO																													
B263921	DDA - Review by IP / DC	28	23-Oct-20	19-Nov-20	77	12-Jan-21 A	29-Mar-21 A	DDA - Review by IP / DC																													
B263881	DDA - Further information required by SO	12	20-Nov-20	03-Dec-20	16	26-Feb-21 A	16-Mar-21 A	DDA - Further information required by SO																													
B263901	DDA - 2nd Sub	0		03-Dec-20	0		16-Mar-21 A	DDA - 2nd Sub																													
B263891	DDA - 2nd Review by SO	35	04-Dec-20	07-Jan-21	14	17-Mar-21 A	30-Mar-21 A	DDA - 2nd Review by SO																													
B2597571	DDA - Further information required by SO	0			28	01-Apr-21 A	08-May-21	DDA - Further information required by SO																													
B2597581	DDA - 2nd Sub	0			0		08-May-21	DDA - 2nd Sub																													
B2597591	DDA - 2nd Review by SO	0			35	09-May-21	12-Jun-21	DDA - 2nd Review by SO																													
B263841	DDA - SO Consent for Construction	0		07-Jan-21	0		12-Jun-21	DDA - SO Consent for Construction																													
DDA CUE Entrance ELS		39	12-Sep-20	30-Oct-20	37	18-Dec-20 A	02-Feb-21 A																														
B260830	DDA - Further information required by SO	12	12-Sep-20	25-Sep-20	24	18-Dec-20 A	18-Jan-21 A	DDA - Further information required by SO																													
B260840	DDA - 2nd Sub	0		25-Sep-20	0		18-Jan-21 A	DDA - 2nd Sub																													
B260850	DDA - 2nd Review by SO	35	26-Sep-20	30-Oct-20	15	19-Jan-21 A	02-Feb-21 A	DDA - 2nd Review by SO																													
B260860	DDA - SO Consent for Construction	0		30-Oct-20	0		02-Feb-21 A	DDA - SO Consent for Construction																													
DDA CUE Permanent Works		0	21-Oct-20	21-Oct-20	48	09-Dec-20 A	05-Feb-21 A																														
B2596431	DDA - Further information required by SO	0			9	09-Dec-20 A	18-Dec-20 A	DDA - Further information required by SO																													
B2596441	DDA - 3rd Sub	0			0		18-Dec-20 A	DDA - 3rd Sub																													
B2596451	DDA - 3rd Review by SO	0			27	19-Dec-20 A	14-Jan-21 A	DDA - 3rd Review by SO																													
B2596641	DDA - Further information required by SO	0			7	15-Jan-21 A	22-Jan-21 A	DDA - Further information required by SO																													
B2596651	DDA - 3rd Sub	0			0		22-Jan-21 A	DDA - 3rd Sub																													
B2596661	DDA - 3rd Review by SO	0			14	23-Jan-21 A	05-Feb-21 A	DDA - 3rd Review by SO																													
B260950	DDA - SO Consent for Construction	0		21-Oct-20	0		05-Feb-21 A	DDA - SO Consent for Construction																													
[STE] AIP CUE L10 (N) Permanent Works		66	03-Dec-21	24-Feb-22	38	05-Dec-20 A	21-Jan-21 A																														
B261240	AIP - Draft - Final Review and prepare for 1st Sub	12	03-Dec-21	16-Dec-21	2	05-Dec-20 A	07-Dec-20 A	AIP - Draft - Final Review and prepare for 1st Sub																													
B261250	AIP - 1st Sub	0		16-Dec-21	0		07-Dec-20 A	AIP - 1st Sub																													
B261270	AIP - Review by SO	28	17-Dec-21	13-Jan-22	16	08-Dec-20 A	23-Dec-20 A	AIP - Review by SO																													
B261260	AIP - Review by IP / DC	28	17-Dec-21	13-Jan-22	16	08-Dec-20 A	23-Dec-20 A	AIP - Review by IP / DC																													
B261280	AIP - Further information required by SO	12	14-Jan-22	27-Jan-22	17	24-Dec-20 A	15-Jan-21 A	AIP - Further information required by SO																													
B261290	AIP - 2nd Sub	0		27-Jan-22	0		15-Jan-21 A	AIP - 2nd Sub																													
B261300	AIP - 2nd Review by SO	28	28-Jan-22	24-Feb-22	6	16-Jan-21 A	21-Jan-21 A	AIP - 2nd Review by SO																													
B261310	AIP - SO Consent for DDA Submission	0		24-Feb-22	0		21-Jan-21 A	AIP - SO Consent for DDA Submission																													
[STE] DDA CUE L10 (N) Permanent Works		88	22-Feb-22	11-Jun-22	116	12-Dec-20 A	10-May-21																														
B261060	DDA - Draft - Final Review and prepare for 1st Sub	12	22-Feb-22	07-Mar-22	26	12-Dec-20 A	14-Jan-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B261070	DDA - 1st Sub	0		07-Mar-22	0		14-Jan-21 A	DDA - 1st Sub																													
B261090	DDA - Review by SO	28	08-Mar-22	04-Apr-22	40	15-Jan-21 A	23-Feb-21 A	DDA - Review by SO																													

Page 6 of 25
Data Date: 01-May-21

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																											
								January			February			March			April			May			June			July									
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11
B261080	DDA - Review by IP / DC	28	08-Mar-22	04-Apr-22	77	15-Jan-21 A	01-Apr-21 A	[Gantt bar: 15-Jan-21 to 01-Apr-21]																											
B261100	DDA - Further information required by SO	24	06-Apr-22	07-May-22	19	24-Feb-21 A	17-Mar-21 A	[Gantt bar: 24-Feb-21 to 17-Mar-21]																											
B261110	DDA - 2nd Sub	0		07-May-22	0			[Milestone: 07-May-22]																											
B261120	DDA - 2nd Review by SO	35	08-May-22	11-Jun-22	53	18-Mar-21 A	09-May-21	[Gantt bar: 18-Mar-21 to 09-May-21]																											
B261130	DDA - SO Consent for Construction	0		11-Jun-22	0			[Milestone: 11-Jun-22]																											
[STE] AIP District Cooling System Permanent Works		0	12-Aug-20	12-Aug-20	0	16-Dec-20 A	16-Dec-20 A	[Milestone: 16-Dec-20]																											
B263931	AIP - SO Consent for DDA Submission	0		12-Aug-20	0			[Milestone: 12-Aug-20]																											
[STE] DDA District Coding System Permanent Works		27	30-Sep-20	04-Nov-20	85	21-Jan-21 A	10-May-21	[Gantt bar: 21-Jan-21 to 10-May-21]																											
B264081	DDA - 2nd Sub	0		30-Sep-20	0			[Milestone: 30-Sep-20]																											
B264071	DDA - 2nd Review by SO	35	01-Oct-20	04-Nov-20	32	22-Jan-21 A	22-Feb-21 A	[Gantt bar: 22-Jan-21 to 22-Feb-21]																											
B2596881	DDA - Further information required by SO	0			38	23-Feb-21 A	12-Apr-21 A	[Gantt bar: 23-Feb-21 to 12-Apr-21]																											
B2596891	DDA - 3rd Sub	0			0			[Milestone: 12-Apr-21]																											
B2596901	DDA - 2nd Review by SO	0			28	13-Apr-21 A	10-May-21	[Gantt bar: 13-Apr-21 to 10-May-21]																											
B264021	DDA - SO Consent for Construction	0		04-Nov-20	0			[Milestone: 04-Nov-20]																											
[STE] AIP District Cooling System Temporary Works		0	14-Aug-20	14-Aug-20	33	08-Dec-20 A	19-Jan-21 A	[Gantt bar: 08-Dec-20 to 19-Jan-21]																											
B2596231	AIP - 3rd Sub	0			0			[Milestone: 08-Dec-20]																											
B2596241	AIP - 3rd Review by SO	0			14	09-Dec-20 A	22-Dec-20 A	[Gantt bar: 09-Dec-20 to 22-Dec-20]																											
B2596461	AIP - Further information required by SO	0			9	23-Dec-20 A	05-Jan-21 A	[Gantt bar: 23-Dec-20 to 05-Jan-21]																											
B2596471	AIP - 4th Sub	0			0			[Milestone: 05-Jan-21]																											
B2596481	AIP - 4th Review by SO	0			14	06-Jan-21 A	19-Jan-21 A	[Gantt bar: 06-Jan-21 to 19-Jan-21]																											
B258970	AIP - SO Consent for DDA Submission	0		14-Aug-20	0			[Milestone: 14-Aug-20]																											
[STE] DDA District Coding System Temporary Works		29	05-Oct-20	09-Nov-20	62	11-Dec-20 A	01-Mar-21 A	[Gantt bar: 11-Dec-20 to 01-Mar-21]																											
B259040	DDA - 2nd Sub	0		05-Oct-20	0			[Milestone: 05-Oct-20]																											
B259050	DDA - 2nd Review by SO	35	06-Oct-20	09-Nov-20	27	12-Dec-20 A	07-Jan-21 A	[Gantt bar: 12-Dec-20 to 07-Jan-21]																											
B2596671	DDA - Further information required by SO	0			10	08-Jan-21 A	19-Jan-21 A	[Gantt bar: 08-Jan-21 to 19-Jan-21]																											
B2596681	DDA - 3rd Sub	0			0			[Milestone: 19-Jan-21]																											
B2596691	DDA - 3rd Review by SO	0			10	20-Jan-21 A	29-Jan-21 A	[Gantt bar: 20-Jan-21 to 29-Jan-21]																											
B2596911	DDA - Further information required by SO	0			11	30-Jan-21 A	11-Feb-21 A	[Gantt bar: 30-Jan-21 to 11-Feb-21]																											
B2596921	DDA - 4th Sub	0			0			[Milestone: 11-Feb-21]																											
B2596931	DDA - 4th Review by SO	0			18	12-Feb-21 A	01-Mar-21 A	[Gantt bar: 12-Feb-21 to 01-Mar-21]																											
B259060	DDA - SO Consent for Construction	0		09-Nov-20	0			[Milestone: 09-Nov-20]																											
[STE] AIP Hoi Bun Road Junction		0	30-Nov-20	30-Nov-20	58	29-Jan-21 A	15-Apr-21 A	[Gantt bar: 29-Jan-21 to 15-Apr-21]																											
B2596501	AIP - 4th Sub	0			0			[Milestone: 29-Jan-21]																											
B2596511	AIP - 4th Review by SO	0			18	30-Jan-21 A	16-Feb-21 A	[Gantt bar: 30-Jan-21 to 16-Feb-21]																											
B2596941	AIP - Further information required by SO	0			10	17-Feb-21 A	27-Feb-21 A	[Gantt bar: 17-Feb-21 to 27-Feb-21]																											
B2596951	AIP - 5th Sub	0			0			[Milestone: 27-Feb-21]																											
B2596961	AIP - 5th Review by SO	0			16	01-Mar-21 A	16-Mar-21 A	[Gantt bar: 01-Mar-21 to 16-Mar-21]																											
B2597391	AIP - Further information required by SO	0			13	17-Mar-21 A	31-Mar-21 A	[Gantt bar: 17-Mar-21 to 31-Mar-21]																											
B2597401	AIP - 6th Sub	0			0			[Milestone: 31-Mar-21]																											
B2597411	AIP - 6th Review by SO	0			15	01-Apr-21 A	15-Apr-21 A	[Gantt bar: 01-Apr-21 to 15-Apr-21]																											
B259780	AIP - SO Consent for DDA Submission	0		30-Nov-20	0			[Milestone: 30-Nov-20]																											
[STE] DDA Hoi Bun Road Junction - Permanent Utility Design		0	01-Mar-21	01-Mar-21	84	20-Jan-21 A	07-May-21	[Gantt bar: 20-Jan-21 to 07-May-21]																											
B2596531	DDA - 3rd Sub	0			0			[Milestone: 20-Jan-21]																											
B2596541	DDA - 3rd Review by SO	0			30	21-Jan-21 A	19-Feb-21 A	[Gantt bar: 21-Jan-21 to 19-Feb-21]																											
B2596971	DDA - Further information required by SO	0			32	20-Feb-21 A	29-Mar-21 A	[Gantt bar: 20-Feb-21 to 29-Mar-21]																											
B2596981	DDA - 4th Sub	0			0			[Milestone: 29-Mar-21]																											
B2596991	DDA - 4th Review by SO	0			39	30-Mar-21 A	07-May-21	[Gantt bar: 30-Mar-21 to 07-May-21]																											
B259510	DDA - SO Consent for Construction	0		01-Mar-21	0			[Milestone: 01-Mar-21]																											
[STE] DDA Hoi Bun Road Junction - Alignment, Traffic Sign, Road Marking and Traffic Light		27	25-Jan-21	01-Mar-21	72	03-Feb-21 A	07-May-21	[Gantt bar: 03-Feb-21 to 07-May-21]																											
B263261	DDA - 2nd Review by SO	35	26-Jan-21	01-Mar-21	22	03-Feb-21 A	25-Feb-21 A	[Gantt bar: 03-Feb-21 to 25-Feb-21]																											

Page 7 of 25
Data Date: 01-May-21


- Milestone
- Actual Milestone
- Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

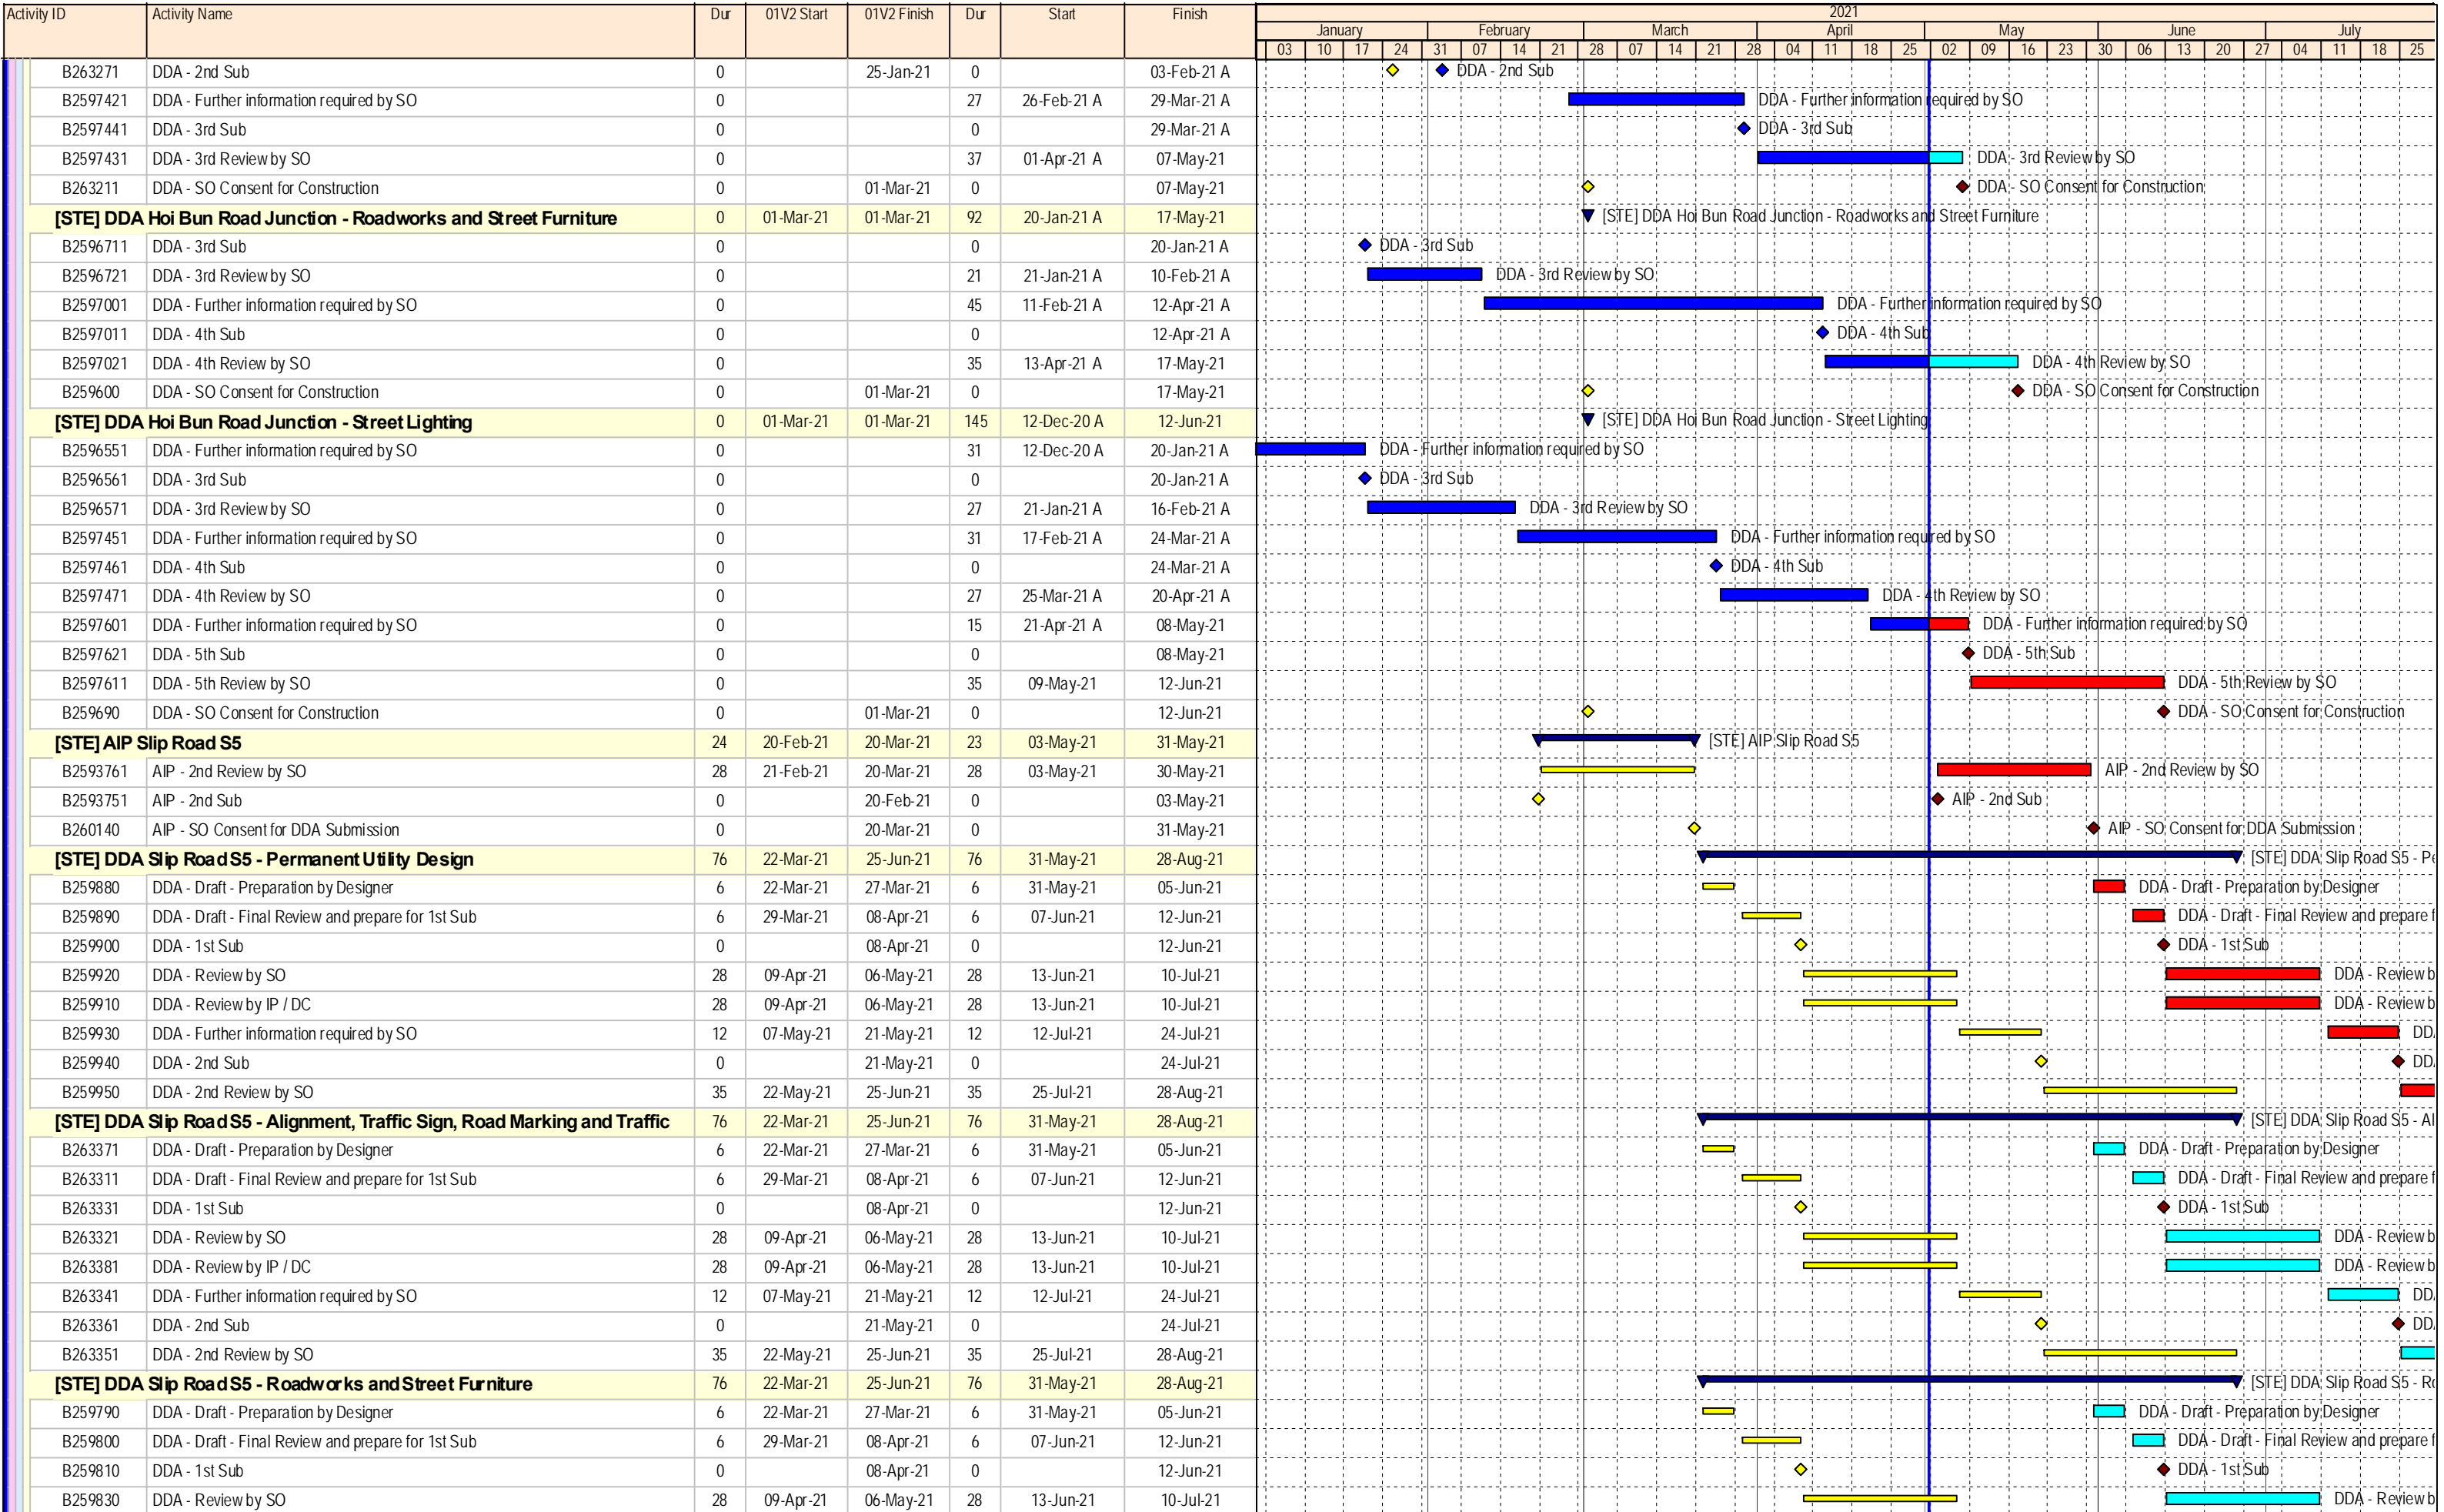


Page 8 of 25
Data Date: 01-May-21

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu


Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																													
								January				February				March				April				May				June				July					
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25
B259820	DDA - Review by IP / DC	28	09-Apr-21	06-May-21	28	13-Jun-21	10-Jul-21	DDA - Review by IP / DC																													
B259840	DDA - Further information required by SO	12	07-May-21	21-May-21	12	12-Jul-21	24-Jul-21	DDA - Further information required by SO																													
B259850	DDA - 2nd Sub	0		21-May-21	0		24-Jul-21	DDA - 2nd Sub																													
B259860	DDA - 2nd Review by SO	35	22-May-21	25-Jun-21	35	25-Jul-21	28-Aug-21	DDA - 2nd Review by SO																													
[STE] DDA Slip Road S5 - Street Lighting		76	22-Mar-21	25-Jun-21	76	31-May-21	28-Aug-21	[STE] DDA Slip Road S5 - Street Lighting																													
B259970	DDA - Draft - Preparation by Designer	6	22-Mar-21	27-Mar-21	6	31-May-21	05-Jun-21	DDA - Draft - Preparation by Designer																													
B259980	DDA - Draft - Final Review and prepare for 1st Sub	6	29-Mar-21	08-Apr-21	6	07-Jun-21	12-Jun-21	DDA - Draft - Final Review and prepare for 1st Sub																													
B259990	DDA - 1st Sub	0		08-Apr-21	0		12-Jun-21	DDA - 1st Sub																													
B260010	DDA - Review by SO	28	09-Apr-21	06-May-21	28	13-Jun-21	10-Jul-21	DDA - Review by SO																													
B260000	DDA - Review by IP / DC	28	09-Apr-21	06-May-21	28	13-Jun-21	10-Jul-21	DDA - Review by IP / DC																													
B260020	DDA - Further information required by SO	12	07-May-21	21-May-21	12	12-Jul-21	24-Jul-21	DDA - Further information required by SO																													
B260030	DDA - 2nd Sub	0		21-May-21	0		24-Jul-21	DDA - 2nd Sub																													
B260040	DDA - 2nd Review by SO	35	22-May-21	25-Jun-21	35	25-Jul-21	28-Aug-21	DDA - 2nd Review by SO																													
SUPPORTING UNDERGROUND STRUCTURE [SUS]		86	04-May-20	13-Aug-20	86	03-May-21	13-Aug-21	SUPPORTING UNDERGROUND STRUCTURE [SUS]																													
AIP SUS - Internal Structure		86	04-May-20	13-Aug-20	86	03-May-21	13-Aug-21	AIP SUS - Internal Structure																													
B24170	AIP - Draft - Preparation by Designer	72	04-May-20	28-Jul-20	72	03-May-21	28-Jul-21	AIP - Draft - Preparation by Designer																													
B24180	AIP - Draft - Final Review and prepare for 1st Sub	14	29-Jul-20	13-Aug-20	14	29-Jul-21	13-Aug-21	AIP - Draft - Final Review and prepare for 1st Sub																													
C&C TUNNEL / LAUNCHING SHAFT [C&C / LS]		192	22-Oct-20	18-Jun-21	147	15-Dec-20 A	18-Jun-21	C&C TUNNEL / LAUNCHING SHAFT [C&C / LS]																													
DDA - C&C/LS Base Slab & Associated Cast-in for TBM Launching		44	27-Oct-20	16-Dec-20	110	24-Dec-20 A	13-May-21	DDA - C&C/LS Base Slab & Associated Cast-in for TBM Launching																													
B10840	DDA - Further information required by SO	14	27-Oct-20	11-Nov-20	39	24-Dec-20 A	10-Feb-21 A	DDA - Further information required by SO																													
B10850	DDA - 2nd Sub	0		11-Nov-20	0		10-Feb-21 A	DDA - 2nd Sub																													
B10860	DDA - 2nd Review by SO	35	12-Nov-20	16-Dec-20	92	11-Feb-21 A	13-May-21	DDA - 2nd Review by SO																													
B10880	DDA - SO Consent for Construction	0		16-Dec-20	0		13-May-21	DDA - SO Consent for Construction																													
DDA - LS Tympanum Structure for TBM Launching		109	02-Nov-20	15-Mar-21	146	16-Dec-20 A	18-Jun-21	DDA - LS Tympanum Structure for TBM Launching																													
B10900	DDA - Draft - Final Review and prepare for 1st Sub	24	02-Nov-20	28-Nov-20	20	16-Dec-20 A	11-Jan-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B10910	DDA - 1st Sub	0		28-Nov-20	0		11-Jan-21 A	DDA - 1st Sub																													
B10940	DDA - Review by SO	28	29-Nov-20	26-Dec-20	17	12-Jan-21 A	28-Jan-21 A	DDA - Review by SO																													
B10930	DDA - Review by GEO via SO	28	29-Nov-20	26-Dec-20	17	12-Jan-21 A	28-Jan-21 A	DDA - Review by GEO via SO																													
B10920	DDA - Review by IP / DC	28	29-Nov-20	26-Dec-20	116	12-Jan-21 A	07-May-21	DDA - Review by IP / DC																													
B10950	DDA - Further information required by SO	36	28-Dec-20	08-Feb-21	83	29-Jan-21 A	14-May-21	DDA - Further information required by SO																													
B10960	DDA - 2nd Sub	0		08-Feb-21	0		14-May-21	DDA - 2nd Sub																													
B10970	DDA - 2nd Review by SO	35	09-Feb-21	15-Mar-21	35	15-May-21	18-Jun-21	DDA - 2nd Review by SO																													
B10980	DDA - SO Consent for Construction	0		15-Mar-21	0		18-Jun-21	DDA - SO Consent for Construction																													
DDA - C&C/LS Permanent Structure		64	29-Mar-21	18-Jun-21	110	24-Dec-20 A	13-May-21	DDA - C&C/LS Permanent Structure																													
B11050	DDA - Further information required by SO	36	29-Mar-21	14-May-21	39	24-Dec-20 A	10-Feb-21 A	DDA - Further information required by SO																													
B11060	DDA - 2nd Sub	0		14-May-21	0		10-Feb-21 A	DDA - 2nd Sub																													
B11070	DDA - 2nd Review by SO	35	15-May-21	18-Jun-21	92	11-Feb-21 A	13-May-21	DDA - 2nd Review by SO																													
B11080	DDA - SO Consent for Construction	0		18-Jun-21	0		13-May-21	DDA - SO Consent for Construction																													
DDA - LS Thrust Frame / Blocks for TBM Launching		96	22-Oct-20	18-Feb-21	147	15-Dec-20 A	18-Jun-21	DDA - LS Thrust Frame / Blocks for TBM Launching																													
B11300	DDA - Draft - Final Review and prepare for 1st Sub	9	22-Oct-20	02-Nov-20	52	15-Dec-20 A	19-Feb-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													
B11310	DDA - 1st Sub	0		02-Nov-20	0		19-Feb-21 A	DDA - 1st Sub																													
B11340	DDA - Review by SO	28	03-Nov-20	30-Nov-20	25	20-Feb-21 A	16-Mar-21 A	DDA - Review by SO																													
B11320	DDA - Review by IP / DC	28	03-Nov-20	30-Nov-20	77	20-Feb-21 A	07-May-21	DDA - Review by IP / DC																													
B11350	DDA - Further information required by SO	36	01-Dec-20	14-Jan-21	46	17-Mar-21 A	14-May-21	DDA - Further information required by SO																													
B11360	DDA - 2nd Sub	0		14-Jan-21	0		14-May-21	DDA - 2nd Sub																													
B11370	DDA - 2nd Review by SO	35	15-Jan-21	18-Feb-21	35	15-May-21	18-Jun-21	DDA - 2nd Review by SO																													
B11380	DDA - SO Consent for Construction	0		18-Feb-21	0		18-Jun-21	DDA - SO Consent for Construction																													
SUB-SEA TBM TUNNEL		252	08-Aug-20	16-Jun-21	189	29-Dec-20 A	19-Aug-21	SUB-SEA TBM TUNNEL																													
DDA - Special Segment for CP construction		104	10-Sep-20	15-Jan-21	144	02-Jan-21 A	02-Jul-21	DDA - Special Segment for CP construction																													
B20180	DDA - Draft - Final Review and prepare for 1st Sub	24	10-Sep-20	09-Oct-20	62	02-Jan-21 A	19-Mar-21 A	DDA - Draft - Final Review and prepare for 1st Sub																													

Page 9 of 25
Data Date: 01-May-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

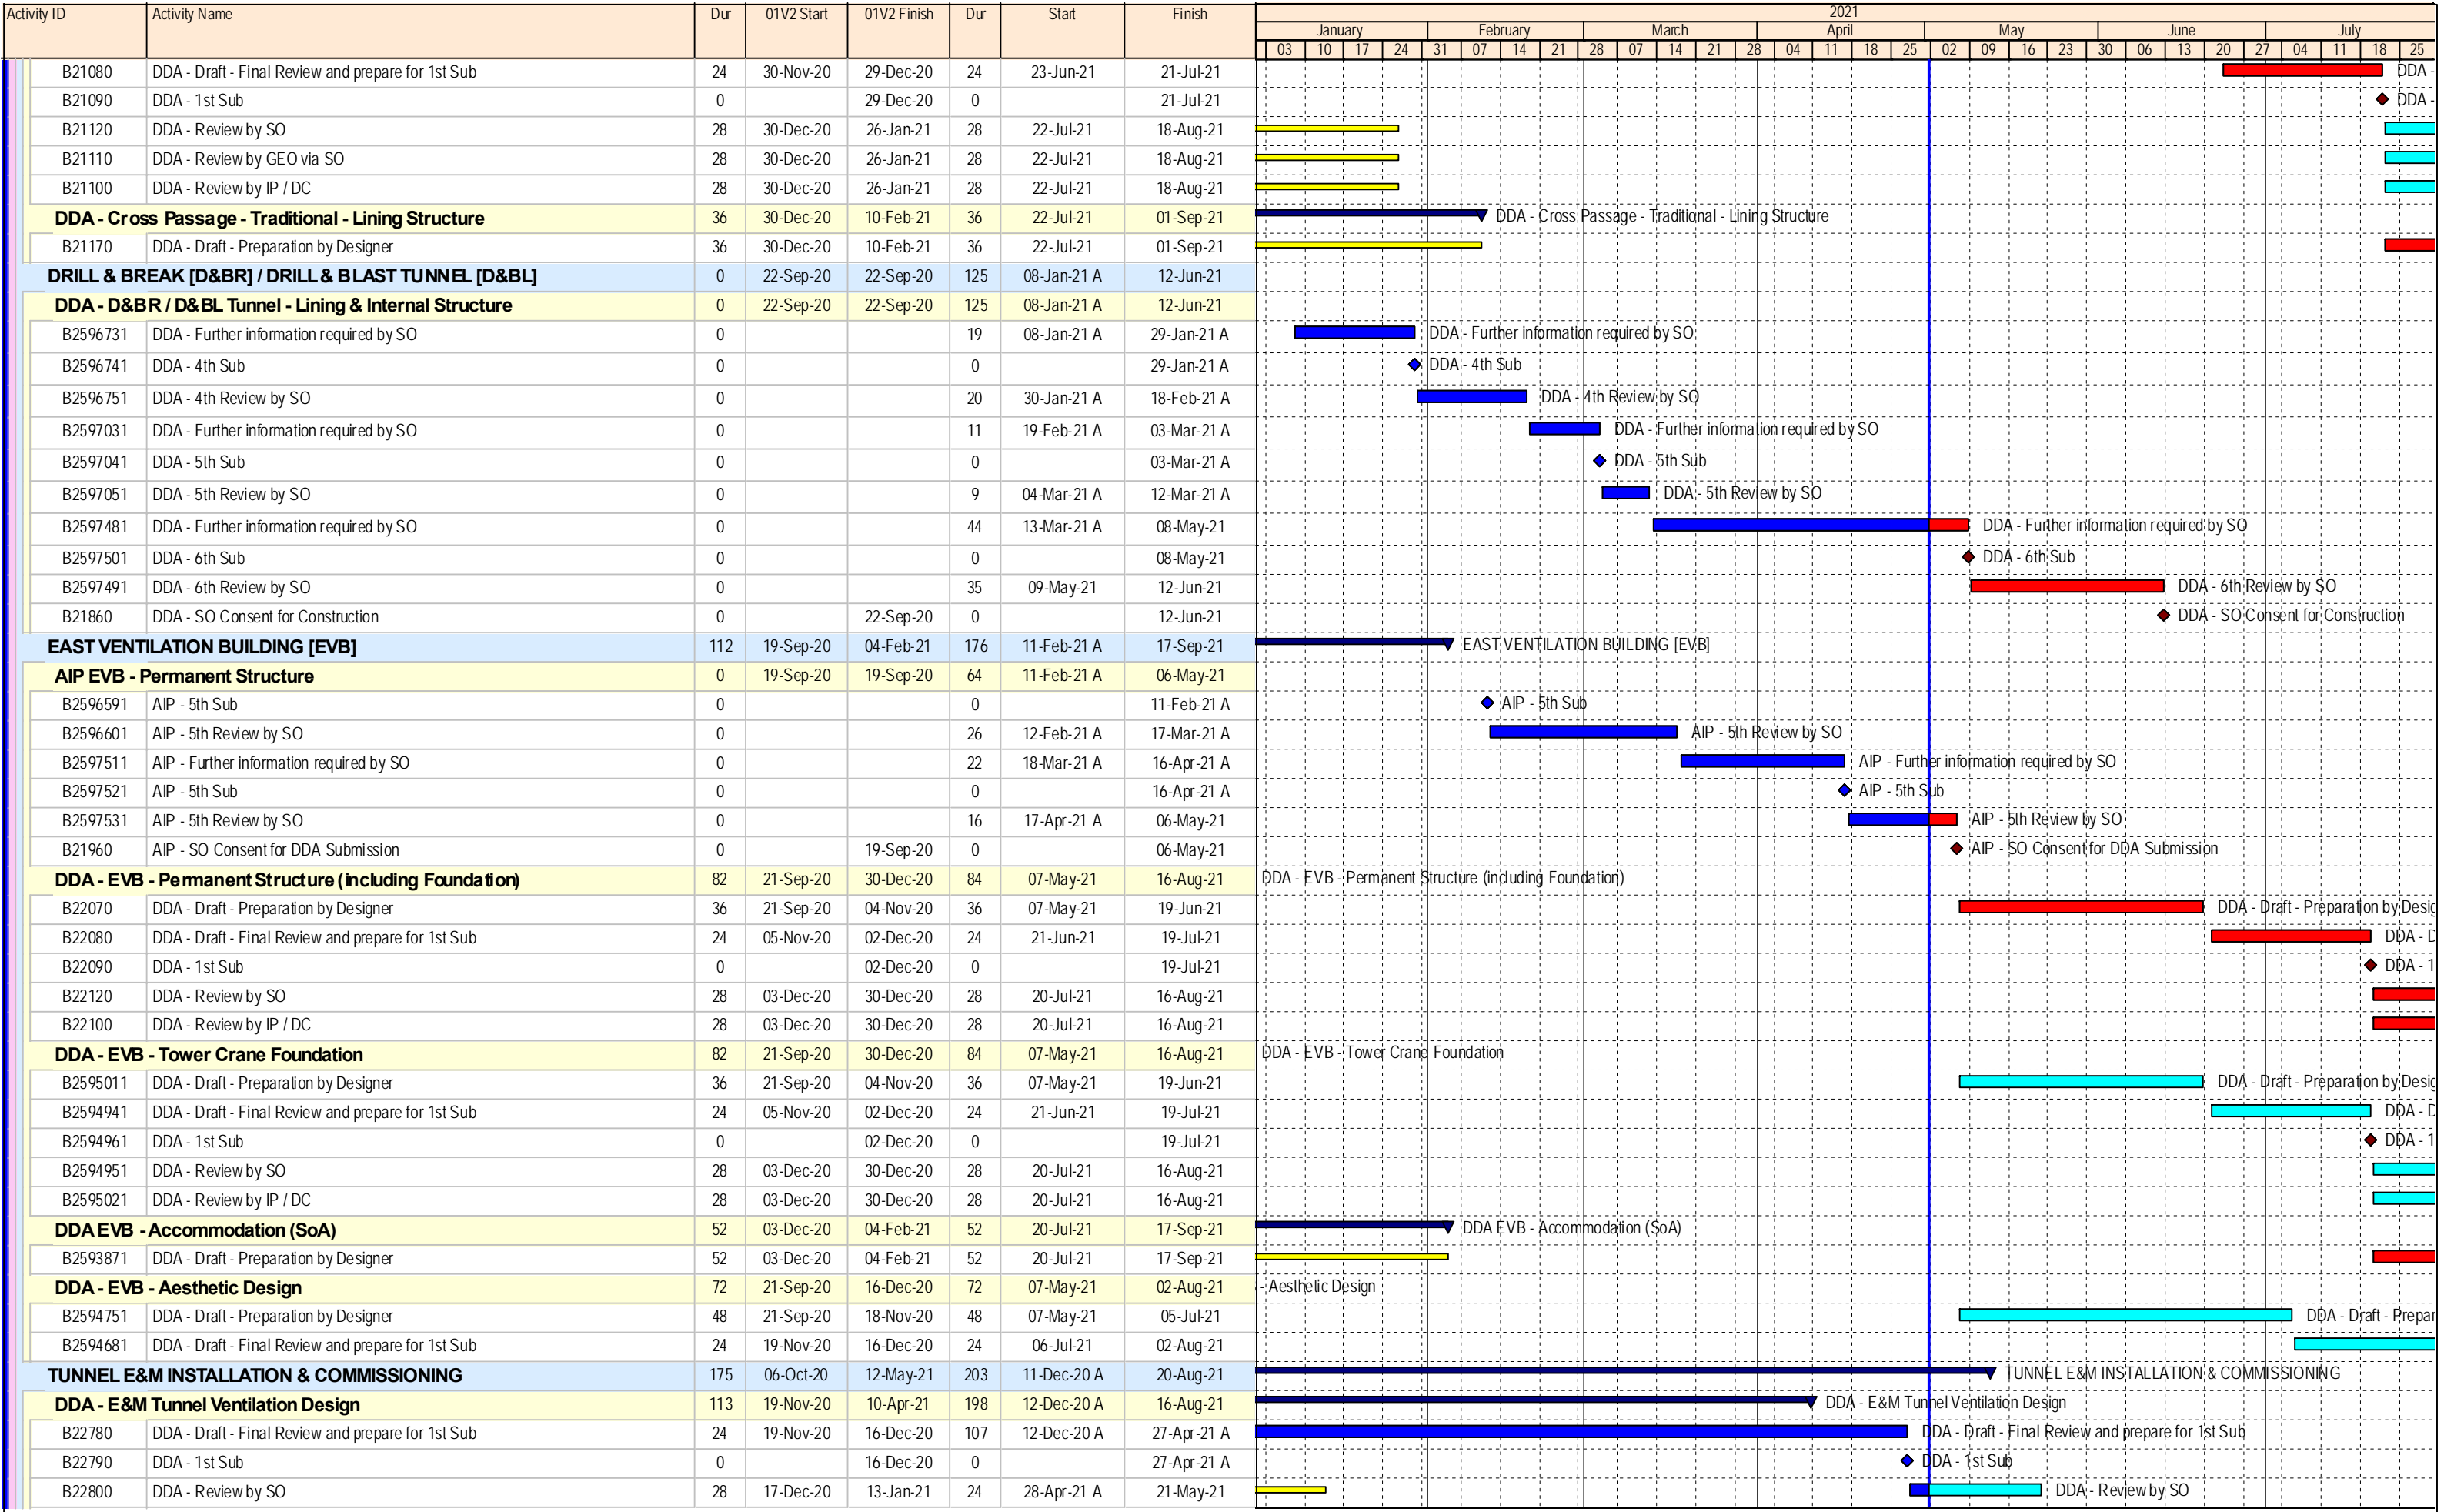

Page 11 of 25
Data Date: 01-May-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

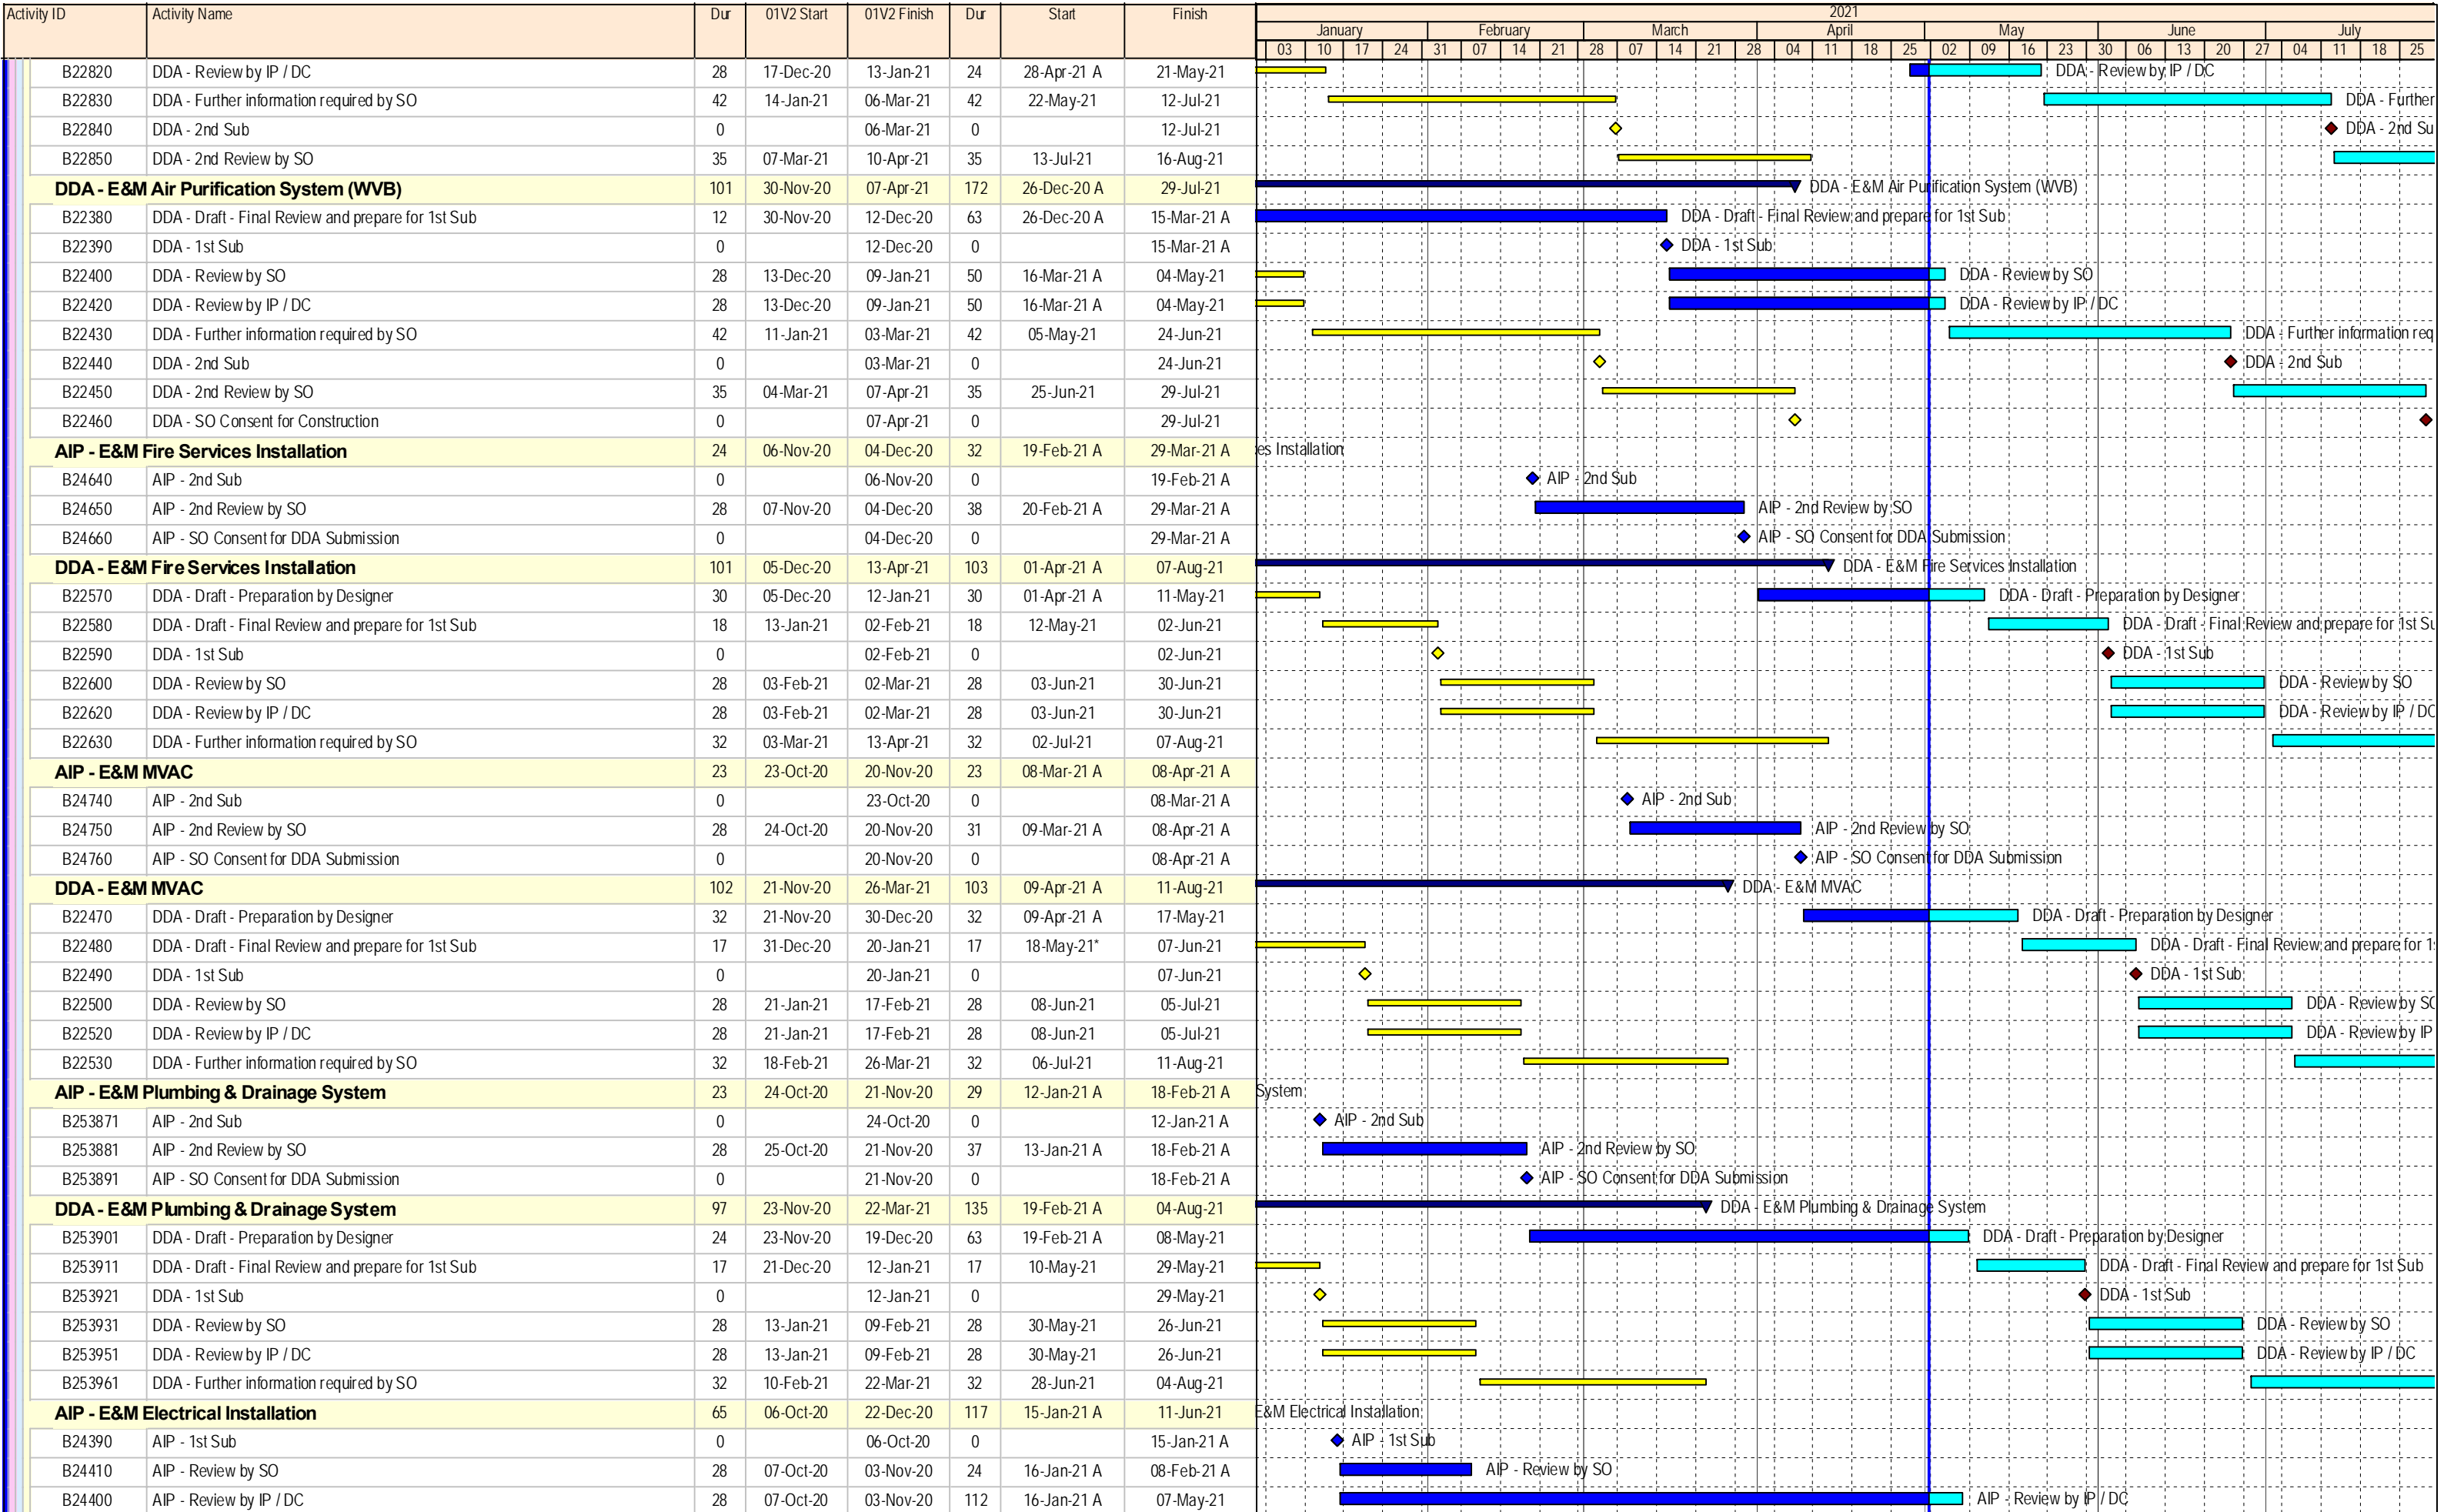

Page 12 of 25
Data Date: 01-May-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

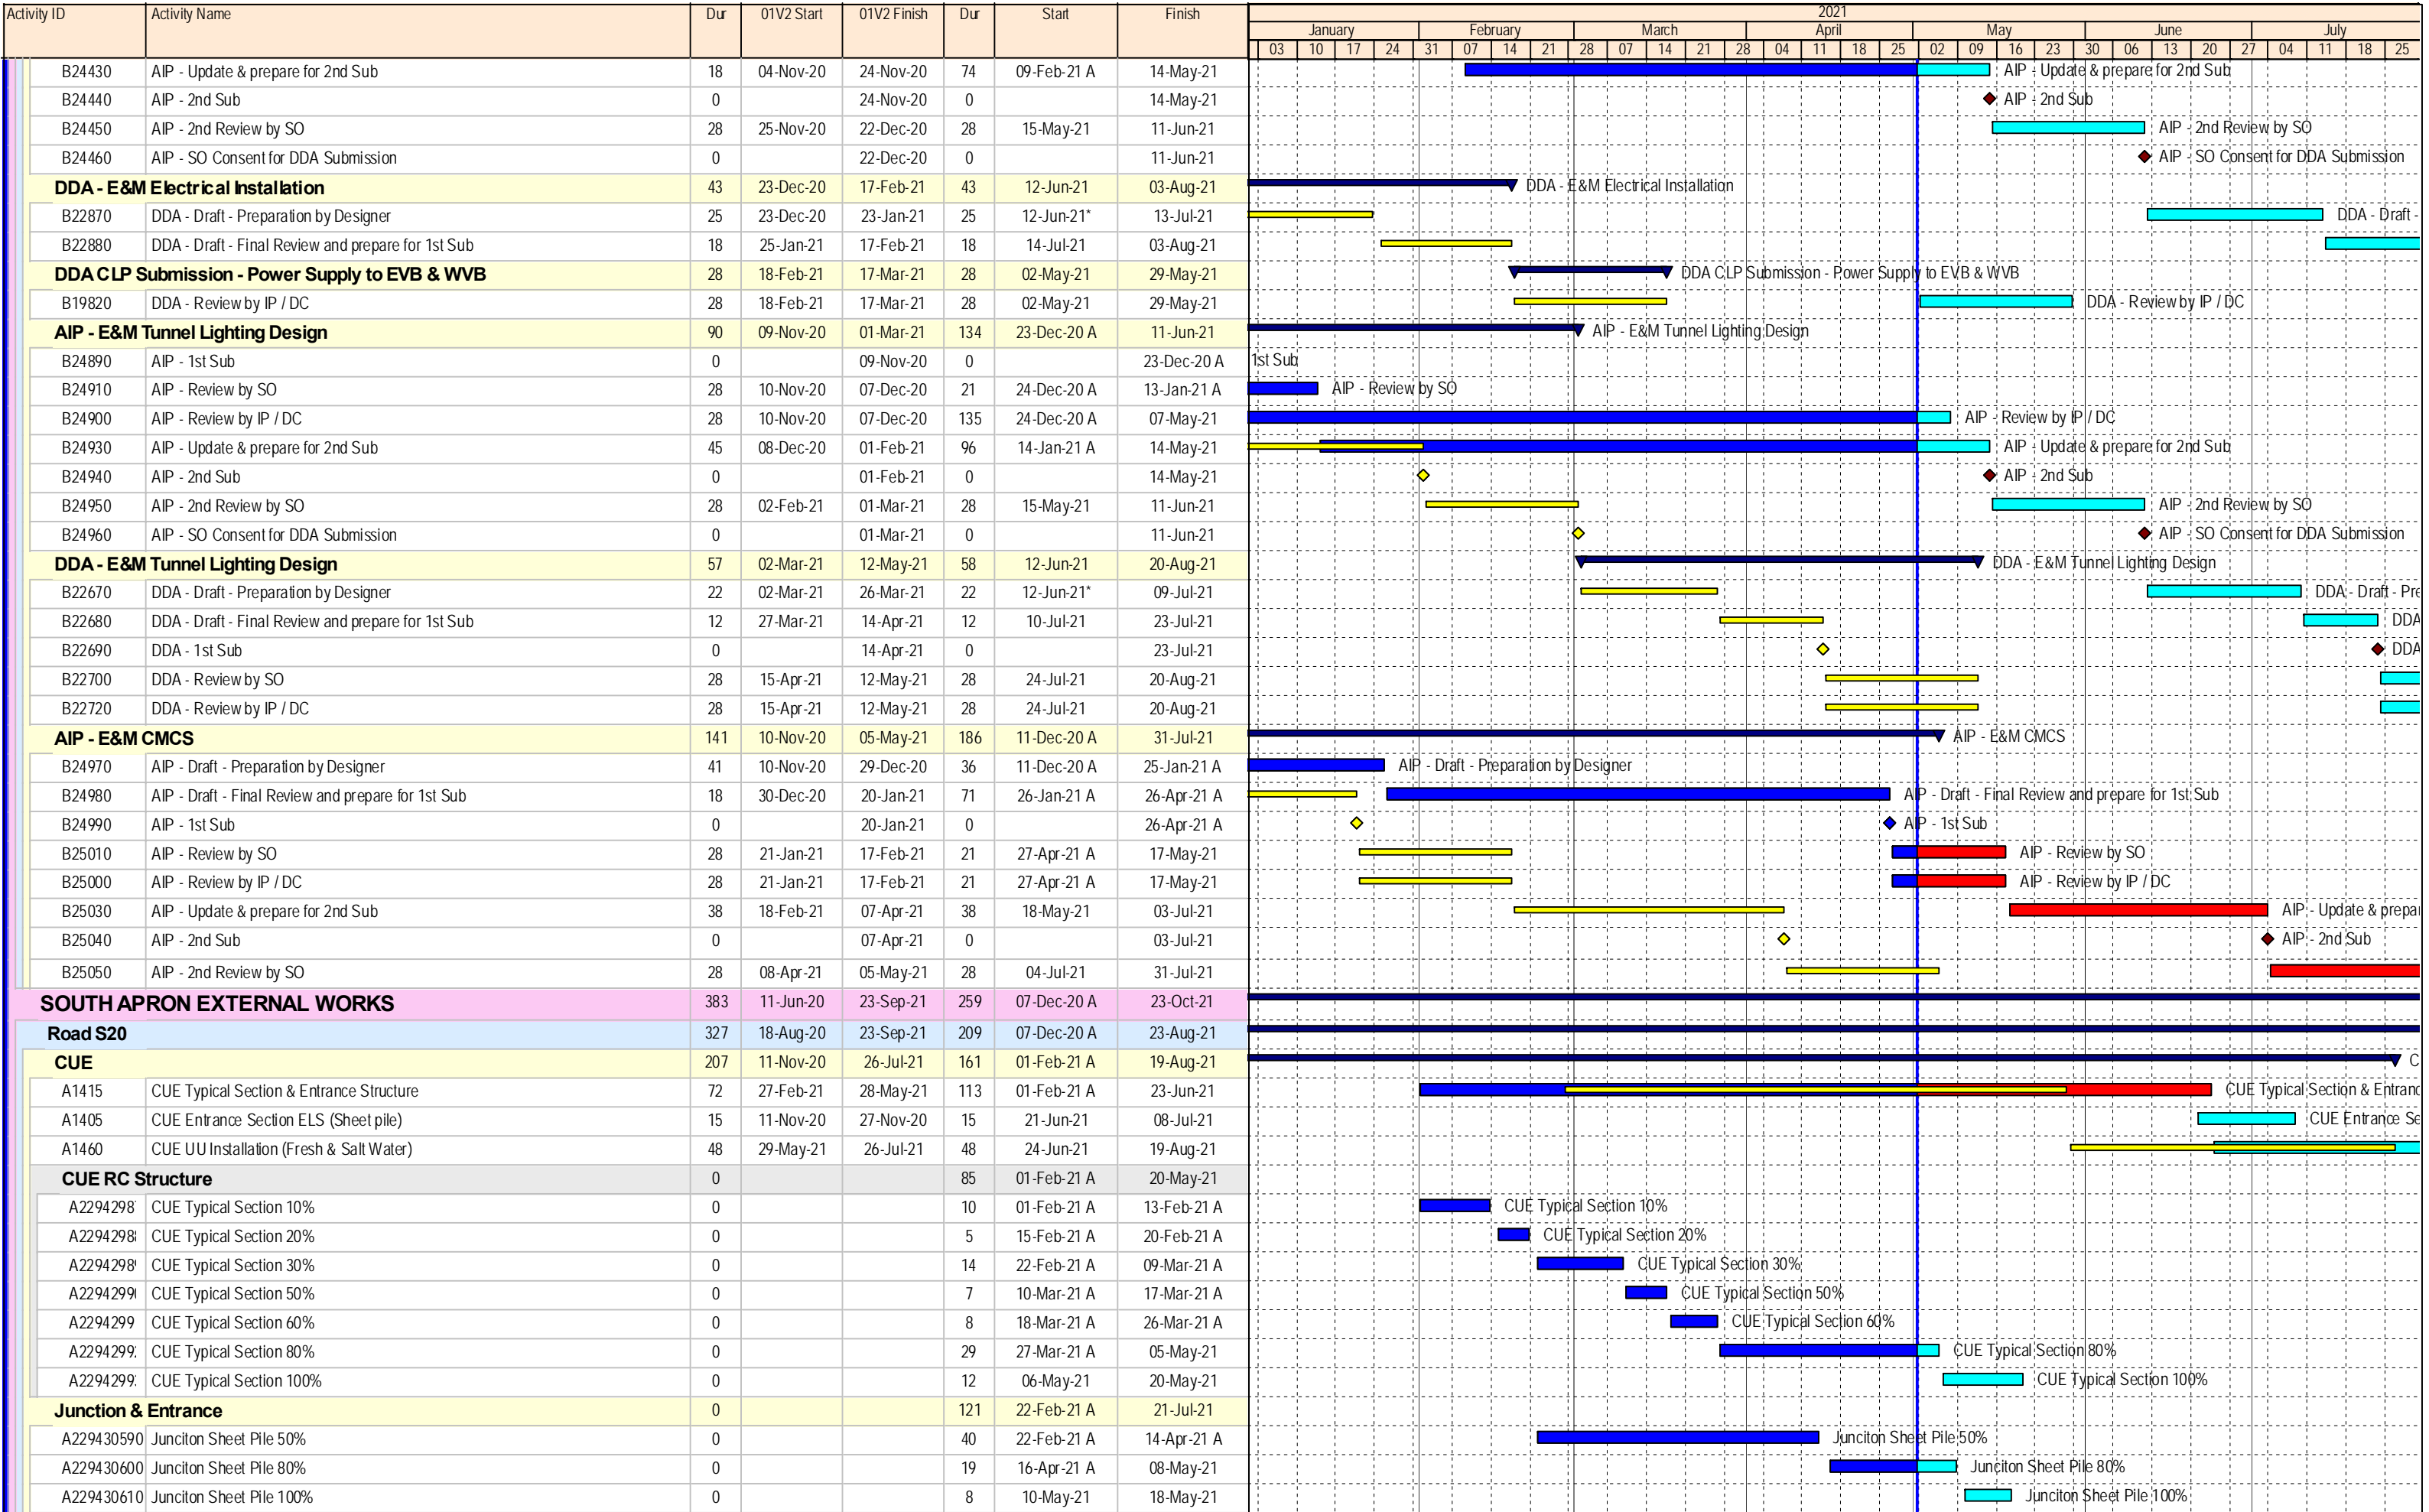

Page 13 of 25
Data Date: 01-May-21


- ◆ Milestone
- ▶ Summary
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

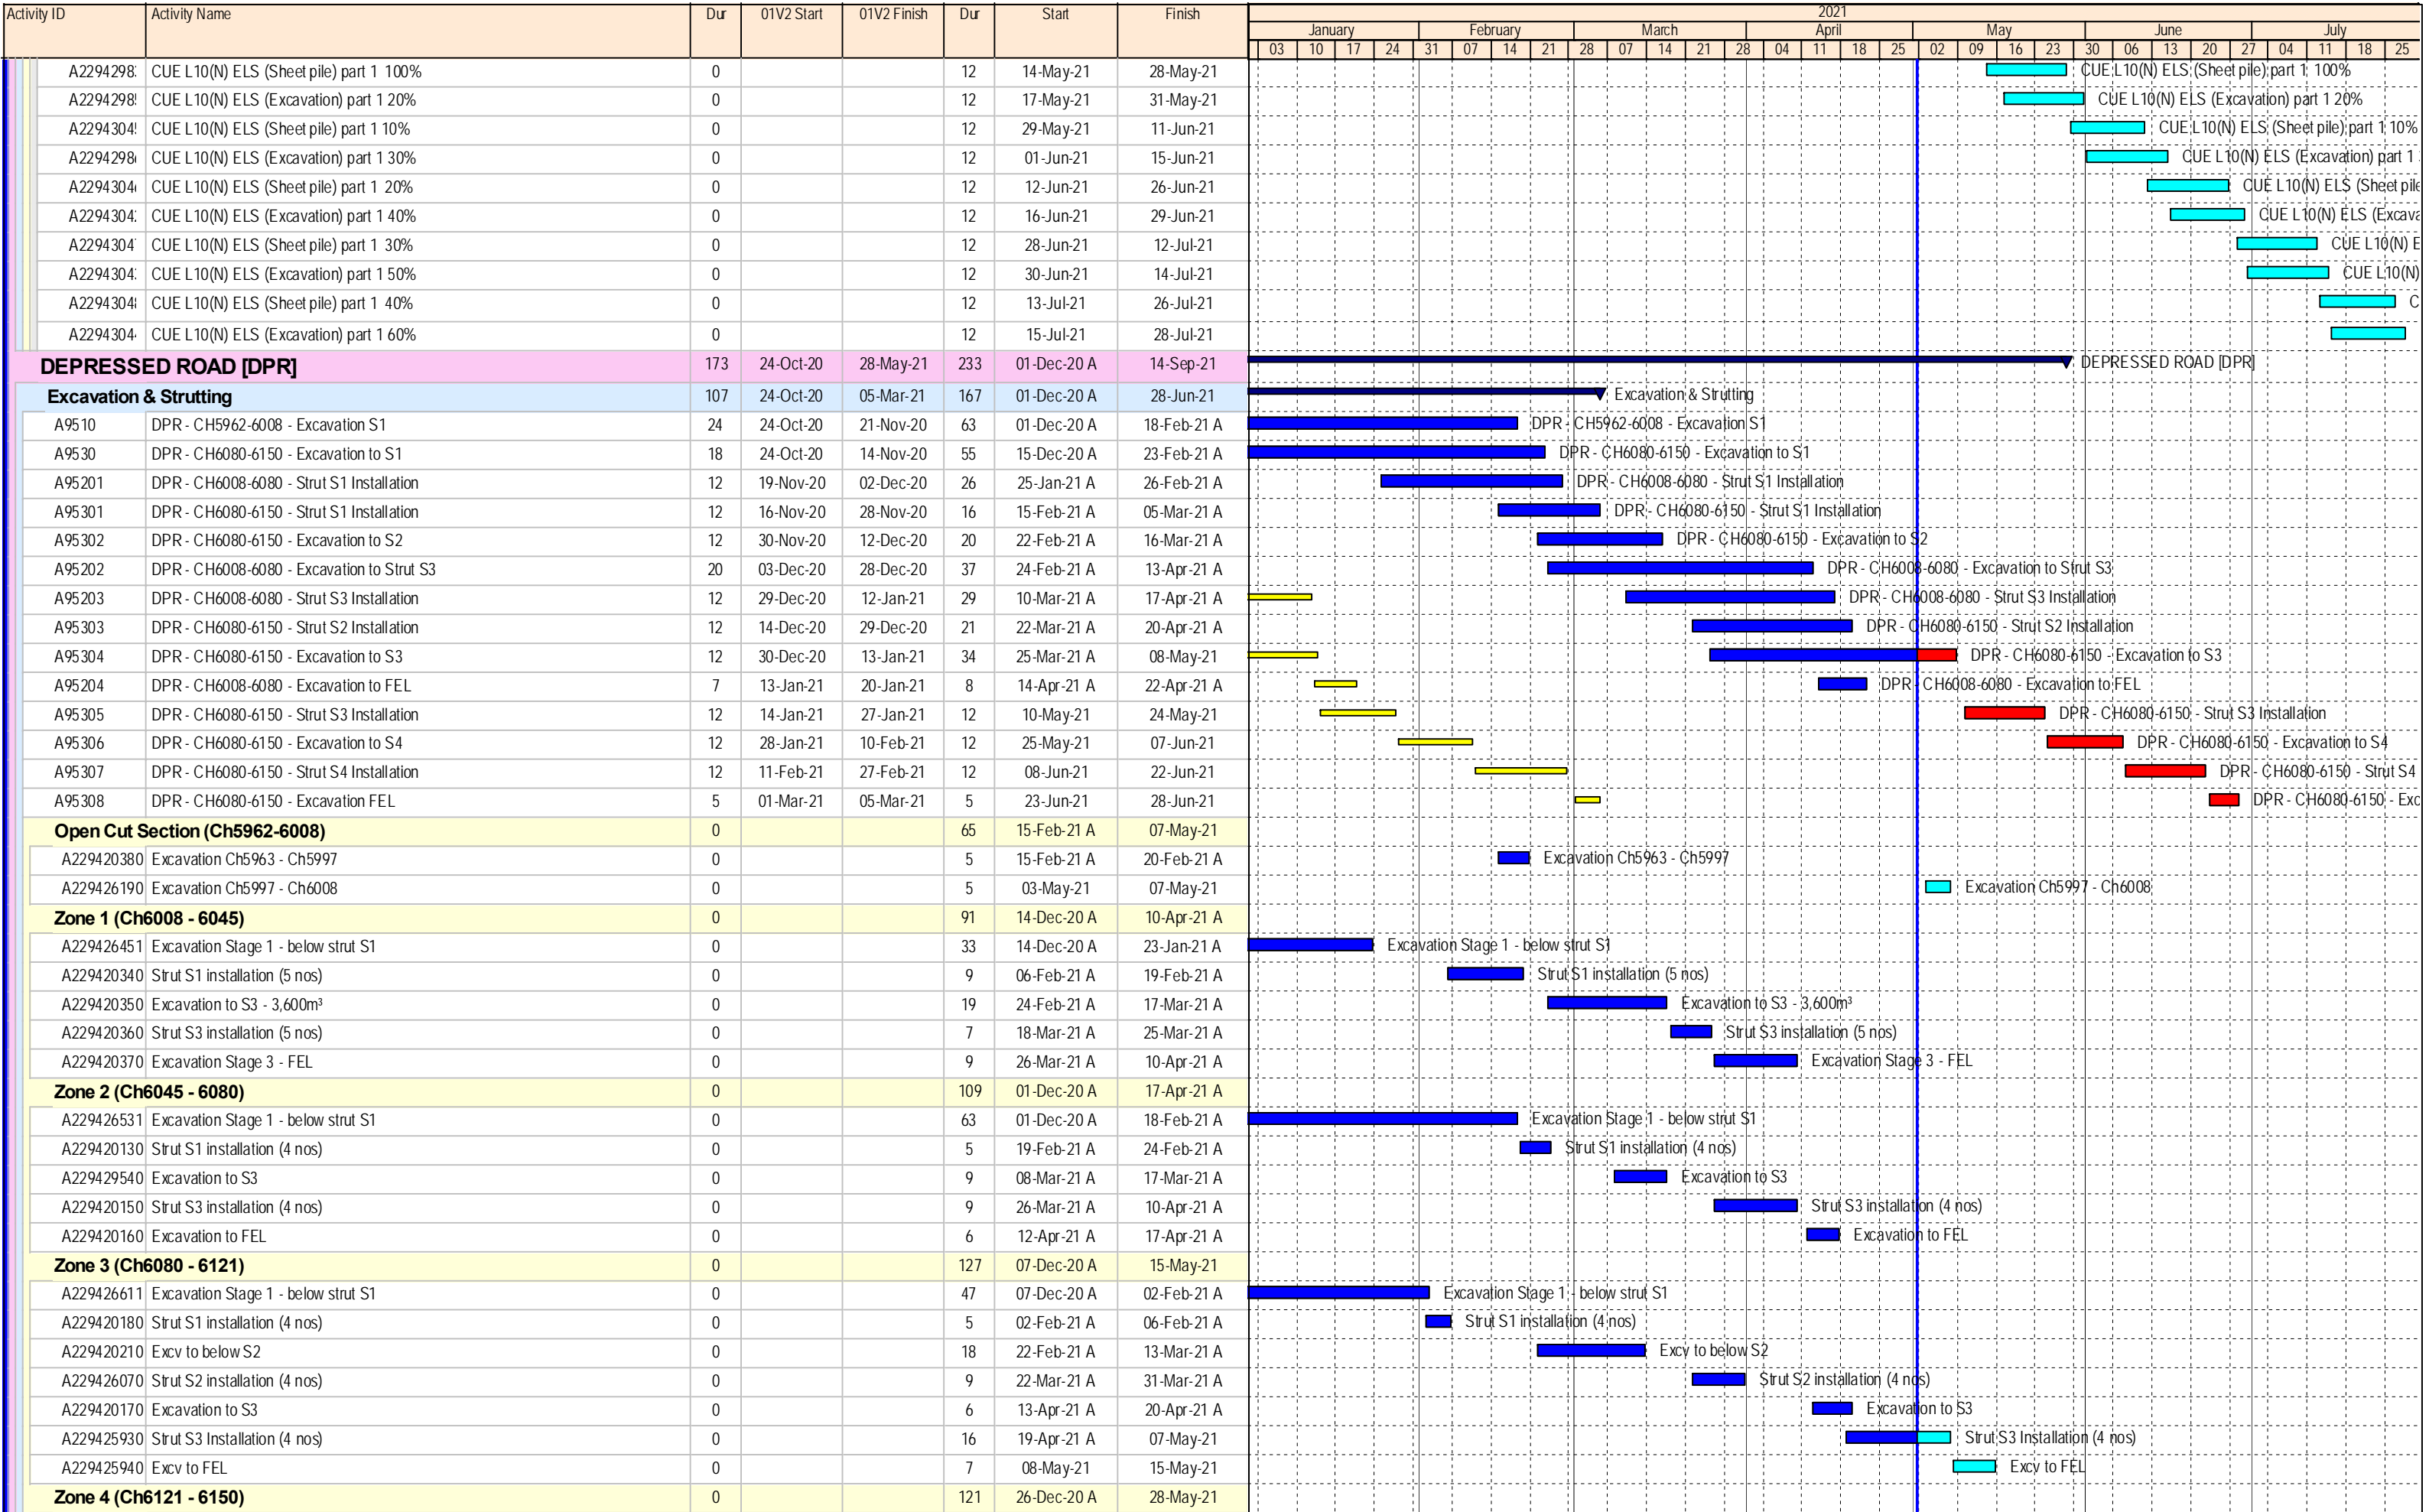


Page 16 of 25
Data Date: 01-May-21

- ◆ Milestone
- ◆ Summary
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


Three Months Rolling Programme (Apr-21)


Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

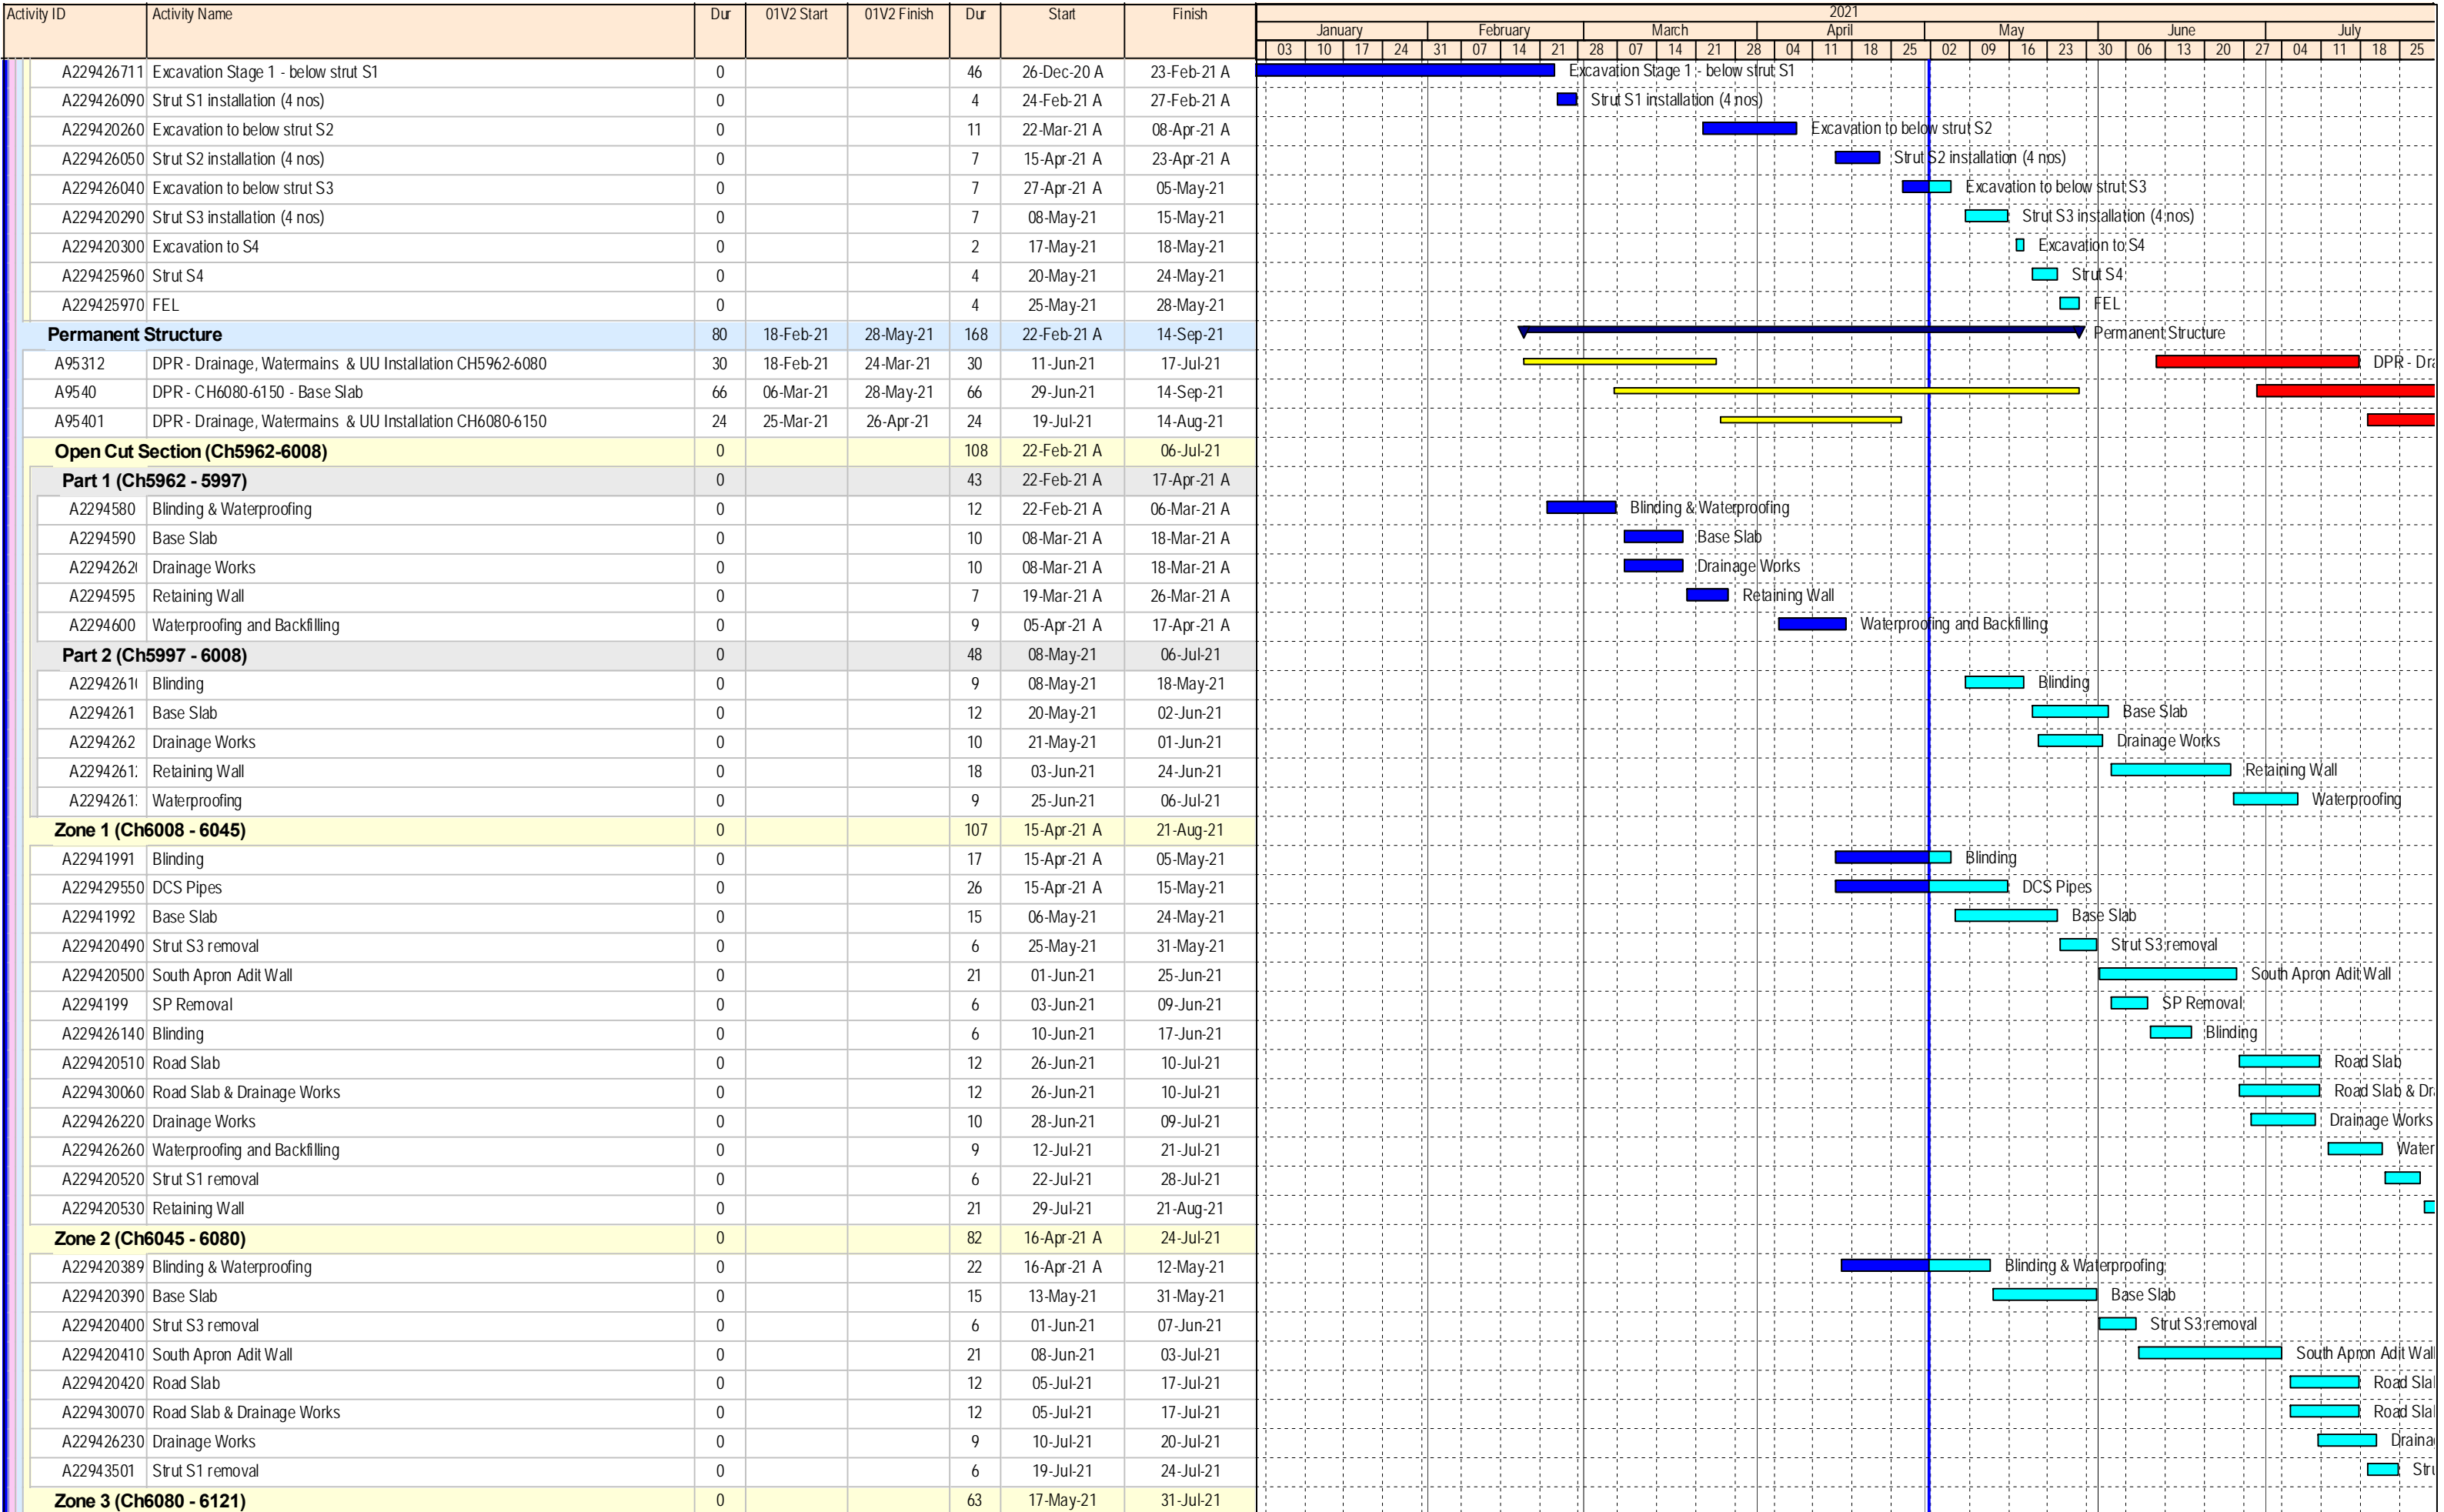

Page 17 of 25 Data Date: 01-May-21		<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme (Apr-21)</h3>		<table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>05-Nov-19</td> <td>00V0</td> <td>WYu</td> <td></td> </tr> <tr> <td>18-Dec-19</td> <td>00V1</td> <td>WYu</td> <td></td> </tr> <tr> <td>22-Feb-20</td> <td>01V0</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Apr-20</td> <td>01V1</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>17-Jul-20</td> <td>01V2</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Oct-20</td> <td>01V3</td> <td>SPa/LLo</td> <td>WYu</td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																													
05-Nov-19	00V0	WYu																														
18-Dec-19	00V1	WYu																														
22-Feb-20	01V0	SPa/LLo	WYu																													
09-Apr-20	01V1	SPa/LLo	WYu																													
17-Jul-20	01V2	SPa/LLo	WYu																													
09-Oct-20	01V3	SPa/LLo	WYu																													

Activity ID	Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2021																													
								January				February				March				April				May				June				July					
								03	10	17	24	31	07	14	21	28	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25
A114241	Formworks erection of Gantry Beam (WKK)	0			4	28-Dec-20 A	31-Dec-20 A	Formworks erection of Gantry Beam (WKK)																													
Overall		0			2	02-Jan-21 A	04-Jan-21 A																														
A114251	Pour 2 Concreting (WKK)	0			1	02-Jan-21 A	02-Jan-21 A	Pour 2 Concreting (WKK)																													
A114261	Pour 2 Formworks removal & CJ Cleaning (WKK & BTP)	0			1	04-Jan-21 A	04-Jan-21 A	Pour 2 Formworks removal & CJ Cleaning (WKK & BTP)																													
Pour 3 (Capping Beam & Strutting Slab S1) Part 2		0			14	05-Jan-21 A	21-Jan-21 A																														
South		0			2	05-Jan-21 A	06-Jan-21 A																														
A114433	ELS Removal at Zone C (DARWIN)	0			2	05-Jan-21 A	06-Jan-21 A	ELS Removal at Zone C (DARWIN)																													
Overall		0			13	06-Jan-21 A	21-Jan-21 A																														
A114281	Blinding Concrete (WKK)	0			2	06-Jan-21 A	07-Jan-21 A	Blinding Concrete (WKK)																													
A229421	Backfilling & Formation	0			2	08-Jan-21 A	09-Jan-21 A	Backfilling & Formation																													
A114291	Steel Fixing Pour 3 (BP)	0			4	11-Jan-21 A	14-Jan-21 A	Steel Fixing Pour 3 (BP)																													
A114311	Pour 3 Concreting (WKK)	0			1	15-Jan-21 A	15-Jan-21 A	Pour 3 Concreting (WKK)																													
A114441	Concrete Strength Gain	0			3	16-Jan-21 A	18-Jan-21 A	Concrete Strength Gain																													
A114451	Cut & Cover Bulk Excavation Start	0			0	21-Jan-21 A		Cut & Cover Bulk Excavation Start																													
Cut & Cover Bulk Excavation		0			140	21-Jan-21 A	15-Jul-21																														
A2294283	Excavation to below S2	0			15	21-Jan-21 A	04-Feb-21 A	Excavation to below S2																													
A2294283	Strut S2 Construction	0			9	05-Feb-21 A	13-Feb-21 A	Strut S2 Construction																													
A2294283	Excavation to below S3	0			8	16-Feb-21 A	23-Feb-21 A	Excavation to below S3																													
A2294283	Strut S3 Construction	0			10	24-Feb-21 A	05-Mar-21 A	Strut S3 Construction																													
A2294283	Excavation to below S4	0			10	09-Mar-21 A	19-Mar-21 A	Excavation to below S4																													
A2294286	Permanent Strutting Slab S4	0			20	20-Mar-21 A	17-Apr-21 A	Permanent Strutting Slab S4																													
A2294289	Excavation to below S5	0			15	20-Apr-21 A	07-May-21	Excavation to below S5																													
A2294289	Steel Strut S5	0			10	08-May-21	20-May-21	Steel Strut S5																													
A2294289	Excavation to below S6	0			9	21-May-21	31-May-21	Excavation to below S6																													
A2294295	Steel Strut S6	0			10	01-Jun-21	11-Jun-21	Steel Strut S6																													
A2294295	Excavation to FEL	0			9	12-Jun-21	23-Jun-21	Excavation to FEL																													
A2294301	Barrette Trimming	0			9	24-Jun-21	05-Jul-21	Barrette Trimming																													
A2294301	Base Slab Construction 50%	0			9	06-Jul-21	15-Jul-21	Base Slab																													
Launching Shaft ELS		0			142	02-Dec-20 A	29-May-21																														
Capping Beam		0			59	02-Dec-20 A	12-Feb-21 A																														
Cell 2		0			49	02-Dec-20 A	31-Jan-21 A																														
Pour 4 (South)		0			17	25-Dec-20 A	16-Jan-21 A																														
A229421	ELS Walling & Struts for Pour 4,5 & 6	0			3	25-Dec-20 A	30-Dec-20 A	ELS Walling & Struts for Pour 4,5 & 6																													
A113311	Dwall Breaking	0			6	31-Dec-20 A	07-Jan-21 A	Dwall Breaking																													
A113321	Trimming	0			2	08-Jan-21 A	09-Jan-21 A	Trimming																													
A113331	Blinding concrete	0			1	09-Jan-21 A	09-Jan-21 A	Blinding concrete																													
A113341	Steel Fixing	0			3	11-Jan-21 A	13-Jan-21 A	Steel Fixing																													
A113351	Formworks Erection	0			2	14-Jan-21 A	15-Jan-21 A	Formworks Erection																													
A229421	Concrete	0			1	16-Jan-21 A	16-Jan-21 A	Concrete																													
Pour 5 (North)		0			31	02-Dec-20 A	09-Jan-21 A																														
A229421	Excavation & GW Breaking	0			18	02-Dec-20 A	22-Dec-20 A	Excavation & GW Breaking																													
A229421	Dwall Breaking / Trimming	0			6	23-Dec-20 A	31-Dec-20 A	Dwall Breaking / Trimming																													
A229421	Blinding concrete	0			1	02-Jan-21 A	02-Jan-21 A	Blinding concrete																													
A229421	Steel Fixing	0			4	04-Jan-21 A	07-Jan-21 A	Steel Fixing																													
A229421	Formworks Erection	0			2	07-Jan-21 A	08-Jan-21 A	Formworks Erection																													
A229421	Concrete	0			1	09-Jan-21 A	09-Jan-21 A	Concrete																													
Gantry Beam South		0			25	02-Jan-21 A	31-Jan-21 A																														
A113951	Dwall Breaking / Trimming	0			12	02-Jan-21 A	15-Jan-21 A	Dwall Breaking / Trimming																													
A113961	Hand Trimming & Blinding	0			3	16-Jan-21 A	19-Jan-21 A	Hand Trimming & Blinding																													
A113971	Steel Fixing	0			4	20-Jan-21 A	23-Jan-21 A	Steel Fixing																													
A113981	Formworks Erection	0			3	25-Jan-21 A	27-Jan-21 A	Formworks Erection																													

Page 20 of 25 Data Date: 01-May-21	<ul style="list-style-type: none"> ◆ Milestone ▬ Planned Bar ▬ Critical Activity ◆ Actual Milestone ▬ Actual Work ◆ Baseline Milestone ▬ Baseline Bar 	<p style="text-align: center;"> ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme (Apr-21) </p>		<table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>05-Nov-19</td> <td>00V0</td> <td>WYu</td> <td></td> </tr> <tr> <td>18-Dec-19</td> <td>00V1</td> <td>WYu</td> <td></td> </tr> <tr> <td>22-Feb-20</td> <td>01V0</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Apr-20</td> <td>01V1</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>17-Jul-20</td> <td>01V2</td> <td>SPa/LLo</td> <td>WYu</td> </tr> <tr> <td>09-Oct-20</td> <td>01V3</td> <td>SPa/LLo</td> <td>WYu</td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																													
05-Nov-19	00V0	WYu																														
18-Dec-19	00V1	WYu																														
22-Feb-20	01V0	SPa/LLo	WYu																													
09-Apr-20	01V1	SPa/LLo	WYu																													
17-Jul-20	01V2	SPa/LLo	WYu																													
09-Oct-20	01V3	SPa/LLo	WYu																													

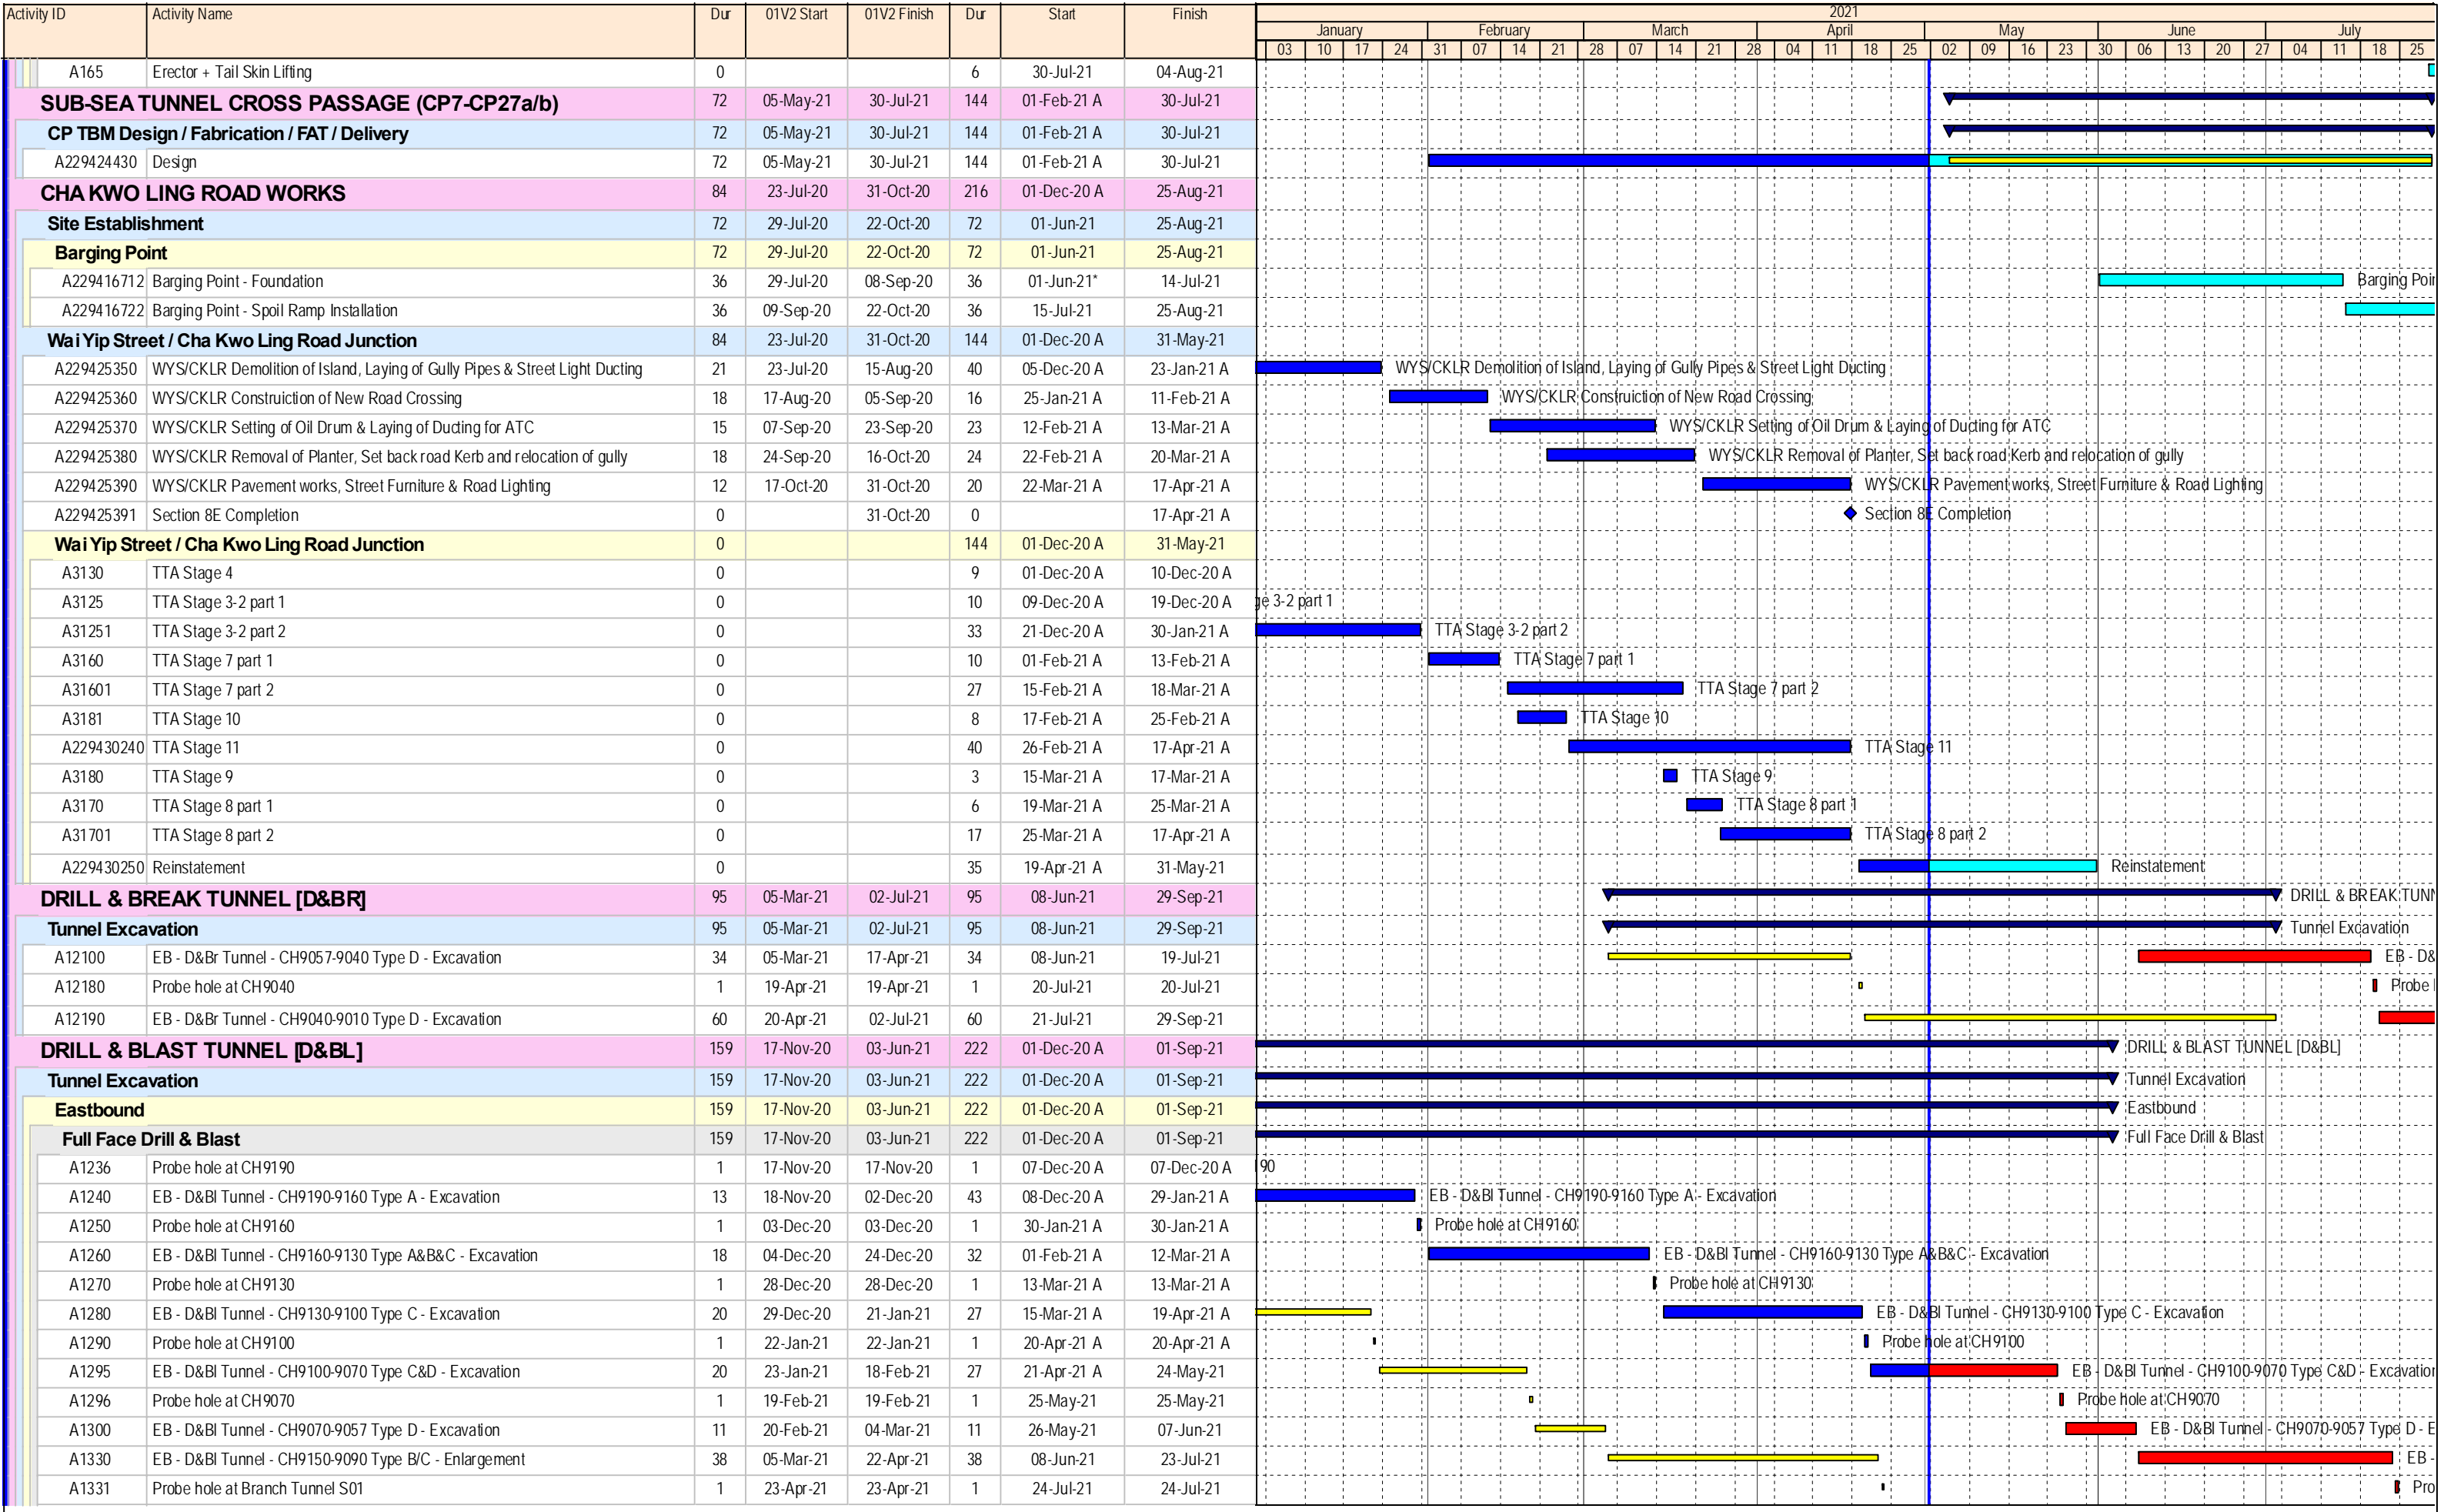

Page 24 of 25
Data Date: 01-May-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Apr-21)



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu

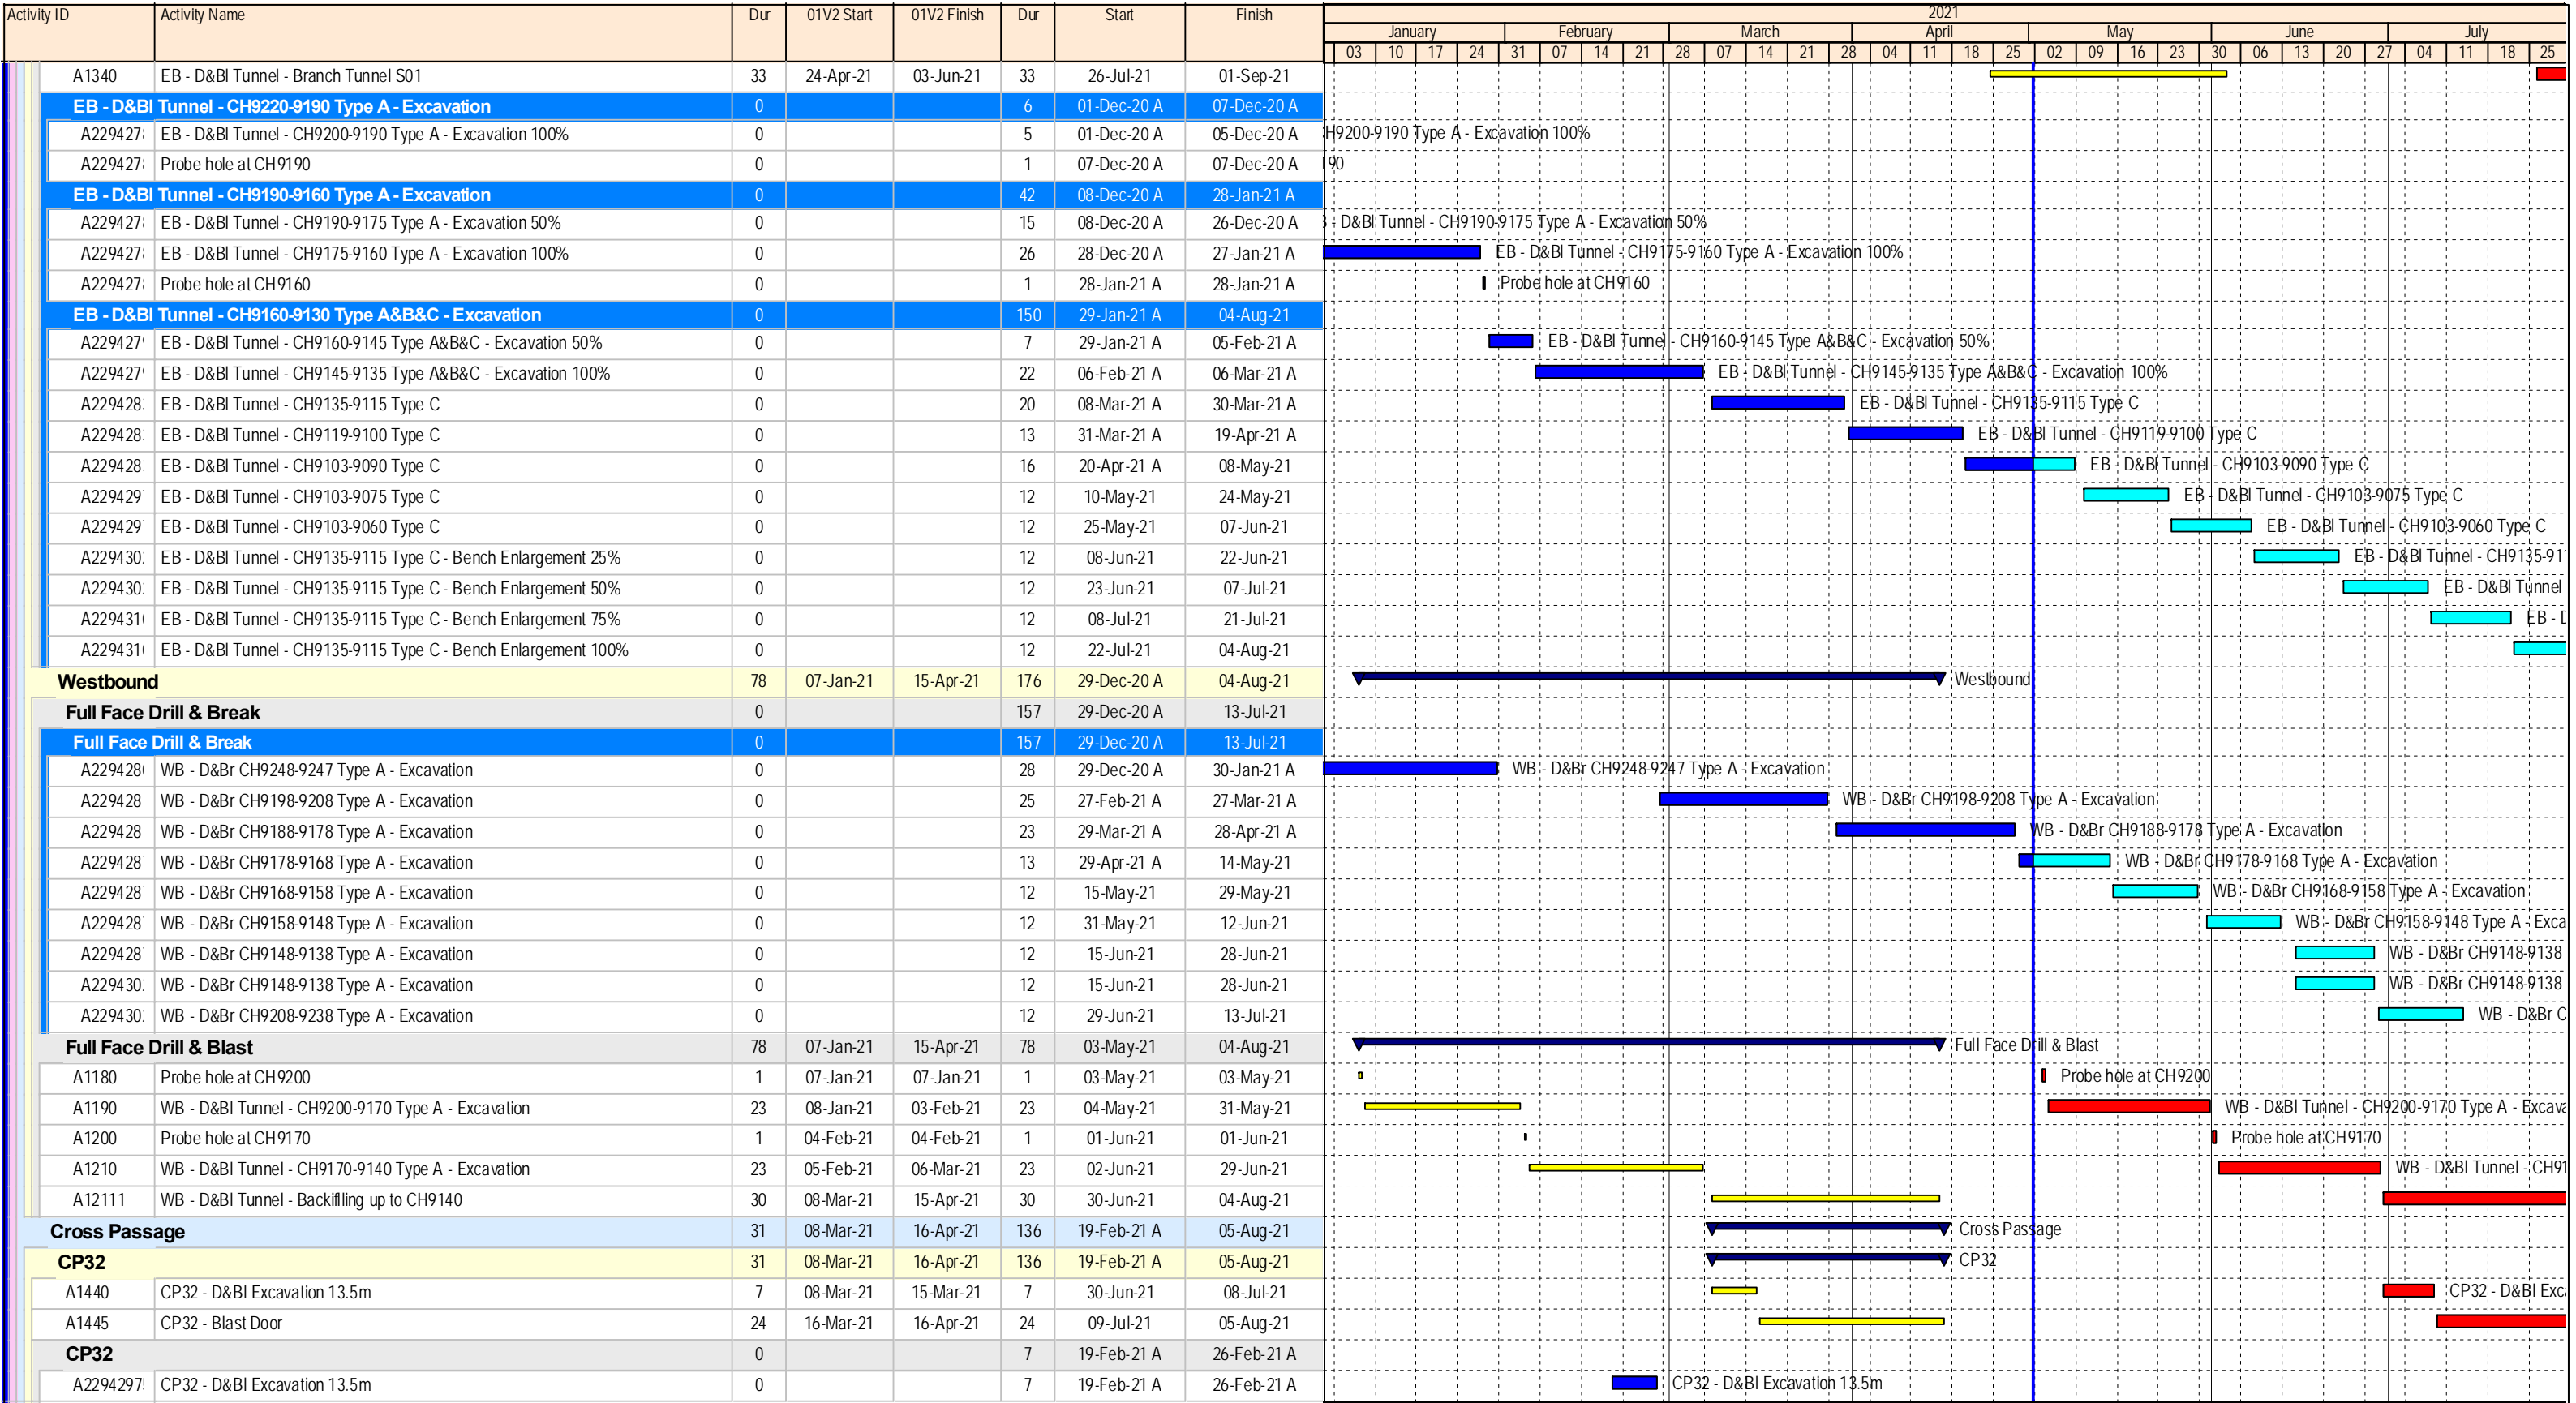

Page 25 of 25 Data Date: 01-May-21	<ul style="list-style-type: none"> Milestone Planned Bar Critical Activity Actual Milestone Actual Work Baseline Milestone Baseline Bar 	<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme (Apr-21)</h3>		Date	Revision	Checked	Approved	05-Nov-19	00V0	WYu		18-Dec-19	00V1	WYu		22-Feb-20	01V0	SPa/LLo	WYu	09-Apr-20	01V1	SPa/LLo	WYu	17-Jul-20	01V2	SPa/LLo	WYu	09-Oct-20	01V3	SPa/LLo	WYu
Date	Revision	Checked	Approved																												
05-Nov-19	00V0	WYu																													
18-Dec-19	00V1	WYu																													
22-Feb-20	01V0	SPa/LLo	WYu																												
09-Apr-20	01V1	SPa/LLo	WYu																												
17-Jul-20	01V2	SPa/LLo	WYu																												
09-Oct-20	01V3	SPa/LLo	WYu																												
