

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021												2022																							
						October				November				December				January			February			March			April			May											
						03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15	22	29	
<b>ED/2018/04 - Trunk Road T2</b>	1360	30-Sep-20	28-Feb-25	27-Oct-20 A	12-Feb-23																																				
<b>DESIGN SUBMISSION &amp; APPROVAL</b>	335	03-Oct-20	19-Sep-22	15-Mar-21 A	21-Jun-22																																				
<b>GENERAL</b>	208	22-Jan-21	20-Dec-21	30-Jun-21 A	12-Mar-22	GENERAL																																			
<b>AIP Roadworks and Street Furniture</b>	87	16-Feb-21	16-Feb-21	30-Jun-21 A	05-Oct-21 A																																				
AIP - Further information required by SO	24			30-Jun-21 A	07-Sep-21 A	ation required by SO																																			
AIP - 5th Sub	0				07-Sep-21 A																																				
AIP - 5th Review by SO	28			08-Sep-21 A	05-Oct-21 A	AIP - 5th Review by SO																																			
AIP - SO Consent for DDA Submission	0		16-Feb-21		05-Oct-21 A	AIP - SO Consent for DDA Submission																																			
<b>DDA Roadworks and Street Furniture</b>	150	19-Jul-21	19-Jul-21	09-Jul-21 A	02-Dec-21 A																																				
DDA - Further information required by SO	24			09-Jul-21 A	23-Oct-21 A	DDA - Further information required by SO																																			
DDA - 3rd Sub	0				23-Oct-21 A	DDA - 3rd Sub																																			
DDA - 3rd Review by SO	35			25-Oct-21 A	02-Dec-21 A	DDA - 3rd Review by SO																																			
DDA - SO Consent for DDA Submission	0		19-Jul-21		02-Dec-21 A	DDA - SO Consent for DDA Submission																																			
<b>DDA Traffic Sign, Road Marking &amp; Sign Gantry</b>	79	20-Dec-21	20-Dec-21	09-Jul-21 A	02-Dec-21 A	DDA Traffic Sign, Road Marking & Sign Gantry																																			
DDA - Further information required by SO	24			09-Jul-21 A	23-Oct-21 A	DDA - Further information required by SO																																			
DDA - 3rd Sub	0				23-Oct-21 A	DDA - 3rd Sub																																			
DDA - 3rd Review by SO	35			25-Oct-21 A	02-Dec-21 A	DDA - 3rd Review by SO																																			
DDA - SO Consent for Construction	0		20-Dec-21		02-Dec-21 A	DDA - SO Consent for Construction																																			
<b>DDA Street Lighting (AGR/ DPR/ S20/ L10/ L18)</b>	197	22-Jan-21	22-Jan-21	16-Jul-21 A	12-Mar-22																																				
DDA - Further information required by SO	12			16-Jul-21 A	07-Sep-21 A	ation required by SO																																			
DDA - 5th Sub	0				07-Sep-21 A																																				
DDA - 5th Review by SO	35			08-Sep-21 A	29-Sep-21 A	DDA - 5th Review by SO																																			
DDA - Further information required by SO	12			30-Sep-21 A	02-Nov-21 A	DDA - Further information required by SO																																			
DDA - 6th Sub	0				02-Nov-21 A	DDA - 6th Sub																																			
DDA - 6th Review by SO	35			03-Nov-21 A	24-Nov-21 A	DDA - 6th Review by SO																																			
DDA - Further information required by SO	12			25-Nov-21 A	21-Dec-21 A	DDA - Further information required by SO																																			
DDA - 7th Sub	0				21-Dec-21 A	DDA - 7th Sub																																			
DDA - 7th Review by SO	35			22-Dec-21 A	07-Jan-22 A	DDA - 7th Review by SO																																			
DDA - Further information required by SO	12			08-Jan-22 A	27-Jan-22 A	DDA - Further information required by SO																																			
DDA - 8th Sub	0				27-Jan-22 A	DDA - 8th Sub																																			
DDA - 8th Review by SO	35			28-Jan-22 A	12-Mar-22	DDA - 8th Review by SO																																			
DDA - SO Consent for DDA Submission	0		22-Jan-21		12-Mar-22	DDA - SO Consent for DDA Submission																																			
<b>DDA Landscape Design</b>	114	22-Apr-21	22-Jul-21	29-Jul-21 A	09-Feb-22																																				
DDA - Review by SO	28	22-Apr-21	19-May-21	29-Jul-21 A	09-Sep-21 A	SO																																			
DDA - Review by IP / DC	28	22-Apr-21	19-May-21	29-Jul-21 A	14-Sep-21 A	by IP / DC																																			
DDA - Further information required by SO	24	20-May-21	17-Jun-21	10-Sep-21 A	05-Jan-22 A	DDA - Further information required by SO																																			
DDA - 2nd Sub	0		17-Jun-21		05-Jan-22 A	DDA - 2nd Sub																																			
DDA - 2nd Review by SO	35	18-Jun-21	22-Jul-21	06-Jan-22 A	09-Feb-22	DDA - 2nd Review by SO																																			
DDA - SO Consent for Construction	0		22-Jul-21		09-Feb-22	DDA - SO Consent for Construction																																			
<b>DEPRESSED ROAD [DPR]</b>	183	07-Nov-20	19-Feb-21	29-May-21 A	11-Feb-22																																				
<b>DDA DPR - Portal Structure</b>	183	07-Nov-20	19-Feb-21	29-May-21 A	11-Feb-22																																				
DDA - Draft - Final Review and prepare for 1st Sub	24	07-Nov-20	04-Dec-20	29-May-21 A	08-Sep-21 A	Review and prepare for 1st Sub																																			
DDA - 1st Sub	0		04-Dec-20		08-Sep-21 A																																				


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

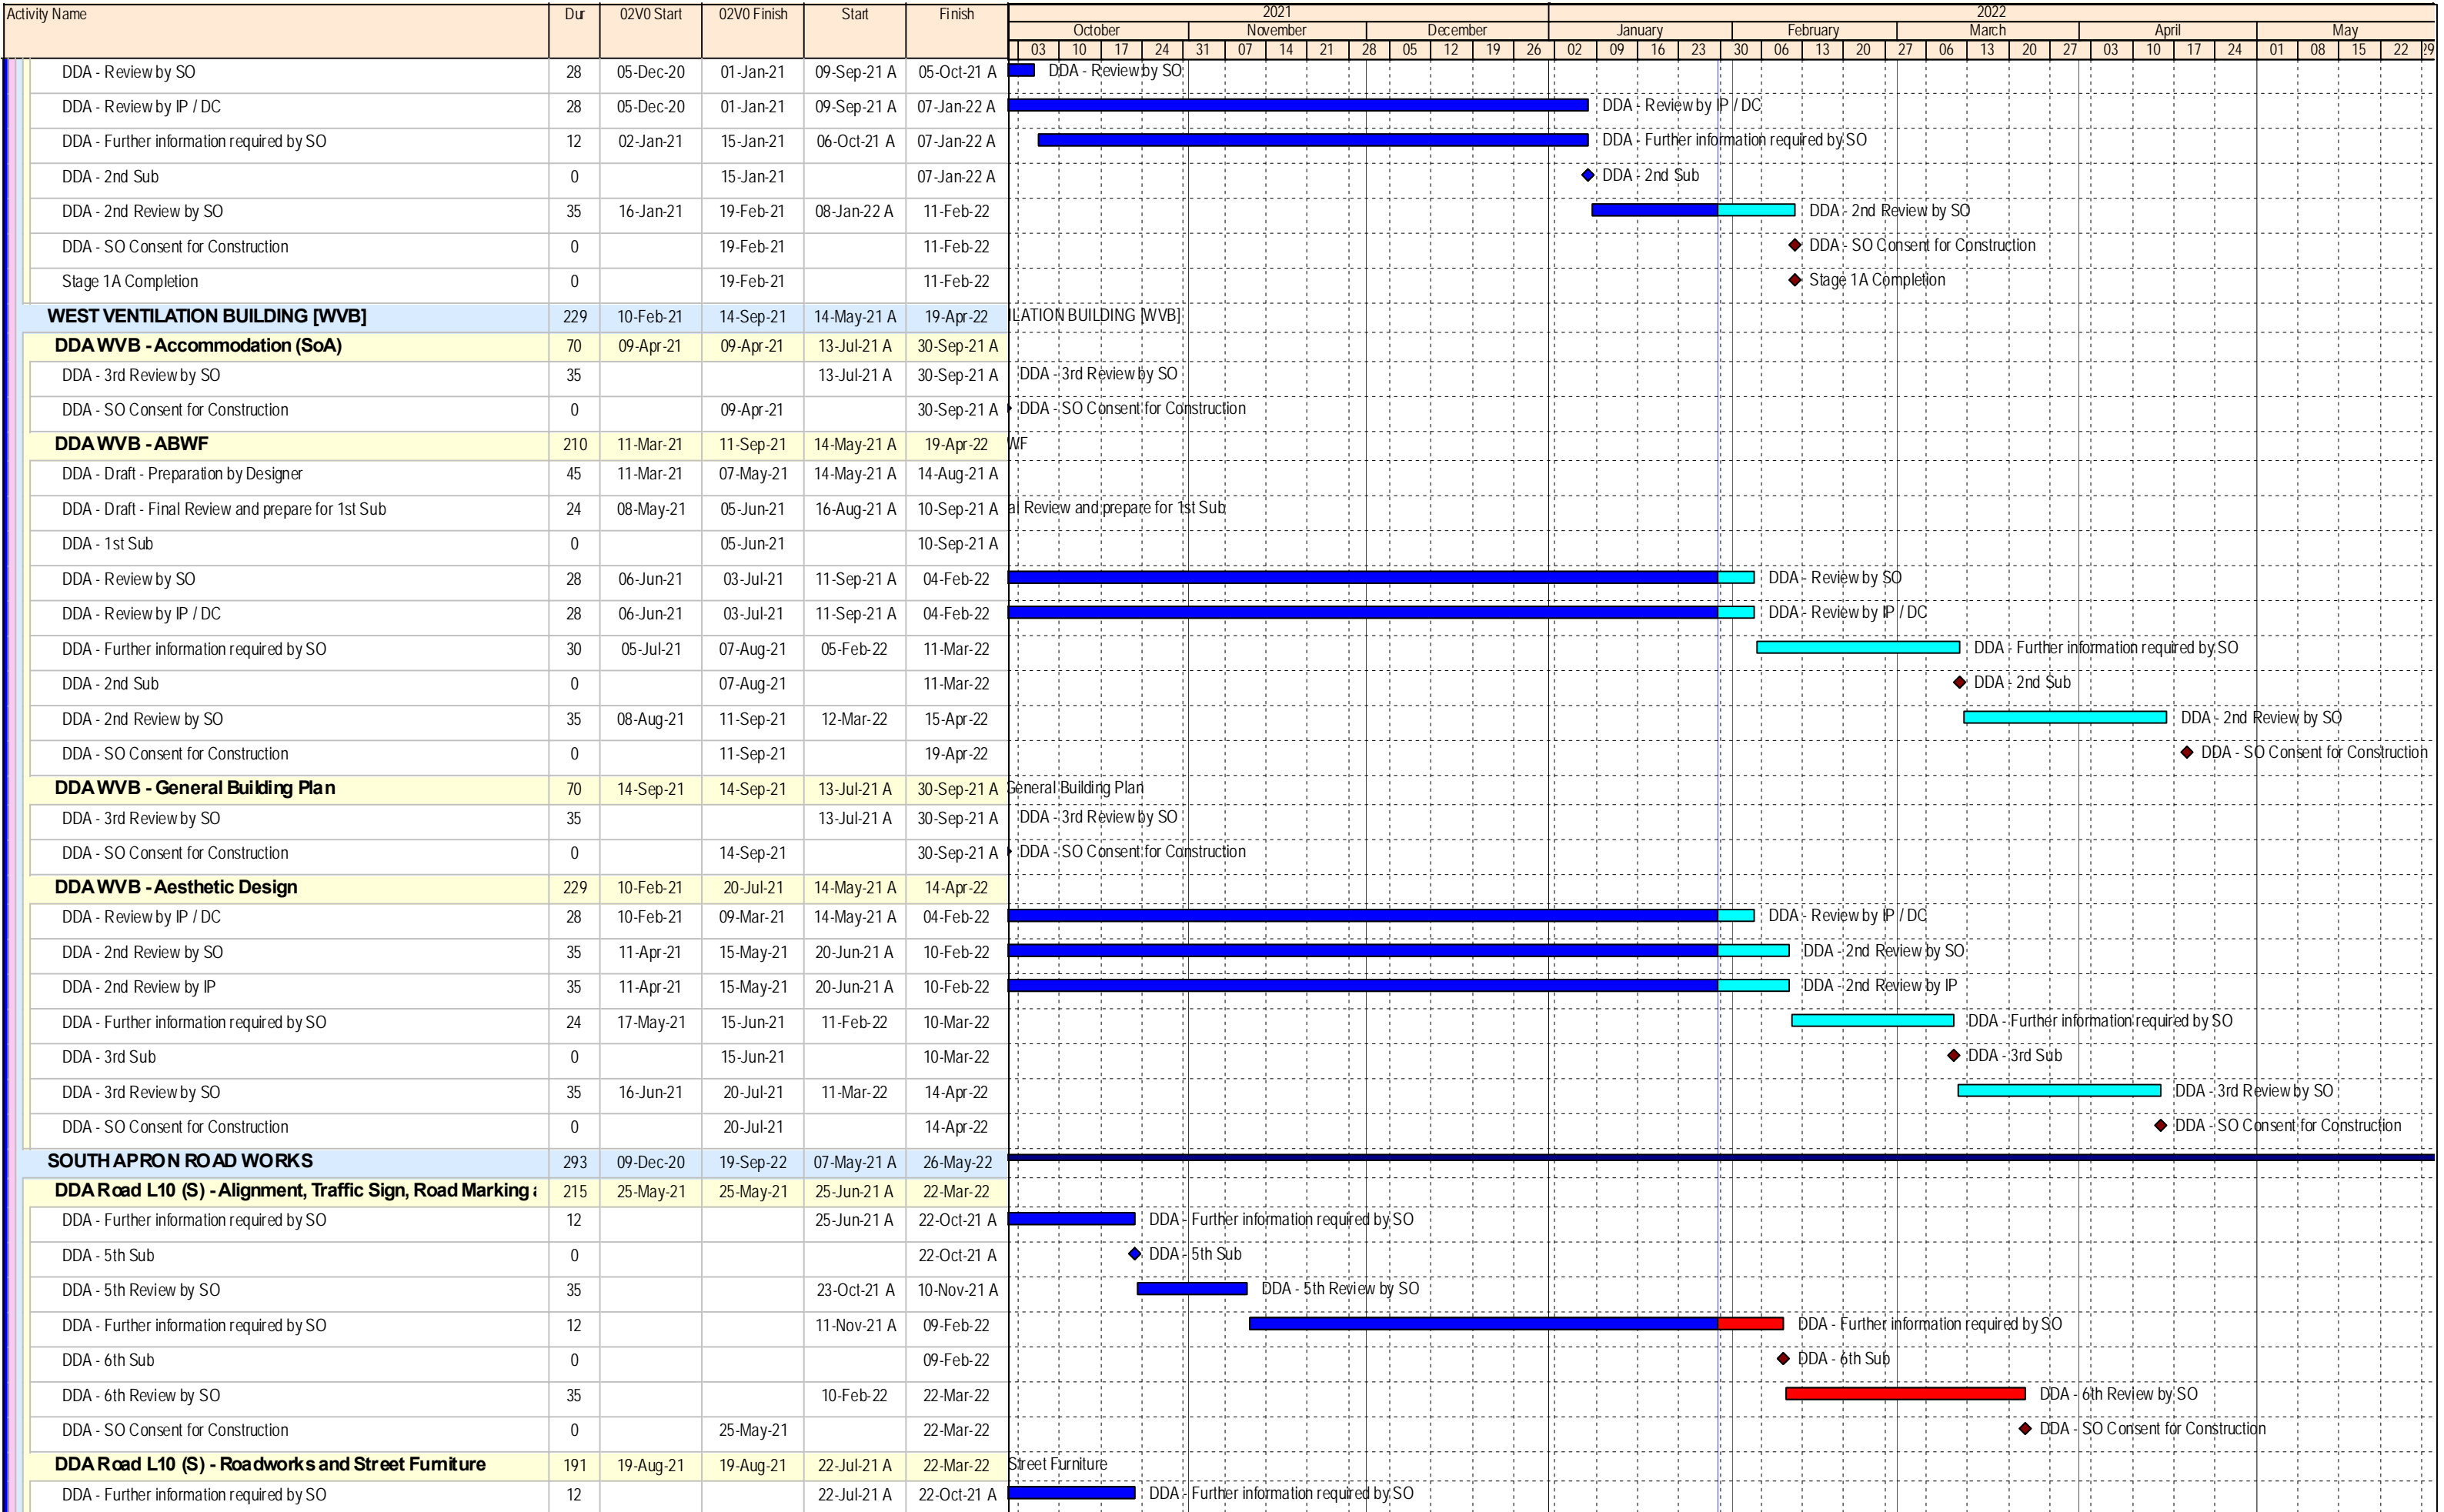


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

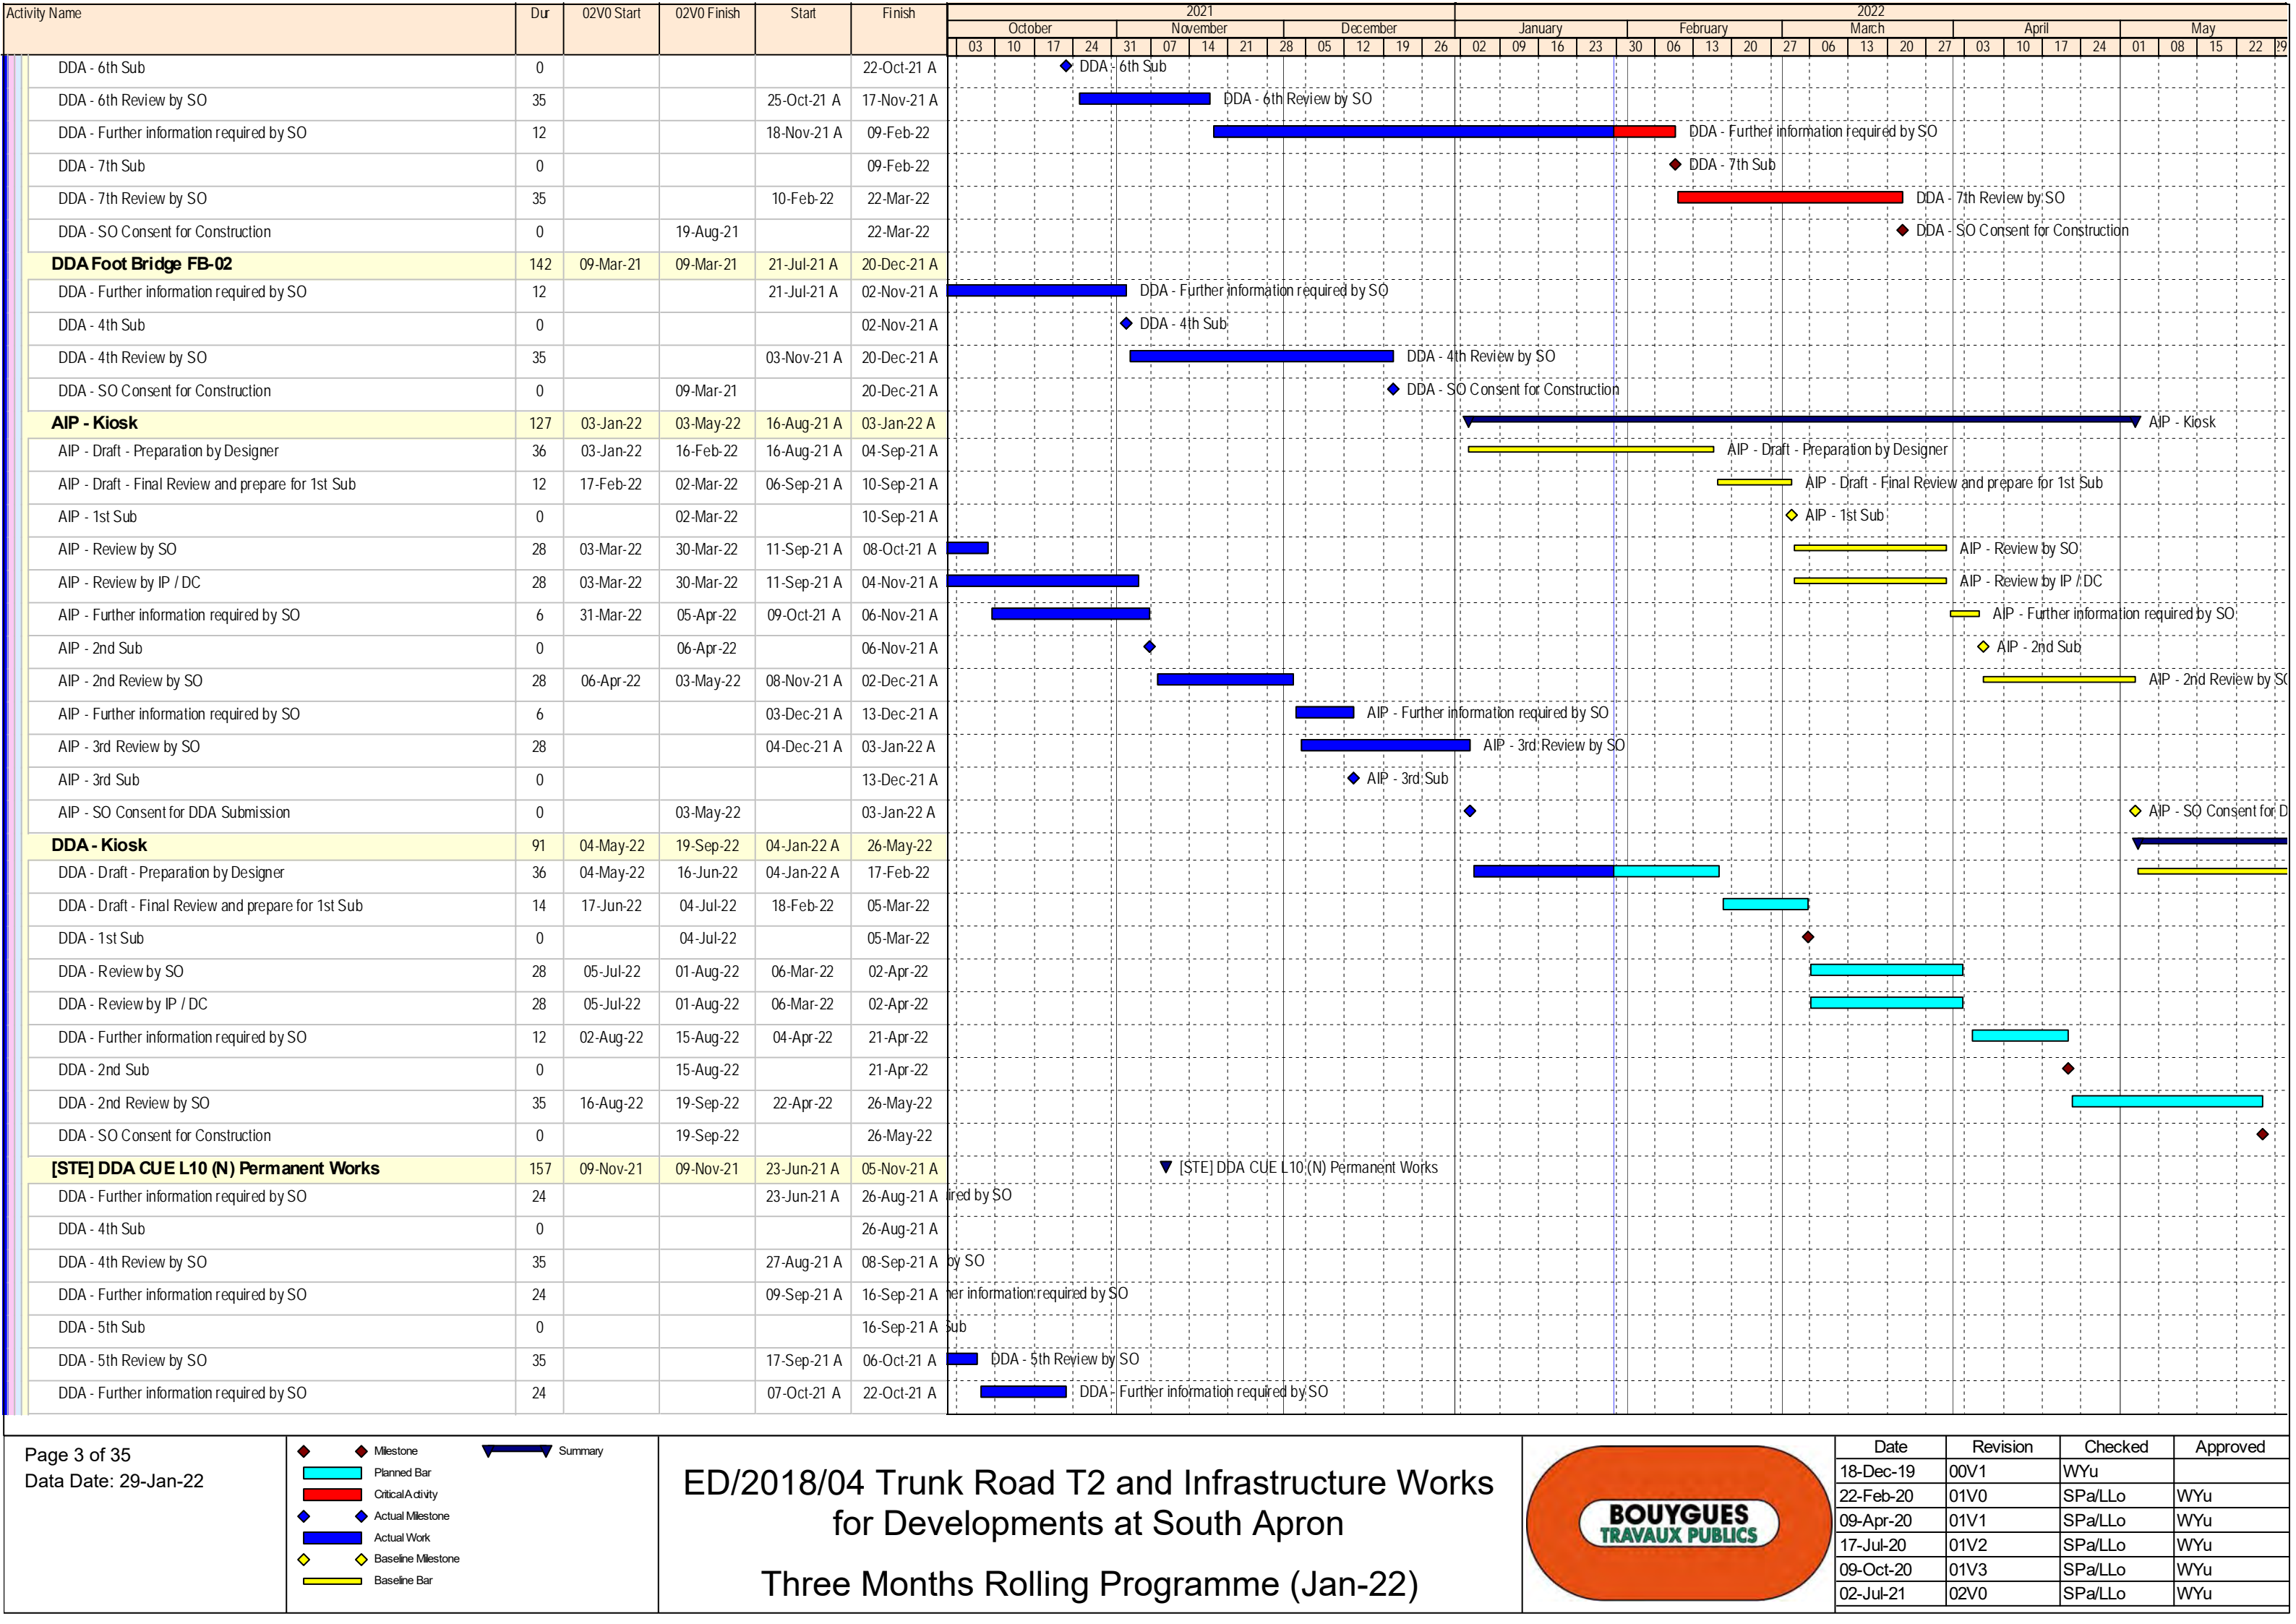


◆ Milestone  
▶ Summary  
 Planned Bar  
◆ Critical Activity  
◆ Actual Milestone  
 Actual Work  
◆ Baseline Milestone  
 Baseline Bar

# ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

## Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

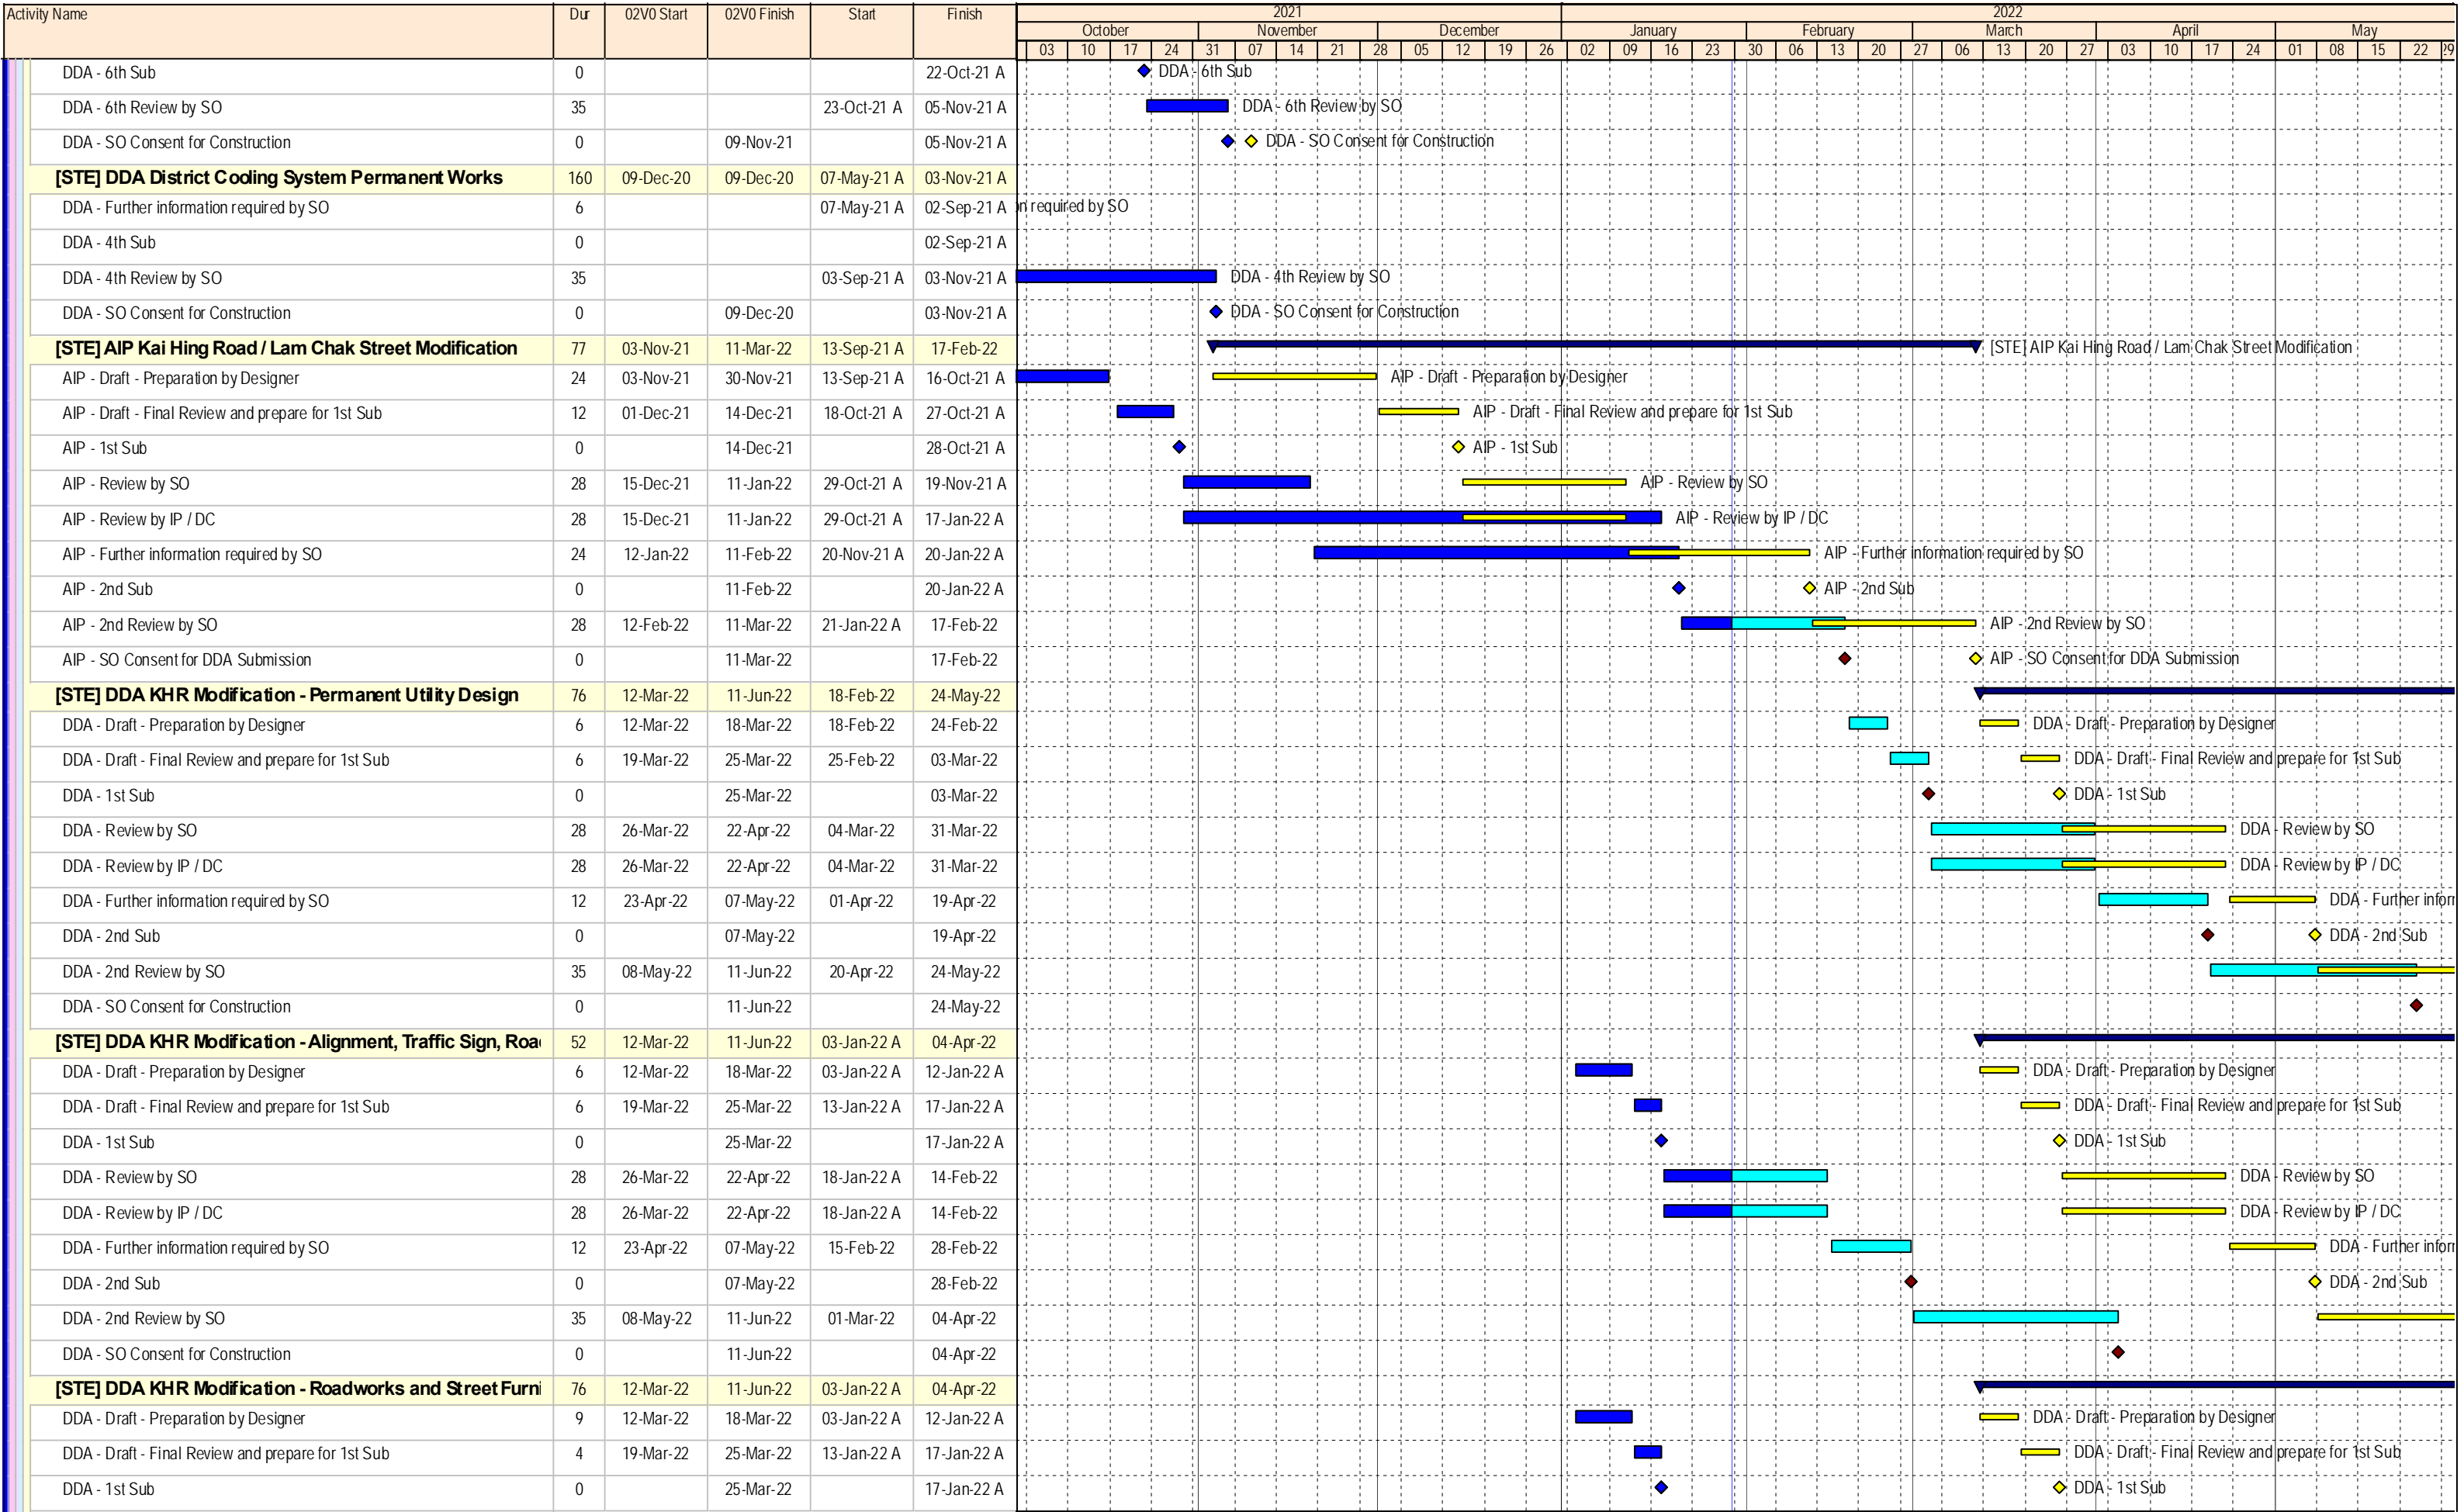

◆ Milestone  
 Planned Bar  
 Critical Activity  
◆ Actual Milestone  
 Actual Work  
◆ Baseline Milestone  
 Baseline Bar  
➤ Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




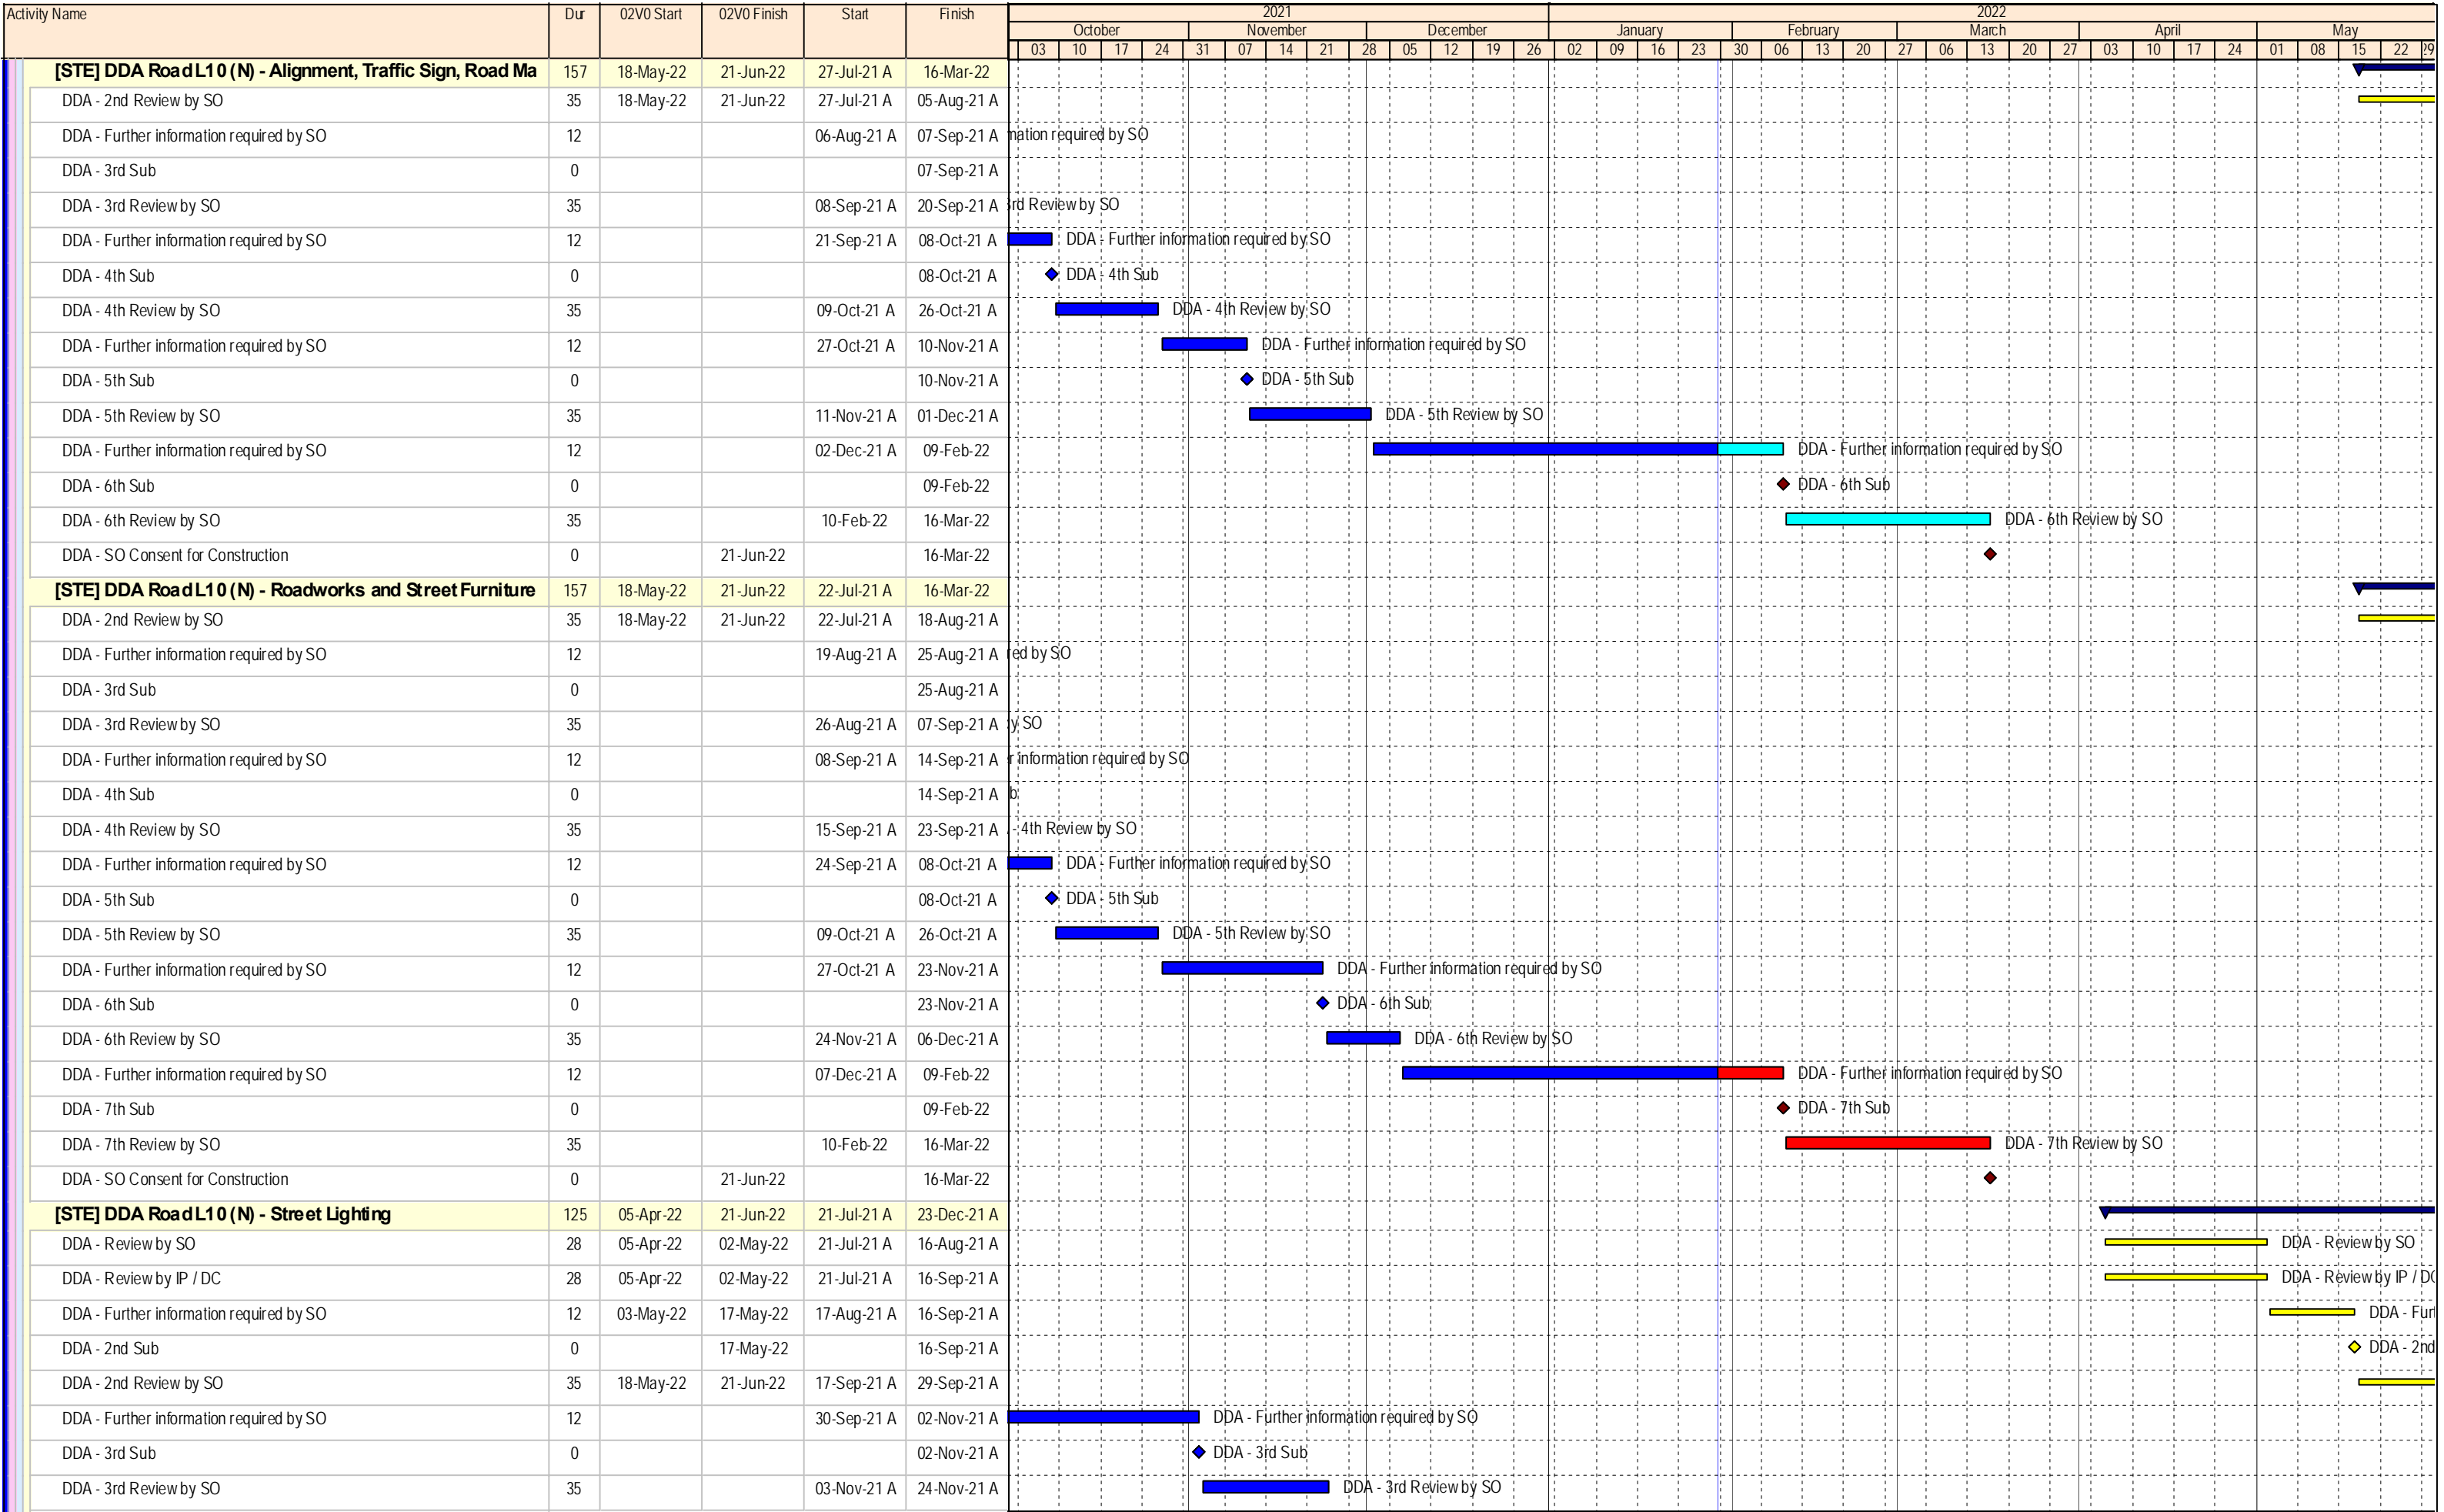

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu



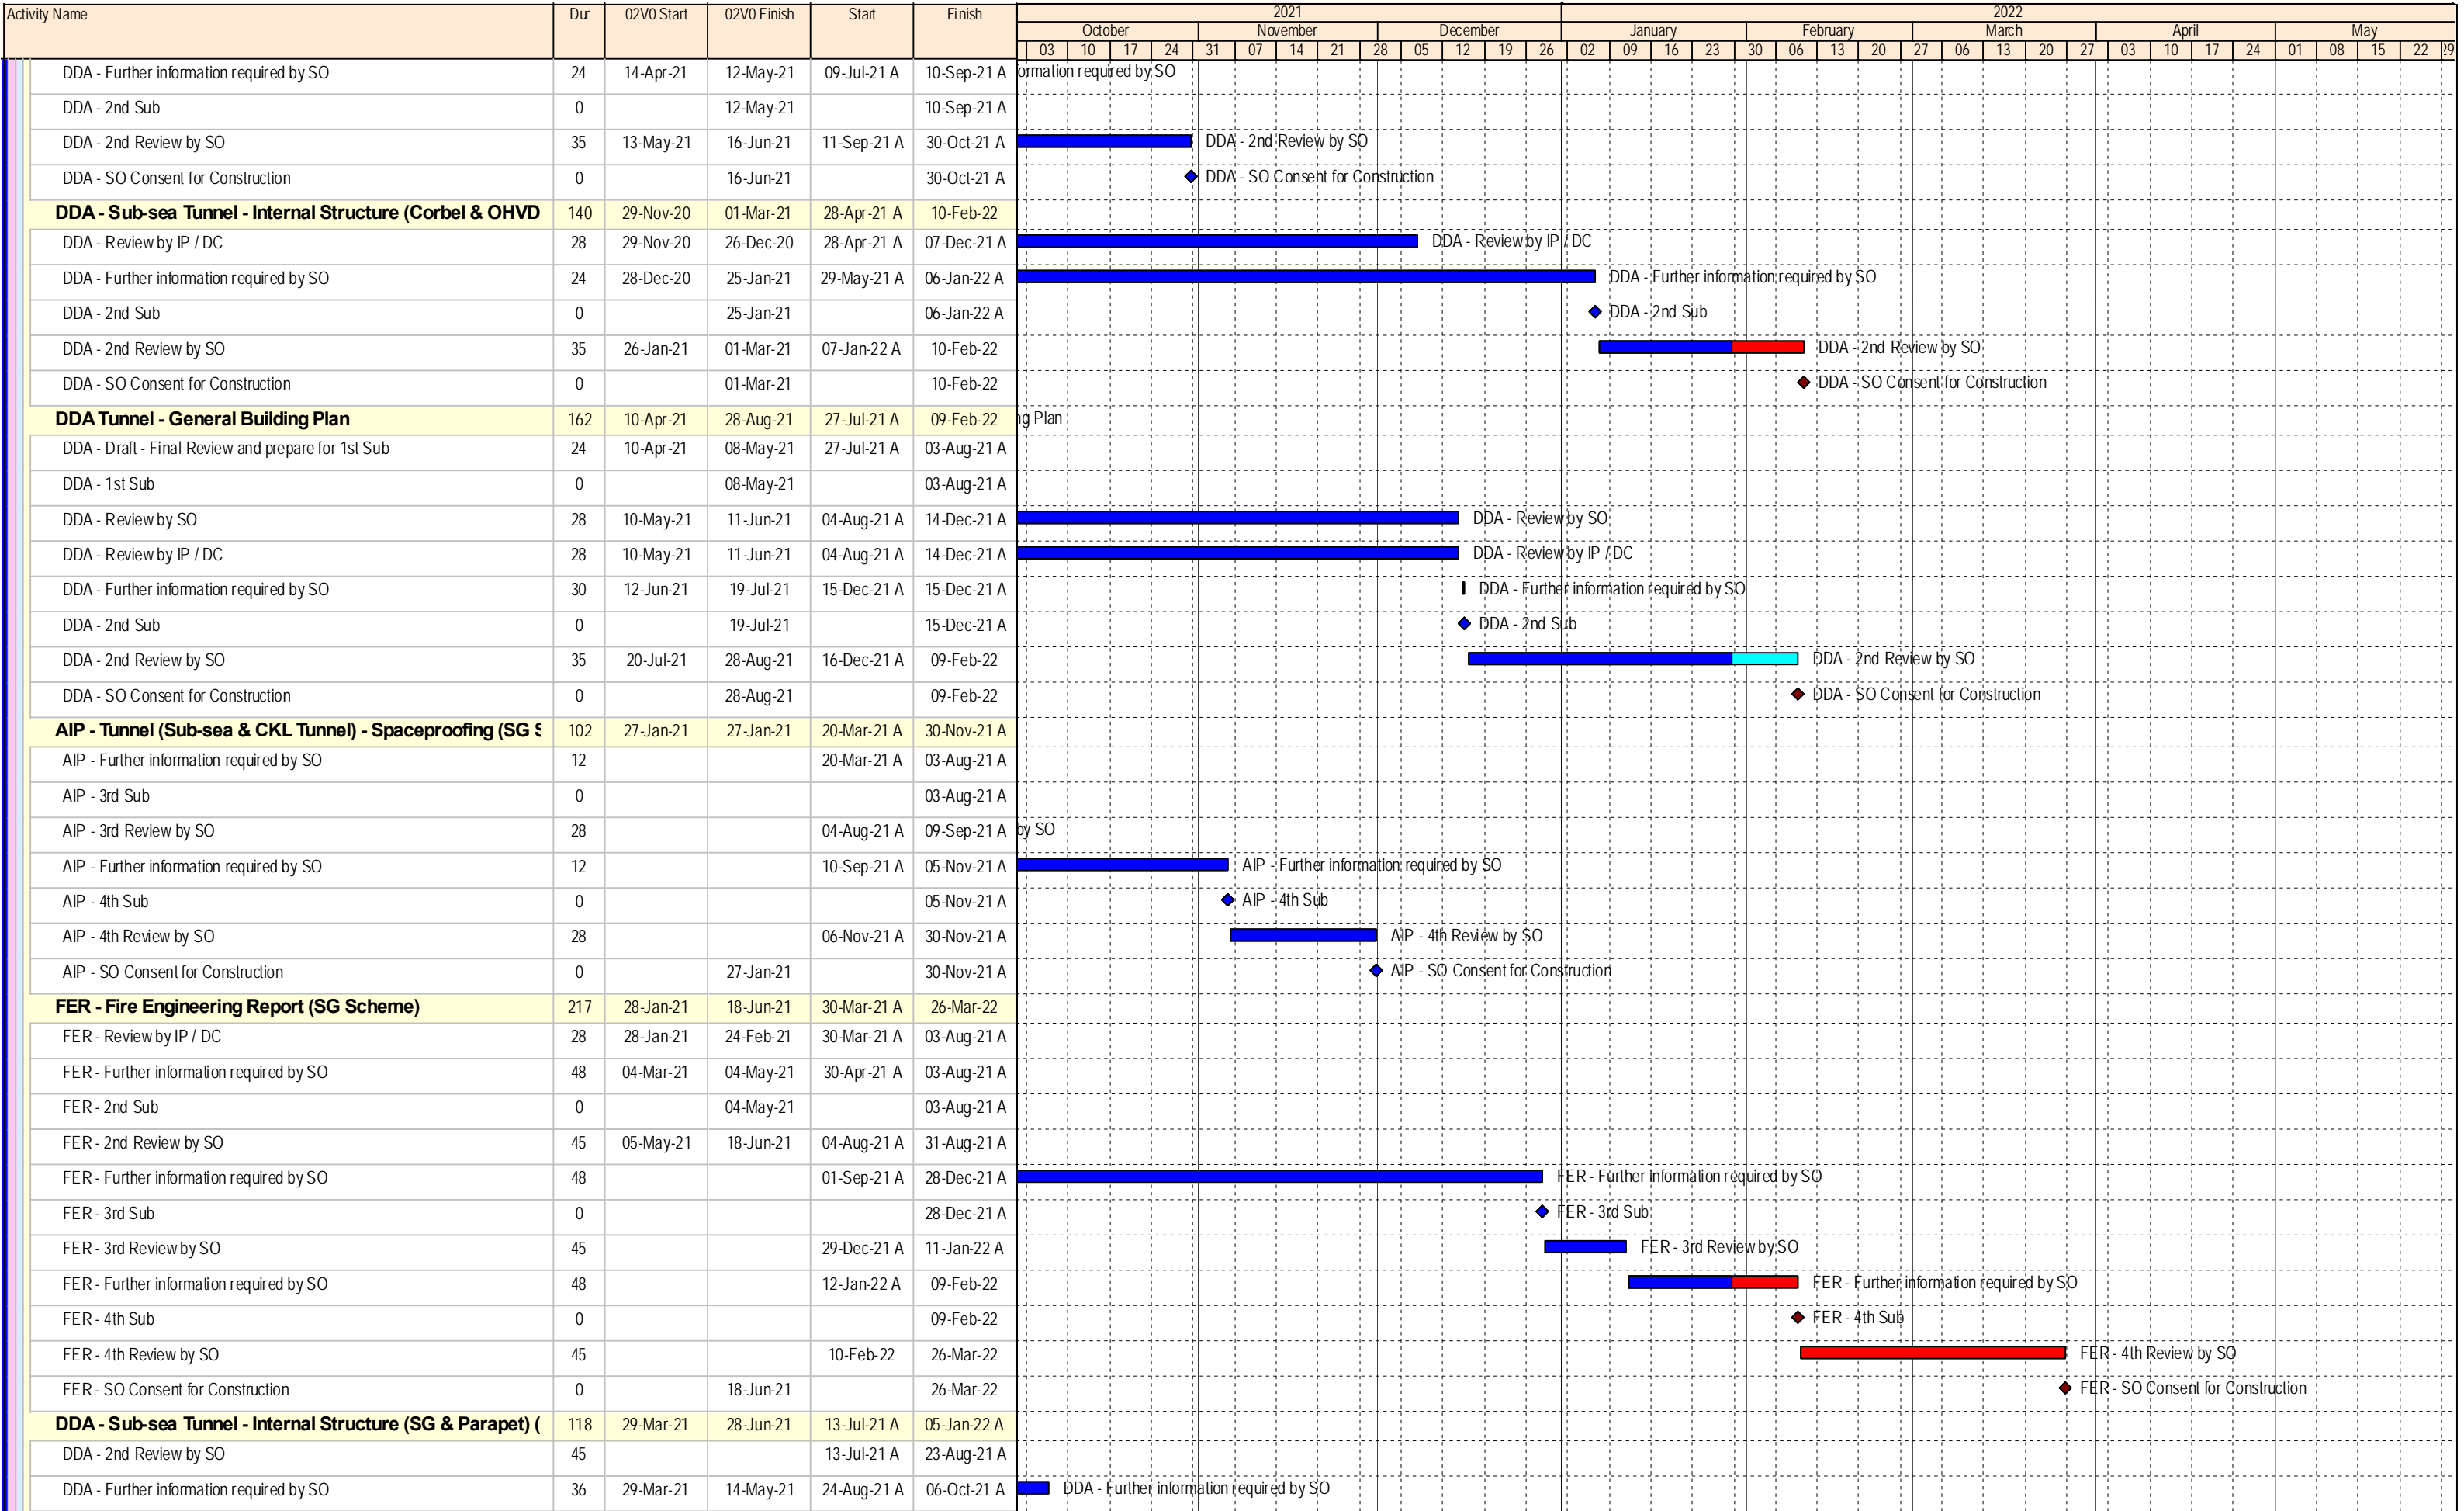

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu



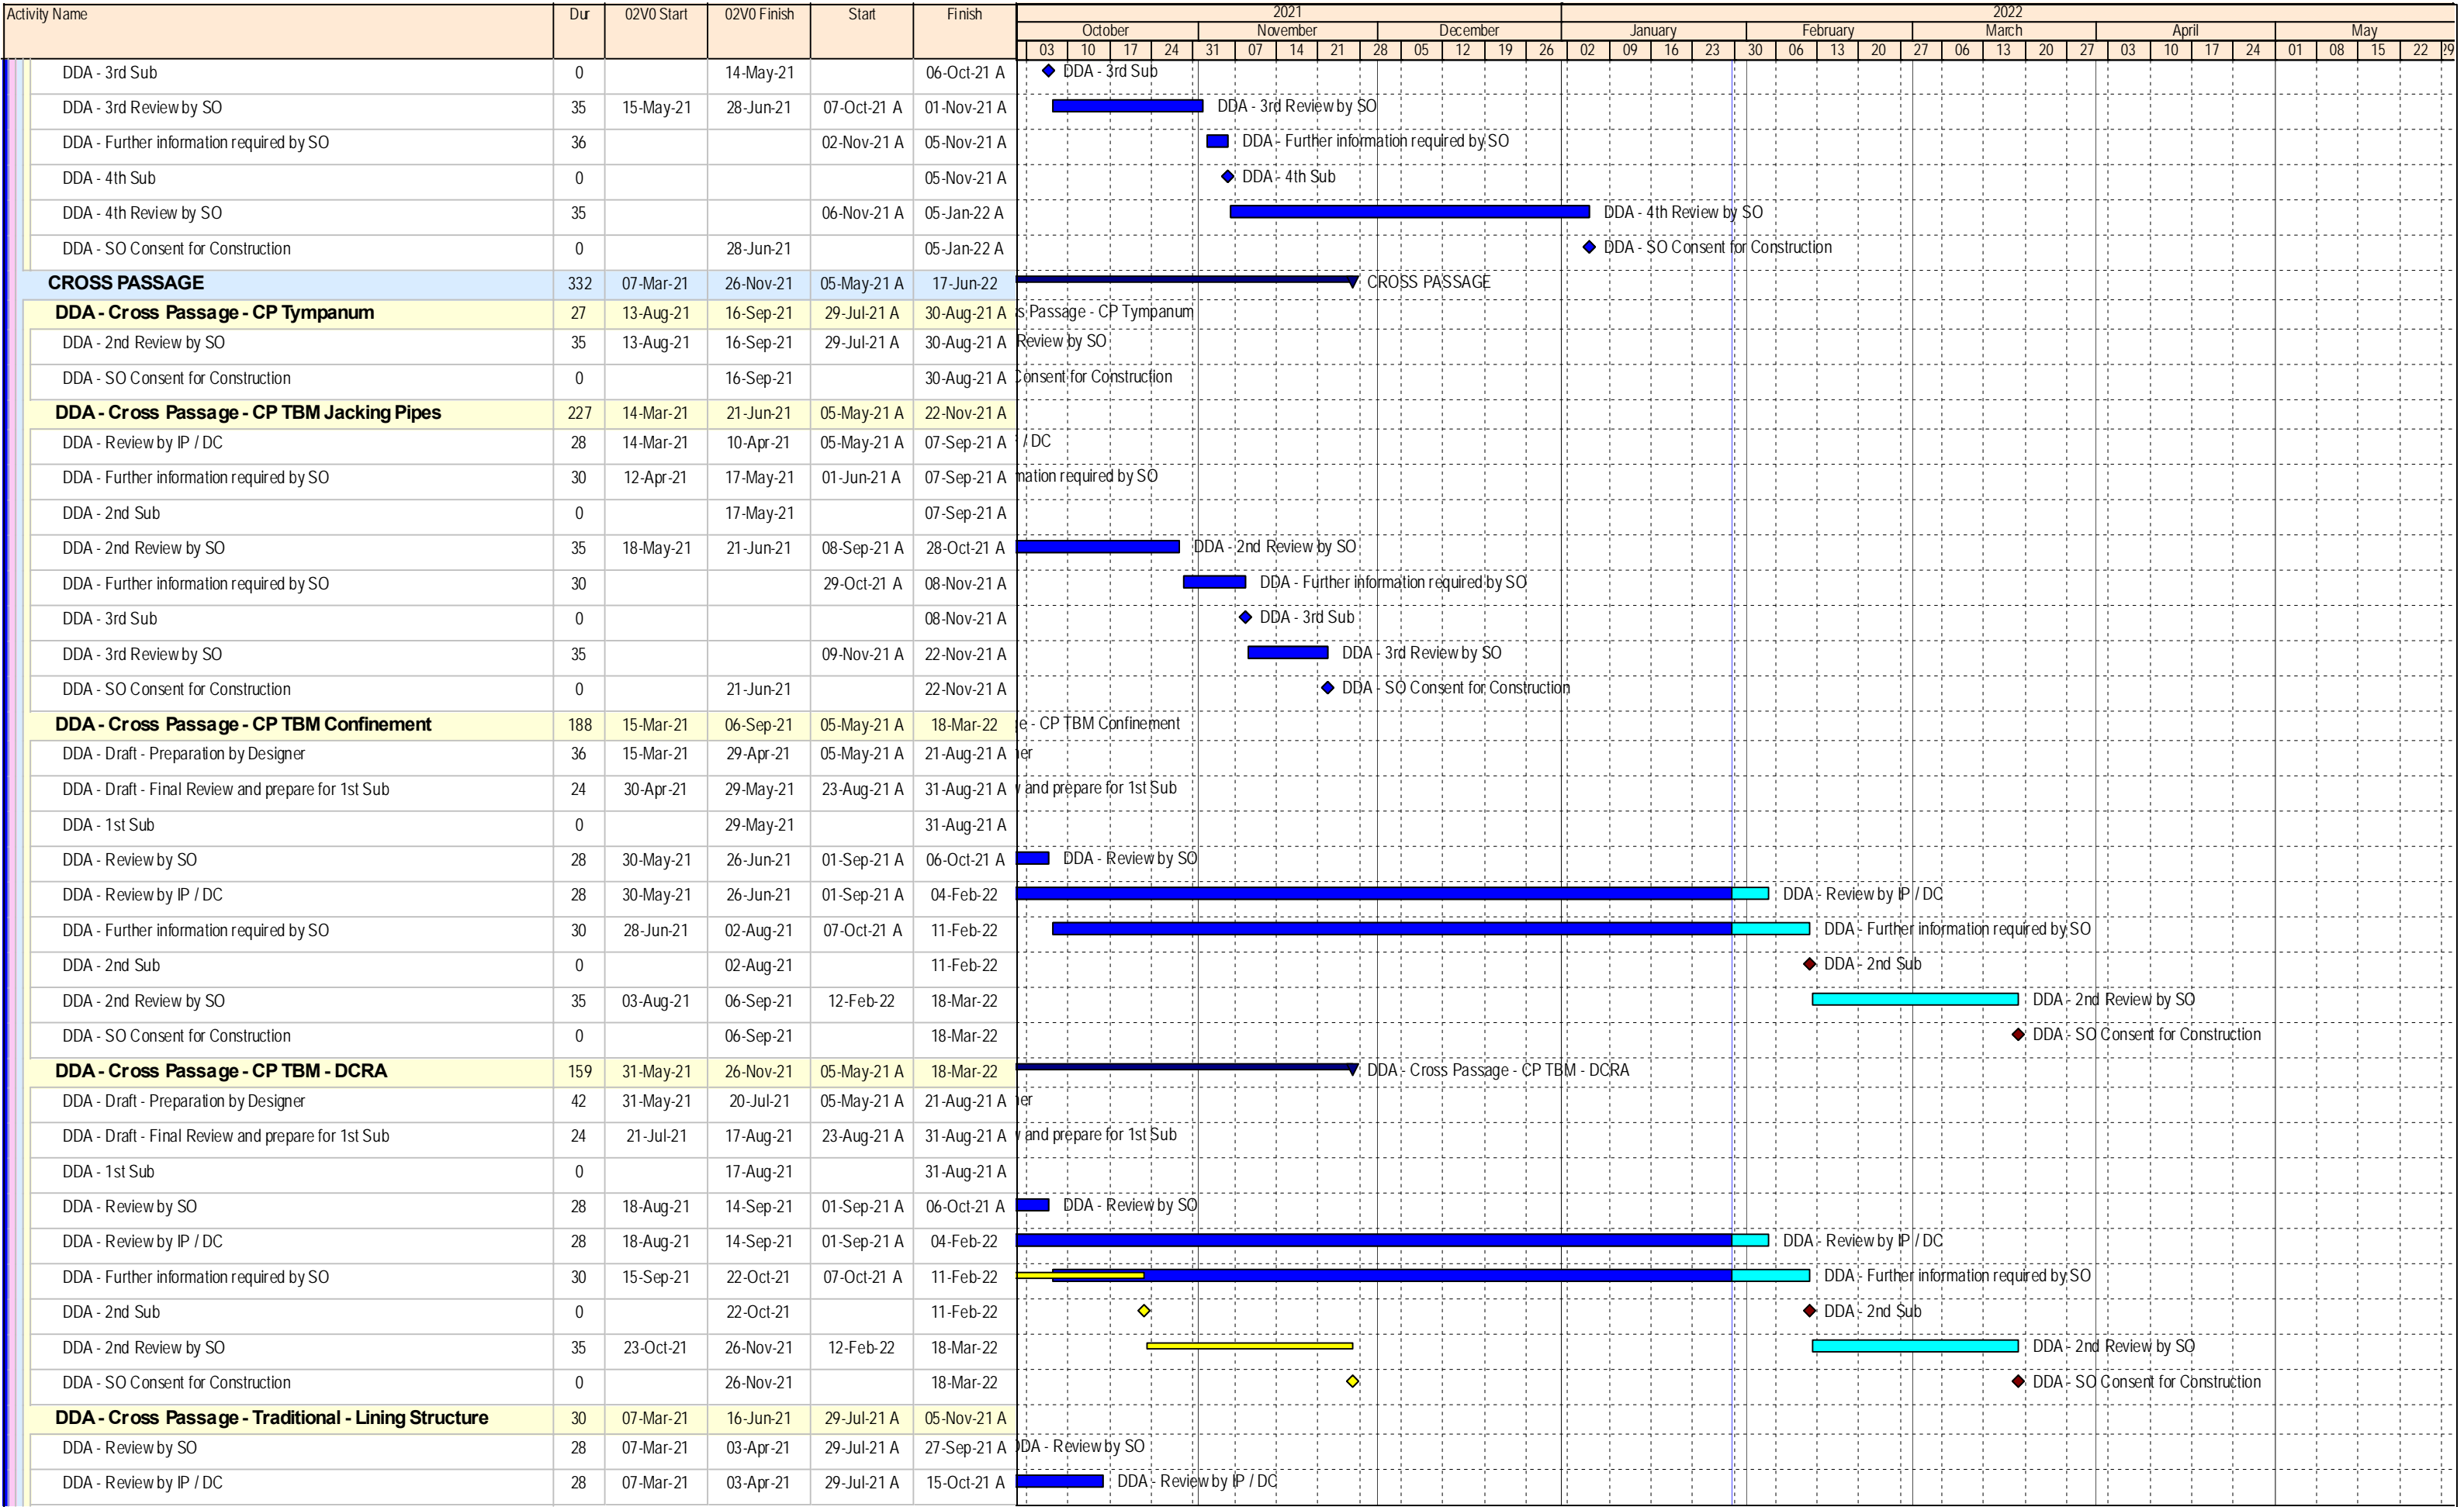


- ◆ Milestone
- ▶ Summary
- █ Planned Bar
- █ Critical Activity
- ◆ Actual Milestone
- █ Actual Work
- ◆ Baseline Milestone
- █ Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

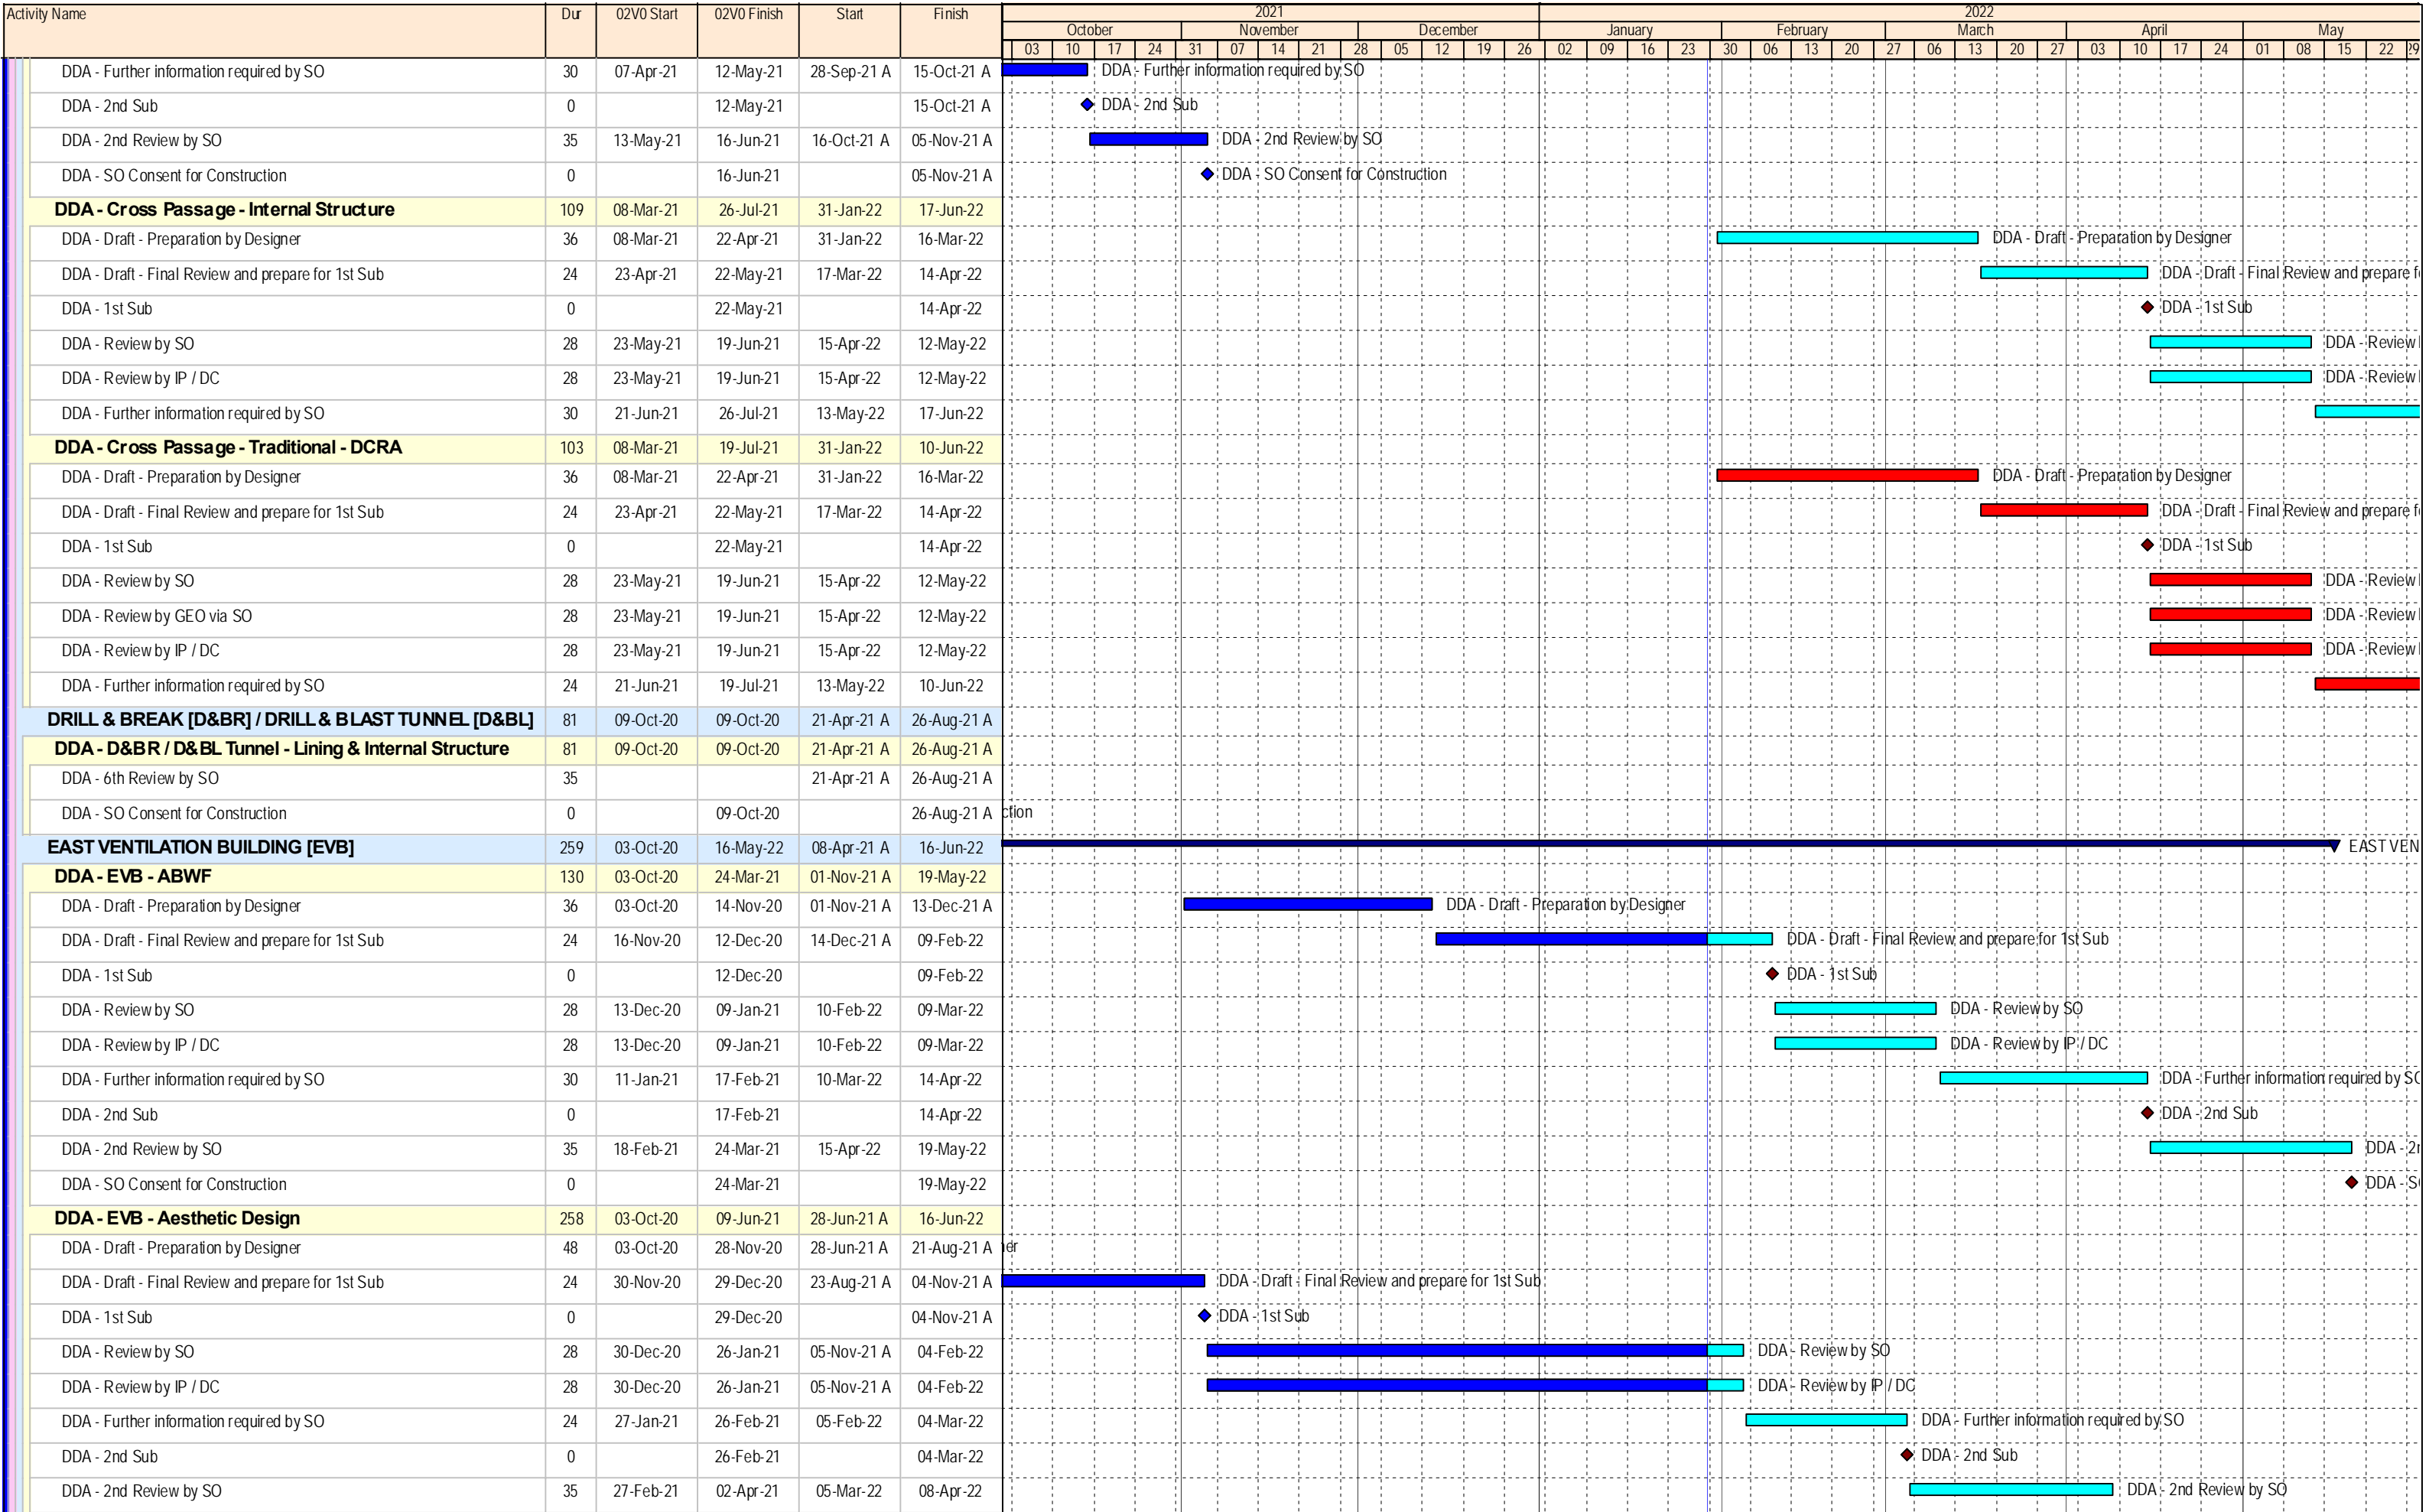

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu













Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021												2022														
						October				November				December				January			February			March			April			May		
						03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	03	10	17	24	01
6.1 .17 Complete whole activities of this cost centre	0		26-May-21		13-Dec-21 A	◆ 6.1 .17 Complete whole activities of this cost centre																										
<b>7.1 Western Ventilation Building</b>	0	21-Jul-21	09-Sep-21	13-Aug-21 A	13-Dec-21 A	ation Building;																										
7.1 .1 Complete mobilization of excavation equipment 0.5	0		21-Jul-21		13-Aug-21 A	equipment 0.5																										
7.1 .3 Complete excavation for WVB 0.5	0		09-Sep-21		13-Dec-21 A	◆ 7.1 .3 Complete excavation for WVB 0.5																										
<b>9.1 Launching Shaft</b>	65	14-Jul-21	13-Aug-21	13-Sep-21 A	13-Oct-21 A																											
9.1 .13 Complete bottom slab for Launching Shaft by area 0.2	0		14-Jul-21		13-Sep-21 A	ete bottom slab for Launching Shaft by area 0.2																										
9.1 .14 Complete bottom slab for Launching Shaft by area 0.4	0		14-Jul-21		13-Oct-21 A	◆ 9.1 .14 Complete bottom slab for Launching Shaft by area 0.4																										
9.1 .15 Complete bottom slab for Launching Shaft by area 0.6	0		26-Jul-21		13-Oct-21 A	◆ 9.1 .15 Complete bottom slab for Launching Shaft by area 0.6																										
9.1 .16 Complete bottom slab for Launching Shaft by area 0.8	0		04-Aug-21		13-Oct-21 A	◆ 9.1 .16 Complete bottom slab for Launching Shaft by area 0.8																										
9.1 .17 Complete bottom slab for Launching Shaft by area 1	0		13-Aug-21		13-Oct-21 A	◆ 9.1 .17 Complete bottom slab for Launching Shaft by area 1																										
<b>11.1 Drill and Break Tunnel</b>	33	13-Jul-21	21-Dec-21	13-Dec-21 A	14-Feb-22	▼ 11.1 Drill and Break Tunnel																										
11.1.2 Complete tunnel excavation 0.2 by length	0		13-Jul-21		13-Dec-21 A	◆ 11.1.2 Complete tunnel excavation 0.2 by length																										
11.1.2 Complete tunnel excavation 0.5 by length	0		19-Oct-21		29-Jan-22*	◆ 11.1.2 Complete tunnel excavation 0.5 by length																										
11.1.2 Complete tunnel excavation 0.3 by length	0		13-Aug-21		29-Jan-22*	◆ 11.1.2 Complete tunnel excavation 0.3 by length																										
11.1.2 Complete tunnel excavation 0.4 by length	0		14-Sep-21		29-Jan-22*	◆ 11.1.2 Complete tunnel excavation 0.4 by length																										
11.1.3 Complete tunnel excavation 0.6 by length	0		19-Nov-21		14-Feb-22*	◆ 11.1.3 Complete tunnel excavation 0.6 by length																										
11.1.5 Complete tunnel excavation 0.7 by length	0		21-Dec-21		14-Feb-22*	◆ 11.1.5 Complete tunnel excavation 0.7 by length																										
<b>12.1 Drill and Blast Tunnel</b>	80	16-Sep-21	14-Feb-22	13-Oct-21 A	29-Jan-22	▼ 12.1 Drill and Blast Tunnel																										
12.1.7 Complete tunnel excavation 0.6 by length	0		16-Sep-21		13-Oct-21 A	◆ 12.1.7 Complete tunnel excavation 0.6 by length																										
12.1.8 Complete tunnel excavation 0.7 by length	0		05-Nov-21		13-Oct-21 A	◆ 12.1.8 Complete tunnel excavation 0.7 by length																										
12.1.9 Complete tunnel excavation 0.8 by length	0		22-Dec-21		13-Dec-21 A	◆ 12.1.9 Complete tunnel excavation 0.8 by length																										
12.1.10 Complete tunnel excavation 0.9 by length	0		14-Feb-22		29-Jan-22*	◆ 12.1.10 Complete tunnel excavation 0.9 by length																										
<b>12.2 Cross Passages for Drill and Blast Tunnel</b>	0	12-Apr-22	12-Apr-22	24-May-22	24-May-22	▼ 12.2 Cross Passages for Drill and Blast Tunnel																										
12.2 .4 Complete cross passages structure by length 0.4	0		12-Apr-22		24-May-22	◆ 12.2 .4 Complete cross passages structure by length 0.4																										
<b>15.0 E&amp;M Design Works</b>	215	02-Jan-21	03-Sep-21	13-Aug-21 A	07-May-22	S;																										
15.0 .9 Submit DDA for electrical system (power supply)	0		28-Apr-21		13-Aug-21 A	ower supply)																										
15.0 .12 Approval AIP for Tunnel extra low voltage system	0		02-Jan-21		13-Aug-21 A	oltage system																										
15.0 .21 Submit DDA for Tunnel plumbing & drainage	0		10-Feb-21		13-Aug-21 A	& drainage																										
15.0 .29 Submit DDA for remaining tunnel and at-grade E&M systems	0		06-Jul-21		13-Aug-21 A	and at-grade E&M systems;																										
15.0 .33 Submit DDA for E&M in WVB	0		24-Feb-21		13-Aug-21 A																											
15.0 .37 Submit DDA for E&M in EVB	0		11-Jun-21		13-Aug-21 A																											
15.0 .25 Submit DDA for Tunnel lighting system	0		10-May-21		14-Feb-22*	◆ 15.0 .25 Submit DDA for Tunnel lighting system																										
15.0 .26 Approval DDA for Tunnel lighting system	0		03-Sep-21		07-May-22	◆ 15.0 .26 Approval DDA for Tunnel lighting system																										
<b>17.1 Works under Sections 6A, 6C and 12 and Associated L</b>	33	23-Dec-20	04-Oct-21	13-Aug-21 A	14-Feb-22	▼ 17.1 Works under Sections 6A, 6C and 12 and Associated Landscape Works																										
17.1 .42 Complete watermain installation 0.25	0		23-Dec-20		13-Aug-21 A	.25																										
17.1 .46 Complete anchor blocks, thrust block etc for waterworks 0.25	0		23-Dec-20		13-Aug-21 A	ock etc for waterworks 0.25																										
17.1 .3 Complete excavation and disposal of material works 0.8	0		23-Jun-21		13-Oct-21 A	◆ 17.1 .3 Complete excavation and disposal of material works 0.8																										
17.1 .13 Complete footpath 0.25	0		21-Sep-21		14-Feb-22*	◆ 17.1 .13 Complete footpath 0.25																										
17.1 .17 Complete street furnitures of at-grade roads 0.25	0		04-Oct-21		14-Feb-22*	◆ 17.1 .17 Complete street furnitures of at-grade roads 0.25																										
<b>17.4 Remaining Stage 5 Infrastructure Works - Road L10 (S</b>	9	02-Aug-22	04-Mar-23	29-Jan-22	14-Feb-22																											
17.4 .1 Complete excavation and disposal of material works 0.25	0		17-Feb-23		29-Jan-22	◆ 17.4 .1 Complete excavation and disposal of material works 0.25																										
17.4 .2 Complete excavation and disposal of material works 0.5	0		04-Mar-23		14-Feb-22*	◆ 17.4 .2 Complete excavation and disposal of material works 0.5																										
17.4 .21 Complete drainage installation 0.2	0		18-Oct-22		14-Feb-22*	◆ 17.4 .21 Complete drainage installation 0.2																										

Page 16 of 35  
Data Date: 29-Jan-22



## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron



### Three Months Rolling Programme (Jan-22)

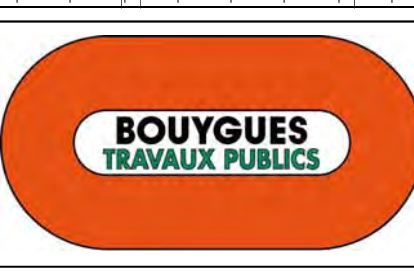

Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu





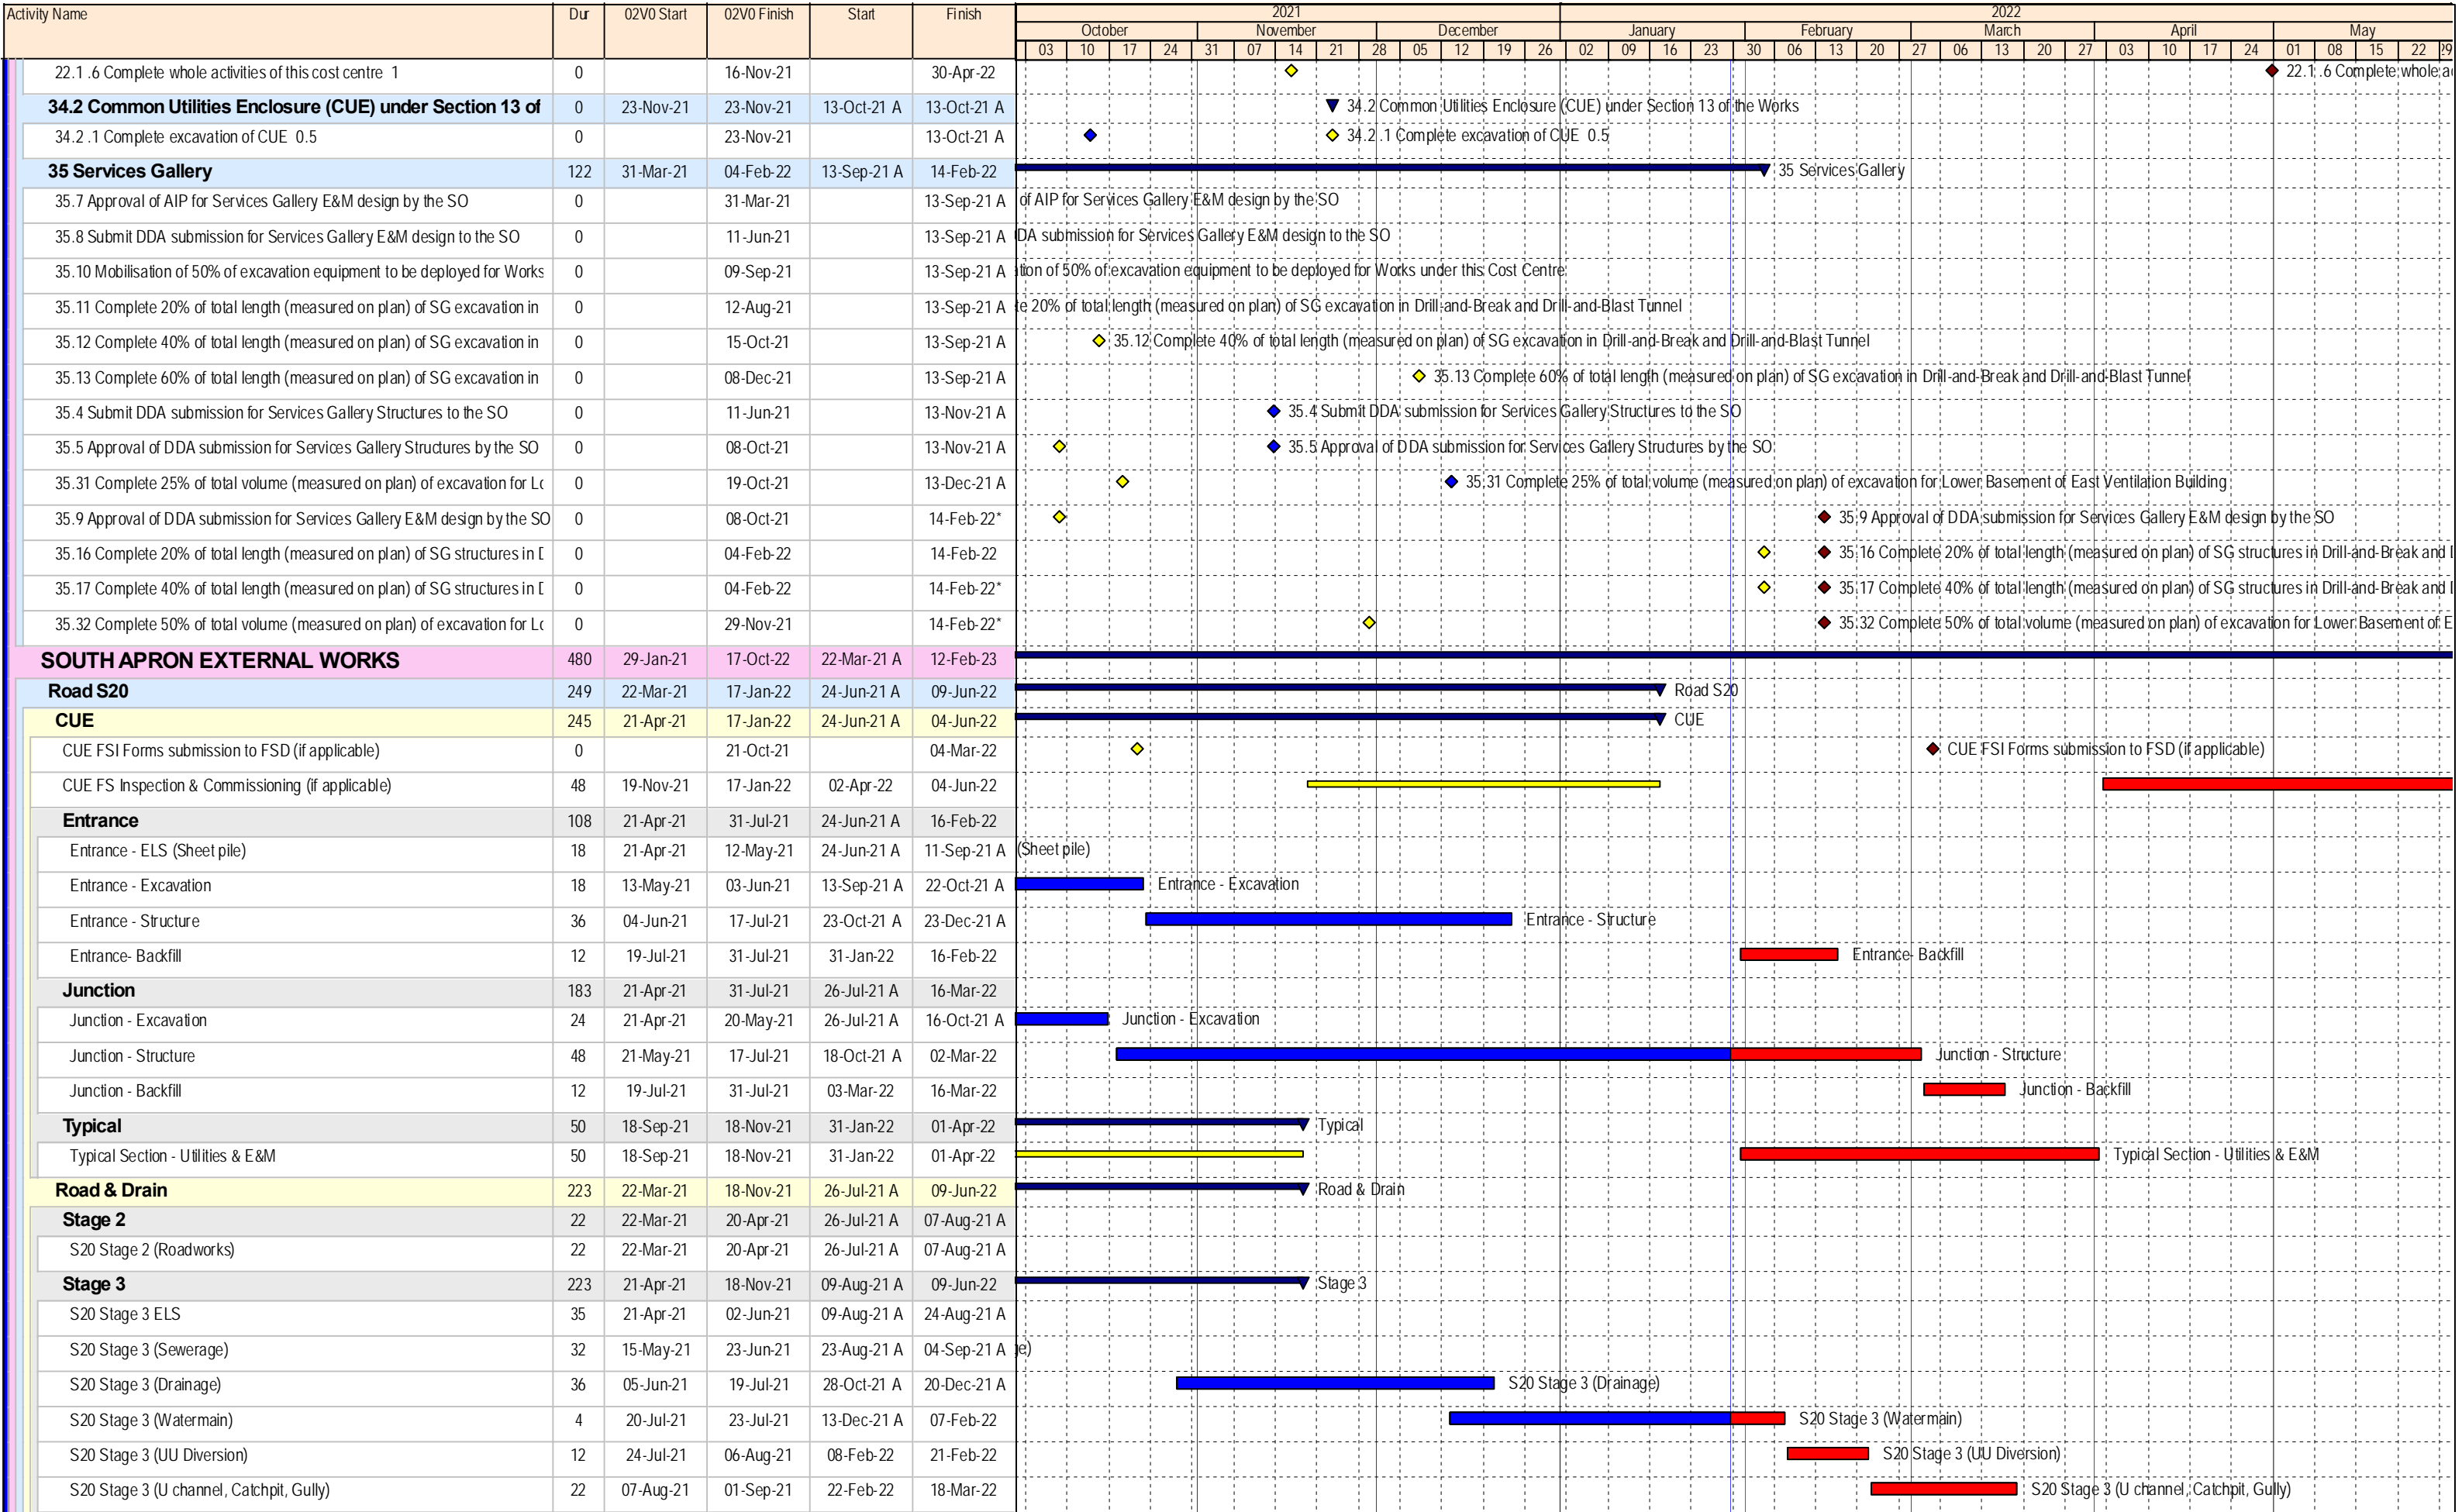


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

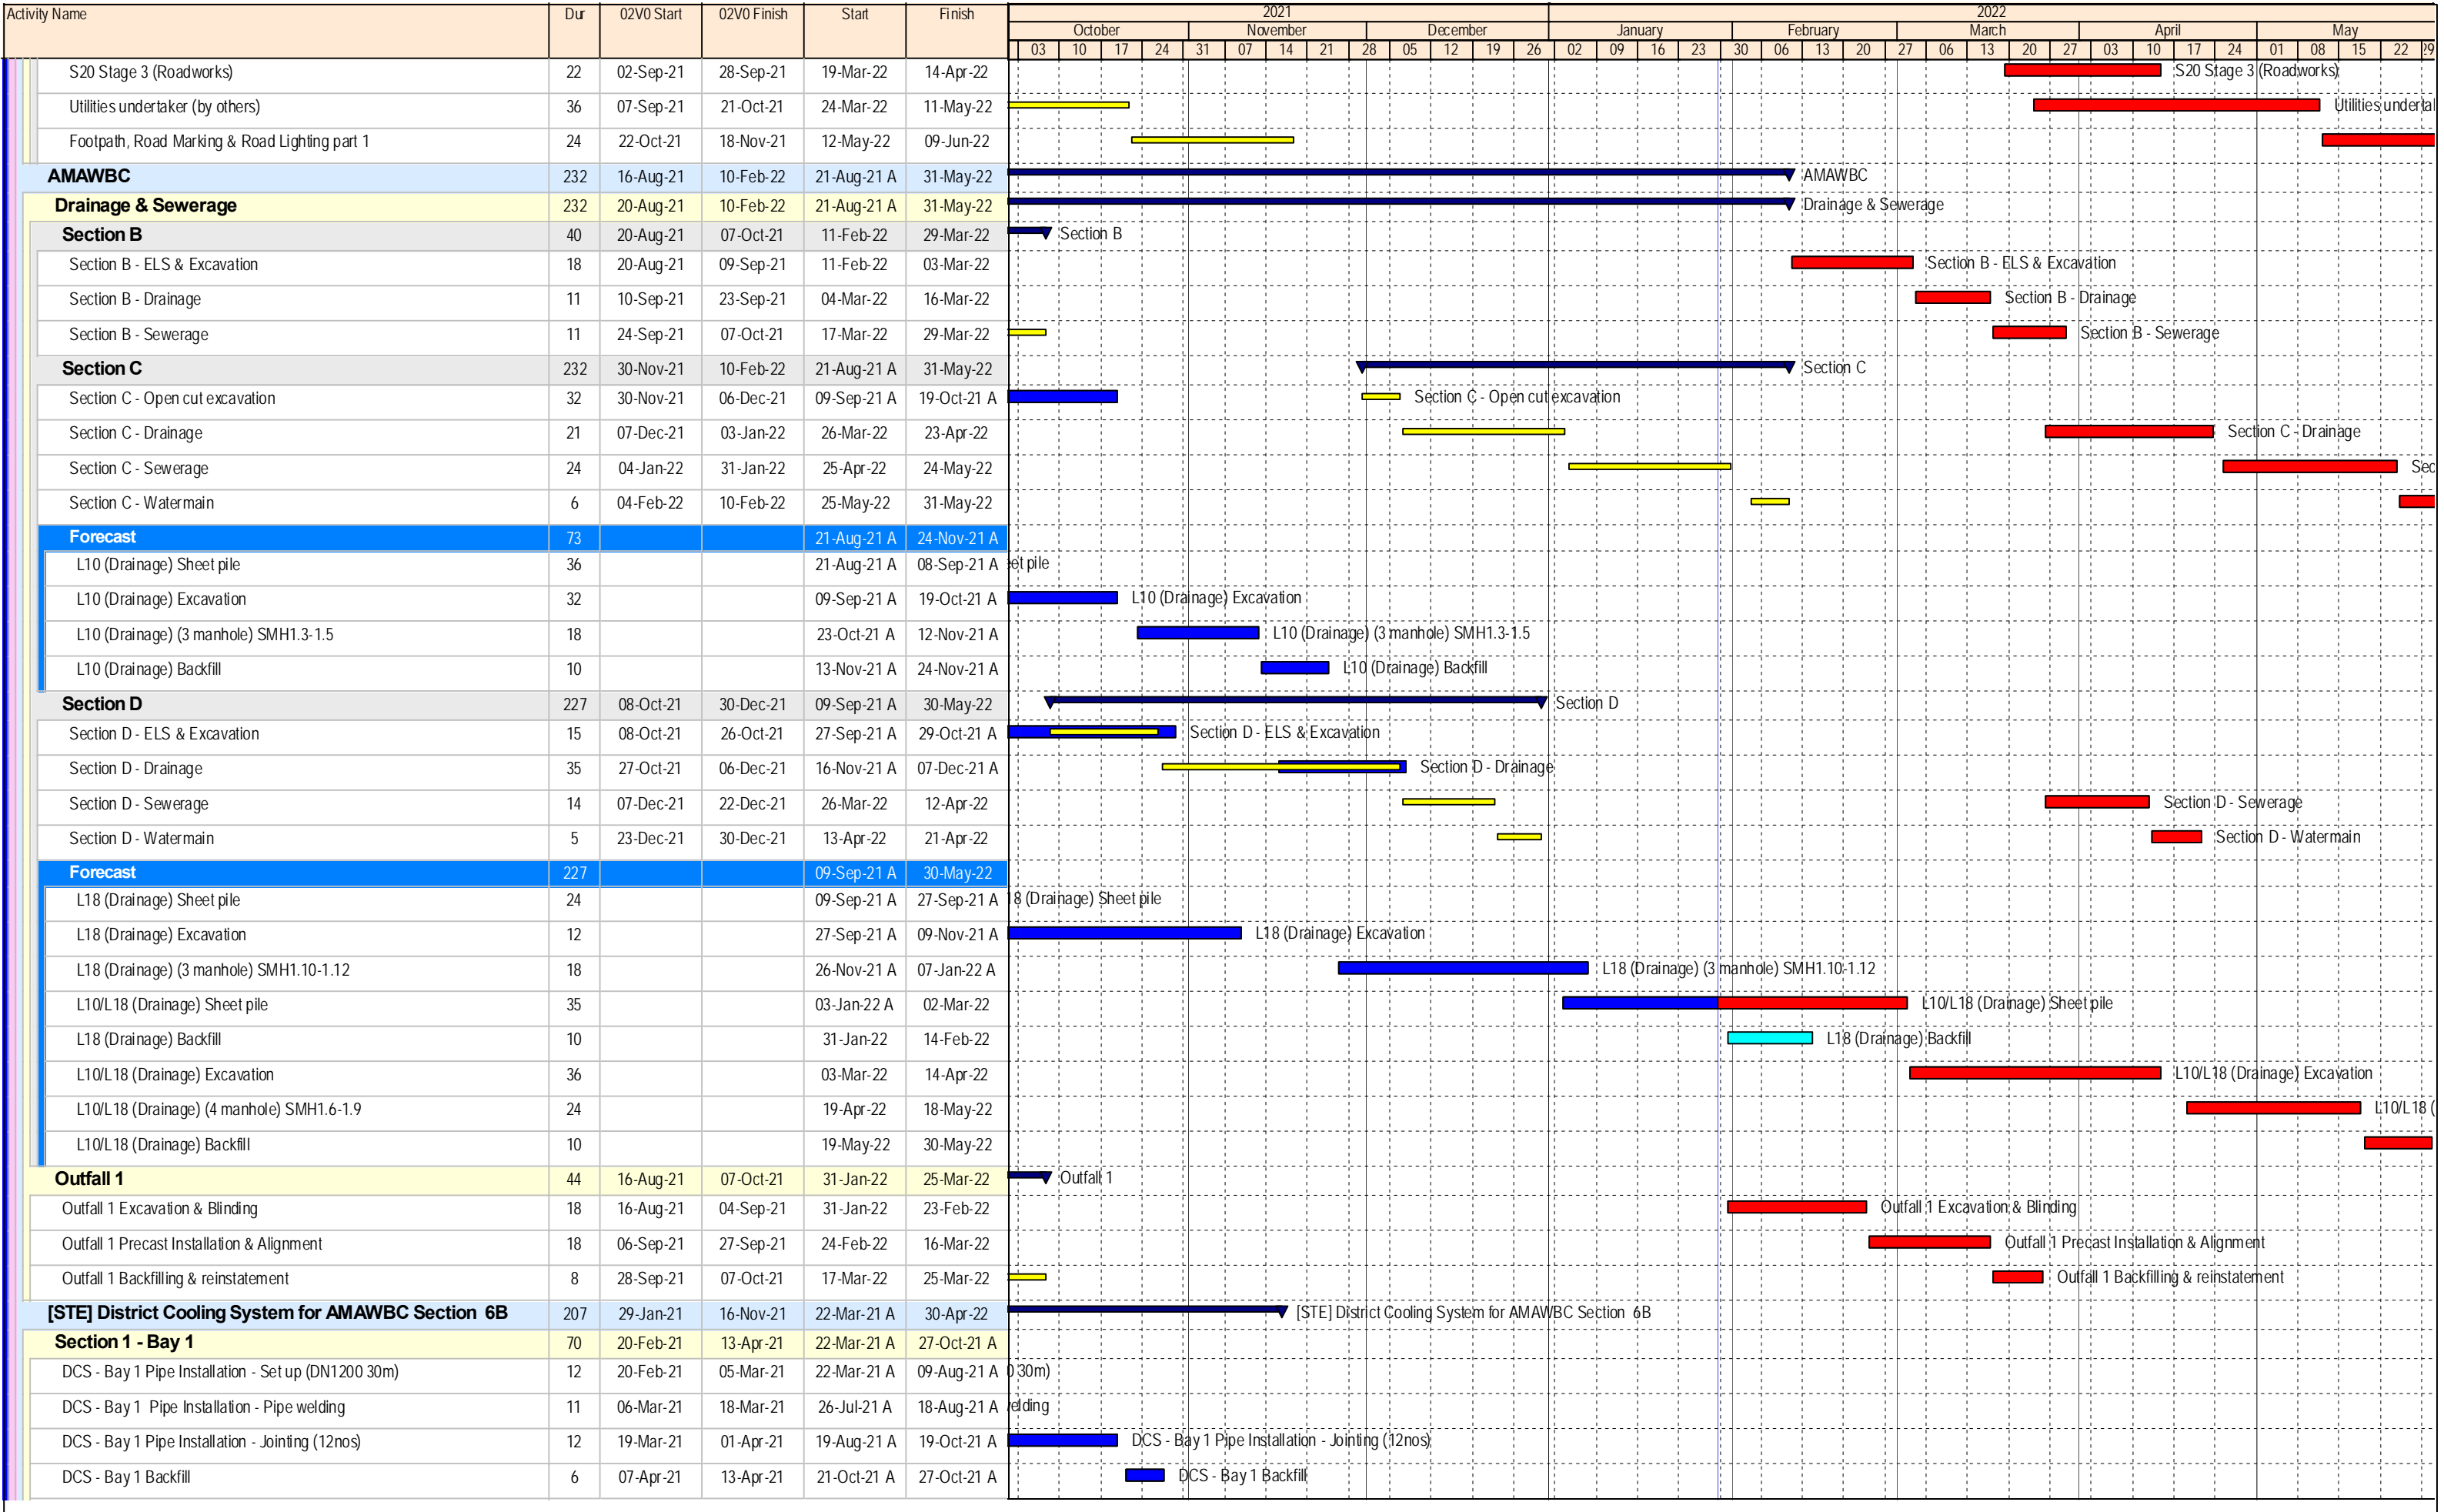


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

**ED/2018/04 Trunk Road T2 and Infrastructure Works**  
**for Developments at South Apron**  
**Three Months Rolling Programme (Jan-22)**




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

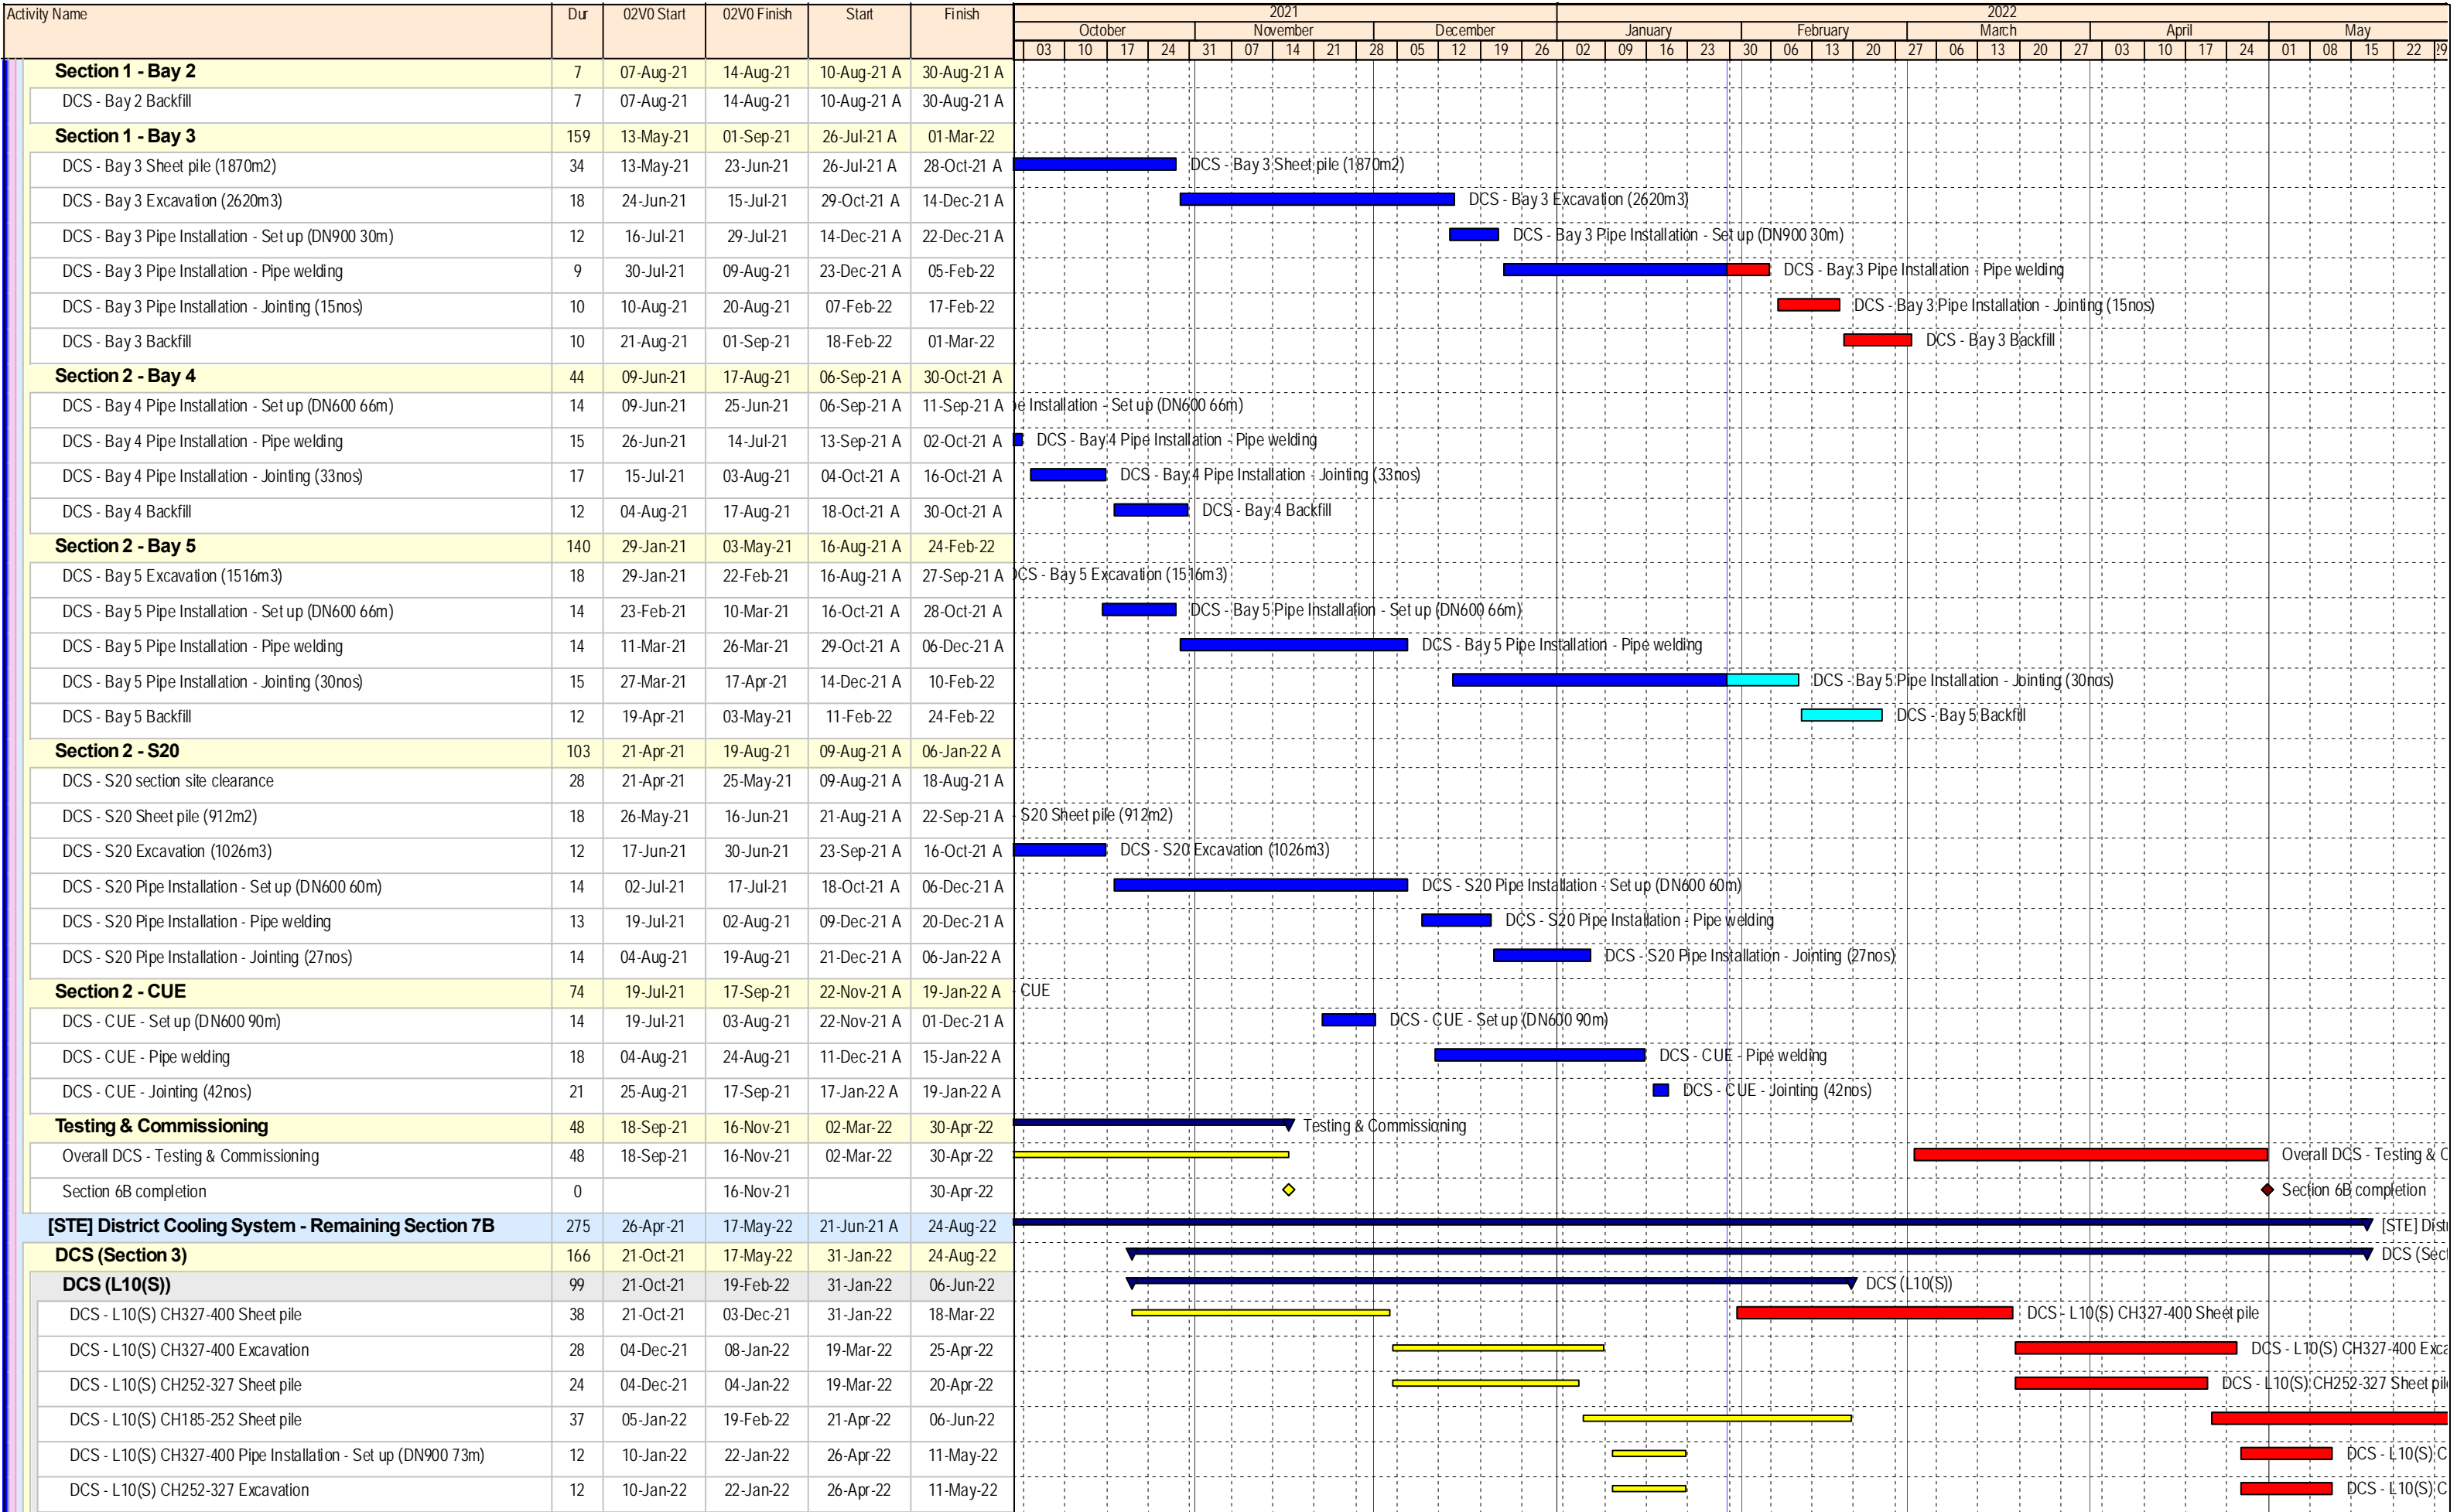


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

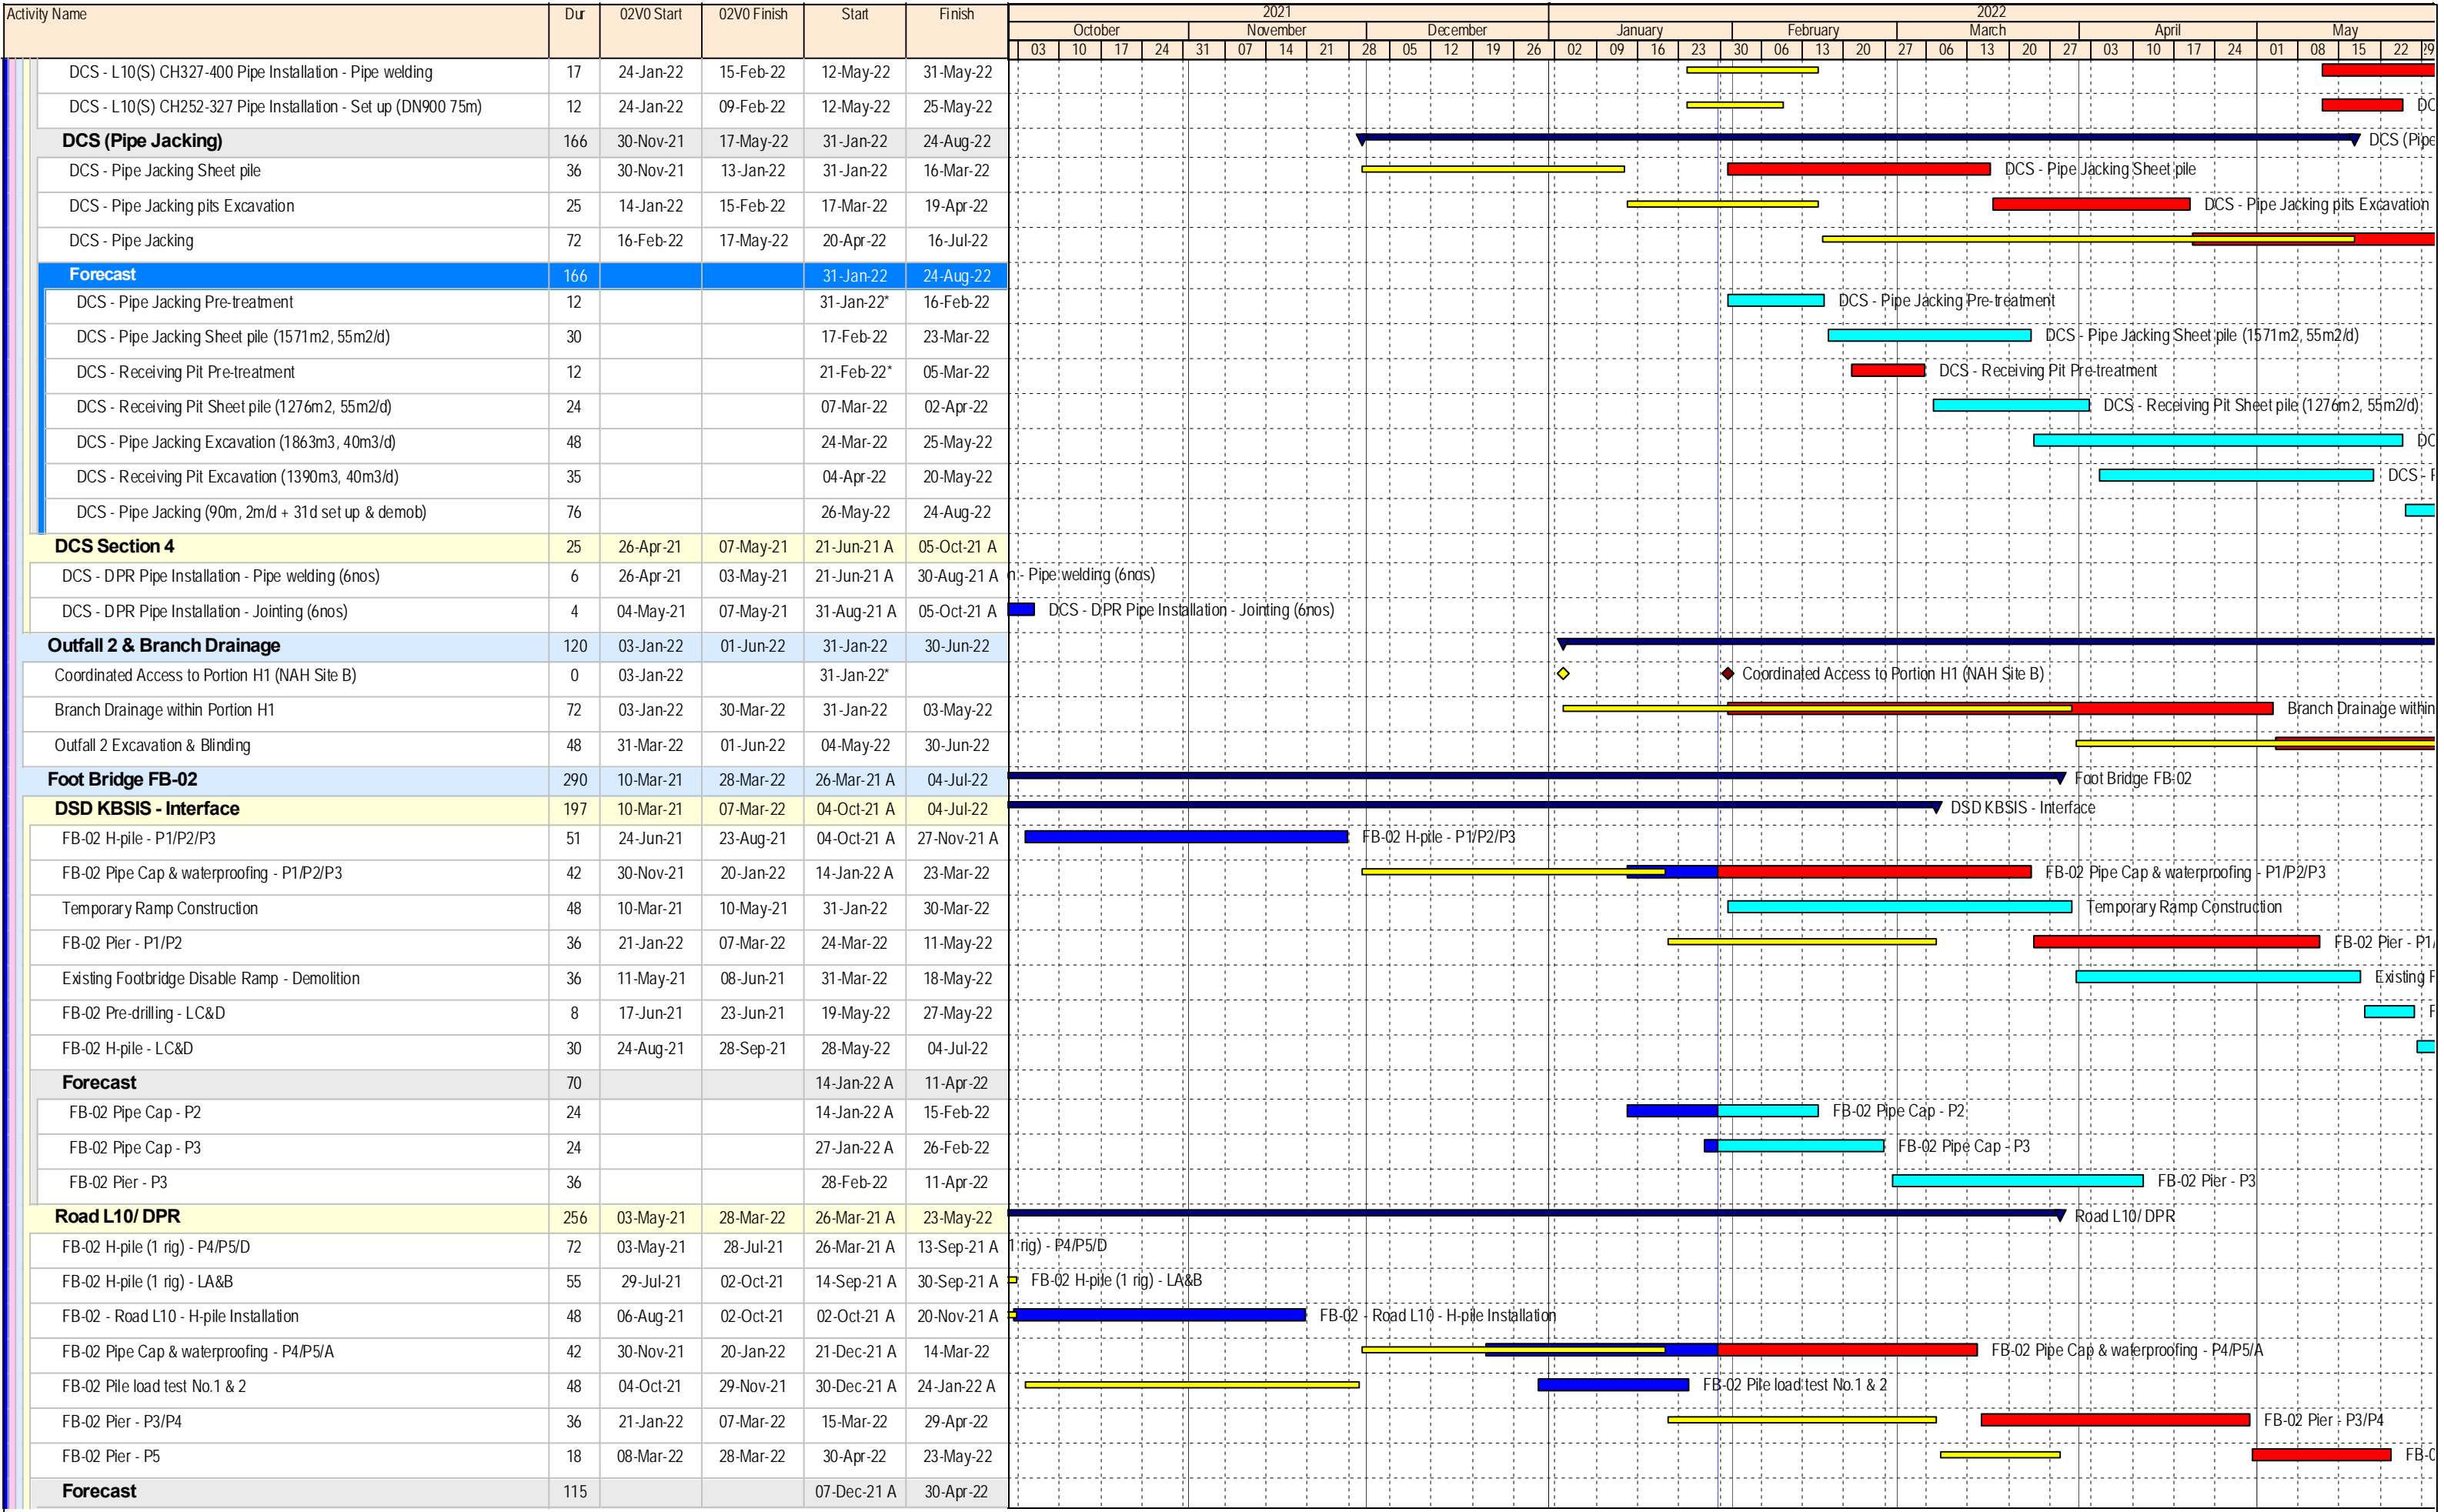

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron









### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021																									2022														
						October					November					December					January					February					March					April					May				
						03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27	03	10	17	24	01	08	15	22	29					
<b>Stage 3D (WCR westbound new traffic island)</b>	36	05-Aug-21	15-Sep-21	02-Oct-21 A	10-Nov-21 A	WCR westbound new traffic island																																							
Demolition of existing pavement	6	05-Aug-21	11-Aug-21	02-Oct-21 A	12-Oct-21 A	Demolition of existing pavement																																							
Connection for PL, ATC and E&M	12	12-Aug-21	25-Aug-21	13-Oct-21 A	20-Oct-21 A	Connection for PL, ATC and E&M																																							
Construction of new traffic island	18	26-Aug-21	15-Sep-21	21-Oct-21 A	10-Nov-21 A	Construction of new traffic island																																							
<b>Stage 4 (Hoi Bun Road)</b>	70	03-Mar-21	04-Aug-21	02-Aug-21 A	21-Sep-21 A																																								
<b>Stage 4A (HBR Planter)</b>	30	03-Mar-21	16-Jun-21	02-Aug-21 A	08-Sep-21 A																																								
Lower down existing manhole	6	03-Mar-21	09-Mar-21	02-Aug-21 A	10-Aug-21 A																																								
Reinstatement of footpath & carriageway	24	18-May-21	16-Jun-21	24-Aug-21 A	08-Sep-21 A	Footpath & carriageway																																							
<b>Stage 4B (HBR Fast Lane)</b>	12	22-Jul-21	04-Aug-21	01-Sep-21 A	21-Sep-21 A																																								
Installation of ducting for PL, ATC and E&M	3	22-Jul-21	24-Jul-21	01-Sep-21 A	08-Sep-21 A	Ducting for PL, ATC and E&M																																							
Reinstatement of carriageway	9	26-Jul-21	04-Aug-21	09-Sep-21 A	21-Sep-21 A	Reinstatement of carriageway																																							
<b>Stage 5 (Gas Station &amp; HBR)</b>	130	10-Mar-21	17-Oct-21	24-Aug-21 A	12-Feb-22	Stage 5 (Gas Station & HBR)																																							
<b>Stage 5A (Gas Station Footpath)</b>	74	10-Mar-21	16-Jun-21	25-Aug-21 A	05-Oct-21 A																																								
Installation of ducting for PL, ATC and E&M	6	10-Mar-21	16-Mar-21	25-Aug-21 A	20-Sep-21 A	Installation of ducting for PL, ATC and E&M																																							
Reinstatement of footpath & carriageway	24	18-May-21	16-Jun-21	21-Sep-21 A	05-Oct-21 A	Reinstatement of footpath & carriageway																																							
<b>Stage 5B (HBR traffic island)</b>	36	05-Aug-21	15-Sep-21	24-Aug-21 A	22-Sep-21 A	HBR traffic island																																							
Demolition of existing traffic island	6	05-Aug-21	11-Aug-21	24-Aug-21 A	31-Aug-21 A	Traffic island																																							
Connection for PL, ATC and E&M	12	12-Aug-21	25-Aug-21	01-Sep-21 A	07-Sep-21 A	ATC and E&M																																							
Construction of new traffic island	18	26-Aug-21	15-Sep-21	08-Sep-21 A	22-Sep-21 A	Construction of new traffic island																																							
<b>Stage 5C (HBR Left Turn Lane 1)</b>	12	16-Sep-21	30-Sep-21	30-Sep-21 A	23-Oct-21 A	Stage 5C (HBR Left Turn Lane 1)																																							
Installation of ducting for PL, ATC and E&M	3	16-Sep-21	18-Sep-21	30-Sep-21 A	09-Oct-21 A	Installation of ducting for PL, ATC and E&M																																							
Reinstatement of carriageway	9	20-Sep-21	30-Sep-21	12-Oct-21 A	23-Oct-21 A	Reinstatement of carriageway																																							
<b>Stage 5D (HBR Left Turn Lane 2)</b>	54	02-Oct-21	17-Oct-21	11-Nov-21 A	12-Feb-22	Stage 5D (HBR Left Turn Lane 2)																																							
Installation of ducting for PL, ATC and E&M	3	02-Oct-21	05-Oct-21	11-Nov-21 A	20-Nov-21 A	Installation of ducting for PL, ATC and E&M																																							
Reinstatement of carriageway	9	06-Oct-21	16-Oct-21	31-Jan-22	12-Feb-22	Reinstatement of carriageway																																							
Section 8D [STE] - Completion	0		17-Oct-21		12-Feb-22*	Section 8D [STE] - Completion																																							
Section 9F [STE] - Completion	0		17-Oct-21		12-Feb-22*	Section 9F [STE] - Completion																																							
<b>Establishment</b>	365	18-Oct-21	17-Oct-22	13-Feb-22	12-Feb-23																																								
HBR/ CYS / WCR Junction Modification - Establishment works	365	18-Oct-21	17-Oct-22	13-Feb-22	12-Feb-23																																								
<b>[STE] Road L10 (Northern)</b>	299	12-Oct-21	24-Aug-22	02-Jul-21 A	06-Jul-22																																								
<b>CUE</b>	299	12-Oct-21	24-Aug-22	02-Jul-21 A	06-Jul-22																																								
CUE L10(N) Excavation part 1	36	12-Oct-21	23-Nov-21	02-Jul-21 A	20-Oct-21 A	CUE L10(N) Excavation part 1																																							
CUE L10(N) ELS (Sheet pile) part 2	45	07-Apr-22	04-Jun-22	25-Aug-21 A	07-Mar-22																																								
CUE L10(N) Structure part 1	108	24-Nov-21	06-Apr-22	01-Dec-21 A	07-Jun-22																																								
CUE L10(N) Pump Test part 2	32	06-Jun-22	13-Jul-22	08-Mar-22	14-Apr-22																																								
CUE L10(N) Excavation part 2	36	14-Jul-22	24-Aug-22	19-Apr-22	01-Jun-22																																								
<b>Part 1</b>	242			02-Jul-21 A	26-Apr-22																																								
CUE L10(N) Part 1 Excavation	128			02-Jul-21 A	07-Oct-21 A	CUE L10(N) Part 1 Excavation																																							
CUE L10(N) Part 1 DL, Blinding, Waterproofing, BS (80m)	21			24-Dec-21 A	11-Feb-22	CUE L10(N) Part 1 DL, Blinding, Waterproofing, BS (80m)																																							
CUE L10(N) Part 1 Backfill & Strut S3 Removal	7			12-Feb-22	21-Feb-22	CUE L10(N) Part 1 Backfill & Strut S3 Removal																																							
CUE L10(N) Part 1 Wall & Top Slab (80m, 10d/20m)	32			21-Feb-22	30-Mar-22	CUE L10(N) Part 1 Wall & Top Slab (80m, 10d/20m)																																							
CUE L10(N) Part 1 Backfill & Remove S2 (80m, 10d/20m)	32			03-Mar-22	11-Apr-22	CUE L10(N) Part 1 Backfill & Remove S2 (80m, 10d/20m)																																							
CUE L10(N) Part 1 Backfill & Remove S1 (80m, 10d/20m)	32			15-Mar-22	26-Apr-22	CUE L10(N) Part 1 Backfill & Remove S1 (80m, 10d/20m)																																							
<b>Part 2</b>	253			25-Aug-21 A	06-Jul-22																																								


-  Milestone
-  Planned Bar
-  Critical Activity
-  Actual Milestone
-  Actual Work
-  Baseline Milestone
-  Baseline Bar
-  Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

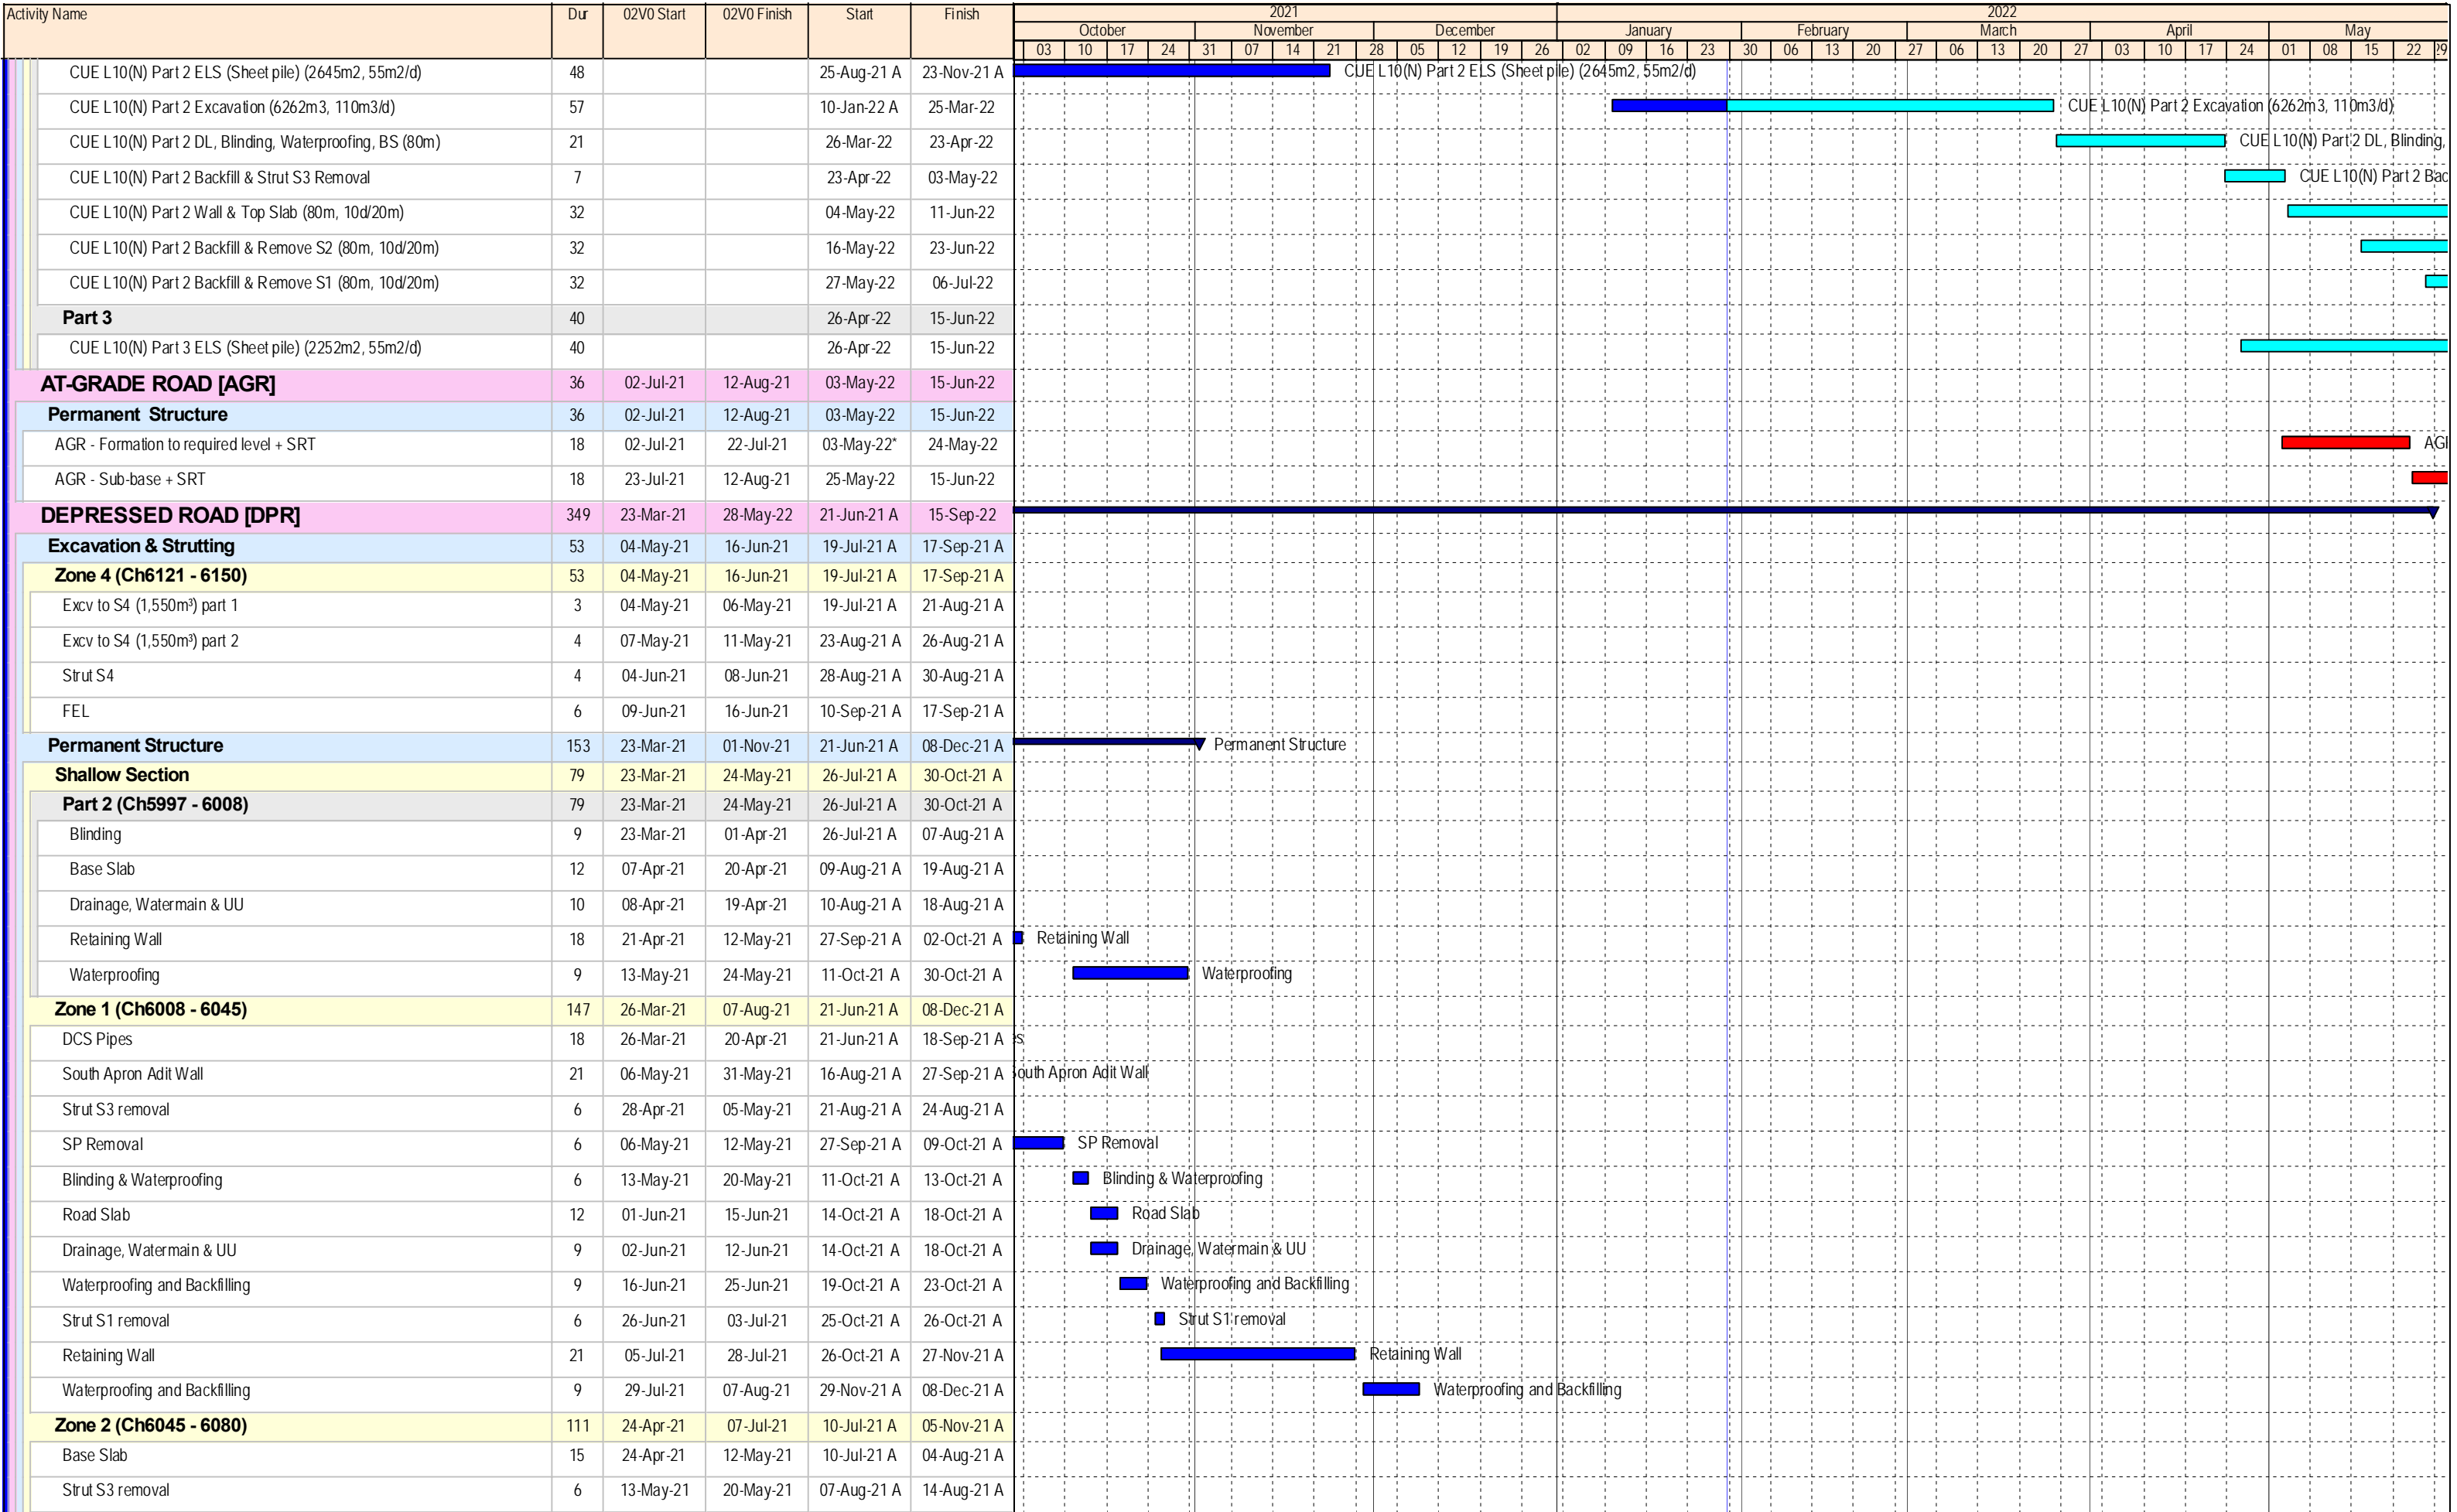

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




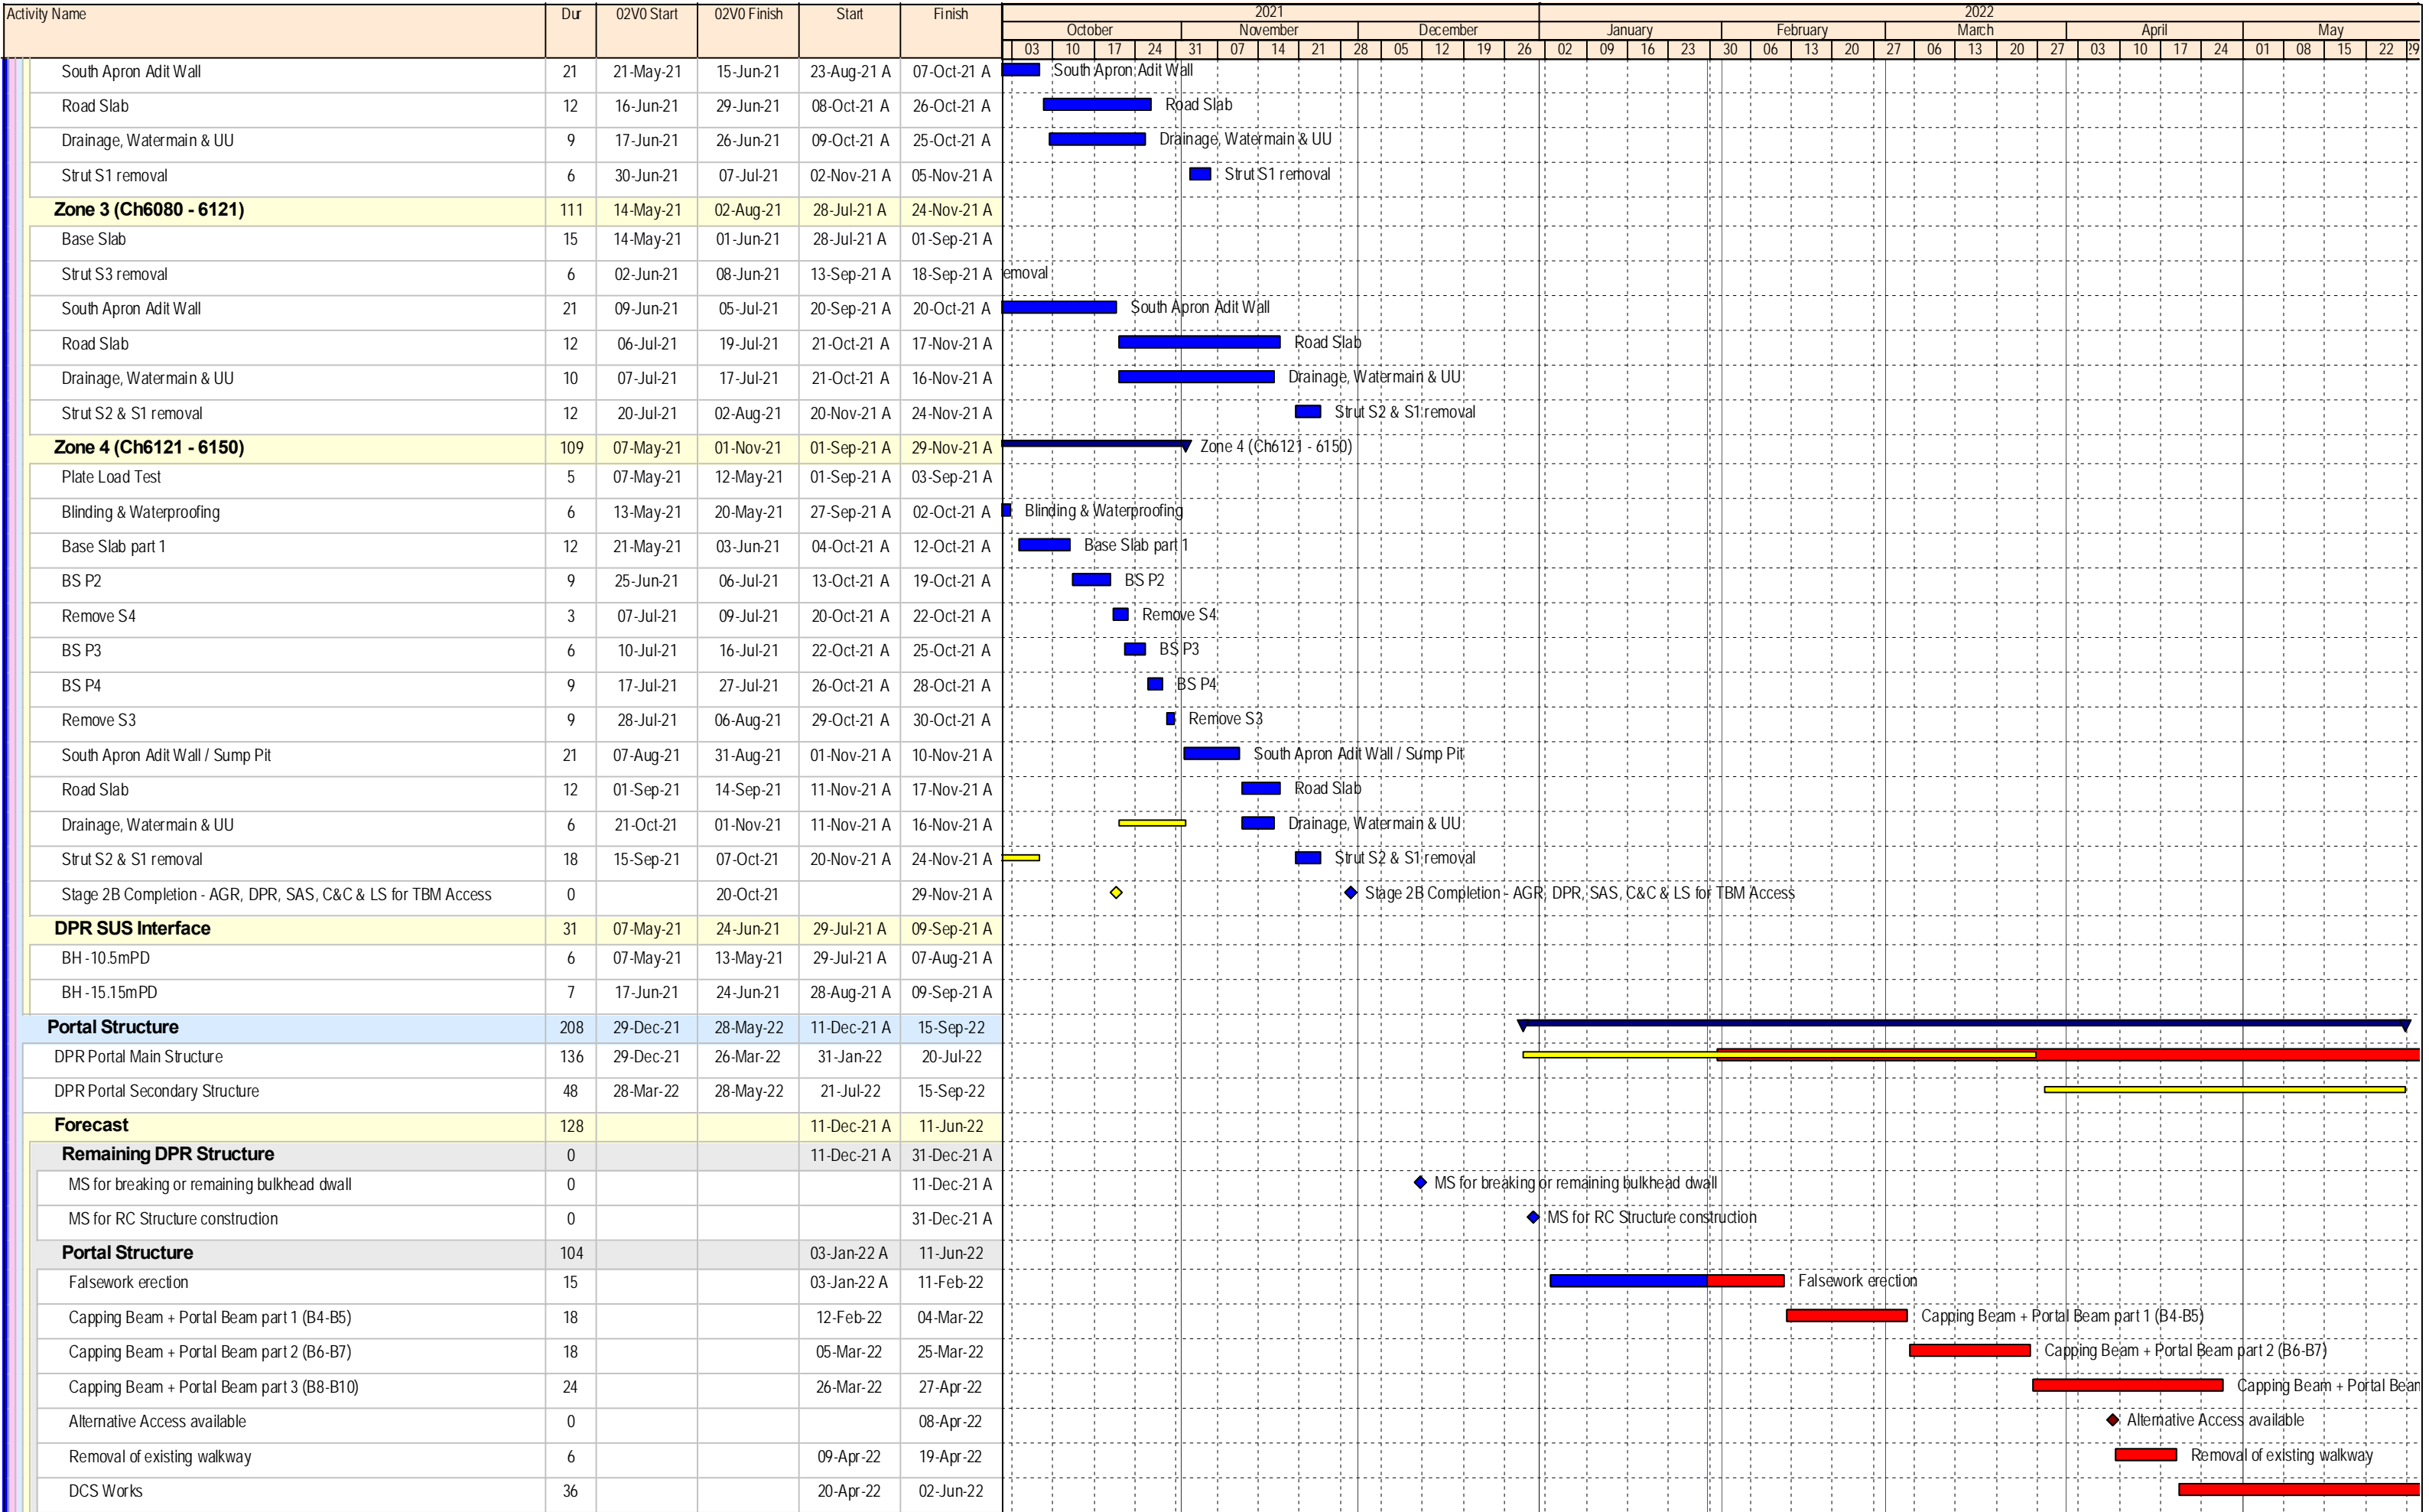

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu






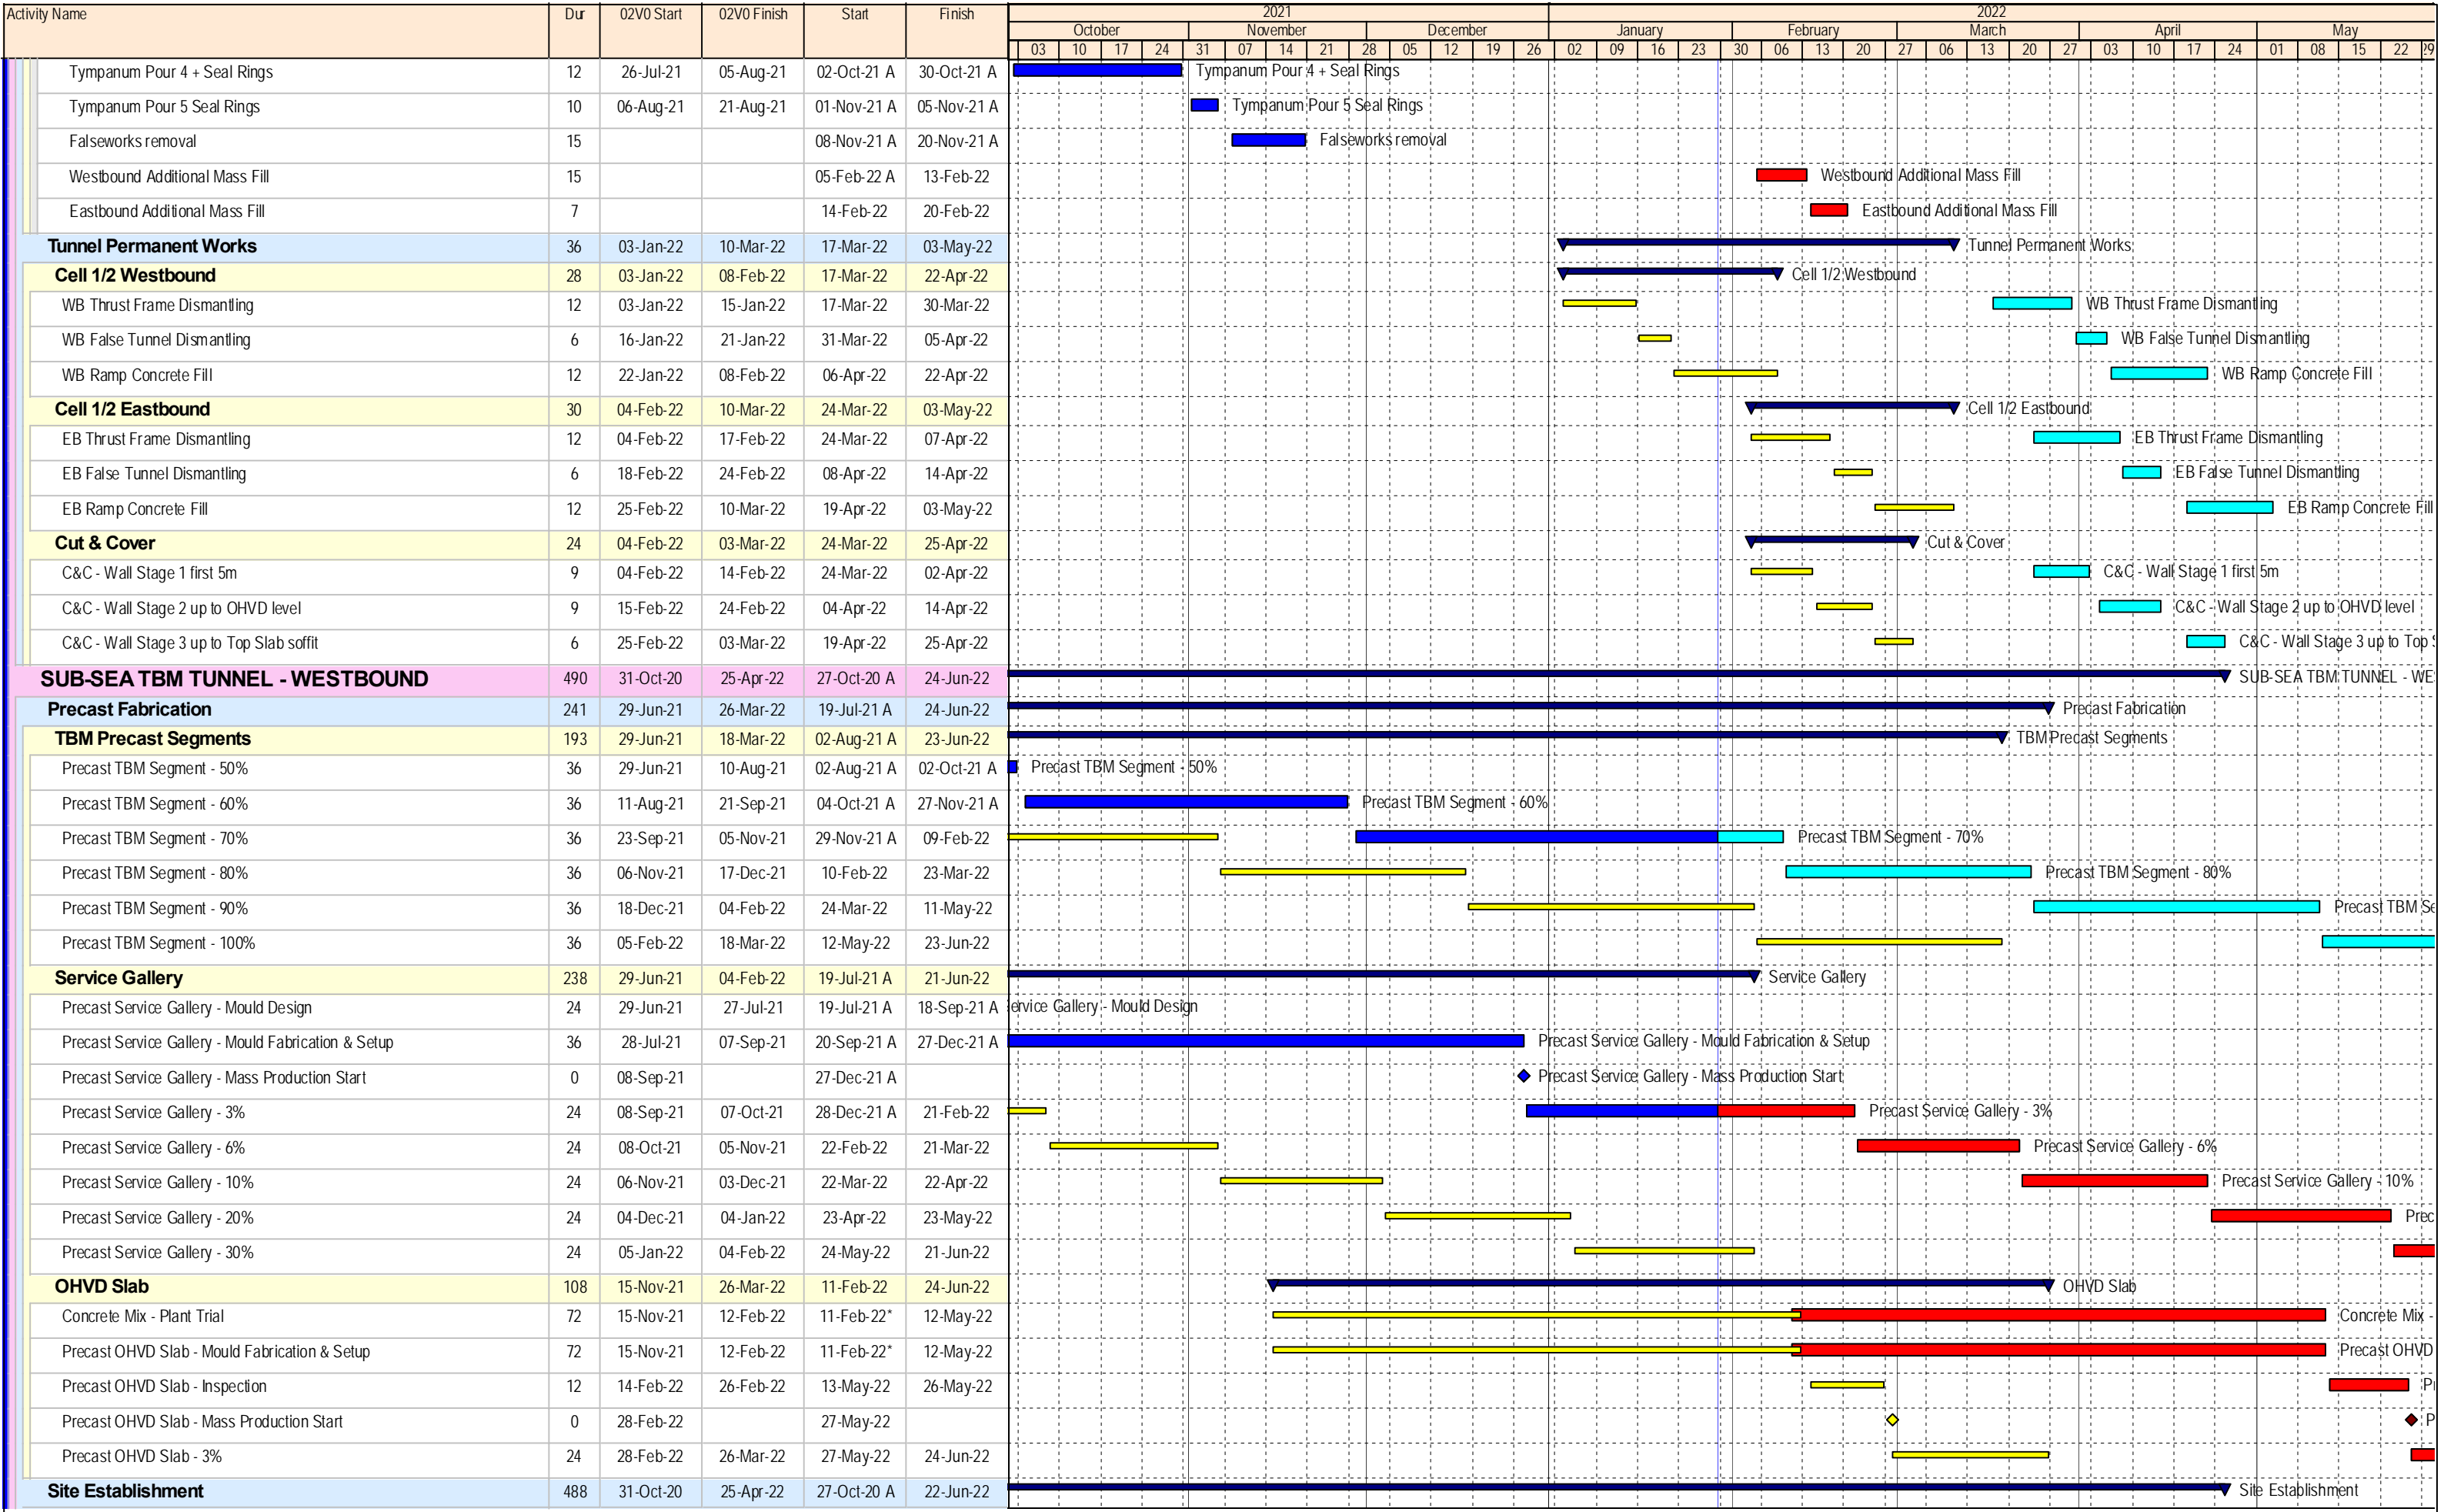

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu




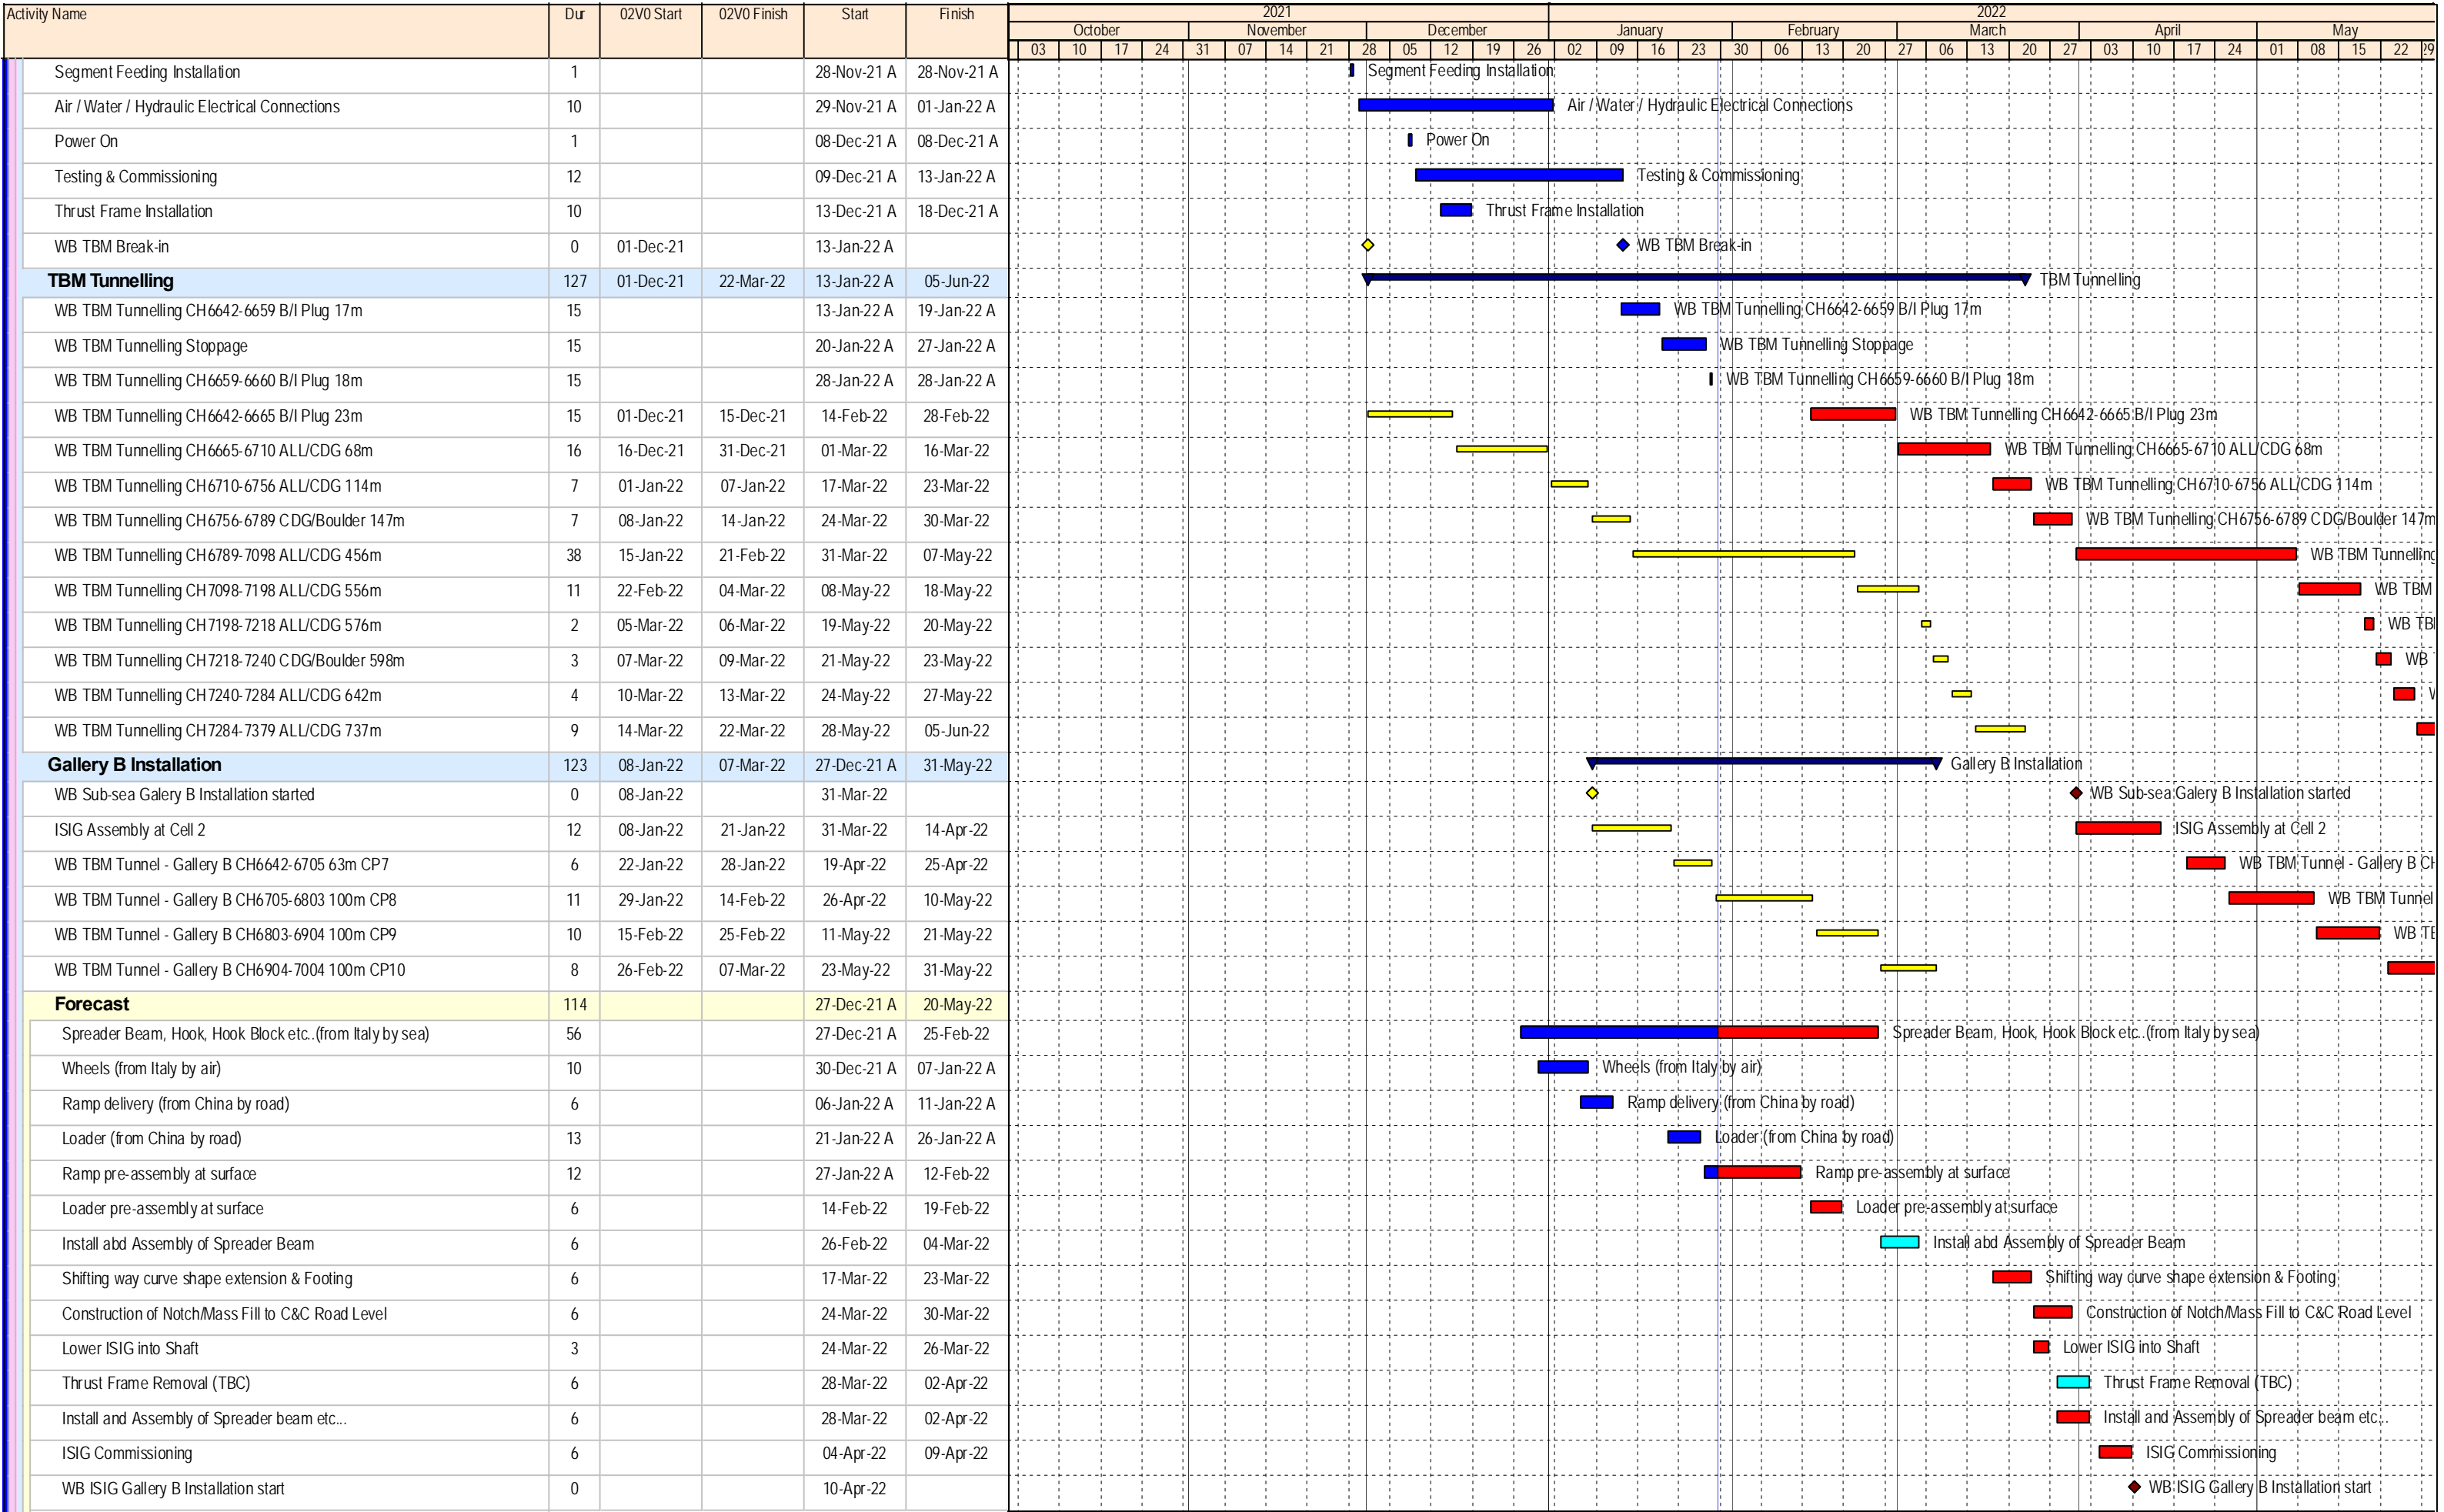

- ◆ Milestone
- ▶ Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar
- ▶ Summary


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu



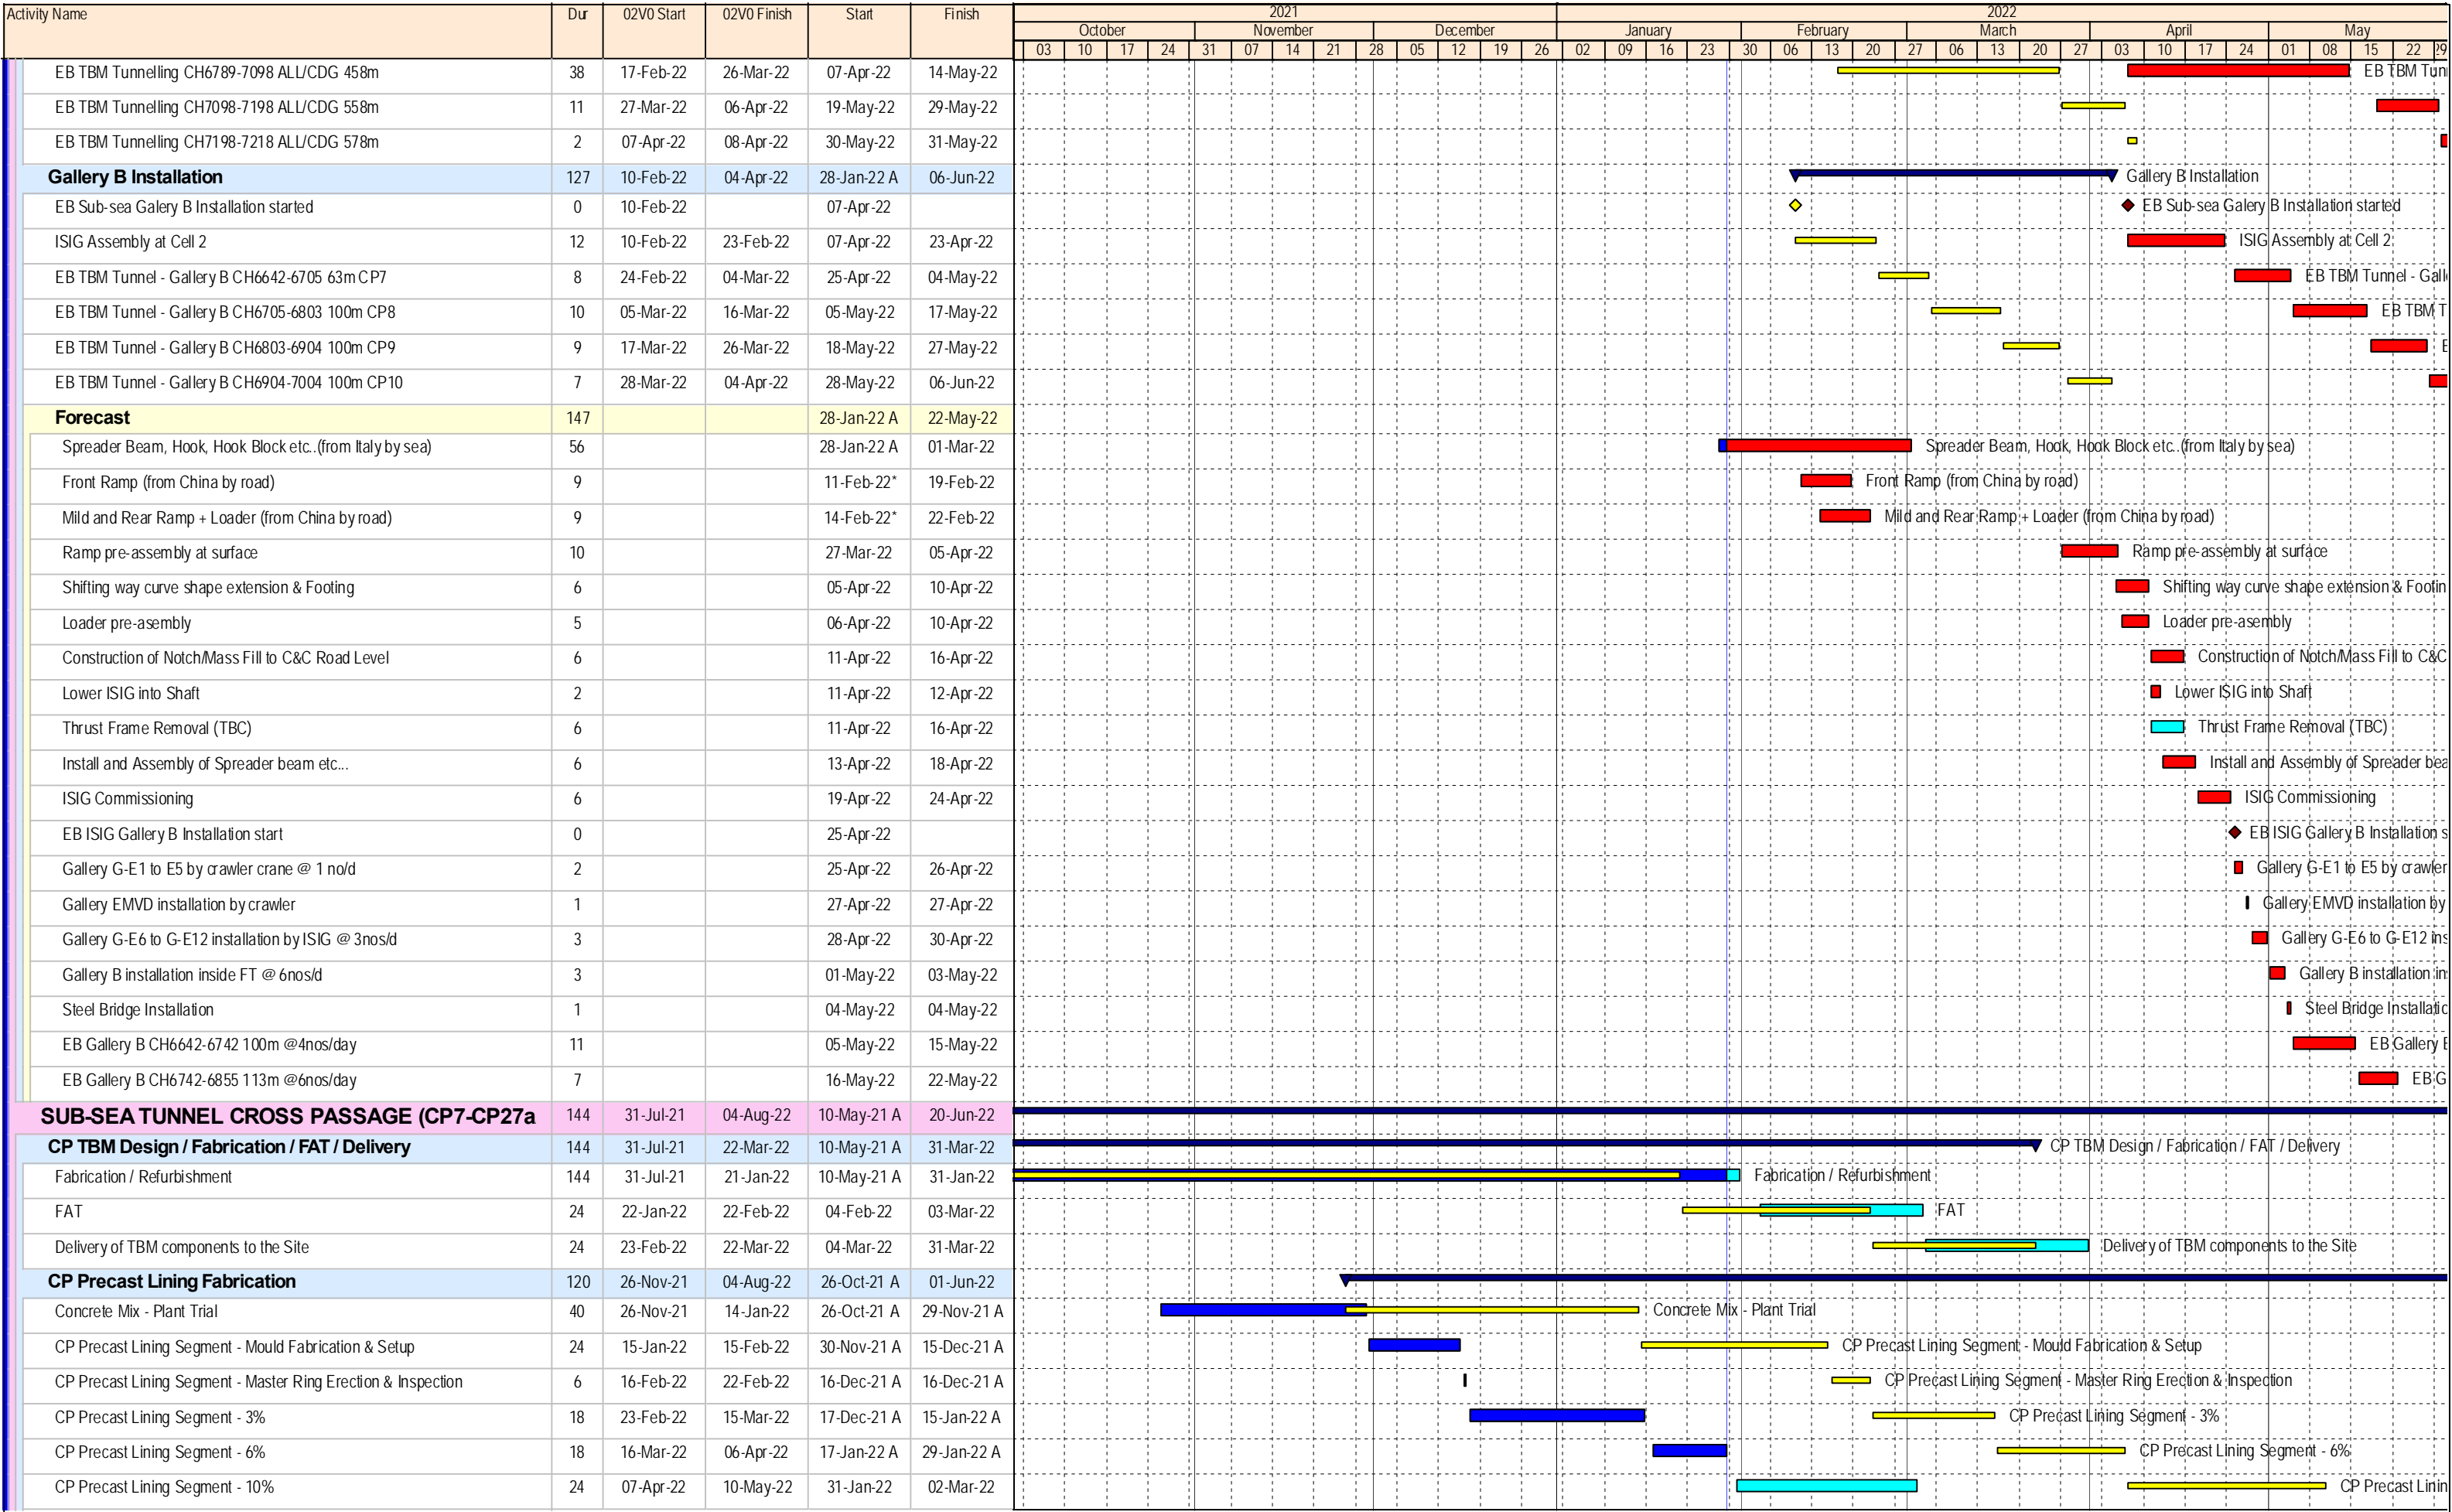

- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Actual Milestone
- Actual Work
- ◆ Baseline Milestone
- Baseline Bar
- ↔ Summary


# ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

## Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/Lo	WYu
09-Apr-20	01V1	SPa/Lo	WYu
17-Jul-20	01V2	SPa/Lo	WYu
09-Oct-20	01V3	SPa/Lo	WYu
02-Jul-21	02V0	SPa/Lo	WYu




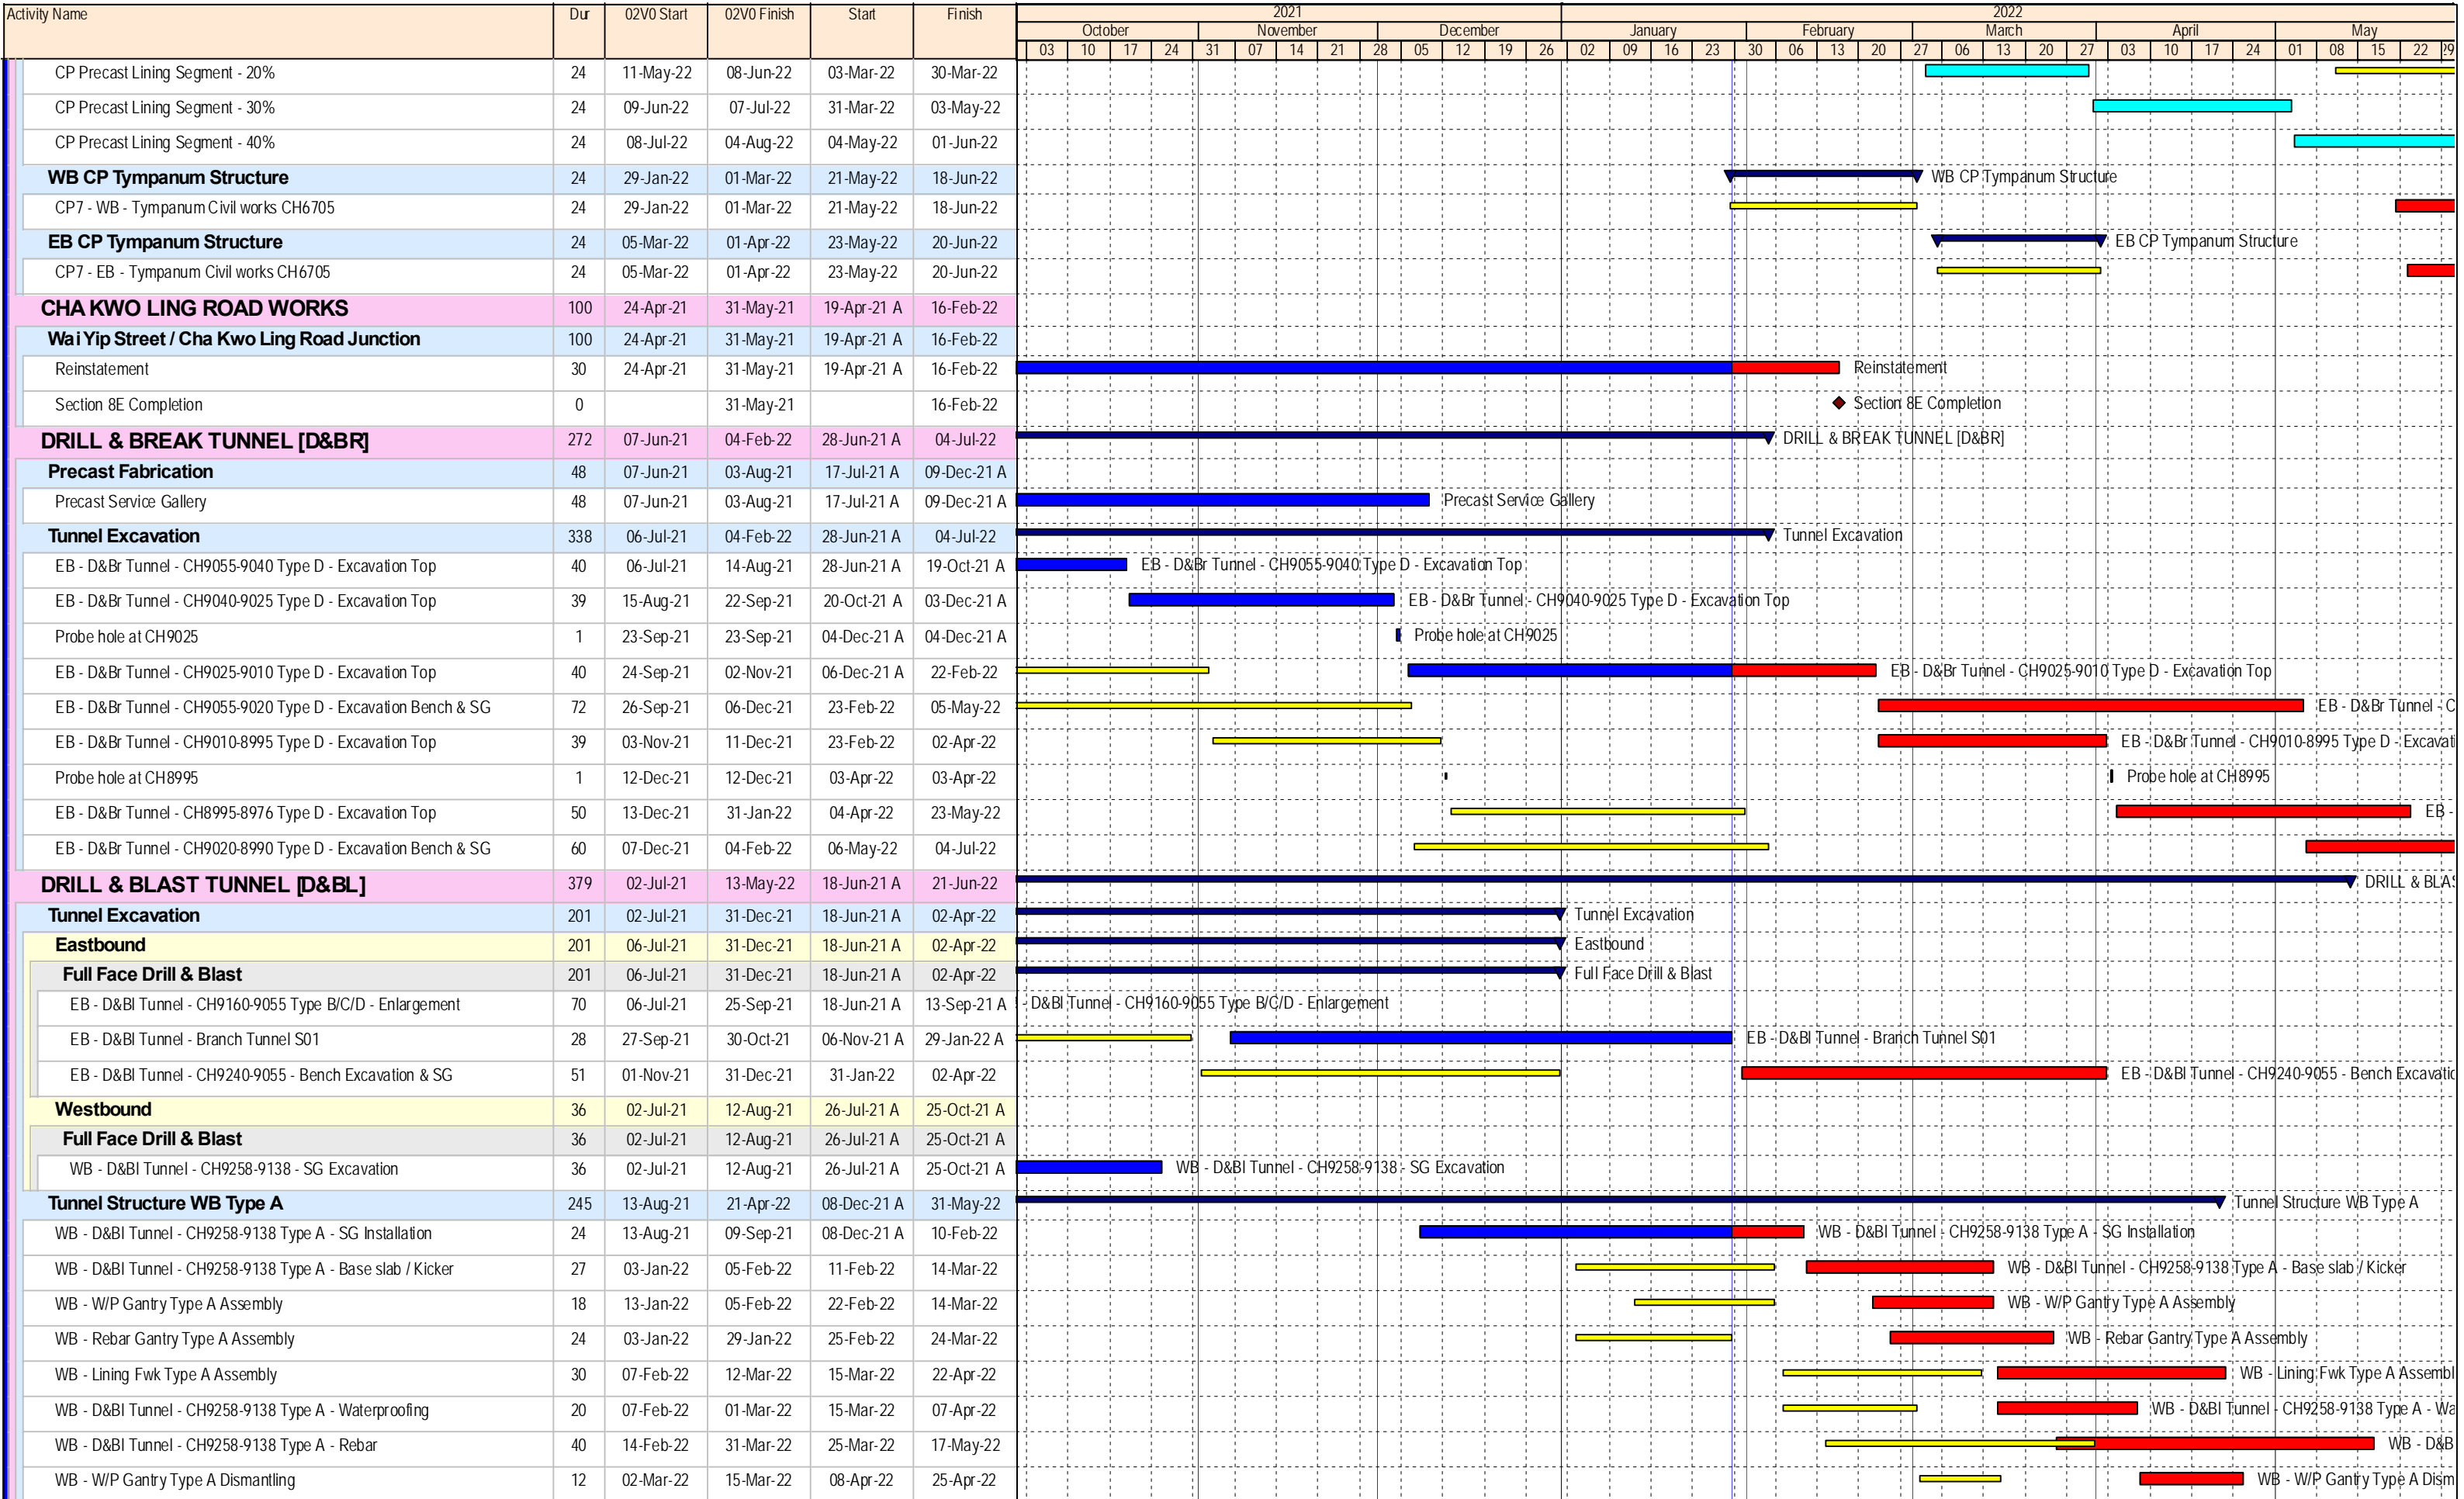

- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ◆ Planned Bar
- ◆ Critical Activity
- ◆ Actual Work
- ◆ Baseline Bar
- ◆ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme (Jan-22)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu



