
Civil Engineering and Development Department

Trunk Road T2 Monthly Environmental Monitoring and Audit Report (under EP-451/2013)

December 2021 (Version 1.0)



REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388 Email: info@cinotech.com.hk



Ref.: CEDKTDT2EM00_0_0310L.22

18 January 2022

Hyder-Meinhardt Joint Venture 17/F, Two Harbour Square 180 Wai Yip Street, Kwun Tong Kowloon, Hong Kong

By Post and Email

Attention: Mr. Edwin China

Dear Mr. Ching,

Re: Agreement No. EDO 01/2019 **Independent Environmental Checker for** Contract No. ED/2018/04 - Trunk Road T2 and Infrastructure Works for **Developments at the Former South Apron**

Monthly EM&A Report (December 2021) for EP-451/2013

Reference is made to the Environmental Team's submission of the Monthly EM&A Report for December 2021 (Version 1.0) certified by the ET Leader and provided to us via e-mail on 17 January 2022. We are pleased to inform you that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 of EP-451/2013.

The ET Leader is reminded that it is the ET's responsibility to ensure the report be timely submitted to the Director of Environmental Protection as per Condition 3.4 of EP-451/2013.

Thank you for your attention. Please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely, For and on behalf of Ramboll Hong Kong Limited

Y H Hui

Independent Environmental Checker

C.C.

CEDD

Attn.: Mr. Tommy Wong

Fax: 2739 0076

BTP

Attn.: Mr. Ivan Chau

By email

Cinotech

Attn.: Mr. K. S. Lee

Fax: 3107 1388

Q:\Projects\CEDKTDT2EM00\02 Proj_Mgt\02 Corr\CEDKTDT2EM00_0_0310L.22.doc

TABLE OF CONTENTS

		Page
EX	ECUTIVE SUMMARY	1
	Introduction	1
	Summary of Main Works Undertaken and Key Measures Implemented	
	Summary of Exceedances, Investigation and Follow-up	
	Complaint Handling, Prosecution and Public Engagement	
	Reporting Changes	
	Review of Status and Location of Monitoring Stations	
1	INTRODUCTION	5
	Background	5
	Purpose of the Report	
	Project Organizations	
	Construction Activities undertaken during the Reporting Month	
	Summary of EM&A Requirements	
	Status of Environmental Licensing and Permitting	
2	AIR QUALITY	
	Monitoring Requirement	
	Monitoring Locations	
	Monitoring Parameters and Frequency	
	Monitoring Methodology	
	Results and Observations	
	Comparison of EM&A Result with EIA Prediction	
3	NOISE	15
	Monitoring Requirements	15
	Monitoring Locations	15
	Monitoring Parameters, Frequency and Duration	
	Monitoring Equipment	
	Monitoring Methodology and QA/QC Procedure	
	Results and Observations	
	Comparison of EM&A Result with EIA Prediction	
4	WATER QUALITY	19
	Monitoring Requirement	19
5	MARINE ECOLOGY	19
6	FISHERIES	19
7	LANDSCAPE AND VISUAL	20
8	CULTURAL HERITAGE	23
9	WASTE MANAGEMENT	23

10	ENVIRO	ONMENTAL AUDIT	24
	Site Au	dits	24
		entation Status of Environmental Mitigation Measures	
		entation Status of Event and Action Plans	
		f Required Submission under Environmental Permit	
11	ENVIRO	ONMENTAL NON-CONFORMANCE	27
		ry of Complaint, Warning, Notification of any Summons and Successful Prosecuti ry of Exceedance	
12	FUTUR	E KEY ISSUES	27
	Monitor	ing Schedule	27
13	CONCL	USIONS AND RECOMMENDATIONS	28
	Conclus	ions	28
		nendations	
LIST	ΓOFTA	BLES	
Tabl	e I	Summary of Complaint/Summons/Prosecution in the Reporting Month	
Tabl	e II	Summary Table for Site Activities in the next Reporting Period	
Tabl		Summary Table for Review of Status and Location of Monitoring Stations	
Tabl		Key Project Contacts	
Tabl		Summary of Environmental License and Permit	
Tabl		Air Quality Monitoring Locations	
Tabl		Frequency and Parameters of Air Quality Monitoring	
Tabl		Air Quality Monitoring Equipment	
Tabl		Major Dust Source during Air Quality Monitoring	7)
Tabl		Comparison of 1-hr TSP Monitoring Data with Predictions in EIA Report (not us	sed)
Tabl		Comparison of 24-hr TSP Monitoring Data with Predictions in EIA Report	
Tabl		Noise Monitoring Stations	
	e 3.2	Frequency and Parameters of Noise Monitoring	
Tabl		Noise Monitoring Equipment	
Tabl		Major Noise Source during Noise Monitoring	
Tabl		Baseline Noise Level and Noise Limit Level for Monitoring Stations	
Table Table		Comparison of Noise Monitoring Data with Predictions in EIA Report	
Tabl		Additional Noise Monitoring Results Construction Phase Landscape and Visual Mitigation Massures	
	e 7.1 e 7.2	Construction Phase Landscape and Visual Mitigation Measures Construction Phase Audit Checklist for Landscape and Visual Mitigation Measures	rec
	e 10.1	Observations and Recommendations of Site Audit	103
	e 10.1 e 10.2	Status of Required Submission under Environmental Permit	
1 aul	C 10.2	Status of Required Submission under Environmental Permit	
LIST	Г OF FIG	GURES	

Figure 1.1	Layout Plan of the Project Site
Figure 1.2	Project Organisation for Environmental Monitoring and Audit
Figure 2	Locations of Air Quality and Construction Noise Monitoring Stations

LIST OF APPENDICES

Appendix A	Action and Limit Levels
Appendix B	Environmental Monitoring Schedules
Appendix C	Copies of Calibration Certificates for Air Quality Monitoring
Appendix D	Weather Information
Appendix E	1-hour TSP Monitoring Results and Graphical Presentations (not used)
Appendix F	24-hour TSP Monitoring Results and Graphical Presentations
Appendix G	Copies of Calibration Certificates for Noise Monitoring
Appendix H	Noise Monitoring Results and Graphical Presentations
Appendix I	Site Audit Summary
Appendix J	Event and Action Plans
Appendix K	Environmental Mitigation Implementation Schedule (EMIS)
Appendix L	Summaries of Environmental Complaint, Warning, Summon and Notification of
••	Successful Prosecution
Appendix M	Summary of Exceedance
Appendix N	Tentative Construction Programme
Appendix O	Waste Generated in the Reporting Month

EXECUTIVE SUMMARY

Introduction

1. This is the 22nd Environmental Monitoring and Audit (EM&A) Report prepared by the Environmental Team (ET), Cinotech Consultants Ltd., for "Trunk Road T2". This report summarized the monitoring results and audits findings of the EM&A programme under the issued Environmental Permit (EP) No. EP-451/2013 and in accordance with the EM&A Manual (AEIAR-174/2013) during the reporting month of December 2021.

Summary of Main Works Undertaken and Key Measures Implemented

2. The main works undertaken during the reporting period are as follows:

Kai Tak:

- Road L10 (North) Excavation, ELS and RC Structure
- Road L18 Sheet Pile Installation
- Westbound TBM Assembly
- Eastbound TBM Assembly
- TBM Shifting way & Rails installation
- TBM WB & EB TBM Thrust Frame installation
- STP Assembly
- 2nd Segment Yard Gantry Crane Erection
- Foot Bridge (FT-02) H pile installation and Pile Cap Construction
- Mortar Plant assembly
- District Cooling System works at Section 6B and 7A
- Depressed Road- Capping Beam
- SUS Remedial works and Bulkhead Removal
- West Ventilation Building Excavation, Steel Strut Installation
- Section 6A Junction & Entrance Sheet Pile
- Break-in Plug wells installation
- 3. Implementation of the key mitigation measures during the reporting period are as follows:

Air Quality

- Water spraying regularly on construction site area to avoid dust generation.
- Excavated dusty materials were covered by impervious sheets.

Noise

- Air compressor was operated with door closed and have valid noise labels.
- Use of Quality Powered Mechanical Equipment (QPME)
- Erecting noise barriers on site to minimize noise impact generated from breaking activities.

Water Quality

• WetSep was constructed to treat the surface runoff prior to discharge.

Landscape and Visual

• Tree protection zone were fenced off to protect the existing tree.

Summary of Exceedances, Investigation and Follow-up

4. Exceedance of Action/Limit levels during the reporting month (December 2021) and the investigation results and/or follow-up actions:

Air Quality Monitoring

- No Action Level exceedance for 24-hour TSP was recorded.
- No Limit Level exceedance for 24-hour TSP was recorded.

Construction Noise Monitoring

- No Limit Level exceedance for day time construction noise was recorded in this reporting month.
- No Action Level exceedance was recorded in this reporting month.

Landscape and Visual Monitoring and Audit

• No non-compliance of the landscape and visual impact was recorded in the reporting month. The implementation of landscape and visual and mitigation measures was checked by a Registered Landscape Architect (RLA) during the environmental site inspections.

Complaint Handling, Prosecution and Public Engagement

Table I Summary of Complaint/Summons/Prosecution in the Reporting Month

E-vo-4	Event Details		Follow-up/	Status/
Event	Number	Brief Description	Remedial Actions	Remarks
Complaints Received	0	-	-	-
Notification of				
Summons and	0	-	-	-
Prosecutions Received				
Public Engagement	0			
Activities	U	-	-	_

Reporting Changes

5. No reporting change in this reporting month.

Future Key Issues

6. The key works or activities will be anticipated in the next reporting period are as follows:

Table II Summary Table for Site Activities in the next Reporting Period

Site Activities (January 2022)	Key Environmental Issues
 CUE Section 6A Junction- RC structure Workshop Assembly West Ventilation Building – Pumping Test Westbound and Eastbound TBM break-in 	(A) / (B) / (C) / (D)

Note

- (A) Dust generation from haul road, stockpile of dusty materials, exposed site area, excavation works and rock breaking activities;
- (B) Noisy construction activity such as rock-breaking activities and piling works;
- (C) Runoff from exposed slope or site area; and
- (D) Wastewater and runoff discharge from site.

Review of Status and Location of Monitoring Stations

7. According to the EM&A Manual (AEIAR-174/2013), the number and location of the monitoring stations and parameters should be reviewed in every six months, or on as -needed basis, in order to cater for any changes in the surrounding environmental and the nature of works in progress. The latest review was conducted in August 2021 and the review of status and location of monitoring stations are summarized as follow:

Table III Summary Table for Review of Status and Location of Monitoring Stations

Monitoring Station ID	Review Status	Follow-up Action/ Recommendation
KTD 2d	ET has reviewed the status and location	
KER1	of KER1, KTD 1, KTD2d, CKL1 and CKL2. To conclude, the environmental	
KTD 1	monitoring conducted at KER1, KTD 1, KTD2d, CKL 1 and CKL 2 are appropriate, and the monitoring results	N/A
CKL 1	reflect how the sensitive receiver(s) is/are impacted by the construction	
CKL 2	activities of the Project.	

N/A: Not Applicable

1 INTRODUCTION

Background

- 1.1 In 2009, Civil Engineering and Development Department (CEDD) commissioned a Kai Tak Development (KTD) Trunk Road T2 and Infrastructure at South Apron Investigation. The assignment covers the provision of the Trunk Road T2 and its connections with the Central Kowloon Route (CKR) at the north apron area and the Tseung Kwan O Lam Tin Tunnel (TKOLTT) to the south in the Cha Kwo Ling area.
- 1.2 The Trunk Road T2 Project is one of the designated Projects under Schedule 2 of the EIAO proposed in the KTD. CEDD submitted the Project Profile (No. PP-379/2009) on 24 March 2009 for application for an EIA study brief for the Trunk Road T2 Project under the EIAO. Accordingly, an EIA Study Brief (ESB-203/2009) for the Trunk Road T2 Project was issued on 30 April 2009. The Environmental Impact Assessment (EIA) Report for the Trunk Road T2 Project was approved under the Environmental Impact Assessment Ordinance (EIAO) on 19 September 2013. The corresponding Environmental Permit (EP) was issued on 19 September 2013 (EP no.: EP-451/2013).
- 1.3 The Contract No. ED/2018/04 is the main contract of Trunk Road T2 ("T2 Main Works") which comprises mainly the design and construction of a dual two-lane trunk road of approximately 3.0km long with about 2.7km of the trunk road in form of tunnel; ventilation and administration buildings, environmental protection and mitigation works and etc. The EM&A programme at Kai Tak area under this Contract is governed by the EP-451/2013 and EM&A Manual (AEIAR-174/2013). The work areas of the T2 Main Works are shown in **Figure 1** and the works to be executed under this Contract and corresponding EP is summarized as follows:

Environmental Permit	Works Description
EP-451/2013 – Trunk Road T2	<u>Trunk Road T2</u>
	• Construction of highway and sub-sea tunnel connecting between
	Central Kowloon Route and Cha Kwo Ling Tunnel
	Western & Eastern Ventilation Buildings

Monitoring Works in Kai Tak under EP-451/2013

1.4 Under Contract No. KL/2014/03 - Kai Tak Development - Stage 3 Infrastructure Works for Development at the Southern Part of the Former Runway ("T2 Advance Works"), the baseline monitoring works in Kai Tak under the EM&A Manual (AEIAR-174/2013) were conducted by the Environmental Team (ET) for the Contract No. KL/2014/03 at the approved relocated monitoring locations (EPD reference: EP2/K19/A/21 pt.5), namely KTD1a, KTD2a & KER1a. During the impact monitoring period, monitoring locations KTD 2a and KER 1a were relocated to new locations, i.e. KTD 2b and KER 1b (EPD reference: () in EP2/K19/A/21 pt. 6 and () in EP2/K19/A/21 pt. 5) respectively. Location KTD2b was then further relocated to location KTD2c, the proposal of such relocation was submitted to EPD on 24 March 2020 and was approved by EPD on 6 April 2020 (EPD reference: () in EP2/K19/A/21 pt.7). The aforementioned relocation was effective from 9 April 2020. Since the major part of work under Contract No. KL/2014/03 has been completed and monitoring works conducted by the ET of Contract No. KL/2014/03 was determined to be ceased, the impact monitoring within the Kai Tak area was then handed over to the ET of Contract No. ED/2018/04 on 1 August 2020. The monitoring location has been reviewed and updated to obtain the data with higher representative

based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to the monitoring location KTD1 and KER1 on 3 August 2020, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Location KTD2c was then further relocated to location KTD2d, the proposal of such relocation was submitted on 9 March 2021 and was approved by EPD on 3 May 2021 (EPD reference: () in EP2/K19/A/21 pt.8). The aforementioned relocation was effective from 24 May 2021. The impact monitoring for the three stations KTD1, KTD2d and KER1 are currently conducted by the ET of T2 Main Works

Monitoring Works in Cha Kwo Ling under EP-451/2013

- 1.5 The environmental impact of the remaining works in Cha Kwo Ling, under EP-451/2013, shall be monitored at the two proposed stations, namely CKL1, CKL2, in accordance to the EM&A Manual (AEIAR-174/2013). The impact monitoring for the two proposed stations shall be conducted by the ET of T2 Main Works.
- 1.6 Cinotech Consultants Ltd. was designated as the Environmental Team (ET) to undertake the EM&A works for "Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron" (hereinafter called the "Project").

Purpose of the Report

1.7 This is the 22nd Monthly EM&A Report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period in December 2021.

Project Organizations

- 1.8 Different Parties with different levels of involvement in the Project organization include:
 - Permit Holder Civil Engineering and Development Department (CEDD)
 - Supervisor Representative Hyder-Meinhardt Joint Venture (HMJV)
 - Environmental Team (ET) Cinotech Consultants Limited (Cinotech)
 - Independent Environmental Checker (IEC) Ramboll Hong Kong Limited (Ramboll)
 - Contractor Bouygues Travaux Publics (BTP)
- 1.9 The key contacts of the Project are shown in **Table 1.1**.

Table 1.1 Key Project Contacts

Party	Role	Contact Person	Phone No.
CEDD	Permit Holder	der Mr. Wong Chi Wai, Tommy	
HMJV	HMJV Supervisor Representative Ms. Hazel Tang		2149 8524
Cincted.	Environmental Team	Mr. KS Lee (ETL)	2151 2091
Cinotech		Ms. Karina Chan	2157 3880

Party	Role	Contact Person	Phone No.
Ramboll	Independent Environmental Checker	Mr. YH Hui	3465 2850
BTP	Contractor	Ms. Ality Chan	5185 4462

1.10 The Organizational Structure for Environmental Management is shown in **Figure 1.2**.

Construction Activities undertaken during the Reporting Month

1.11 The major site activities undertaken in the reporting month included:

Kai Tak:

- Road L10 (North) Excavation, ELS and RC Structure
- Road L18 Sheet Pile Installation
- Westbound TBM Assembly
- Eastbound TBM Assembly
- TBM Shifting way & Rails installation
- TBM WB & EB TBM Thrust Frame installation
- STP Assembly
- 2nd Segment Yard Gantry Crane Erection
- Foot Bridge (FT-02) H pile installation and Pile Cap Construction
- Mortar Plant assembly
- District Cooling System works at Section 6B and 7A
- Depressed Road- Capping Beam
- SUS Remedial works and Bulkhead Removal
- West Ventilation Building Excavation, Steel Strut Installation
- Section 6A Junction & Entrance Sheet Pile
- Break-in Plug wells installation

Summary of EM&A Requirements

- 1.12 The EM&A programme requires construction noise, air quality monitoring and environmental site audit, etc. The EM&A requirements for each parameter are described in the following sections, including:
 - All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event Action Plans:
 - Environmental mitigation measures, as recommended in the Project EIA Report.
- 1.13 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in **Section 10** of this report.
- 1.14 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the monitoring parameters of the required environmental monitoring works and audit works for the Project in December 2021.

Status of Environmental Licensing and Permitting

1.15 All permits/licenses obtained for the Project are summarized in **Table 1.3**.

Table 1.3 Summary of Environmental License and Permit

D	Valid Period		G
Permit / License No.	From	To	Status
Environmental Permit (EP)			
EP-451/2013	19 Sep 2013	N/A	Valid
Notification pursuant to Air Pollution (Const	ruction Dust) R	egulation	
Ref. No.: 451120	20 Nov 2019	N/A	Valid
Billing Account for Construction Waste Disp	osal		
A/C No.: 7036016	09 Dec 2019	N/A	Valid
Billing Account for Vessel Disposal			
A/C No.:7037747 (Application No.: CEDD01126)	20 Oct 2021	25 Jan 2022	Valid
Construction Noise Permit			
CNP No.(For Junction of Hoi Bun Road, Wang Chiu Road and Cheung Yip Street): GW-RE0816-21	24 Aug 2021	23 Feb 2022	Valid
CNP No.(For Junction of Hoi Bun Road and Kai Hing Road): GW-RE1272-21	30 Dec 2021	22 Jun 2022	Valid
CNP No. (For Site Office and Support Area): GW-RE0534-21	16 Jun 2021	14 Dec 2021	Expired on 14 Dec 2021
CNP No. (For West Ventilation Building): PP-RE0023-21	3 Aug 2021	31 Jan 2022	Valid
CNP No. (For Depressed Road): GW- RE0887-21	14 Sep 2021	28 Feb 2022	Valid
CNP No. (For Depressed Road and Support Area): GW-RE0992-21	15 Oct 2021	13 Apr 2022	Valid
CNP No. (For Depressed Road and Support Area): GW-RE1269-21	26 Dec 2021	25 Mar 2022	Valid
CNP No. (For Launching Shaft and Barging Point): GW-RE1022-21	27 Oct 2021	26 Dec 2021	Expired on 26 Dec 2021
CNP No. (For Launching Shaft and Barging Point): GW-RE1260-21	26 Dec 2021	25 Feb 2022	Valid
Wastewater Discharge License			
WT00036183-2020 (For Depressed Road Area)	27 Jul 2020	31 Jul 2025	Valid
WT00036228-2020 (For Launching Shaft)	10 Nov 2021	31 Jul 2025	Valid
WT00039117-2021 (For Site Office and Support Area)	28 Sep 2021	30 Sep 2026	Valid
Chemical Waste Producer License			
WPN: 5213-286-B2557-03	09 Mar 2020	N/A	Valid

2 AIR QUALITY

Monitoring Requirement

2.1 According to the EM&A Manual (AEIAR-174/2013), 24-hour Total Suspended Particulates (TSP) monitoring was conducted to monitor the air quality for this Project. For regular impact monitoring, a sampling frequency of at least once in every six days at all of the monitoring stations for 24-hour TSP monitoring. In case of complaints, 1-hour TSP monitoring should be conducted at least three times in every six days when the highest dust impacts are likely to occur. **Appendix A** shows the established Action/Limit Levels for the environmental monitoring works.

Monitoring Locations

- 2.2 Five designated monitoring stations were selected for air quality monitoring programme. **Table** 2.1 describes the air quality monitoring locations, which are also depicted in **Figure 2**.
- 2.3 The monitoring location at Kai Tak area has been reviewed and updated to obtain the data with higher representative based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to KTD1 and KER1 respectively, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Monitoring location KTD2c was then further relocated to KTD2d after the review of status and location of monitoring station conducted in between February and March 2021.

Table 2.1 Air Quality Monitoring Locations

Monitoring Stations	Location
KTD1	Centre of Excellence in Paediatrics (Children's Hospital)
KTD2d	Next to the SOR Office of Trunk Road T2 in Kai Tak Area
KER1	Future Residential Development at Kerry Godown
CKL1	Flat 121 Cha Kwo Ling Village
CKL2	Flat 103 Cha Kwo Ling Village

Monitoring Parameters and Frequency

2.4 **Table 2.2** summarizes the monitoring parameters, monitoring period and frequencies of impact air quality monitoring. The monitoring schedule is shown in **Appendix B**.

Table 2.2 Frequency and Parameters of Air Quality Monitoring

Monitoring Stations	Parameter	Period	Frequency
KTD1, KTD2d, KER1, CKL1 & CKL2	1-hour TSP	0700 – 1900	3 times per 6 days (as required in case of complaints)
KTD1, KTD2d, KER1,	24 h TCD	241	1 /
CKL1 & CKL2	24-hour TSP	24 hours	Once every 6 days

Monitoring Equipment

- 2.5 High Volume Samplers (HVS) in compliance with the specification stipulated in the EM&A Manual (AEIAR-174/2013), Section 2.2.1.4, were used to carry out 24-hour TSP monitoring. Direct reading dust meter were also used to measure 1-hour average TSP levels. The 1-hour sampling was determined by HVS to check the validity and accuracy of the results measured by direct reading method.
- 2.6 Wind data monitoring equipment was set at rooftop (about 41/F) of Yau Lai Estate Bik Lai House, Lam Tin for logging wind speed and wind direction such that the wind sensors were clear of obstructions or turbulence caused by building. The wind data monitoring equipment was recalibrated at least once every six months and the wind directions were divided into 16 sectors of 22.5 degrees each. Wind data is attached in **Appendix D**.
- 2.7 **Table 2.3** summarizes the equipment used for air quality monitoring. Copies of calibration certificates are attached in **Appendix C**.

Table 2.3 Air Quality Monitoring Equipment

Equipment	Model	Quantity
HVS Sampler	TISCH Model: TE-5170 (Serial no. 0723, 1956, 10595, 1316, 5280)	5
Calibrator	TISCH Model: TE-5025A (Serial no. 3864)	1
Wind Anemometer	Davis Weather Monitor II, Model no. 7440 (Serial no. MC01010A44)	1

Monitoring Methodology

1-hour TSP Monitoring

Measuring Procedures

2.8 The measuring procedures of the 1-hour dust meter are in accordance with the Manufacturer's Instruction Manual as follows:

(Sibata Model No.: LD-3B/LD-5R)

- The 1-hour dust meter is placed at least 1.3 meters above ground.
- Set POWER to "ON" and make sure that the battery level was not flash or in low level.
- Allow the instrument to stand for about 3 minutes and then the cap of the air sampling inlet has been released.
- Push the knob at MEASURE position.

- Set time/mode setting to [BG] by pushing the time setting switch. Then, start the background measurement by pushing the start/stop switch once. It will take 6 sec. to complete the background measurement.
- Push the time setting switch to change the time setting display to [MANUAL] at the bottom left of the liquid crystal display. Finally, push the start/stop switch to stop the measuring after 1 hour sampling.
- Information such as sampling date, time, count value and site condition were recorded during the monitoring period.

Maintenance/Calibration

- 2.9 The following maintenance/calibration is required for the 1-hour dust meter:
 - Check and calibrate the meter by HVS to check the validity and accuracy of the results measured by direct reading method at 2-month intervals throughout all stages of the air quality monitoring.

24-hour TSP Monitoring

Instrumentation

- 2.10 High volume samplers (HVS) (TISCH Model: TE-5170) complete with appropriate sampling inlets was employed for 24-hour TSP monitoring. The sampler was composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complied with that required by USEPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50). Moreover, the HVS also met all the requirements in Section 2.2 of the Annex II Specification.
- 2.11 The positioning of the HVS samplers are as follows:
 - A horizontal platform with appropriate support to secure the samplers against gusty wind shall be provided;
 - No two samplers shall be placed less than 2 meter apart;
 - The distance between the sampler and an obstacle, such as buildings, must be at least twice the height that the obstacle protrudes above the sampler;
 - A minimum of 2 metres of separation from walls, parapets and penthouses is required for rooftop samplers;
 - A minimum of 2 metres of separation from any supporting structure, measured horizontally is required;
 - No furnace or incinerator flue is nearby;
 - Airflow around the sampler is unrestricted;
 - The sampler is more than 20 metres from the dripline;
 - Any wire fence and gate, to protect the sampler, shall not cause any obstruction during monitoring;
 - Permission must be obtained to set up the samplers and to obtain access to the monitoring stations; and
 - A secured supply of electricity is needed to operate the samplers.

Operating/analytical procedures for the operation of HVS

- 2.12 Operating/analytical procedures for the air quality monitoring are highlighted as follows:
 - Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6 m³/min. and 1.7 m³/min.) in accordance with the EM&A manual (AEIAR-174/2013). The flow rate shall be indicated on the flow rate chart.
 - For TSP sampling, fiberglass filters with a collection efficiency of > 99% for particles of 0.3 µm diameter were used.
 - The power supply was checked to ensure the sampler worked properly. On sampling, the sampler was operated for 5 minutes to establish thermal equilibrium before placing any filter media at the designated air monitoring station.
 - The filter holding frame was then removed by loosening the four nuts and a weighted and conditioned filter was carefully centered with the stamped number upwards, on a supporting screen.
 - The filter was aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter. Then the filter holding frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
 - The shelter lid was closed and secured with the aluminum strip.
 - The timer was then programmed. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number).
 - After sampling, the filter was removed and sent to the HOKLAS laboratory (High Precision Chemical Testing Ltd.) for weighing. The elapsed time was also recorded.
 - Before weighing, all filters were equilibrated in a conditioning environment for 24 hours. The conditioning environment temperature should be between 25°C and 30°C and not vary by more than ±3°C; the relative humidity (RH) should be < 50% and not vary by more than ±5%. A convenient working RH is 40%.

Maintenance/Calibration

- 2.13 The following maintenance/calibration is required for the HVS:
 - The high volume motors and their accessories were properly maintained. Appropriate
 maintenance such as routine motor brushes replacement and electrical wiring checking were
 made to ensure that the equipment and necessary power supply are in good working
 condition.
 - High volume samplers were calibrated at bi-monthly intervals using TE-5025A Calibration Kit throughout all stages of the air quality monitoring.

Results and Observations

- 2.14 Impact air quality monitoring was conducted at five monitoring stations as scheduled. The monitoring schedule is shown in **Appendix B**.
- 2.15 No Action and Limit Level exceedance was recorded for 24-hour TSP monitoring in the reporting month. Details of the exceedance are presented in **Appendix M**.
- 2.16 The air temperature, relative humidity, and the precipitation data were obtained from daily extracts of Hong Kong Observatory Climate Information Service. This weather information for the reporting month is summarized in **Appendix D**.
- 2.17 The monitoring data and graphical presentations of 24-hour TSP monitoring results are shown in **Appendix F**.
- 2.18 According to field observations observed in the reporting period, the major dust source identified at the designated air quality monitoring stations are as follows:

Table 2.4 Major Dust Source during Air Quality Monitoring

Monitoring Stations	Major Dust Source
KTD 1 - Centre of Excellence in Paediatrics (Children's Hospital)	 Project related construction activities (i.e., Loading and unloading of C&D wastes, drilling, crushing of material); Vehicle movement in the site;
KER 1 – Future Residential Development at Kerry Godown	 Construction activities at the nearby construction sites of New Acute Hospital; and, Road traffic along Shing Fung Road, Shing Cheong Road, Cheung Yip Street, Kai Hing Road and Kwun Tong Bypass.
KTD 2d – Next to the SOR Office of Trunk Road T2 in Kai Tak Area	 Project related construction activities (i.e., Loading and unloading of C&D material, crushing of material); Vehicle movement in the site; and, Non-project related construction activities
CKL1 - Flat 121 Cha Kwo Ling Village	Road Traffic along Cha Kwo Ling Road
CKL2 - Flat 103 Cha Kwo Ling Village	Road Traffic along Cha Kwo Ling Road

Comparison of EM&A Result with EIA Prediction

2.19 The air monitoring data was compared with the predictions in Table 4.14 of EIA Report, AEIAR-174/2013 (as approved in 2013) as summarised in **Table 2.6** for 24-hour TSP.

Table 2.6 Comparison of 24-hr TSP Monitoring Data with Predictions in EIA Report

Monitoring Stations	ASR ID	Predicted Maximum 24-hr TSP Concentration in EIA Report (AEIAR- 174/2013), μg/m ³	Maximum 24-hr TSP Concentration in the Reporting Month (December 2021), μg/m³
KTD 1 - Centre of Excellence in Paediatrics (Children's Hospital)	KTD3	126	79.4
KTD 2d – Next to the SOR Office of Trunk Road T2 in Kai Tak Area	N/A ⁽¹⁾	N/A ⁽¹⁾	127.0
KER 1 – Future Residential Development at Kerry Godown	KTD6	169	157.6
CKL1 - Flat 121 Cha Kwo Ling Village	N/A ⁽¹⁾	N/A ⁽¹⁾	143.2
CKL2 - Flat 103 Cha Kwo Ling Village	N/A ⁽¹⁾	N/A ⁽¹⁾	107.8

Remarks:

2.20 In the reporting month the 24-hour TSP concentration at KTD1 and KER1 were lower than the prediction in the EIA Report, AEIAR-174/2013 (as approved in 2013). No Action and Limit level exceedance for 24-hour TSP was recorded in the reporting period.

⁽¹⁾ No 24-hr TSP concentration was predicted in EIA Report (AEIAR-174/2013)

3 NOISE

Monitoring Requirements

3.1 According to the EM&A Manual (AEIAR-174/2013), construction noise monitoring was conducted to monitor the construction noise arising from the construction activities. The regular monitoring frequency for each monitoring station shall be on a weekly basis and conduct one set of measurements between 0700 and 1900 hours on normal weekdays. **Appendix A** shows the established Action and Limit Levels for the environmental monitoring works.

Monitoring Locations

- 3.2 Noise monitoring was conducted at five designated monitoring stations, namely KTD1, KTD2d, KER1, CKL1 and CKL2 in the reporting period. **Table 3.1** and **Figure 2** show the locations of these stations.
- 3.3 The monitoring location at Kai Tak area has been reviewed and updated to obtain the data with higher representative based on several conditions, such as distance between monitoring location and the sensitive receiver, non-project related interference, obstruction to the construction works on site and the power supply problem. The monitoring location KTD1a and KER1b has been updated to KTD1 and KER1 respectively, where are the original location as proposed in the EM&A manual (AEIAR-174/2013). And the monitoring location KTD2c was remained unchanged after the aforementioned review. Monitoring location KTD2c was then further relocated to KTD2d after the review of status and location of monitoring station conducted in between February and March 2021.

Table 3.1 Noise Monitoring Stations

Monitoring Stations	Location
KTD1	Centre of Excellence in Paediatrics (Children's Hospital)
KTD2d	Next to the SOR Office of Trunk Road T2 in Kai Tak Area
KER1	Future Residential Development at Kerry Godown
CKL1 Flat 121 Cha Kwo Ling Village	
CKL2	Flat 103 Cha Kwo Ling Village

Monitoring Parameters, Frequency and Duration

3.4 **Table 3.2** summarizes the monitoring parameters, frequency and total duration of monitoring. The noise monitoring schedule is shown in **Appendix B**.

Free Field Measurement

Monitoring Stations	Time Period	Duration	Frequency	Parameter	Measurement
KTD1					Façade Measurement
				L ₁₀ (30 min.)	
KTD2d				dB(A)	Free Field Measurement
KER1	0700-1900 hrs on normal	30 minutes	Once per	L ₉₀ (30 min.)	Free Field Measurement
	weekdays		week	dB(A)	
CKL1	·J =			Leg(30 min.)	Free Field Measurement
CIXLI			I	Lieat IV IIIIII. I	

dB(A)

Table 3.2 Frequency and Parameters of Noise Monitoring

Monitoring Equipment

CKL2

3.5 Integrating Sound Level Meter was used for impact noise monitoring. The meters were Type 1 sound level meter capable of giving a continuous readout of the noise level readings including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x) that also complied with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1) specifications. **Table 3.3** summarizes the noise monitoring equipment being used within the reporting period. Copies of calibration certificates are attached in **Appendix G**.

Table 3.3 Noise Monitoring Equipment

Equipment	Model	Quantity
	BSWA 308 (Serial no. 580238)	1
Integrating Sound Level Meter	SVAN959 (Serial no. 22452)	1
	SVAN957 (Serial no. 23851, 23852)	2
Calibratan	ST-120 (Serial no. 181001608)	1
Calibrator	SV30A (Serial no. 10965)	1

Monitoring Methodology and QA/QC Procedure

- 3.6 The monitoring procedures are as follows:
 - The monitoring station was normally be at a point 1m from the exterior of the sensitive receivers building façade and be at a position 1.2m above the ground.
 - For free field measurement, the meter was positioned away from any nearby reflective surfaces. All records for free field noise levels were adjusted with a correction of +3 dB(A).
 - The battery condition was checked to ensure the correct functioning of the meter.
 - Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting: A
 - Time weighting: Fast
 - Time measurement: 30 minutes
 - Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94.0 dB at 1000 Hz. If the difference in the calibration level before and after measurement was more than 1.0 dB, the measurement would be considered invalid and repeat of noise

- measurement would be required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with the portable wind meter.
- At the end of the monitoring period, the L_{eq}, L₉₀ and L₁₀ were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Noise monitoring would be cancelled in the presence of fog, rain, and wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10 m/s. Supplementary monitoring would be provided to ensure sufficient data would be obtained.

Maintenance and Calibration

- 3.7 The microphone head of the sound level meter and calibrator were cleaned with a soft cloth at quarterly intervals.
- 3.8 The sound level meter and calibrator were checked and calibrated at yearly intervals.
- 3.9 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements were accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

Results and Observations

- 3.10 Impact noise monitoring was conducted at five monitoring stations as scheduled. The monitoring schedule is shown in **Appendix B**. No Action/ Limit Level exceedance was recorded for day time construction noise monitoring in the reporting month.
- 3.11 Noise monitoring results and graphical presentations are shown in **Appendix H**.
- 3.12 According to field observations observed in the reporting period, the major noise sources identified at the noise monitoring stations are shown in **Table 3.4**.

Table 3.4 Other Noise Source Identified during Noise Monitoring

Monitoring Stations	Major Noise Source		
KTD 1	 Project related construction activities (Loading and unloading of C&D waste, travel of vehicles, use of PME and other plants, and other construction activities); Vehicle movement in the site; Road traffic along Shing Cheong Road; and, Non-project related construction activities at the nearby construction site of New Acute Hospital. 		
KTD 2d	 Project related construction activities (Loading and unloading of C&D waste, travel of vehicles, use of PME and other plants, and other construction activities); Vehicle movement in the site; and, Non-project related construction activities. 		
 Road traffic along Kai Hing Road. Froject related construction activities (Travel of vehicle PME and other plants, and other construction activities) 			
CKL1	Road traffic along Cha Kwo Ling Road.		
CKL2	Road traffic along Cha Kwo Ling Road		

3.13 The baseline noise level and the Noise Limit Level at each designated noise monitoring station are presented in **Table 3.5**.

Table 3.5 Baseline Noise Level and Noise Limit Level for Monitoring Stations

Monitoring Stations	Baseline Noise Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)	Noise Limit Level, dB (A) (at 0700 – 1900 hrs on normal weekdays)
KTD1	78	
KTD2d	64	
KER1	65	75
CKL1	72.4	
CKL2	71.4	

Comparison of EM&A Result with EIA Prediction

3.14 The noise monitoring data was compared with the predictions in Table 5.13 of EIA Report (AEIAR-174/2013) as summarised in **Table 3.6**.

Table 3.6 Maximum Predicted Mitigated Construction Noise Levels in EIA Report

NSR ID	Maximum Predicted Mitigated Construction Noise Levels in EIA Report (AEIAR- 174/2013), dB(A)	Maximum Construction Noise Levels in the Reporting Month (December 2021), Leq (30min) dB(A)
KTD1	74	74.1
(1)	(1)	
$N/A^{(1)}$	$N/A^{(1)}$	67.1
KER1	75	72.2
CKI 4	71	69.3
CKL4	/ 1	09.3
CKI 5	69	69.8
CKLS	09	07.0
	KTD1 N/A ⁽¹⁾	NSR ID Mitigated Construction Noise Levels in EIA Report (AEIAR-174/2013), dB(A) KTD1 74 N/A ⁽¹⁾ N/A ⁽¹⁾ KER1 75 CKL4 71

Remarks:

(1): No Maximum Predicted Mitigated Construction Noise Levels was predicted in EIA Report (AEIAR-174/2013)

3.15 The results at CKL2 and KTD1 was higher than the maximum predicted mitigated construction noise level in the EIA Report, AEIAR-174/2013 (as approved in 2013), this may be due to fluctuations of traffic flow along Cha Kwo Ling Road and Shing Cheong Road throughout the day respectively. Besides, the result at CKL1 and KER1 were lower than the maximum predicted mitigated construction noise level in the EIA Report. No Action/ Limit Level exceedance were recorded in the reporting period.

4 WATER QUALITY

Monitoring Requirement

- 4.1 According to Section 4.3.1.1 of EM&A Manual (AEIAR-174/2013), no water quality monitoring is required during the construction phase.
- 4.2 According to Section 4.3.1.5 of EM&A Manual (AEIAR-174/2013), compliance site audits are to be undertaken by the Engineer and ET and escorted by the Contractor to ensure that a valid discharge license has been issued by the EPD prior to the discharge of the effluent from the construction activities of the Project site. Monitoring of the quality of the treated effluent from the works areas should be carried out in accordance with the Water Pollution Control Ordinance (WPCO) license. The audit results reflect whether the effluent quality is in compliance with the discharge license requirements, the summaries of site audits are attached in **Appendix I**.
- 4.3 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event / Action plan attached in **Appendix J**.

5 MARINE ECOLOGY

- 5.1 According to Section 5.3.1.1 of EM&A Manual (AEIAR-174/2013), ET will be required to undertake audit of good site practice for habitat protection as detailed below. The summaries of site audits are attached in **Appendix I**.
 - Avoid damage and disturbance to the remaining and surrounding natural habitat;
 - Ensure placement of equipment is within designated areas within the existing disturbed land;
 - Ensure construction activities are restricted to within the proposed works boundary;
 - Ensure spoil heaps are be covered at all times;
 - Ensure that disturbed areas are reinstated immediately after completion of the works; and
 - Ensure enhancement planting works undertaken.

6 FISHERIES

- 6.1 According to Section 6.3.1.2 of EM&A Manual (AEIAR-174/2013), no specific fisheries monitoring and audit programme is required during the construction phase.
- 6.2 The implementation of the water quality mitigation measures stated in the Water Quality Impact Assessment (Refer to Section 6 of the EIA Report (AEIAR-174/2013)) will be audited as part of the EM&A procedures during the construction period and the details are presented in **Section 4.2** of this Report. The summaries of site audits are attached in **Appendix I**.

7 LANDSCAPE AND VISUAL

7.1 According to the EM&A Manual (AEIAR-174/2013), a series of mitigation measures were recommended to ameliorate the landscape and visual impacts of the Project. The mitigation measures for construction stage are summarized in **Table 7.1** below and provided in **Appendix K**:

 Table 7.1
 Construction Phase Landscape and Visual Mitigation Measures

ID No.	Landscape and Visual Mitigation Measure	
CM1	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	
CM2 Existing trees of good quality and condition that are unavorable affected by the works should be transplanted.		
CM3	Not used.	
CM4	Not used.	
CM5	Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	
CM6	Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance	
CM7	Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	
CM8	All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	

- 7.2 A specialist Landscape Sub-Contractor should be employed by the Contractor for the implementation of landscape construction works and subsequent maintenance operations during the establishment period. It is proposed that the planting works will be on-site and the planting should be completed during the construction contract. The monitoring of the planting establishment should be undertaken for a 12 month period which could extend throughout the Contractor's one-year maintenance period, which will be within the first operational year of the Project.
- 7.3 All measures undertaken by both the Contractor and the specialist Landscape Sub-Contractor during the construction phase and first year of the operational phase shall be audited by a Registered Landscape Architect (RLA), as a member of the Environmental Team (ET), on a regular basis to ensure compliance with the intended aims of the measures. To fulfil the aforementioned requirements, on-site landscape and visual mitigation measures were audited by

RLA in the reporting month.

- 7.4 According to Section 7.3.1.2 of the EM&A Manual (AEIAR-174/2013), site audits shall be undertaken at least once every two weeks throughout the construction period to monitor and audit the timely implementation of landscape and visual mitigation measures within the site boundaries of this Project.
- 7.5 The broad scope of the audit is detailed below but should also be undertaken with reference to the more specific checklist provided in **Table 7.2**. The summaries of site audits are attached in **Appendix I**:
 - The extent of the agreed works areas should be regularly checked during the construction phase. Any trespass by the Contractor outside the limit of the works, including any damage to existing trees and soft landscape areas shall be prohibited;
 - the progress of the engineering works should be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken;
 - all existing trees and vegetation within the study area which are not directly affected by the works are retained and protected;
 - the methods of protecting existing vegetation proposed by the Contractor are acceptable and enforced;
 - preparation, lifting transport and re-planting operations for any transplanted trees;
 - all landscaping works are carried out in accordance with the specifications;
 - the planting of new trees, shrubs, groundcover, climbers, ferns, grasses and other plans, together with the replanting of any transplanted trees are carried out properly and within the right season; and
 - all necessary horticultural operations and replacement planting are undertaken throughout the Establishment Period to ensure the healthy establishment and growth of both transplanted trees and all newly established plants.

Table 7.2 Construction Phase Audit Checklist for Landscape and Visual Mitigation Measures

Area of Works	Items to be Monitored
Advance planting	Monitoring of implementation and maintenance of planting, and against possible incursion, physical damage, fire, pollution, surface erosion, etc.

Area of Works	Items to be Monitored	
Protection of all trees and existing soft landscape areas to be retained	Identification and demarcation of trees / vegetation to be retained, erection of physical protection (e.g. fencing), monitoring against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Clearance of existing vegetation	Identification and demarcation of trees / vegetation to be cleared, checking of extent of works to minimise damage, monitoring of adjacent areas against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Pruning of trees	Identification and demarcation of trees / vegetation to be pruned, monitoring of extent of pruning to minimise damage, timing of operations, implementation of all stages of preparatory and pruning works, and maintenance of pruned vegetation, etc.	
Plant supply	Monitoring of operations relating to the supply of specialist plant material (including the collecting, germination and growth of plants from seed) to ensure that plants will be available in time to be used within the construction works.	
Soiling, planting, etc.	Monitoring of implementation and maintenance of soiling and planting works and against possible incursion, physical damage, fire, pollution, surface erosion, etc.	
Site fencing and hoarding	Implementation and maintenance, to ensure compliance with agreed designs and check that it matches the surrounding environment and does not cause visual intrusion.	
Architectural treatment of engineering works.	Implementation and maintenance of mitigation measures, to ensure compliance with agreed designs as applicable.	
Establishment Works	Monitoring of implementation of maintenance operations during Establishment Period.	

- 7.6 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event / Action plan attached in **Appendix J**.
- 7.7 In the reporting month, no non-compliance of the landscape and visual mitigation measures was recorded by RLA.

8 CULTURAL HERITAGE

- 8.1 According to Section 8.3.1.1 of EM&A Manual (AEIAR-174/2013), as a precautionary measure, it is recommended that if any antiquity or supposed antiquity is discovered during the course of the excavation works undertaken by the Contractor, the discovery shall be reported to the AMO immediately and all necessary measures taken to preserve it.
- 8.2 According to Section 8.3.1.2 of EM&A Manual (AEIAR-174/2013), no EM&A is required during the construction and operational phase.

9 WASTE MANAGEMENT

- 9.1 According to Section 9.3.1.1 of EM&A Manual (AEIAR-174/2013), the effective management of waste arisings during the construction phase will be monitored through the site audit programme. Regular audits and site inspections should be carried out by the Engineer, ET and Contractor to ensure that the recommended good site practices and other mitigation measures are implemented by the Contractor. The summaries of site audits are attached in **Appendix I**.
- 9.2 According to Sections 9.3.1.3 and 9.3.1.4 of EM&A Manual (AEIAR-174/2013), documents including licenses, permits, disposal and recycling records should be reviewed and audited during site audits for the compliance with the legislation and contract requirements to ensure proper records are being maintained and procedures undertaken in accordance with the Waste Management Plan.
- 9.3 With reference to the relevant handing records of this Project, the quantities of different types of waste generated in the reporting month are summarized and presented in the **Appendix O**.

10 ENVIRONMENTAL AUDIT

Site Audits

- 10.1 Site audits were carried out on a weekly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix I**.
- 10.2 Site audits were conducted on 02, 09, 16, 23 and 30 December 2021 in the reporting month. Site inspection of the IEC was conducted on 16 December 2021. No non-compliance was observed during the site audit.

Implementation Status of Environmental Mitigation Measures

- 10.3 According to Environmental Permits, the approved EIA Reports (Register No.: AEIAR-174/2013 and AEIAR-173/2013), and the EM&A Manuals of the Project (AEIAR-174/2013 and AEIAR-173/2013), the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An Environmental Mitigation Implementation Schedule (EMIS) is provided in **Appendix K**.
- 10.4 The ET weekly site inspections were carried out during the reporting month and the observations and recommendations are summarized in **Table 10.1**. Refer to **Appendix I** for the site inspection summary reports in the reporting month.

Table 10.1 Observations and Recommendations of Site Audit

Parameters	Date	Observations and Recommendations	Follow-up	
Air Quality	N/A	There was no observation in the reporting period.	N/A	
Noise	N/A	There was no observation in the reporting period.	N/A	
Water Quality	16 December 2021	Manhole outside the launching shaft area shall be sealed to prevent silt from discharging into drainage system.	Manholes were covered by impervious sheets and surrounded by sandbags to prevent muddy surface runoff accidentally discharge into drainage system	
Ecology	N/A	There was no observation in the reporting period.	N/A	
Landscape and Visual	N/A	There was no observation in the reporting period.	N/A	
Waste / Chemical Management	16 December 2021	Contractor is reminded to avoid accumulation and timely dispose of construction waste on site.	Waste was disposed.	

Parameters	Date	Observations and Recommendations	Follow-up	
	30 December 2021	Oil drum and grease were observed on site. Drip tray should be provided.	To be followed up in the next reporting period.	
Permits /Licences	N/A	There was no observation in the reporting period.	N/A	

Implementation Status of Event and Action Plans

10.5 The Event and Action Plans for air quality, construction noise, and landscape and visual are presented in **Appendix J**.

Air Quality Monitoring

• No Action and Limit Level exceedance for 24-hour TSP monitoring was recorded.

Construction Noise Monitoring

• No Action / Limit Level exceedance was recorded in the reporting month.

Landscape and Visual

• No landscape and visual non-conformity was recorded.

Status of Required Submission under Environmental Permit

10.6 According the Section 11.3.2.1 (c) of the EM&A Manual (AEIAR-174/2013), status of required submission under EP-451/2013 during the reporting period are summarized in **Table 10.2**.

Table 10.2 Status of Required Submission under Environmental Permit

EP Condition	Submission	Submission Date			
EP-451/2013					
Condition 2.3	Management Organization of Main Construction Companies	20 January 2020			
Condition 2.4	Design Drawing of the Project	20 January 2020			
Condition 2.5	Landscape Mitigation Plan(s)	7 May 2020			
Condition 2.10 (a)	Supplementary Contamination Assessment Plan	18 December 2015			
Condition 2.10 (b)	Supplementary Contamination Assessment Report	6 December 2016			
Condition 3.3	Updated Baseline Monitoring Report	03 November 2020			
Condition 3.4	Monthly EM&A Report (November 2021)	15 December 2021			

11 ENVIRONMENTAL NON-CONFORMANCE

Summary of Complaint, Warning, Notification of any Summons and Successful Prosecution

11.1 The summaries of environmental complaint, warning, summon and notification of successful prosecution for the Project is presented in **Appendix L**.

Summary of Exceedance

- 11.2 The summary of exceedance record in the reporting month is shown in **Appendix M**.
- 11.3 No non-conformity was recorded for landscape and visual inspections conducted in the reporting month.

12 FUTURE KEY ISSUES

Tentative construction programmes for the next three months are provided in **Appendix N**.

- 12.1 Major site activities undertaken for the coming months are summarized as follows:
 - CUE Section 6A Junction- RC structure
 - Workshop Assembly
 - West Ventilation Building Pumping Test
 - Westbound and Eastbound TBM break-in
- 12.2 Key environmental issues in the coming months include:
 - Wheel washing bay at site exits;
 - Temporary noise barriers for PMEs;
 - Sedimentation tank for settling muddy water; and
 - Make sure open stockpiles are covered during rainstorm.

Monitoring Schedule

12.3 The tentative environmental monitoring schedule for the next three months are shown in **Appendix B**.

13 CONCLUSIONS AND RECOMMENDATIONS

Conclusions

13.1 This is the 22nd Monthly EM&A Report which presents the EM&A works undertaken during the reporting month in accordance with the EM&A Manual (AEIAR-174/2013) and the requirement under EP.

Air Quality Monitoring

13.2 No Action and Limit Level exceedance was recorded for 24-hour TSP monitoring in the reporting month.

Construction Noise Monitoring

- 13.3 No Limit Level exceedance was recorded for day-time construction noise monitoring in the reporting month.
- 13.4 No Action Level exceedance was recorded in the reporting month.

Site Audit

13.5 5 ET joint weekly environmental site inspections were conducted in the reporting month.

Complaint, Notification of Summons and Successful Prosecution

13.6 No environmental complaint was received in the reporting month. No notifications of summons and successful prosecutions were received in the reporting month.

Recommendations

13.7 According to the environmental audit performed in the reporting month, the following recommendations was made:


Water Quality

• Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.


Waste / Chemical Management


- Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest.
- General refuse should be cleared daily and disposed of to the nearest licensed landfill.


FIGURES

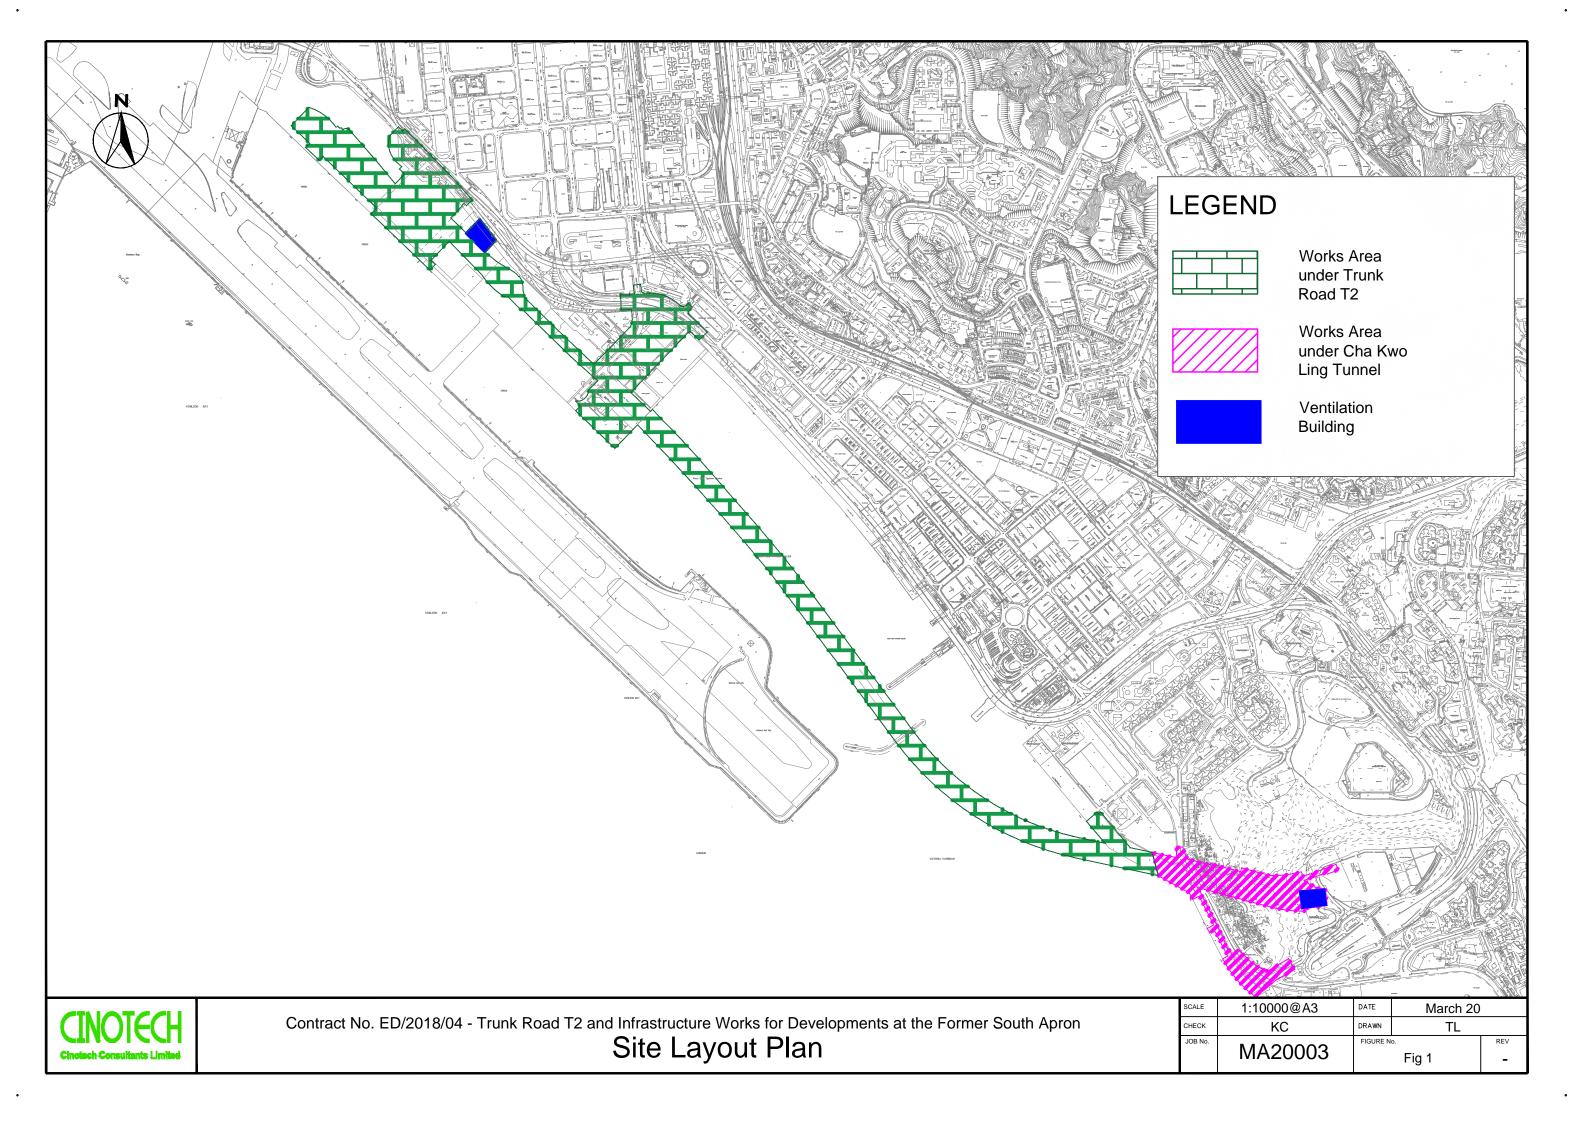




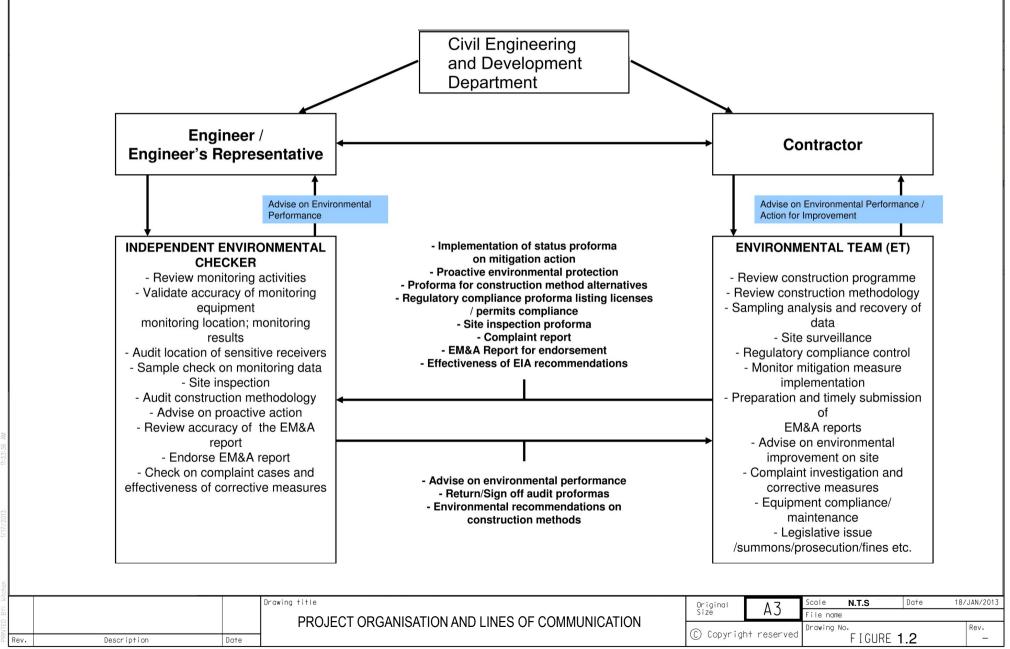

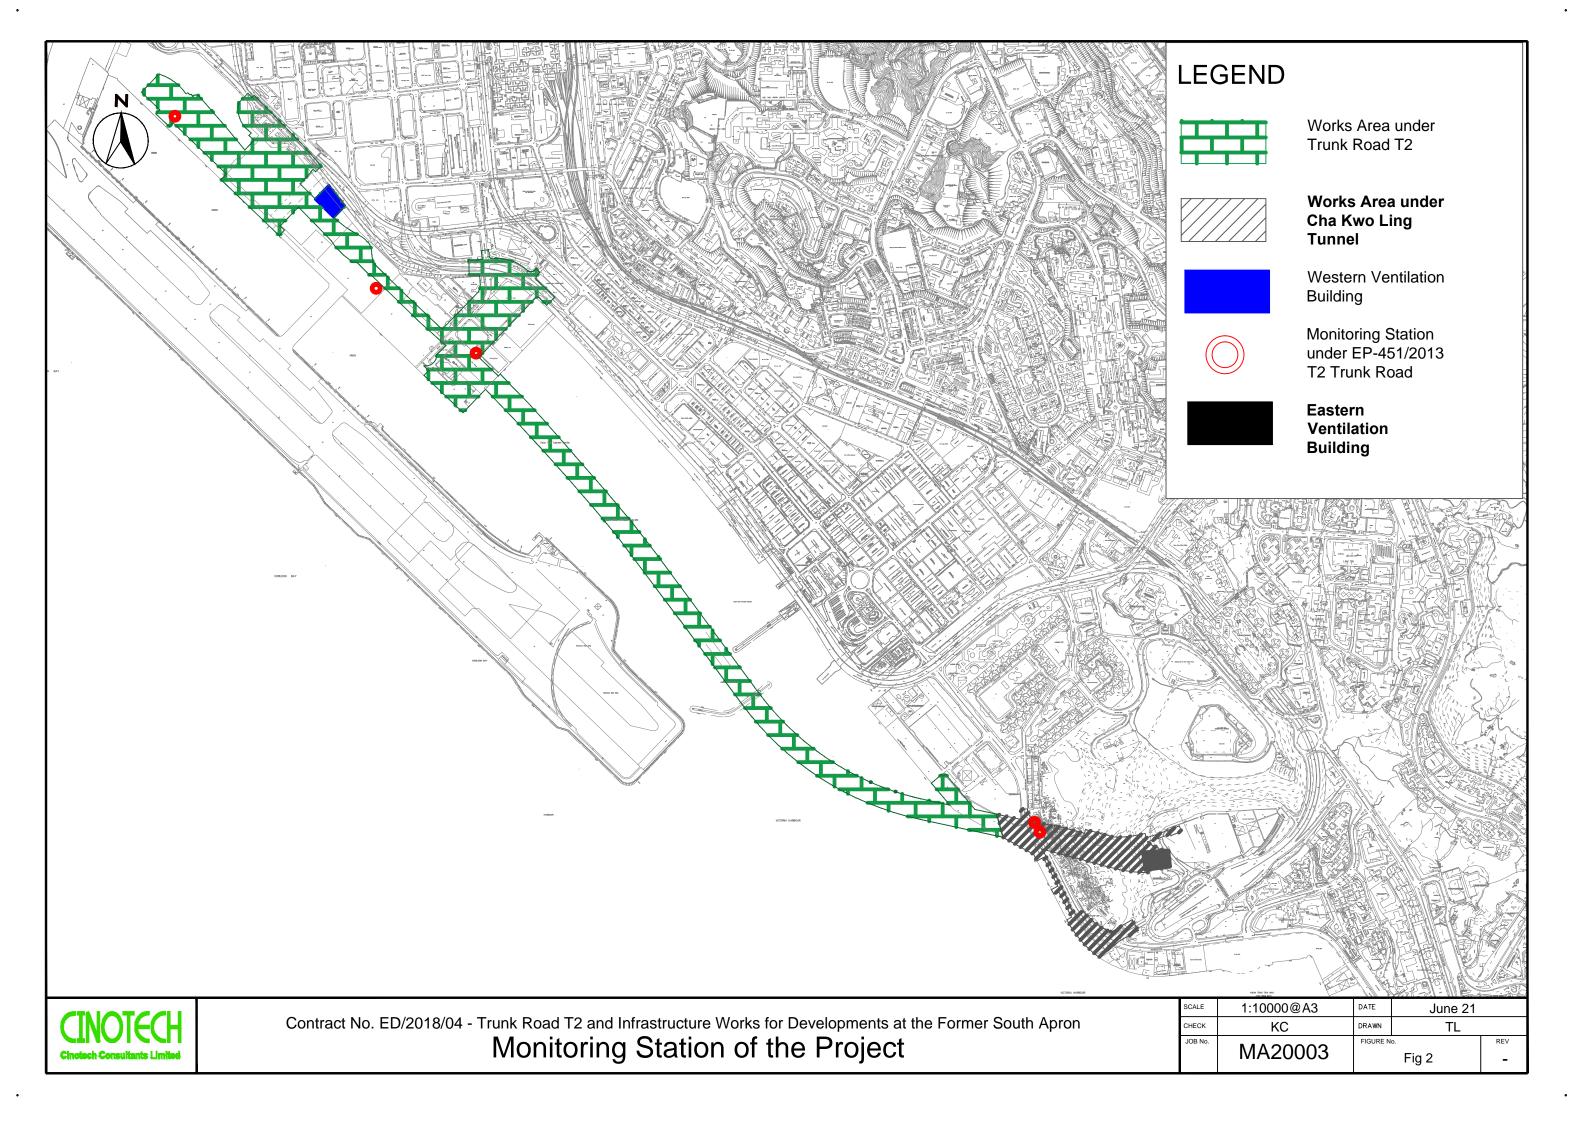

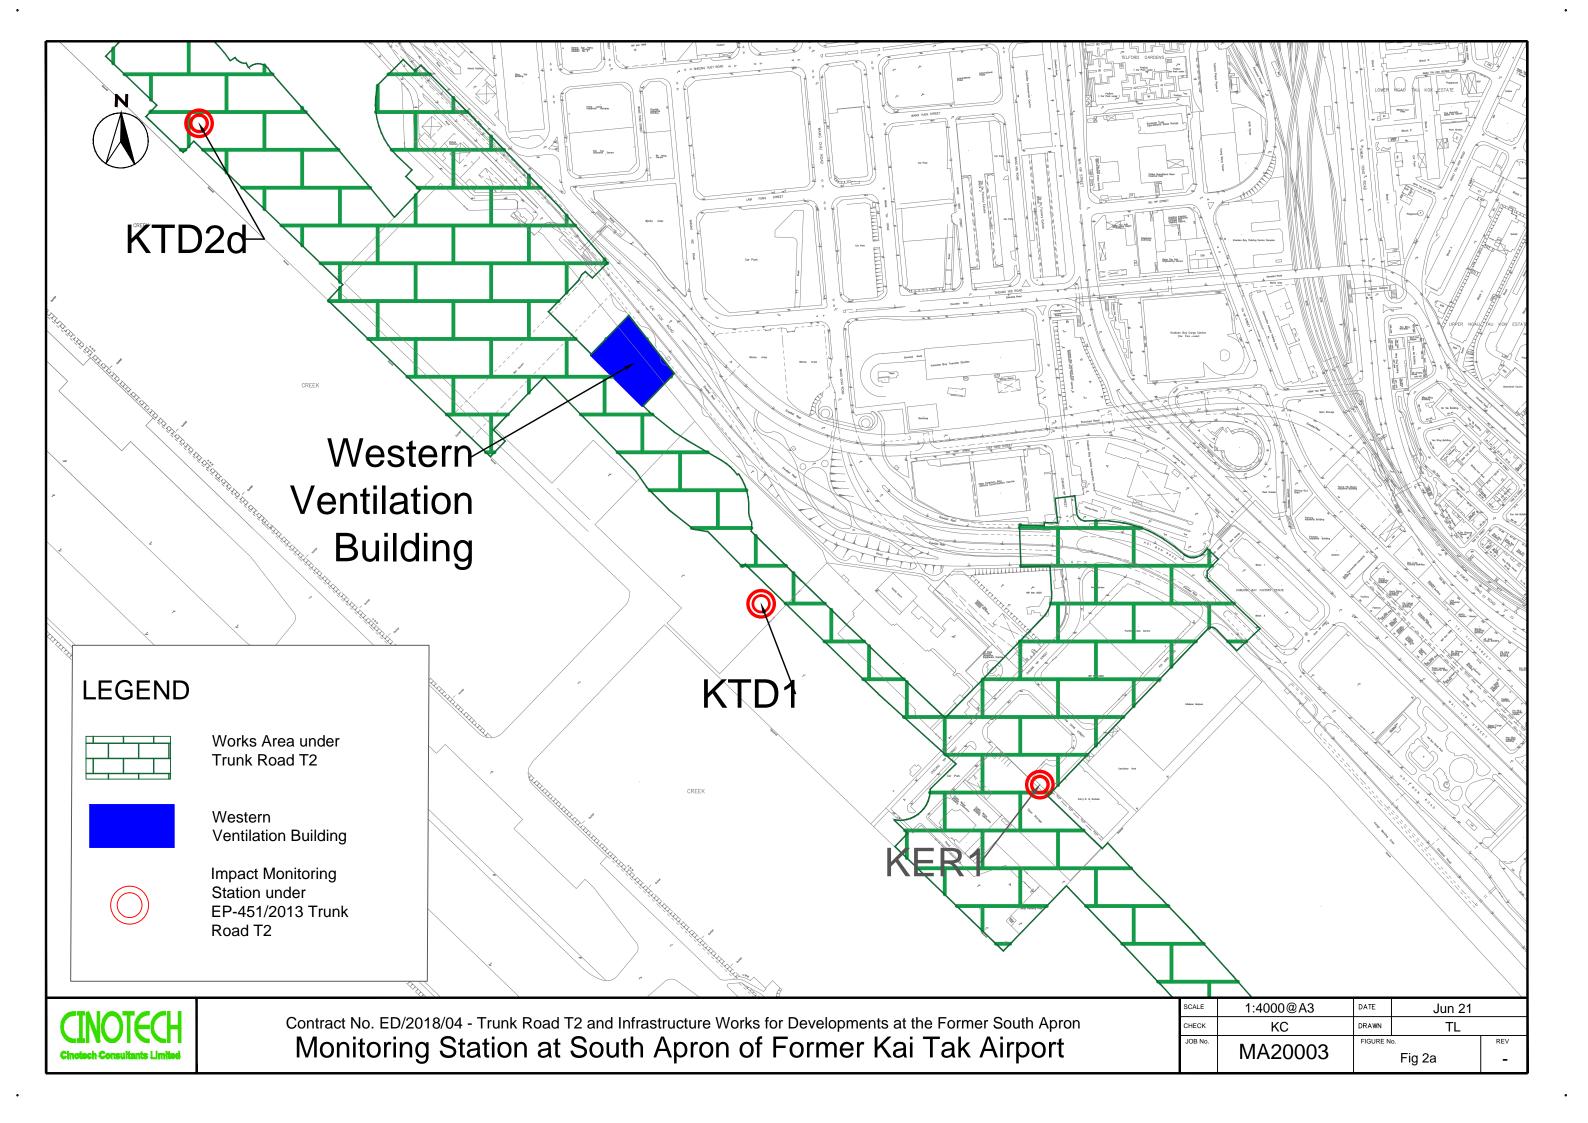

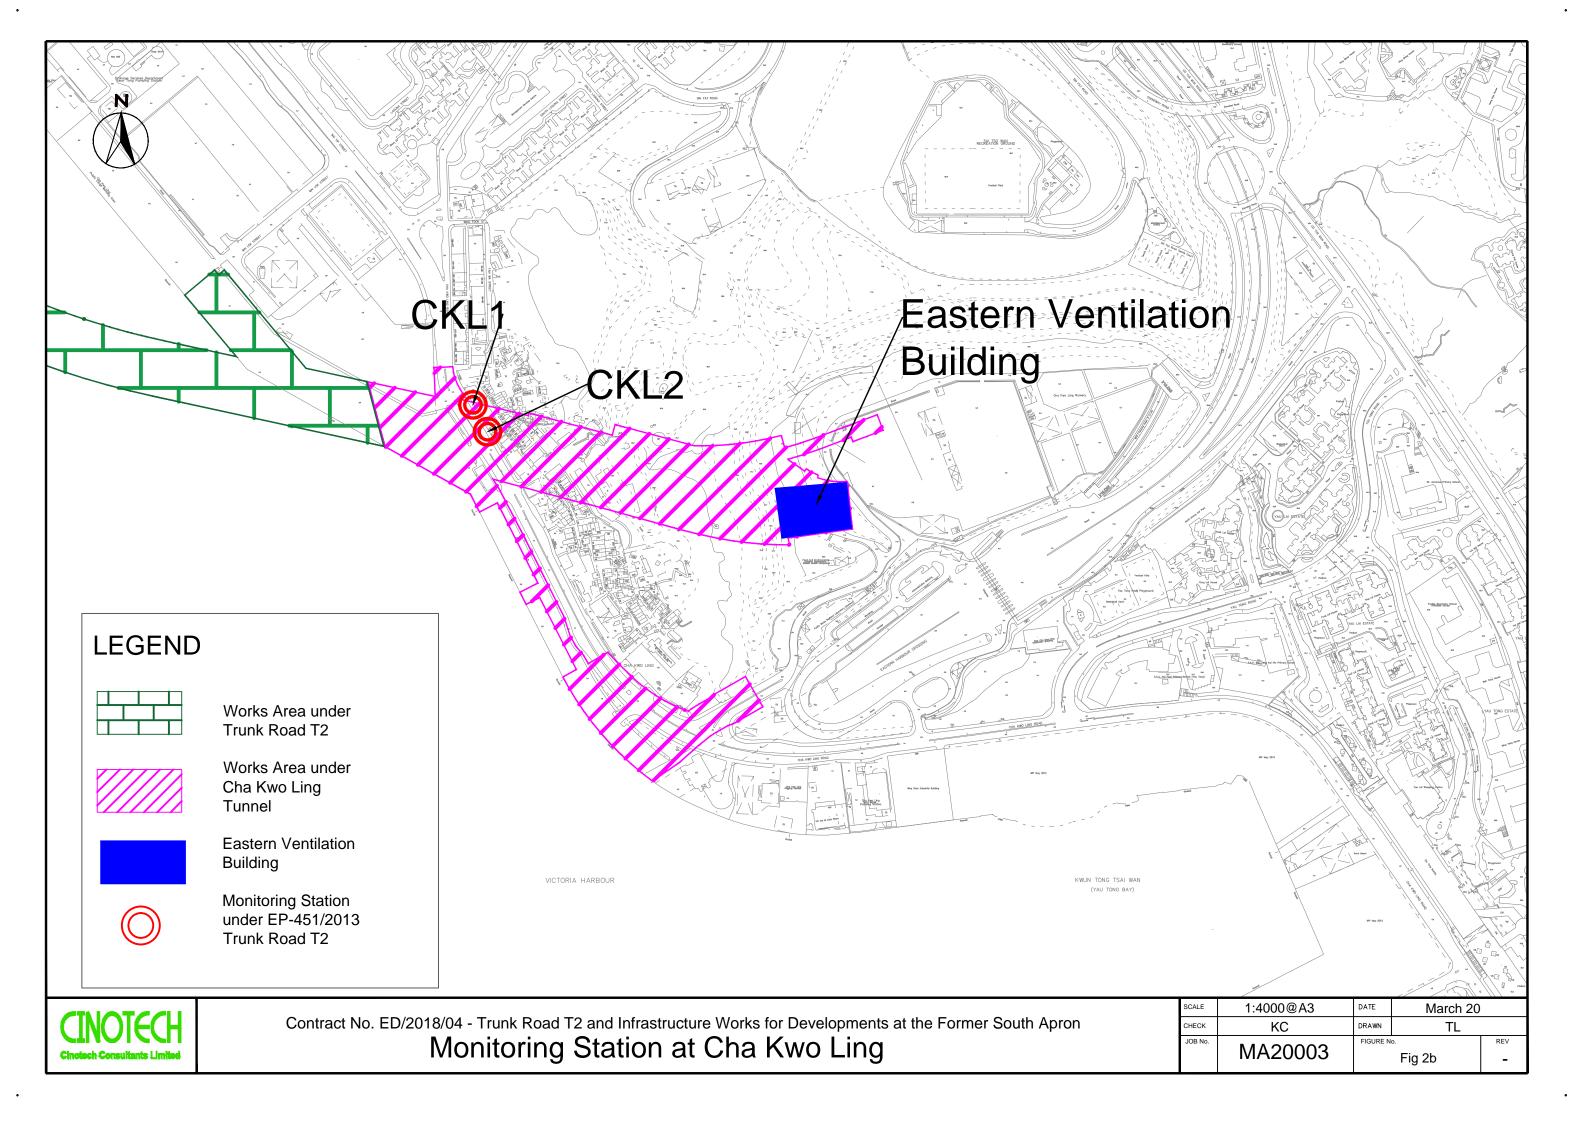

APPENDIX A ACTION AND LIMIT LEVELS

Appendix A - Action and Limit Levels

Table A-1 Action and Limit Levels for 1-hour TSP (in case of complaints)

Location	Action Level, μg/m ³	Limit Level, μg/m ³
KTD1	285	
KTD2d	279	
KER1	295	500
CKL1	323	
CKL2	327	

Table A-2 Action and Limit Levels for 24-hour TSP

Location	Action Level, μg/m ³	Limit Level, μg/m³
KTD1	177	
KTD2d	157	
KER1	172	260
CKL1	191	
CKL2	183	

Table A-3 Action and Limit Levels for Noise during Construction Period

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) ⁽¹⁾

Note:

⁽¹⁾ If works are to be carried out during restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

APPENDIX B ENVIRONMENTAL MONITORING SCHEDULES

Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Impact Air and Noise Monitoring Schedule (December 2021)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1-Dec	2-Dec	3-Dec	4-Dec
				24-hr TSP		
5-Dec	6-Dec	7-Dec	8-Dec	9-Dec	10-Dec	11-Dec
			24-hr TSP	Noise		
12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec
		24-hr TSP	Noise			
19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec
	24-hr TSP	Noise		24-hr TSP		
26-Dec	27-Dec	28-Dec	29-Dec	30-Dec	31-Dec	
			24-hr TSP	Noise		

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital) KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital) KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Contract No. ED/2018/04

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (January 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
•	j	j	Ž	j	j	1-Jan
2-Jan	3-Jan	4-Jan	5-Jan	6-Jan	7-Jan	8-Jan
		24-hr TSP	Noise			
0.7	10.4		12.7	12.1		15.4
9-Jan	10-Jan	11-Jan	12-Jan	13-Jan	14-Jan	15-Jan
	24-hr TSP	Noise				24-hr TSP
16-Jan	17-Jan	18-Jan	19-Jan	20-Jan	21-Jan	22-Jan
10 0411	17 0411	10 0411	1, 0411	20 0411	21 000	22 0111
	Noise			24-hr TSP		
23-Jan	24-Jan	25-Jan	26-Jan	27-Jan	28-Jan	29-Jan
			24 b., TCD	Noise		
			24-hr TSP	Noise		
30-Jan	31-Jan					
	24-hr TSP					
	2					

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village

CKL2 - Flat 103 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (February 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Feb	2-Feb	3-Feb	4-Feb	5-Feb
					Noise	24-hr TSP
6-Feb	7-Feb	8-Feb	9-Feb	10-Feb	11-Feb	12-Feb
	Noise			24-hr TSP		
13-Feb	14-Feb	15-Feb	16-Feb	17-Feb	18-Feb	19-Feb
			24-hr TSP	Noise		
20-Feb	21-Feb	22-Feb	23-Feb	24-Feb	25-Feb	26-Feb
		24-hr TSP	Noise			
27-Feb	28-Feb					
	24-hr TSP					

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital) KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital) KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

Contract No. ED/2018/04

Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Tentative Impact Air and Noise Monitoring Schedule (March 2022)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1-Mar	2-Mar	3-Mar	4-Mar	5-Mar
		Noise			24-hr TSP	
6-Mar	7-Mar	8-Mar	9-Mar	10-Mar	11-Mar	12-Mar
	Noise			24-hr TSP	Noise	
13-Mar	14-Mar	15-Mar	16-Mar	17-Mar	18-Mar	19-Mar
			24-hr TSP	Noise		
20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar
		24-hr TSP	Noise			
27-Mar	28-Mar	29-Mar	30-Mar	31-Mar		
	24-hr TSP	Noise				

The schedule may be changed due to unforeseen circumstances (adverse weather, safety concerns, etc.)

Air Quality Monitoring Station

24-hr TSP

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

KER1 - Future Residential Development at Kerry Godown

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

Noise Monitoring Station

KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

KER1 - Future Residential Development at Kerry Godown

KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

CKL1 - Flat 121 Cha Kwo Ling Village CKL2 - Flat 103 Cha Kwo Ling Village

^{*}Noise: Noise Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

^{**24-}hr TSP:24-hr TSP Monitoring works in both Kai Tak and Cha Kwo Ling (KTD1, KTD2d, KER1, CKL1 and CKL2)

APPENDIX C
COPIES OF CALIBRATION
CERTIFICATES FOR AIR QUALITY
MONITORING



Certificate of Calibration - Wind Monitoring Station

Description: Yau Lai Estate, Bik Lai House

Manufacturer: <u>Davis Instruments</u>

Model No.: <u>Davis7440</u>

Serial No.: MC01010A44

Equipment No.: <u>SA-03-04</u>

Date of Calibration <u>20-Aug-2021</u>

Next Due Date <u>20-Feb-2022</u>

1. Performance check of Wind Speed

Wind Sp	peed, m/s	Difference D (m/s)
Wind Speed Reading (V1)	Anemometer Value (V2)	D = V1 - V2
0.0	0.0	0.0
1.5	1.5	0.0
2.8	2.7	0.1
4.0	4.1	-0.1

2. Performance check of Wind Direction

Wind Di	rection (°)	Difference D (°)
Wind Direction Reading (W1)	Marine Compass Value (W2)	D = W1 - W2
0	0	0.0
90	90	0.0
180	180	0.0
270	270	0.0

Test Specification:

- 1. Performance Wind Speed Test The wind meter was on-site calibrated against the anemometer
- 2. Performance Wind Direction Test The wind meter was on-site calibrated against the marine compass at four direction

Calibrated by: Approved by: Approved by: Henry Leung



RECALIBRATION **DUE DATE:**

January 11, 2022

Calibration Certification Information

January 11, 2021 Cal. Date:

Rootsmeter S/N: 438320

°K

Operator: Jim Tisch Ta: 297 Pa: 750.1

mm Hg

Calibration Model #: TE-5025A

Calibrator S/N: 3864

Γ		Vol. Init	Vol. Final	ΔVol.	ΔTime	ΔΡ	ΔΗ
	Run	(m3)	(m3)	(m3)	(min)	(mm Hg)	(in H2O)
Γ	1	1	2	1	1.4470	3.2	2.00
Γ	2	3	4	1	1.0210	6.4	4.00
	3	5	6	1	0.9140	8.0	5.00
Г	4	, 7	8	1	0.8670	8.8	5.50
	5	9	10	1	0.7140	12.9	8.00

	Data Tabulation					
Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right) \left(\frac{Tstd}{Ta}\right)}$		Qa	$\sqrt{\Delta H (Ta/Pa)}$	
(m3)	(x-axis)	(y-axis)	Va	(x-axis)	(y-axis)	
0.9860	0.6814	1.4073	0.9957	0.6881	0.8899	
0.9818	0.9616	1.9902	0.9915	0.9711	1.2585	
0.9797	1.0719	2.2251	0.9893	1.0824	1.4071	
0.9786	1.1288	2.3337	0.9883	1.1399	1.4757	
0.9732	1.3630	2.8146	0.9828	1.3765	1.7798	
	m=	2.06566		m=	1.29348	
QSTD	b=	0.00315	QA	b=	0.00199	
	r= 0.99996		r=	0.99996		

Calculations					
$Vstd = \Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta) $ $Va = \Delta Vol((Pa-\Delta P)/Pa)$					
Qstd=	Vstd/ΔTime	Qa=	Va/∆Time		
For subsequent flow rate calculations:					
Qstd=	$1/m\left(\left(\sqrt{\Delta H\left(\frac{Pa}{Pstd}\right)\left(\frac{Tstd}{Ta}\right)}\right)-b\right)$	Qa=	$1/m\left(\left(\sqrt{\Delta H\left(Ta/Pa\right)}\right)-b\right)$		

Standard Conditions						
Tstd:	298.15 °K					
Pstd:	760 mm Hg					
	Key					
ΔH: calibrator manometer reading (in H2O)						
ΔP: rootsme	ter manometer reading (mm Hg)					
Ta: actual ab	Ta: actual absolute temperature (°K)					
Pa: actual ba	Pa: actual barometric pressure (mm Hg)					
b: intercept						
m: slope	m: slope					

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

5-POINT CALIBRATION DATA SHEET



File No. MA20003/44/0010

Project No.	KTD1 - Centre	of Excellence in	Paediatrics (Childs	en's Hospital)			
Date:	2-De	2-Dec-21 Next Due Date: 2-Feb-22		Operator:	SK		
Equipment No.:	A-0	1-44	-		TE-5170		1316
			Ambient C	ondition			
Temperatu	re, Ta (K)	290.4	Pressure, Pa			766.2	
	-				-		
		Ori	ifice Transfer Star	ndard Informa	ation		
Serial	l No.	3864	Slope, mc	0.05846	Intercept		-0.00313
Last Calibra	ation Date:	11-Jan-21			$c = [\Delta H \times (Pa/760]]$		
Next Calibr	ration Date:	11-Jan-22	($Qstd = \{ [\Delta H \ x] $	(Pa/760) x (298/	Γa)] ^{1/2} -bc} / n	nc
	T		Calibration of	TSP Sampler	T		
Calibration		Or	fice	I = 2.2		HVS	1.40
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		60) x (298/Ta)] ^{1/2} Y-axis
1	13.4		3.72	63.74	9.4		3.12
2	11.0		3.37	57.76	7.4		2.77
3	8.4		2.95	50.48	5.6		2.41
4	5.6		2.41	41.23	3.3	1.85	
5	3.2		1.82	31.18	1.8		1.36
	ression of Y on 2 0.0541 coefficient* =	_	9993	Intercept, bw	-0.345	51	
*If Correlation (Coefficient < 0.99	90, check and red	calibrate.				
			Set Point Ca	alculation			
From the TSP Fi	ield Calibration (Curve, take Qstd					
From the Regres	ssion Equation, th	ne "Y" value acc	ording to				
C	•		C		1/2		
		mw x Q	$\mathbf{pstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (7	Га / 298) =	3.80		
Remarks:							
				h	<u> </u>		
Conducted by:	Wong Sh	ing Kwai	Signature:		<u> </u>	Date:	2-Dec-21
Checked by:	Henry	Leung	Signature:	1-8-	2 Kon	Date:	2-Dec-21

5-POINT CALIBRATION DATA SHEET



File No. MA20003/04/0009

Project No.	KER 1 - Future	Residential Dev	elopment at Kerry	Godown		_	
Date:	2-Dec-21 Next Due Date: 2-Fe		eb-22 Operator:		SK		
Equipment No.:	A-0	1-04	•		E 5170	Serial No.	10595
			Ambient C	ondition			
Temperatu	re, Ta (K)	290.4	Pressure, Pa			766.2	
•	, , , ,		,	· •			
		Or	ifice Transfer Sta	ndard Informa	ation		
Serial	l No.	3864	Slope, mc	0.05846	Intercept		-0.00313
Last Calibra	ation Date:	11-Jan-21	r	nc x Qstd + bo	$c = [\Delta H \times (Pa/760]]$) x (298/Ta)] ¹	/2
Next Calibr	ration Date:	11-Jan-22		$Qstd = \{ [\Delta H x] \}$	(Pa/760) x (298/	Γa)] ^{1/2} -bc} / n	nc
			Calibration of	TSP Sampler			
Calibration		Or	fice	T		HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	(0) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		60) x (298/Ta)] ^{1/2} /-axis
1	13.2		3.70	63.27	9.2		3.09
2	10.4		3.28	56.16	7.0		2.69
3	8.2		2.91	49.88	5.6		2.41
4	5.2		2.32	39.73	3.2		1.82
5	3.0		1.76	30.19	2.1		1.47
Slope , mw =	ression of Y on Y 0.0495 coefficient* =	_	9 972	Intercept, bw =	-0.070	99	
*If Correlation (Coefficient < 0.99	90, check and red	calibrate.				
			Set Point Ca	alculation			
From the TSP Fi	ield Calibration (Curve, take Qstd					
From the Regres	ssion Equation, th	ne "Y" value acc	ording to				
_	•		-		1/2		
		mw x Q	$\mathbf{pstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (⁷	Ta / 298) =	4.08		
Remarks:							
Conducted by:	Wong Sh	ing Kwai	Signature:		<u> </u>	Date:	2-Dec-21
				1 -			
Checked by:	Henry	Leung	Signature:	1-Pa	xon 7	Date:	2-Dec-21

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



File No. MA20003/41/0009

Project No.	KTD 2D - Next	to the SOR Offic	ce of Trunk Road T	2 in Kai Tak A	area		
Date:	25-N	Jov-21	ov-21 Next Due Date: 25-Jan-22		Operator:	SK	
Equipment No.:)1-41		TE	E 5170	_	5280
			Ambient C	ondition			
Temperature, Ta (K) 293.6 Pressure, Pa (mmHg)						763.5	
Temperature, Ta (II)							
		Or	ifice Transfer Star	ndard Informa	ation		
Serial No. 3864 Slope, mc 0.05846 Intercept, bc -0					-0.00313		
Last Calibra	ation Date:	11-Jan-21	r	nc x Qstd + bo	$c = [\Delta H \times (Pa/760)]$) x (298/Ta)]	1/2
Next Calibra	ation Date:	11-Jan-22		$Qstd = \{ [\Delta H \ x] \}$	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / r	nc
		•					
			Calibration of T	ΓSP Sampler			
Calibration		Or	fice			HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		760) x (298/Ta)] ^{1/2} Y-axis
1	13.2		3.67	62.81	9.2		3.06
2	11.4		3.41	58.37	7.4		2.75
3	8.2		2.89	49.52	5.8		2.43
4	6.0		2.47	42.36	4.2		2.07
5	3.0		1.75	29.97	2.3		1.53
By Linear Regr Slope , mw = Correlation *If Correlation C	0.0454 coefficient* =	_	.9974	intercept, bw =	0.1604	4	
			Set Point Ca	lculation			
		Curve, take Qstd he "Y" value acco					
rom me regres	sion Equation, u		_				
		mw x Q	$\mathbf{Qstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	nw x Qstd + bw)	² x (760 / Pa) x (7	Γa / 298) =	4.38		
Remarks:							
Conducted by:	Wong Sl	ning Kwai	Signature:	K	<u></u>	Date:	25-Nov-21
Checked by:	Henry	Leung	Signature:	Plan	y day	Date: _	25-Nov-21

High-Volume TSP Sampler 5-POINT CALIBRATION DATA SHEET



File No. MA20003/55/0011

Project No.	CKL 2 - Flat 103	3 Cha Kwo Ling	Village				
Date:	6-No	6-Nov-21 Next Du		6-Jan-22		Operator:	SK
Equipment No.:	A-0	1-55	Model No.:	TE	E 5170	Serial No.	1956
			Ambient C	ondition			
Temperatur	re. Ta (K)	299.4	Pressure, Pa			757.5	
T T T T T T T T T T T T T T T T T T T	10, 10 (11)	2,,,,	11000010,10	(IIIIII 1g)		70710	
		Or	ifice Transfer Sta	ndard Informa	ation		
Serial	No.	3864	Slope, mc	0.05846	Intercept	t, bc	-0.00313
Last Calibra	ation Date:	11-Jan-21	1	mc x Qstd + bo	$c = [\Delta H \times (Pa/760)]$	$(298/Ta)^{1/2}$	
Next Calibra	ation Date:	11-Jan-22		$Qstd = \{ [\Delta H \ x]$	(Pa/760) x (298/7	Γa)] ^{1/2} -bc} / mc	:
		•					
	ı		Calibration of	TSP Sampler			
Calibration		Or	fice	,		HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		0) x (298/Ta)] ^{1/2} •axis
1	12.7		3.55	60.77	9.8	3	.12
2	10.7		3.26	55.78	7.6	2	.75
3	8.4		2.89	49.43	6.0	2	.44
4	5.5		2.34	40.01	3.6	1	.89
5	2.9		1.70	29.07	1.9	1	.37
By Linear Regr	ession of Y on X						
Slope , mw =	0.0544		1	Intercept, bw	-0.246	i1	
Correlation	coefficient* =	0	.9978	_		<u> </u>	
*If Correlation C	Coefficient < 0.99	0, check and red	calibrate.	-			
			Set Point Ca	alculation			
	eld Calibration C	-					
From the Regres	sion Equation, th	e "Y" value acco	ording to				
		mw v C	$\mathbf{pstd} + \mathbf{bw} = \mathbf{\Delta W} \mathbf{x}$	(Pa/760) v (20	08/Ta)l ^{1/2}		
		IIIW X Q	gstu · bw <u>μ</u> Δ · · · Δ	(1 a/ 100) A (2)	70/1 a)j		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (7	Ta / 298) =	4.42		
Remarks:							
Kemarks.							
					101		
Conducted by:	Wong Sh	ing Kwai	Signature:	X	<u> </u>	Date:	6-Nov-21
				1			
Checked by:	Henry	Leung	Signature:	Plan	y May	Date:	6-Nov-21
				105.03	./		





						File No. N	/IA20003/18/0011
Project No.	CKL 1 - Flat 12	1 Cha Kwo Ling	; Village			_	
Date:	6-No	ov-21	Next Due Date:	6-J	an-22	Operator:	SK
Equipment No.:	A-0				5170		
			•				
			Ambient	Condition			
Temperatur	re, Ta (K)	299.4	Pressure, Pa	(mmHg)		757.5	
G : 1	N		rifice Transfer Sta			. 1	0.00212
Serial		3864	Slope, mc	0.05846	Intercept $c = [\Delta H \times (Pa/76)]$		-0.00313
Last Calibra Next Calibra		11-Jan-21 11-Jan-22			с – _[ДП х (Га/76 х (Ра/760) х (298		
Next Callora	ation Date:	11-Jan-22		Qstu – \[\Dir	1 (1 a//00) x (290)	/1a)j -bc//m	
		•	Calibration of	TSP Sampler			
Calibration		Or	fice	•		HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	50) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water	I - ') x (298/Ta)] ^{1/2} Y-axis
1	12.9		3.58	61.25	9.8		3.12
2	10.3		3.20	54.73	8.0	1	2.82
3	8.5	:	2.90	49.73	5.9		2.42
4	6.2		2.48	42.48	4.0		1.99
5	3.4		1.84	31.47	1.9		1.37
-	ression of Y on Y	X					
Slope, $mw = \frac{1}{2}$		_		Intercept, bw =	-0.524	<u> </u>	
Correlation of			.9982	-			
*If Correlation C	Coefficient < 0.99	90, check and rec	calibrate.				
			Set Point (Calculation			
From the TSP Fi	eld Calibration (Curve, take Qstd	= 43 CFM				
From the Regress	sion Equation, th	ne "Y" value acco	ording to				
		,	0.41.1. [AW	(D. /5(0) (3	100 /m \11/2		
		mw x ($Qstd + bw = [\Delta W]$	x (Pa//60) x (2	(98/1a)]		
Therefore, Se	et Point; W = (m	nw x Qstd + bw)	² x (760 / Pa) x (Ta / 298) =	4.23		
Remarks:							
Canduated Les	W 01	in a Vive	C:	Xr	Σ	D-4	6 Nov. 21
Conducted by:	Wong Sh	iing Kwai	Signature:	1		Date:	6-Nov-21
Checked by:	Цапи	Leung	Signature:	10	Chan 1	Date:	6-Nov-21
Checked by.	11C1II y	Leung	. Signatuic.	_ lem	70-0-1	. Date	U-1101-71

5-POINT CALIBRATION DATA SHEET



File No. MA20003/44/0009

Project No.	KTD1 - Centre	of Excellence in	Paediatrics (Childa	ren's Hospital)			
Date:	2-0	2-Oct-21 Next Due Date: 2-Dec-21		Dec-21	Operator:	SK	
Equipment No.:	A-0	1-44	Model No.:	TE	TE-5170		1316
			Ambient C	ondition			
Temperatu	re, Ta (K)	303	Pressure, Pa	(mmHg)		758.1	
	•		-		-		
		Ori	fice Transfer Sta	ndard Informa	ation		
Serial	l No.	3864	Slope, mc	0.05846	Intercept		-0.00313
Last Calibra	ation Date:	11-Jan-21			$c = [\Delta H \times (Pa/760]]$		
Next Calibr	ation Date:	11-Jan-22		$Qstd = \{ [\Delta H \ x] $	(Pa/760) x (298/	Γa)] ^{1/2} -bc} / n	nc
	T		Calibration of	TSP Sampler			
Calibration	ATT ('C')	Or	fice	O +1 (OP) 0	ANI (HING)	HVS	(200 / 1/2
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	(0) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		(60) x (298/Ta)] ^{1/2} Y-axis
1	13.6	:	3.65	62.54	9.2		3.00
2	11.2		3.31	56.75	7.2		2.66
3	8.2		2.84	48.57	5.6		2.34
4	5.6		2.34	40.15	3.3	1.80	
5	3.2		1.77	30.36	1.8		1.33
	cession of Y on 2	_		Intercept, bw =	-0.251	.5	
	Coefficient < 0.99		ealibrate.				
			Set Point Ca	alculation			
From the TSP Fi	ield Calibration (Curve, take Qstd					
From the Regres	ssion Equation, th	ne "Y" value acc	ording to				
				~ (= co)	20 (57.) 21/2		
		mw x Q	$\mathbf{pstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)]***		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (′	Ta / 298) =	4.01		
Remarks:							
				h	<u> </u>		
Conducted by:	Wong Sh	ing Kwai	Signature:		<u> </u>	Date:	2-Oct-21
Checked by:	Henry	Leung	Signature:	\-P-	2 Xon	Date:	2-Oct-21

5-POINT CALIBRATION DATA SHEET



File No. MA20003/04/0008

Project No.	KER 1 - Future	Residential Dev	elopment at Kerry	Godown			
Date:	2-Oct-21 Next Due Date: 2-		2-I	Dec-21	Operator:	SK	
Equipment No.:	A-0	1-04	•		E 5170	Serial No.	10595
			Ambient C	ondition			
Temperatu	re, Ta (K)	303	Pressure, Pa			758.1	
	· · ·						
		Ori	fice Transfer Sta	ndard Informa	ation		
Serial	l No.	3864	Slope, mc	0.05846	Intercept		-0.00313
Last Calibra	ation Date:	11-Jan-21	r	nc x Qstd + bo	$c = [\Delta H \times (Pa/760]]$)) x (298/Ta)] ¹	/2
Next Calibr	ation Date:	11-Jan-22		$Qstd = \{ [\Delta H x] \}$	(Pa/760) x (298/	Γa)] ^{1/2} -bc} / n	nc
	ı		Calibration of	TSP Sampler			
Calibration		Or	fice	1		HVS	
Point	ΔH (orifice), in. of water	[ΔH x (Pa/76	(0) x (298/Ta)] ^{1/2}	Qstd (CFM) X - axis	ΔW (HVS), in. of water		60) x (298/Ta)] ^{1/2} /-axis
1	13.4		3.63	62.07	9.1		2.99
2	10.6		3.22	55.22	7.0		2.62
3	8.4	:	2.87	49.16	5.6		2.34
4	5.2	:	2.26	38.69	3.2		1.77
5	3.0		1.72	29.40	2.1		1.44
_	coefficient* =	_	9978	Intercept, bw =	-0.028	80	
*If Correlation C	Coefficient < 0.9	90, check and red	calibrate.				
			Set Point Ca	alculation			
From the TSP Fi	ield Calibration (Curve, take Qstd					
From the Regres	ssion Equation, tl	ne "Y" value acc	ording to				
	_		-		1/2		
		mw x Q	$\mathbf{pstd} + \mathbf{bw} = [\Delta \mathbf{W} \ \mathbf{x}]$	(Pa/760) x (29	98/Ta)] ^{1/2}		
Therefore, Se	et Point; W = (m	w x Qstd + bw)	² x (760 / Pa) x (⁷	Ta / 298) =	4.26		
Remarks:							
				la	ما		
Conducted by:	Wong Sh	ing Kwai	Signature:		//	Date:	2-Oct-21
•		-				_	
Checked by:	Henry	Leung	Signature:	1-Pa	- Mon	Date:	2-Oct-21

APPENDIX D WEATHER INFORMATION

Appendix C - Weather Conditions During Impact Monitoring Period

Date	Mean Air Temperature (°C) ¹	Mean Relative Humidity (%) ²	Precipitation (mm) ³
1-Dec-21	17.3	40	0.0
2-Dec-21	17.4	42	0.0
3-Dec-21	18.0	35	0.0
4-Dec-21	18.1	46	0.0
5-Dec-21	19.1	55	0.0
6-Dec-21	19.2	59	0.0
7-Dec-21	19.9	65	0.0
8-Dec-21	20.1	67	0.0
9-Dec-21	20.2	72	0.0
10-Dec-21	20.9	73	0.0
11-Dec-21	21.4	74	0.0
12-Dec-21	21.5	75	0.0
13-Dec-21	19.4	67	0.0
14-Dec-21	20.5	72	Trace
15-Dec-21	21.5	78	0.2
16-Dec-21	23.2	81	Trace
17-Dec-21	21.7	69	0.0
18-Dec-21	18.1	58	0.0
19-Dec-21	17.9	51	0.0
20-Dec-21	17.2	78	9.4
21-Dec-21	17.3	88	2.4
22-Dec-21	19.3	80	Trace
23-Dec-21	19.9	77	0.8
24-Dec-21	19.9	84	1.7
25-Dec-21	19.6	75	Trace
26-Dec-21	15.0	78	3.5
27-Dec-21	12.0	81	1.3
28-Dec-21	15.3	74	0.2
29-Dec-21	18.4	74	0.0
30-Dec-21	18.1	77	0.0
31-Dec-21	18.0	78	Trace

(Reporting Month: December 2021)

Remarks:

Source - Hong Kong Observatory

 $^{^{1\}text{--}3}Retrieved$ from Manned Weather Station (Hong Kong Observatory) (22°18'07" N, 114°10'27" E)

December 2021									
	Wind Speed and Directions								
Date	Time	Wind Speed m-s	Direction						
1 Dec 2021	12:00 AM	ESE	0.4						
1 Dec 2021	1:00 AM	NNW	0.4						
1 Dec 2021	2:00 AM	ESE	0.4						
1 Dec 2021	3:00 AM	SE	0.4						
1 Dec 2021	4:00 AM	SE	0.4						
1 Dec 2021	5:00 AM	SE	0.4						
1 Dec 2021	6:00 AM	SE	0.4						
1 Dec 2021	7:00 AM	ESE	1.3						
1 Dec 2021	8:00 AM	SE	0.4						
1 Dec 2021	9:00 AM	NW	0.4						
1 Dec 2021	10:00 AM	NW	0.4						
1 Dec 2021	11:00 AM	NNW	1.3						
1 Dec 2021	12:00 PM	NNW	0.9						
1 Dec 2021	1:00 PM	NNW	1.3						
1 Dec 2021	2:00 PM	NNW	1.3						
1 Dec 2021	3:00 PM	NNE	1.3						
1 Dec 2021	4:00 PM	NNE	1.3						
1 Dec 2021	5:00 PM	ENE	1.8						
1 Dec 2021	6:00 PM	SE	1.3						
1 Dec 2021	7:00 PM	NE	1.3						
1 Dec 2021	8:00 PM	NE NE	1.8						
1 Dec 2021	9:00 PM	SE	1.8						
		SE SE	2.2						
1 Dec 2021	10:00 PM								
1 Dec 2021	11:00 PM	N	0.9						
2 Dec 2021	12:00 AM	E	1.3						
2 Dec 2021	1:00 AM	ESE	1.3						
2 Dec 2021	2:00 AM	Е	1.3						
2 Dec 2021	3:00 AM	Е	1.3						
2 Dec 2021	4:00 AM	Е	1.8						
2 Dec 2021	5:00 AM	Е	1.3						
2 Dec 2021	6:00 AM	Е	1.3						
2 Dec 2021	7:00 AM	ESE	1.8						
2 Dec 2021	8:00 AM	E	1.8						
2 Dec 2021	9:00 AM	E	2.2						
2 Dec 2021	10:00 AM	SE	1.3						
2 Dec 2021	11:00 AM	SE	3.1						
2 Dec 2021	12:00 PM	Е	3.1						
2 Dec 2021	1:00 PM	ESE	3.6						
2 Dec 2021	2:00 PM	Е	2.2						
2 Dec 2021	3:00 PM	Е	1.8						
2 Dec 2021	4:00 PM	ESE	1.8						
2 Dec 2021	5:00 PM	ESE	1.8						
2 Dec 2021	6:00 PM	E	1.8						
2 Dec 2021	7:00 PM	ESE	1.8						
2 Dec 2021	8:00 PM	E	1.8						
2 Dec 2021	9:00 PM	W	1.3						
2 Dec 2021	10:00 PM	W	1.3						
2 Dec 2021	11:00 PM	W	1.3						
3 Dec 2021	12:00 PM	W	0.9						
3 Dec 2021 3 Dec 2021			-						
	1:00 AM	W NNW/	0.9						
3 Dec 2021	2:00 AM	NNW	0.9						
3 Dec 2021	3:00 AM	ENE	0.9						
3 Dec 2021	4:00 AM	NW	0.9						
3 Dec 2021	5:00 AM	W	1.8						
3 Dec 2021	6:00 AM	W	1.3						
3 Dec 2021	7:00 AM	W	1.3						
3 Dec 2021	8:00 AM	NNW	1.3						

December 2021								
Wind Speed and Directions								
Date	Time	Wind Speed m-s	Direction					
3 Dec 2021	9:00 AM	NW	1.8					
3 Dec 2021	10:00 AM	W	1.3					
3 Dec 2021	11:00 AM	NW	1.8					
3 Dec 2021	12:00 PM	NW	1.3					
3 Dec 2021	1:00 PM	W	0.9					
3 Dec 2021	2:00 PM	NW	1.3					
3 Dec 2021	3:00 PM	WNW	1.3					
3 Dec 2021	4:00 PM	NW	2.2					
3 Dec 2021	5:00 PM	WNW	1.8					
3 Dec 2021	6:00 PM	NW	0.4					
3 Dec 2021	7:00 PM	NW	0.9					
3 Dec 2021	8:00 PM	W	1.3					
3 Dec 2021	9:00 PM	W	1.3					
3 Dec 2021	10:00 PM	WNW	1.3					
3 Dec 2021	11:00 PM	SE	0.9					
4 Dec 2021	12:00 AM	SE	0.9					
4 Dec 2021	1:00 AM	E	0.9					
4 Dec 2021	2:00 AM	ESE	0.9					
4 Dec 2021	3:00 AM	ESE	0.9					
4 Dec 2021	4:00 AM	E E	1.8					
4 Dec 2021	5:00 AM	ESE	1.3					
4 Dec 2021	6:00 AM	E E	1.3					
4 Dec 2021	7:00 AM	E	1.3					
4 Dec 2021	8:00 AM	NNW	1.3					
	9:00 AM							
4 Dec 2021		<u>E</u>	1.3					
4 Dec 2021	10:00 AM	E	1.8					
4 Dec 2021	11:00 AM	SE	1.8					
4 Dec 2021	12:00 PM	ESE	2.7					
4 Dec 2021	1:00 PM	ESE	1.8					
4 Dec 2021	2:00 PM	ESE	1.8					
4 Dec 2021	3:00 PM	W	1.8					
4 Dec 2021	4:00 PM	W	1.8					
4 Dec 2021	5:00 PM	W	1.8					
4 Dec 2021	6:00 PM	W	1.3					
4 Dec 2021	7:00 PM	W	1.3					
4 Dec 2021	8:00 PM	NNW	1.3					
4 Dec 2021	9:00 PM	ENE	1.3					
4 Dec 2021	10:00 PM	NW	1.3					
4 Dec 2021	11:00 PM	W	1.3					
5 Dec 2021	12:00 AM	W	0.9					
5 Dec 2021	1:00 AM	W	0.9					
5 Dec 2021	2:00 AM	NNW	0.9					
5 Dec 2021	3:00 AM	NW	0.9					
5 Dec 2021	4:00 AM	W	0.9					
5 Dec 2021	5:00 AM	NW	1.8					
5 Dec 2021	6:00 AM	NW	1.3					
5 Dec 2021	7:00 AM	W	1.3					
5 Dec 2021	8:00 AM	NW	0.9					
5 Dec 2021	9:00 AM	WNW	1.3					
5 Dec 2021	10:00 AM	NW	0.9					
5 Dec 2021	11:00 AM	WNW	0.9					
5 Dec 2021	12:00 PM	NW	0.9					
5 Dec 2021	1:00 PM	NW	0.4					
5 Dec 2021	2:00 PM	W	0.9					
5 Dec 2021	3:00 PM	W	0.9					
5 Dec 2021	4:00 PM	WNW	0.4					
5 Dec 2021	5:00 PM	WNW	0.4					
J DOU 2021	J.00 I IVI	11 1 1 1 1	V•T					

December 2021							
Wind Speed and Directions							
Date	Time	Wind Speed m-s	Direction				
5 Dec 2021	6:00 PM	WNW	0.4				
5 Dec 2021	7:00 PM	WNW	0.9				
5 Dec 2021	8:00 PM	N	0.9				
5 Dec 2021	9:00 PM	Е	1.3				
5 Dec 2021	10:00 PM	ESE	1.8				
5 Dec 2021	11:00 PM	Е	1.8				
6 Dec 2021	12:00 AM	ESE	1.3				
6 Dec 2021	1:00 AM	Е	1.8				
6 Dec 2021	2:00 AM	ESE	3.1				
6 Dec 2021	3:00 AM	E	3.6				
6 Dec 2021	4:00 AM	ESE	2.2				
6 Dec 2021	5:00 AM	E	3.1				
6 Dec 2021	6:00 AM	E	2.2				
6 Dec 2021	7:00 AM	ESE	1.8				
6 Dec 2021	8:00 AM	E	2.2				
6 Dec 2021	9:00 AM	ESE	2.7				
6 Dec 2021	10:00 AM	Е	1.8				
6 Dec 2021	11:00 AM	Е	1.8				
6 Dec 2021	12:00 PM	ESE	2.2				
6 Dec 2021	1:00 PM	ESE	1.8				
6 Dec 2021	2:00 PM	ESE	1.3				
6 Dec 2021	3:00 PM	ESE	0.9				
6 Dec 2021	4:00 PM	ESE	0.9				
6 Dec 2021	5:00 PM	ESE	1.3				
6 Dec 2021	6:00 PM	SE	0.9				
6 Dec 2021	7:00 PM	NNW	1.3				
6 Dec 2021	8:00 PM	NNW	1.3				
6 Dec 2021	9:00 PM	WNW	1.3				
6 Dec 2021	10:00 PM	WNW	0.9				
6 Dec 2021	11:00 PM	NNW	0.9				
7 Dec 2021	12:00 AM	ESE	0.9				
7 Dec 2021	1:00 AM	ESE	0.9				
7 Dec 2021	2:00 AM	ESE	0.9				
7 Dec 2021	3:00 AM	ESE	1.8				
7 Dec 2021	4:00 AM	SE	1.3				
7 Dec 2021	5:00 AM	ESE	1.3				
7 Dec 2021	6:00 AM	ESE	1.3				
7 Dec 2021	7:00 AM	SE	0.9				
7 Dec 2021	8:00 AM	ESE	0.9				
7 Dec 2021	9:00 AM	ESE	1.3				
7 Dec 2021	10:00 AM	Е	1.8				
7 Dec 2021	11:00 AM	ESE	1.8				
7 Dec 2021	12:00 PM	Е	1.3				
7 Dec 2021	1:00 PM	WNW	1.3				
7 Dec 2021	2:00 PM	NW	0.9				
7 Dec 2021	3:00 PM	SE	0.9				
7 Dec 2021	4:00 PM	WNW	0.9				
7 Dec 2021	5:00 PM	W	0.9				
7 Dec 2021	6:00 PM	WNW	0.9				
7 Dec 2021	7:00 PM	NNW	0.9				
7 Dec 2021	8:00 PM	WNW	0.4				
7 Dec 2021	9:00 PM	NW	0.4				
7 Dec 2021	10:00 PM	WNW	0.4				
7 Dec 2021	11:00 PM	SE	0.0				
8 Dec 2021	12:00 AM	WNW	0.4				
8 Dec 2021	1:00 AM	WNW	0.9				
8 Dec 2021	2:00 AM	NW	0.9				

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
8 Dec 2021	3:00 AM	W	0.9	
8 Dec 2021	4:00 AM	WNW	0.4	
8 Dec 2021	5:00 AM	WNW	0.9	
8 Dec 2021	6:00 AM	WNW	0.9	
8 Dec 2021	7:00 AM	WNW	0.4	
8 Dec 2021	8:00 AM	WNW	0.4	
8 Dec 2021	9:00 AM	W	0.4	
8 Dec 2021	10:00 AM	W	0.9	
8 Dec 2021	11:00 AM	NNW	1.3	
8 Dec 2021	12:00 PM	NNW	0.9	
8 Dec 2021	1:00 PM	NNW	1.8	
8 Dec 2021	2:00 PM	NNW	3.1	
8 Dec 2021	3:00 PM	NNW	1.3	
8 Dec 2021	4:00 PM	NNW	1.3	
8 Dec 2021	5:00 PM	WNW	1.3	
8 Dec 2021	6:00 PM	NNW	0.9	
8 Dec 2021	7:00 PM	NNW	0.9	
8 Dec 2021	8:00 PM	W	0.9	
8 Dec 2021	9:00 PM	WNW	0.9	
8 Dec 2021	10:00 PM	WNW	0.9	
8 Dec 2021	11:00 PM	NW	1.8	
9 Dec 2021	12:00 AM	W	1.3	
9 Dec 2021	1:00 AM	SE	1.3	
9 Dec 2021	2:00 AM	SSE	0.4	
9 Dec 2021	3:00 AM	SSE	0.4	
9 Dec 2021	4:00 AM	SSE	0.0	
9 Dec 2021	5:00 AM	SE	0.4	
9 Dec 2021	6:00 AM	ESE	0.9	
9 Dec 2021	7:00 AM	Е	0.4	
9 Dec 2021	8:00 AM	ESE	0.9	
9 Dec 2021	9:00 AM	ESE	1.8	
9 Dec 2021	10:00 AM	Е	2.2	
9 Dec 2021	11:00 AM	ESE	1.8	
9 Dec 2021	12:00 PM	SE	1.8	
9 Dec 2021	1:00 PM	Е	1.8	
9 Dec 2021	2:00 PM	ESE	1.3	
9 Dec 2021	3:00 PM	SSE	1.3	
9 Dec 2021	4:00 PM	SE	0.9	
9 Dec 2021	5:00 PM	ESE	0.9	
9 Dec 2021	6:00 PM	WNW	0.4	
9 Dec 2021	7:00 PM	ESE	0.9	
9 Dec 2021	8:00 PM	ESE	1.3	
9 Dec 2021	9:00 PM	ESE	1.3	
9 Dec 2021	10:00 PM	Е	1.8	
9 Dec 2021	11:00 PM	ESE	1.3	
10 Dec 2021	12:00 AM	ESE	1.8	
10 Dec 2021	1:00 AM	ESE	1.8	
10 Dec 2021	2:00 AM	W	1.8	
10 Dec 2021	3:00 AM	W	2.2	
10 Dec 2021	4:00 AM	W	1.8	
10 Dec 2021	5:00 AM	W	1.8	
10 Dec 2021	6:00 AM	W	1.3	
10 Dec 2021	7:00 AM	NNW	1.8	
10 Dec 2021	8:00 AM	ENE	1.8	
10 Dec 2021	9:00 AM	NW	1.8	
10 Dec 2021	10:00 AM	W	1.8	
10 Dec 2021	11:00 AM	W	1.8	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
10 Dec 2021	12:00 PM	W	1.8	
10 Dec 2021	1:00 PM	NNW	3.6	
10 Dec 2021	2:00 PM	NW	4.0	
10 Dec 2021	3:00 PM	W	4.5	
10 Dec 2021	4:00 PM	NW	3.1	
10 Dec 2021	5:00 PM	NW	4.0	
10 Dec 2021	6:00 PM	W	1.8	
10 Dec 2021	7:00 PM	NW	0.9	
10 Dec 2021	8:00 PM	WNW	0.9	
10 Dec 2021	9:00 PM	NW	0.4	
10 Dec 2021	10:00 PM	WNW	0.4	
10 Dec 2021	11:00 PM	NW	0.4	
11 Dec 2021	12:00 AM	NW	0.9	
11 Dec 2021	1:00 AM	W	1.8	
11 Dec 2021	2:00 AM	W	1.8	
11 Dec 2021	3:00 AM	WNW	2.2	
11 Dec 2021	4:00 AM	ESE	1.8	
11 Dec 2021	5:00 AM	Е	1.8	
11 Dec 2021	6:00 AM	Е	1.3	
11 Dec 2021	7:00 AM	ESE	1.8	
11 Dec 2021	8:00 AM	SE	1.8	
11 Dec 2021	9:00 AM	SE	1.8	
11 Dec 2021	10:00 AM	ESE	1.8	
11 Dec 2021	11:00 AM	ESE	1.8	
11 Dec 2021	12:00 PM	NW	1.8	
11 Dec 2021	1:00 PM	NW	3.6	
11 Dec 2021	2:00 PM	NW	4.0	
11 Dec 2021	3:00 PM	NW	4.5	
11 Dec 2021	4:00 PM	NW	3.1	
11 Dec 2021	5:00 PM	NW	4.0	
11 Dec 2021	6:00 PM	NW	1.8	
11 Dec 2021	7:00 PM	NW	0.9	
11 Dec 2021	8:00 PM	W	0.9	
11 Dec 2021	9:00 PM	N	0.4	
11 Dec 2021	10:00 PM	NW	0.4	
11 Dec 2021	11:00 PM	WNW	0.4	
12 Dec 2021	12:00 AM	W	1.3	
12 Dec 2021	1:00 AM	W	1.3	
12 Dec 2021	2:00 AM	W	1.3	
12 Dec 2021	3:00 AM	W	0.9	
12 Dec 2021	4:00 AM	W	0.9	
12 Dec 2021	5:00 AM	W	0.9	
12 Dec 2021	6:00 AM	W	0.9	
12 Dec 2021	7:00 AM	W	0.9	
12 Dec 2021	8:00 AM	W	1.8	
12 Dec 2021	9:00 AM	NNW	1.3	
12 Dec 2021	10:00 AM	ENE	1.3	
12 Dec 2021	11:00 AM	NW	1.8	
12 Dec 2021	12:00 PM	W	1.3	
12 Dec 2021	1:00 PM	W	1.8	
12 Dec 2021	2:00 PM	W	1.3	
12 Dec 2021	3:00 PM	NNW	0.9	
12 Dec 2021	4:00 PM	NW	1.3	
12 Dec 2021	5:00 PM	W	0.9	
12 Dec 2021	6:00 PM	NW	0.9	
12 Dec 2021	7:00 PM	NW	1.3	
12 Dec 2021	8:00 PM	W	1.3	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
12 Dec 2021	9:00 PM	NW	0.9	
12 Dec 2021	10:00 PM	WNW	1.3	
12 Dec 2021	11:00 PM	NW	1.8	
13 Dec 2021	12:00 AM	WNW	1.8	
13 Dec 2021	1:00 AM	NW	1.8	
13 Dec 2021	2:00 AM	NW	1.8	
13 Dec 2021	3:00 AM	W	1.3	
13 Dec 2021	4:00 AM	W	0.9	
13 Dec 2021	5:00 AM	WNW	0.9	
13 Dec 2021	6:00 AM	ENE	0.9	
13 Dec 2021	7:00 AM	NW	0.4	
13 Dec 2021	8:00 AM	W	0.9	
13 Dec 2021	9:00 AM	W	1.3	
13 Dec 2021	10:00 AM	W	1.3	
13 Dec 2021	11:00 AM	W	1.3	
13 Dec 2021	12:00 PM	W	1.8	
13 Dec 2021	1:00 PM	WNW	1.3	
13 Dec 2021	2:00 PM	NW	1.8	
13 Dec 2021		NW NW	2.2	
	3:00 PM			
13 Dec 2021	4:00 PM	NW	1.3	
13 Dec 2021	5:00 PM	NW	1.3	
13 Dec 2021	6:00 PM	NW	1.3	
13 Dec 2021	7:00 PM	NW	0.9	
13 Dec 2021	8:00 PM	NW	0.9	
13 Dec 2021	9:00 PM	WNW	0.9	
13 Dec 2021	10:00 PM	WNW	0.9	
13 Dec 2021	11:00 PM	W	0.9	
14 Dec 2021	12:00 AM	WNW	1.8	
14 Dec 2021	1:00 AM	NW	1.3	
14 Dec 2021	2:00 AM	NW	1.3	
14 Dec 2021	3:00 AM	NW	1.3	
14 Dec 2021	4:00 AM	NW	1.3	
14 Dec 2021	5:00 AM	NW	1.8	
14 Dec 2021	6:00 AM	NW	1.3	
14 Dec 2021	7:00 AM	NW	0.9	
14 Dec 2021	8:00 AM	NW	0.9	
14 Dec 2021	9:00 AM	NW	1.8	
14 Dec 2021	10:00 AM	NW	1.3	
14 Dec 2021	11:00 AM	NW	1.8	
14 Dec 2021	12:00 PM	W	1.3	
14 Dec 2021	1:00 PM	W	1.8	
14 Dec 2021	2:00 PM	W	1.3	
14 Dec 2021	3:00 PM	NW	1.8	
14 Dec 2021	4:00 PM	NW	4.0	
14 Dec 2021	5:00 PM	NW	3.6	
14 Dec 2021	6:00 PM	NW NW	3.6	
14 Dec 2021	7:00 PM	NW	1.3	
14 Dec 2021	8:00 PM	NW	1.3	
14 Dec 2021	9:00 PM	NW	1.3	
14 Dec 2021	10:00 PM	W	0.9	
14 Dec 2021	11:00 PM	W	1.3	
15 Dec 2021	12:00 AM	W	1.8	
15 Dec 2021	1:00 AM	W	1.3	
15 Dec 2021	2:00 AM	W	1.3	
15 Dec 2021	3:00 AM	W	0.9	
15 Dec 2021	4:00 AM	WNW	0.9	
15 Dec 2021	5:00 AM	W	0.9	
·		·		

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
15 Dec 2021	6:00 AM	NW	0.9	
15 Dec 2021	7:00 AM	WNW	1.3	
15 Dec 2021	8:00 AM	W	1.3	
15 Dec 2021	9:00 AM	W	1.3	
15 Dec 2021	10:00 AM	NW	1.3	
15 Dec 2021	11:00 AM	NW	1.3	
15 Dec 2021	12:00 PM	NW	1.3	
15 Dec 2021	1:00 PM	NW	0.9	
15 Dec 2021	2:00 PM	NW	1.3	
15 Dec 2021	3:00 PM	W	1.3	
15 Dec 2021	4:00 PM	NW	1.3	
15 Dec 2021	5:00 PM	W	0.9	
15 Dec 2021	6:00 PM	NW	0.9	
15 Dec 2021	7:00 PM	NW	0.9	
15 Dec 2021	8:00 PM	NW	0.9	
15 Dec 2021	9:00 PM	NW	0.9	
15 Dec 2021	10:00 PM	NW	1.8	
15 Dec 2021	11:00 PM	NW	1.3	
16 Dec 2021	12:00 AM	NW	1.3	
16 Dec 2021	1:00 AM	NW	1.8	
16 Dec 2021	2:00 AM	NW	1.3	
16 Dec 2021	3:00 AM	WNW	0.9	
16 Dec 2021	4:00 AM	NW	1.3	
16 Dec 2021	5:00 AM	W	0.9	
16 Dec 2021	6:00 AM	W	1.3	
16 Dec 2021	7:00 AM	NW	1.3	
16 Dec 2021	8:00 AM	NW	2.2	
16 Dec 2021	9:00 AM	NW	1.8	
16 Dec 2021	10:00 AM	NW	1.8	
16 Dec 2021	11:00 AM	Е	1.8	
16 Dec 2021	12:00 PM	NW	1.3	
16 Dec 2021	1:00 PM	NW	2.7	
16 Dec 2021	2:00 PM	NW	1.8	
16 Dec 2021	3:00 PM	NW	1.8	
16 Dec 2021	4:00 PM	NW	2.7	
16 Dec 2021	5:00 PM	NW	1.8	
16 Dec 2021	6:00 PM	NW	1.8	
16 Dec 2021	7:00 PM	NW	1.8	
16 Dec 2021	8:00 PM	NW	1.8	
16 Dec 2021	9:00 PM	NW	2.2	
16 Dec 2021	10:00 PM	NW	1.8	
16 Dec 2021	11:00 PM	NW	0.9	
17 Dec 2021	12:00 AM	NW	1.3	
17 Dec 2021	1:00 AM	NE	0.9	
17 Dec 2021	2:00 AM	NNE	0.4	
17 Dec 2021	3:00 AM	NE NW	0.4	
17 Dec 2021	4:00 AM	NW	0.4	
17 Dec 2021	5:00 AM	N	0.4	
17 Dec 2021	6:00 AM	NE NE	0.9	
17 Dec 2021	7:00 AM	NE NE	0.9	
17 Dec 2021	8:00 AM	NE NW	0.9	
17 Dec 2021	9:00 AM	NW NW	0.9	
17 Dec 2021	10:00 AM	NW NW	0.9	
17 Dec 2021	11:00 AM	NW NW	0.9	
17 Dec 2021	12:00 PM	NW NW	1.3	
17 Dec 2021 17 Dec 2021	1:00 PM	NW NW		
1 / Dec 2021	2:00 PM	IN W	2.2	

December 2021				
	Wind Speed a	nd Directions		
Date	Time	Wind Speed m-s	Direction	
17 Dec 2021	3:00 PM	NW	2.7	
17 Dec 2021	4:00 PM	NW	4.5	
17 Dec 2021	5:00 PM	NW	3.1	
17 Dec 2021	6:00 PM	NW	1.3	
17 Dec 2021	7:00 PM	NW	1.3	
17 Dec 2021	8:00 PM	NW	1.3	
17 Dec 2021	9:00 PM	NW	0.9	
17 Dec 2021	10:00 PM	NE	0.9	
17 Dec 2021	11:00 PM	N	0.9	
18 Dec 2021	12:00 AM	N	0.9	
18 Dec 2021	1:00 AM	N	0.9	
18 Dec 2021	2:00 AM	N	1.8	
18 Dec 2021	3:00 AM	N	1.3	
18 Dec 2021	4:00 AM	N	1.3	
			1.3	
18 Dec 2021	5:00 AM			
18 Dec 2021	6:00 AM		1.3	
18 Dec 2021	7:00 AM		1.3	
18 Dec 2021	8:00 AM	NNW	0.9	
18 Dec 2021	9:00 AM	NNW	0.9	
18 Dec 2021	10:00 AM	NE	0.9	
18 Dec 2021	11:00 AM	NE	0.9	
18 Dec 2021	12:00 PM	NW	0.9	
18 Dec 2021	1:00 PM	NW	1.8	
18 Dec 2021	2:00 PM	NW	1.3	
18 Dec 2021	3:00 PM	NW	1.3	
18 Dec 2021	4:00 PM	NW	2.2	
18 Dec 2021	5:00 PM	W	1.3	
18 Dec 2021	6:00 PM	W	1.3	
18 Dec 2021	7:00 PM	NW	1.8	
18 Dec 2021	8:00 PM	W	1.3	
18 Dec 2021	9:00 PM	W	1.3	
		W		
18 Dec 2021	10:00 PM		1.3	
18 Dec 2021	11:00 PM	WNW	1.3	
19 Dec 2021	12:00 AM	W	1.3	
19 Dec 2021	1:00 AM	W	1.3	
19 Dec 2021	2:00 AM	WNW	1.3	
19 Dec 2021	3:00 AM	W	0.9	
19 Dec 2021	4:00 AM	W	0.9	
19 Dec 2021	5:00 AM	W	0.9	
19 Dec 2021	6:00 AM	W	0.9	
19 Dec 2021	7:00 AM	NW	0.9	
19 Dec 2021	8:00 AM	NW	0.9	
19 Dec 2021	9:00 AM	W	0.4	
19 Dec 2021	10:00 AM	W	0.4	
19 Dec 2021	11:00 AM	NW	0.9	
19 Dec 2021	12:00 PM	NW	1.3	
19 Dec 2021	1:00 PM	W	0.9	
19 Dec 2021	2:00 PM	WSW	0.9	
19 Dec 2021	3:00 PM	W	0.9	
19 Dec 2021	4:00 PM	NW	0.9	
19 Dec 2021	5:00 PM	W	0.9	
19 Dec 2021	6:00 PM	ESE	1.8	
19 Dec 2021	7:00 PM	ESE	1.8	
19 Dec 2021	8:00 PM	<u>E</u>	2.2	
19 Dec 2021	9:00 PM	Е	2.2	
19 Dec 2021	10:00 PM	ESE	1.3	
19 Dec 2021	11:00 PM	SE	0.9	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
20 Dec 2021	12:00 AM	SE	0.4	
20 Dec 2021	1:00 AM	ESE	1.3	
20 Dec 2021	2:00 AM	ENE	0.9	
20 Dec 2021	3:00 AM	ESE	0.9	
20 Dec 2021	4:00 AM	Е	1.3	
20 Dec 2021	5:00 AM	ESE	0.9	
20 Dec 2021	6:00 AM	ESE	0.9	
20 Dec 2021	7:00 AM	Е	0.9	
20 Dec 2021	8:00 AM	Е	1.3	
20 Dec 2021	9:00 AM	Е	0.9	
20 Dec 2021	10:00 AM	ESE	1.8	
20 Dec 2021	11:00 AM	NW	1.8	
20 Dec 2021	12:00 PM	NW	1.8	
20 Dec 2021	1:00 PM	NW	2.7	
20 Dec 2021	2:00 PM	NW	3.6	
20 Dec 2021	3:00 PM	NW	2.7	
20 Dec 2021	4:00 PM	NW	4.0	
20 Dec 2021	5:00 PM	NW	2.7	
20 Dec 2021	6:00 PM	NW	1.3	
20 Dec 2021	7:00 PM	W	1.3	
20 Dec 2021	8:00 PM	W	1.3	
20 Dec 2021	9:00 PM	W	0.9	
20 Dec 2021	10:00 PM	WNW	0.9	
20 Dec 2021	11:00 PM	SE	0.9	
21 Dec 2021	12:00 AM	ESE	0.9	
21 Dec 2021	1:00 AM	ESE	0.9	
21 Dec 2021	2:00 AM	SE	1.8	
21 Dec 2021	3:00 AM	Е	1.3	
21 Dec 2021	4:00 AM	ESE	1.3	
21 Dec 2021	5:00 AM	ESE	1.3	
21 Dec 2021	6:00 AM	ESE	0.9	
21 Dec 2021	7:00 AM	ESE	0.9	
21 Dec 2021	8:00 AM	Е	0.9	
21 Dec 2021	9:00 AM	ESE	0.4	
21 Dec 2021	10:00 AM	NW	1.8	
21 Dec 2021	11:00 AM	NW	1.8	
21 Dec 2021	12:00 PM	NW	2.2	
21 Dec 2021	1:00 PM	NW	1.8	
21 Dec 2021	2:00 PM	NW	2.7	
21 Dec 2021	3:00 PM	NW	1.8	
21 Dec 2021	4:00 PM	NW	2.7	
21 Dec 2021	5:00 PM	NE	0.9	
21 Dec 2021	6:00 PM	NW	1.8	
21 Dec 2021	7:00 PM	NW	1.8	
21 Dec 2021	8:00 PM	NW	0.9	
21 Dec 2021	9:00 PM	NW	1.8	
21 Dec 2021	10:00 PM	NW	2.2	
21 Dec 2021	11:00 PM	NW	1.8	
22 Dec 2021	12:00 AM	NW	1.3	
22 Dec 2021	1:00 AM	NW	0.4	
22 Dec 2021	2:00 AM	NW	0.4	
22 Dec 2021	3:00 AM	NW	0.9	
22 Dec 2021	4:00 AM	WNW	0.4	
22 Dec 2021	5:00 AM	WNW	0.4	
22 Dec 2021	6:00 AM	NW	0.9	
22 Dec 2021	7:00 AM	NW	0.4	
22 Dec 2021	8:00 AM	NW	1.3	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
22 Dec 2021	9:00 AM	NW	0.9	
22 Dec 2021	10:00 AM	NW	1.8	
22 Dec 2021	11:00 AM	NW	1.8	
22 Dec 2021	12:00 PM	NW	1.3	
22 Dec 2021	1:00 PM	ESE	0.9	
22 Dec 2021	2:00 PM	NW	0.9	
22 Dec 2021	3:00 PM	NW	0.9	
22 Dec 2021	4:00 PM	NW	2.2	
22 Dec 2021	5:00 PM	NW	1.8	
22 Dec 2021	6:00 PM	NW	1.3	
22 Dec 2021	7:00 PM	NW	0.4	
22 Dec 2021	8:00 PM	NW	0.9	
22 Dec 2021	9:00 PM	NNW	1.3	
22 Dec 2021	10:00 PM	NW	1.3	
22 Dec 2021	11:00 PM	ESE	1.3	
23 Dec 2021	12:00 AM	ESE	0.9	
23 Dec 2021	1:00 AM	ESE	0.9	
23 Dec 2021	2:00 AM	ESE	0.9	
23 Dec 2021	3:00 AM		0.9	
23 Dec 2021	4:00 AM		0.9	
23 Dec 2021	5:00 AM	NNW	1.8	
23 Dec 2021	6:00 AM	W	1.3	
23 Dec 2021	7:00 AM	NW	1.3	
23 Dec 2021	8:00 AM	NW	1.3	
23 Dec 2021	9:00 AM	W	1.3	
23 Dec 2021	10:00 AM	NW	1.3	
23 Dec 2021	11:00 AM	W	0.9	
23 Dec 2021	12:00 PM	NW	1.3	
23 Dec 2021	1:00 PM	NW	1.8	
23 Dec 2021	2:00 PM	NW	1.3	
23 Dec 2021	3:00 PM	W	1.3	
23 Dec 2021	4:00 PM	W	1.3	
23 Dec 2021	5:00 PM	W	1.3	
23 Dec 2021	6:00 PM	NW	1.3	
23 Dec 2021	7:00 PM	W	1.3	
23 Dec 2021	8:00 PM	NW	1.3	
23 Dec 2021	9:00 PM	W	0.9	
23 Dec 2021	10:00 PM	W	0.9	
23 Dec 2021	11:00 PM	W	1.3	
24 Dec 2021	12:00 AM	W	1.3	
24 Dec 2021	1:00 AM	W	0.9	
24 Dec 2021	2:00 AM	W	0.9	
24 Dec 2021	3:00 AM	W	0.9	
24 Dec 2021	4:00 AM	WNW	1.3	
24 Dec 2021	5:00 AM	W	0.4	
24 Dec 2021	6:00 AM	W	0.4	
24 Dec 2021	7:00 AM	W	0.4	
24 Dec 2021	8:00 AM	WNW	0.9	
24 Dec 2021	9:00 AM	NW	1.3	
24 Dec 2021	10:00 AM	W	0.9	
24 Dec 2021	11:00 AM	W	1.3	
24 Dec 2021	12:00 PM	NW	1.8	
24 Dec 2021	1:00 PM	NW	3.1	
24 Dec 2021	2:00 PM	NW	4.9	
24 Dec 2021	3:00 PM	NW	3.1	
24 Dec 2021	4:00 PM	NW	3.1	
24 Dec 2021	5:00 PM	NW	1.8	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
24 Dec 2021	6:00 PM	NW	1.3	
24 Dec 2021	7:00 PM	NW	1.8	
24 Dec 2021	8:00 PM	NE	0.9	
24 Dec 2021	9:00 PM	NW	0.9	
24 Dec 2021	10:00 PM	NW	1.3	
24 Dec 2021	11:00 PM	NW	1.3	
25 Dec 2021	12:00 AM	NW	1.3	
25 Dec 2021	1:00 AM	NW	1.3	
25 Dec 2021	2:00 AM	Е	0.9	
25 Dec 2021	3:00 AM	Е	0.9	
25 Dec 2021	4:00 AM	Е	0.9	
25 Dec 2021	5:00 AM	Е	0.9	
25 Dec 2021	6:00 AM	ESE	0.9	
25 Dec 2021	7:00 AM	ESE	1.8	
25 Dec 2021	8:00 AM	ENE	1.3	
25 Dec 2021	9:00 AM	ENE	1.3	
25 Dec 2021	10:00 AM	NW	1.3	
25 Dec 2021	11:00 AM	NW	1.3	
25 Dec 2021	12:00 PM	NW	1.3	
25 Dec 2021	1:00 PM	NW	1.8	
25 Dec 2021	2:00 PM	ESE	0.9	
25 Dec 2021	3:00 PM	NW	1.3	
25 Dec 2021	4:00 PM	NNW	1.3	
25 Dec 2021	5:00 PM	ENE	1.3	
25 Dec 2021	6:00 PM	ESE	1.3	
25 Dec 2021	7:00 PM	Е	1.8	
25 Dec 2021	8:00 PM	ESE	1.8	
25 Dec 2021	9:00 PM	SE	2.7	
25 Dec 2021	10:00 PM	E	2.2	
25 Dec 2021	11:00 PM	Е	2.2	
26 Dec 2021	12:00 AM	Е	1.8	
26 Dec 2021	1:00 AM	Е	1.3	
26 Dec 2021	2:00 AM	Е	1.3	
26 Dec 2021	3:00 AM	NW	0.9	
26 Dec 2021	4:00 AM	WNW	0.4	
26 Dec 2021	5:00 AM	WNW	0.9	
26 Dec 2021	6:00 AM	W	0.9	
26 Dec 2021	7:00 AM	W	0.9	
26 Dec 2021	8:00 AM	WNW	0.9	
26 Dec 2021	9:00 AM	ESE	0.4	
26 Dec 2021	10:00 AM	WNW	0.4	
26 Dec 2021	11:00 AM	W	0.9	
26 Dec 2021	12:00 PM	W	0.9	
26 Dec 2021	1:00 PM	W	0.9	
26 Dec 2021	2:00 PM	W	1.3	
26 Dec 2021	3:00 PM	W	0.9	
26 Dec 2021	4:00 PM	W	0.4	
26 Dec 2021	5:00 PM	ESE	0.4	
26 Dec 2021	6:00 PM	ENE	0.4	
26 Dec 2021	7:00 PM	W	0.9	
26 Dec 2021	8:00 PM	W	1.3	
26 Dec 2021	9:00 PM	W	1.3	
26 Dec 2021	10:00 PM	W	1.3	
26 Dec 2021	11:00 PM	NW	0.9	
27 Dec 2021	12:00 AM	Е	1.3	
27 Dec 2021	1:00 AM	NW	1.3	
27 Dec 2021	2:00 AM	NW	4.9	

	Dl.	2021			
December 2021					
Wind Speed and Directions					
Date	Time	Wind Speed m-s	Direction		
27 Dec 2021	3:00 AM	NW	3.1		
27 Dec 2021	4:00 AM	NW	3.1		
27 Dec 2021	5:00 AM	NW	1.3		
27 Dec 2021	6:00 AM	W	0.4		
27 Dec 2021	7:00 AM	NW	1.3		
27 Dec 2021	8:00 AM	NW	0.9		
27 Dec 2021	9:00 AM	WNW	0.9		
27 Dec 2021	10:00 AM	W	0.4		
27 Dec 2021	11:00 AM	W	0.9		
27 Dec 2021	12:00 PM	W	0.4		
27 Dec 2021	1:00 PM	WNW	0.4		
27 Dec 2021	2:00 PM	W	0.4		
27 Dec 2021	3:00 PM	WNW	0.4		
27 Dec 2021	4:00 PM	WNW	0.4		
27 Dec 2021	5:00 PM	WNW	0.4		
27 Dec 2021	6:00 PM	WNW	0.4		
27 Dec 2021	7:00 PM	WNW	0.4		
27 Dec 2021	8:00 PM	WNW	0.4		
27 Dec 2021	9:00 PM	NW	0.4		
27 Dec 2021	10:00 PM	WNW	0.9		
27 Dec 2021	11:00 PM	WNW	0.9		
28 Dec 2021	12:00 AM	NW	0.4		
28 Dec 2021	1:00 AM	NW	0.9		
28 Dec 2021	2:00 AM	NW	0.9		
28 Dec 2021	3:00 AM	NW	0.4		
28 Dec 2021	4:00 AM	NW	0.4		
28 Dec 2021	5:00 AM	NW	1.3		
28 Dec 2021	6:00 AM	WNW	1.3		
28 Dec 2021	7:00 AM	NE	1.3		
28 Dec 2021	8:00 AM	NE	0.9		
28 Dec 2021	9:00 AM	NW	0.9		
28 Dec 2021	10:00 AM	NW	0.9		
28 Dec 2021	11:00 AM	NW	0.9		
28 Dec 2021	12:00 PM	NW	0.9		
28 Dec 2021	1:00 PM	NW	1.8		
28 Dec 2021	2:00 PM	NE	1.3		

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
28 Dec 2021	3:00 PM	NE	1.3	
28 Dec 2021	4:00 PM	NW	0.4	
28 Dec 2021	5:00 PM	WNW	0.0	
28 Dec 2021	6:00 PM	W	0.4	
28 Dec 2021	7:00 PM	W	0.0	
28 Dec 2021	8:00 PM	W	0.0	
28 Dec 2021	9:00 PM	WNW	0.4	
28 Dec 2021	10:00 PM	W	0.4	
28 Dec 2021	11:00 PM	WNW	1.3	
29 Dec 2021	12:00 AM	WNW	1.3	
29 Dec 2021	1:00 AM	WNW	0.9	
29 Dec 2021	2:00 AM	WNW	0.9	
29 Dec 2021	3:00 AM	WNW	0.9	
29 Dec 2021	4:00 AM	WNW	1.3	
29 Dec 2021	5:00 AM	NW	1.3	
29 Dec 2021	6:00 AM	WNW	0.4	
29 Dec 2021	7:00 AM	WNW	1.3	
29 Dec 2021	8:00 AM	W	0.9	
29 Dec 2021	9:00 AM	W	1.8	
29 Dec 2021	10:00 AM	W	1.3	
29 Dec 2021	11:00 AM	W	0.9	
29 Dec 2021	12:00 PM	W	0.9	
29 Dec 2021	1:00 PM	NW	0.4	
29 Dec 2021	2:00 PM	NW	0.9	
29 Dec 2021	3:00 PM	NW	1.3	
29 Dec 2021	4:00 PM	NW	1.3	
29 Dec 2021	5:00 PM	NW	1.3	
29 Dec 2021	6:00 PM	NW	0.9	
29 Dec 2021	7:00 PM		0.0	
29 Dec 2021	8:00 PM		0.0	
29 Dec 2021	9:00 PM	NNW	0.0	
29 Dec 2021	10:00 PM	NNW	0.0	
29 Dec 2021	11:00 PM	NW	0.4	
30 Dec 2021	12:00 AM	NW	1.3	
30 Dec 2021	1:00 AM	NW	2.2	
30 Dec 2021	2:00 AM	NW	4.0	
30 Dec 2021	3:00 AM	NW	4.9	
30 Dec 2021	4:00 AM	NW	4.0	
30 Dec 2021	5:00 AM	NW	3.1	
30 Dec 2021	6:00 AM	NW	1.3	
30 Dec 2021	7:00 AM	NW	1.3	
30 Dec 2021	8:00 AM	NW	1.3	
30 Dec 2021	9:00 AM	NW	0.9	
30 Dec 2021	10:00 AM	NW	0.9	
30 Dec 2021	11:00 AM	NW	0.9	
30 Dec 2021	12:00 PM	NW	0.9	
30 Dec 2021	1:00 PM	NW	0.9	
30 Dec 2021	2:00 PM	NW	1.8	
30 Dec 2021	3:00 PM	WNW	1.3	
30 Dec 2021	4:00 PM	W	1.3	
30 Dec 2021	5:00 PM	W	0.9	
30 Dec 2021	6:00 PM	W	0.9	
30 Dec 2021	7:00 PM	WNW	0.9	
30 Dec 2021	8:00 PM	W	1.3	
30 Dec 2021	9:00 PM	WNW	1.8	
30 Dec 2021	10:00 PM	WNW	1.8	
30 Dec 2021	11:00 PM	WNW	0.9	

December 2021				
Wind Speed and Directions				
Date	Time	Wind Speed m-s	Direction	
31 Dec 2021	12:00 AM	WNW	1.3	
31 Dec 2021	1:00 AM	WNW	2.2	
31 Dec 2021	2:00 AM	WNW	1.3	
31 Dec 2021	3:00 AM	NW	1.8	
31 Dec 2021	4:00 AM	WNW	1.3	
31 Dec 2021	5:00 AM	WNW	1.3	
31 Dec 2021	6:00 AM	WNW	1.3	
31 Dec 2021	7:00 AM	WNW	1.3	
31 Dec 2021	8:00 AM	WNW	1.3	
31 Dec 2021	9:00 AM	N	0.9	
31 Dec 2021	10:00 AM	N	0.9	
31 Dec 2021	11:00 AM	WNW	0.9	
31 Dec 2021	12:00 PM	WNW	0.9	
31 Dec 2021	1:00 PM	WNW	0.9	
31 Dec 2021	2:00 PM	WNW	1.8	
31 Dec 2021	3:00 PM	WNW	1.3	
31 Dec 2021	4:00 PM	WNW	1.3	
31 Dec 2021	5:00 PM	WNW	0.9	
31 Dec 2021	6:00 PM	WNW	1.3	
31 Dec 2021	7:00 PM	WNW	1.3	
31 Dec 2021	8:00 PM	WNW	1.3	
31 Dec 2021	9:00 PM	NNE	0.9	
31 Dec 2021	10:00 PM	Е	0.9	
31 Dec 2021	11:00 PM	ENE	0.4	

APPENDIX F 24-HOUR TSP MONITORING RESULTS AND GRAPHICAL PRESENTATIONS

Appendix F - 24-hour TSP Impact Monitoring Results

Location CKL1 - Flat 121 Cha Kwo Ling Village

	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate	Elapse	e Time	C	Flow Rate	e (m³/min.)	Av. Flour	Total vol.	Conc.	Action	Limit
Start Date	Condition	(K)	Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Sampling Time (hrs.)	Initial	Final	(m³/min)		(µg/m³)	Level (µ g/m3)	Level (µ g/m3)
2-Dec-21	Sunny	290.7	767.2	3.3424	3.4116	0.0692	3462.8	3486.8	24.0	1.24	1.24	1.24	1783.0	38.8		
8-Dec-21	Sunny	293.2	767.7	3.3605	3.6019	0.2414	3486.9	3510.9	24.0	1.23	1.23	1.23	1777.5	135.8		
14-Dec-21	Fine	294.0	764.0	3.3643	3.6181	0.2538	3510.9	3534.9	24.0	1.23	1.23	1.23	1772.0	143.2	191.0	260.0
20-Dec-21	Rainy	290.3	762.7	3.3061	3.3870	0.0809	3534.9	3558.9	24.0	1.24	1.23	1.24	1779.8	45.4	131.0	200.0
23-Dec-21	Fine	292.9	763.8	3.3219	3.4415	0.1197	3558.9	3582.9	24.0	1.23	1.23	1.23	1774.4	67.4		
29-Dec-21	Sunny	291.3	768.9	3.3340	3.6513	0.3173	3582.9	3606.9	24.0	1.24	1.24	1.24	1783.2	177.9		
Note:	Bold Italic means A	ction Level exce	edance										Min	38.8		
	Bold Italic with und	derline means L	imit Level exceedance										Max	143.2		
													Average	86.1		

Location CKL2 - Flat 103 Cha Kwo Ling Village

	Weather	Air Temp.	Atmospheric	Filter Weight (g)		Particulate	Elapse	e Time	Sampling	Flow Rate (m ³ /min.)		Av. Flow	Total vol	Conc.	g/m3)	Limit
Start Date	Condition		Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final	(m³/min)	(m ³)	(μg/m ³)		Level (µ g/m3)
2-Dec-21	Sunny	290.7	767.2	3.3451	3.4349	0.0898	15488.5	15512.5	24.0	1.24	1.24	1.24	1786.5	50.3		
8-Dec-21	Fine	293.2	767.7	3.3236	3.5154	0.1918	15655.2	15679.2	24.0	1.24	1.24	1.24	1779.6	107.8		
14-Dec-21	Rainy	294.0	764.0	3.3007	3.4078	0.1071	15679.2	15703.2	24.0	1.23	1.23	1.23	1774.9	60.3	183.0	260.0
20-Dec-21	Sunny	290.3	762.7	3.3308	3.4320	0.1012	15703.2	15727.2	24.0	1.24	1.24	1.24	1782.2	56.8	103.0	260.0
23-Dec-21	Fine	292.9	763.8	3.3170	3.4000	0.0830	15727.2	15751.2	24.0	1.23	1.23	1.23	1777.6	46.7		
29-Dec-21	Sunny	291.3	768.9	3.3169	3.4831	0.1662	15751.2	15775.2	24.0	1.24	1.24	1.24	1786.8	93.0		
Note:	Bold Italic means A	Action Level exce	edance										Min	46.7		

 kote:
 Bold Italic means Action Level exceedance
 Min
 46.7

 Bold Italic with underline means Limit Level exceedance
 Max
 107.8

 Average
 64.4

Appendix F - 24-hour TSP Impact Monitoring Results

Location KTD1 - Centre of Excellence in Paediatrics (Children's Hospital)

	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate	Elaps	e Time	Sampling	Flow Rate	e (m³/min.)	Av. Flow	Total vol.	Conc.	Action	Limit
Start Date	Condition	(K)	Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final	(m³/min)	(m ³)	(μg/m ³)	Level (µ g/m3)	Level (µ g/m3)
2-Dec-21	Sunny	290.7	767.2	3.3511	3.4684	0.1173	15031.4	15055.4	24.0	1.25	1.24	1.25	1793.6	65.4		
8-Dec-21	Sunny	293.2	767.7	3.3184	3.4572	0.1388	15055.4	15079.4	24.0	1.21	1.21	1.21	1748.0	79.4		
14-Dec-21	Sunny	294.0	764.0	3.3803	3.5129	0.1326	15055.4	15079.4	24.0	1.21	1.21	1.21	1742.2	76.1	177.0	260.0
20-Dec-21	Cloudy	290.3	762.7	3.3103	3.3548	0.0445	15103.5	15127.5	24.0	1.22	1.21	1.22	1750.4	25.4	177.0	200.0
23-Dec-21	Fine	292.9	763.8	3.3149	3.4104	0.0955	15127.5	15151.4	24.0	1.21	1.21	1.21	1744.0	54.8		
29-Dec-21	Sunny	291.3	768.9	3.3387	3.5239	0.1852	15151.4	15175.4	24.0	1.22	1.22	1.22	1754.0	105.6		
Note:	Bold Italic means A	ction Level exce	edance										Min	25.4		
	Bold Italic with und	derline means L	imit Level exceedance										Max	79.4		
													Average	60.2		


Location KER1 - Future Residential Development at Kerry Godown


	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate	Elaps	e Time	Sampling	Flow Rate	e (m³/min.)	Av. Flow	Total vol.	Conc.	Action	Limit
Start Date	Condition	(K)	Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final	(m³/min)	(m ³)	(µg/m ³)	Level (µ g/m3)	Level (µ g/m3)
2-Dec-21	Sunny	290.7	767.2	3.3580	3.6415	0.2836	12697.2	12721.2	24.0	1.25	1.25	1.25	1798.9	157.6		
8-Dec-21	Sunny	293.2	767.7	3.3149	3.4392	0.1243	12721.2	12745.2	24.0	1.21	1.21	1.21	1743.5	71.3		
14-Dec-21	Sunny	294.0	764.0	3.3261	3.5878	0.2617	12745.2	12769.2	24.0	1.21	1.20	1.21	1737.0	150.7	172.0	260.0
20-Dec-21	Cloudy	290.3	762.7	3.3058	3.5218	0.2160	12769.3	12793.3	24.0	1.21	1.21	1.21	1746.3	123.7	172.0	200.0
23-Dec-21	Fine	292.9	763.8	3.2885	3.4968	0.2083	12793.3	12817.3	24.0	1.21	1.21	1.21	1739.1	119.7		
29-Dec-21	Sunny	291.3	768.9	3.3178	3.4465	0.1287	12817.3	12841.3	24.0	1.21	1.22	1.22	1750.3	73.5	1	
Note:	Bold Italic means A	Action Level exce	edance										Min	71.3		
	Rold Italic with un-	darlina magne l	imit Level exceedance										May	157.6		


Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area

	Weather	Air Temp.	Atmospheric	Filter W	eight (g)	Particulate	Elaps	e Time	Sampling	Flow Rate	(m³/min.)	Av. Flow	Total vol.	Conc.	Action	Limit
Start Date	Condition		Pressure, Pa (mmHg)	Initial	Final	weight (g)	Initial	Final	Time (hrs.)	Initial	Final	(m³/min)	(m ³)	(μg/m ³)	Level (µ g/m3)	Level (µ g/m3)
2-Dec-21	Sunny	290.7	767.2	3.2924	3.4744	0.1821	13453.0	13477.0	24.0	1.23	1.23	1.23	1767.1	103.0		
8-Dec-21	Sunny	293.2	767.7	3.3346	3.5581	0.2235	13477.0	13501.0	24.0	1.22	1.22	1.22	1759.7	127.0		
14-Dec-21	Sunny	294.0	764.0	3.3791	3.4959	0.1168	13501.0	13525.0	24.0	1.22	1.21	1.22	1752.3	66.7	172.0	260.0
20-Dec-21	Cloudy	290.3	762.7	3.3152	3.4263	0.1112	13525.0	13549.0	24.0	1.23	1.22	1.22	1762.9	63.1	172.0	200.0
23-Dec-21	Fine	292.9	763.8	3.3253	3.4829	0.1576	13549.0	13573.0	24.0	1.22	1.22	1.22	1755.6	89.8		
29-Dec-21	Sunny	291.3	768.9	3.3063	3.5404	0.2341	13573.0	13597.0	24.0	1.23	1.23	1.23	1767.4	132.5		
Note:	Bold Italic means A	Action Level exce	edance										Min	63.1		
	De let tre l'e colete con	d	facility and an experience										Mov	127.0		

Bold Italic with underline means Limit Level exceedance

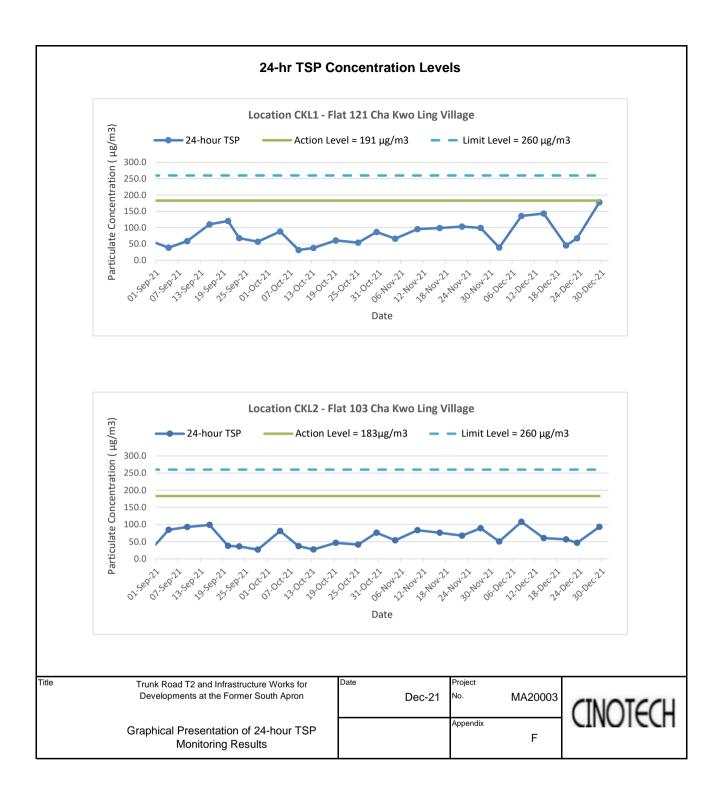

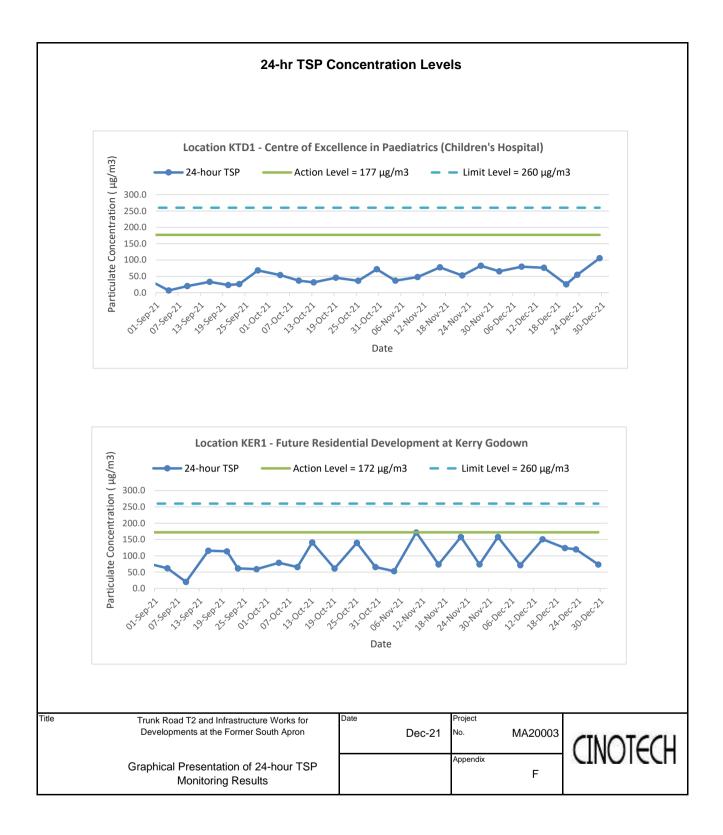

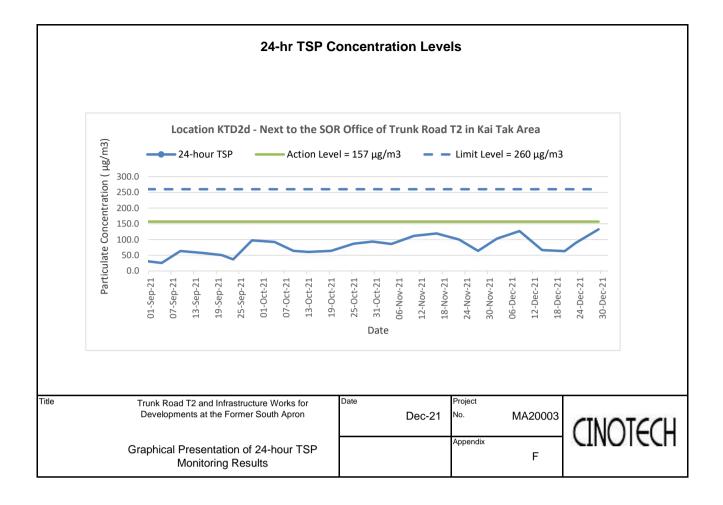

APPENDIX G COPIES OF CALIBRATION CERTIFICATES FOR NOISE MONITORING

High Precision Chemical Testing Ltd.

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong &ng

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00150 Issue Date : 16 Nov 2021

Application No. : HP00032

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong King

Sample Description : Submitted equipment stated to be Sound Level Calibrator.

Equipment No.: : N-13-01

Manufacturer: : SOUNDTEK

Other information : | Model No. | ST-120

Serial No. 181001608

Date Received : 05 Nov 2021

Test Period : 08 Nov 2021 to 12 Nov 2021

Test Requested : Performance checking for Sound Level Calibrator

Test Method : The Sound Level Meter and Calibrator has been calibrated in accordance with

the documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark : 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai K

Laboratory Manager

High Precision Chemical Testing Ltd.

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong King

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00150 | Issue Date : 16 Nov 2021

Application No. : HP00032

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Ker
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Description	Sound Meter
Manufacturer	BSWA Technology
Model No.	BSWA 308
Serial No.	570188
Microphone No.	570608
Equipment No.	N-12-03

Test Result

Reference value, dB	Indication value, dB	Deviation, dB	Allowed deviation, dB
94.0	94.1	+0.1	± 0.3
114.0	114.0	0.0	± 0.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -



0025915

SVAN959 SLM Object 1: Customer: Cinotech Consultants Limited Serial No. /Ref. No. : 11275 / N-08-01 RM 1710, Technology Park, Object 2: Microphone Serial No. /Ref. No. : 18 On Lai Street, Shatin, N.T. 22452 Hong Kong **SVANTEK** Manufacturer: Customer Code: SVEC09005 Certificate No.: 0025915 Date of calibration: 22/01/2021 Date of the recommended re-calibration: 22/01/2022 Handle by: E0002

Measuring results

	Reference value	Indication value	Deviation	Allowed deviation	Object
	94.0dB	93.9dB	-0.1dB	+/- 1.5dB	1
Γ	114.0dB	113.8dB	-0.2dB	+/- 1.5dB	1

Measuring equipment

	index	Calibrator / Master	Traceability
0.000	1	Master Sound Meter, SVAN949,sn:8571	IEC61672
	2	Sound Calibrator, SV30A sn:32580	IEC60942

Ambient conditions

Temperature (20...26)°C

Humidity (20...60)%RH

Measuring procedure

Calibrated by Type 1 Sound Calibrator with Master Sound Level Meter under 1kHz Frequency.

Uncertainty

+/- 0.2 dB for probability not less than 95%.

Conformity

- 1. The resulted values were those obtained at the time of test and applies only to the item calibrated.
- 2.The measurement uncertainty was calculated according to the regulations of GUM with the coverage factor k=2 and contains the uncertainty of the measuring procedure and the uncertainty of the measuring system.
- 3. The equipment being used in this calibration are regularly calibrated by laboratory according to ISO/IEC17025.
- 4.HKAS has accredited this laboratory (HOKLAS 267) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories.
- 5. The calibrations certificate may not be reproduced.

Measured value(s)	within	the allowable deviation.
-------------------	--------	--------------------------

Performed by

Approved by

Calibration Technician

Quality Manager

High Precision Chemical Testing Ltd.

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong King

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00149 | Issue Date : 16 Nov 2021

Application No. : HP00031

Certificate of Calibration

Applicant : Cinotech Consultants Limited

RM 1710, Technology Park,

18 On Lai Street,

Shatin, N.T., Hong King

Sample Description : Submitted equipment stated to be Integrating Sound Level Meter.

Equipment No.: : N-12-04

Manufacturer: : BSWA Technology

Other information : N

Model No.	BSWA 308
Serial No.	580238
Microphone No.	590073

Date Received : 05 Nov 2021

Test Period : 08 Nov 2021 to 12 Nov 2021

Test Requested : Performance checking for Sound Level Meter

Test Method : The Sound Level Calibrator has been calibrated in accordance with the

documented procedures and using standard and instrument which are

recommended by the manufacturer, or equivalent.

Test conditions : Room Temperature: 22-25 degree Celsius

Relative Humidity: 35-70%

Test Result : Refer to the test result(s) on page 2.

Remark: 1. Information of the sample description provided by the Applicant.

2. The result(s) relate only to the items tested or calibrated.

For and on behalf of HIGH PRECISION CHEMICAL TESTING LIMITED

Lee Wai K Laboratory Manager

High Precision Chemical Testing Ltd.

Rm 1904, Technology Park 18 On Lai Street, Shatin

NT, Hong king

Tel: +852 3841 4388 Website: https://www.hpct.com.hk



Report No. : 00149 | Issue Date : 16 Nov 2021

Application No. : HP00031

Certificate of Calibration

Measuring equipment

Description	Sound Calibrator
Manufacturer	Brüel & Kær
Model No.	TYPE 4231
Serial No.	2326353
Equipment No.	N-02-01

Test Result

Reference value, dB Indication value, dB		Deviation, dB	Allowed deviation, dB
94.0	93.7	-0.3	± 1.5
114.0	114.0	0.0	± 1.5

Note

- : 1. "Instrument Readings" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.
 - 2. The indication value was obtained from the average of ten replicated measurement.

- End of report -



0025913

Customer: Cinotech Consultants Limited RM 1710, Technology Park, 18 On Lai Street, Shatin, N.T. Hong Kong		Object 1 : Serial No. /Ref. No. : Object 2 : Serial No. /Ref. No. :	Microphone
Customer Code: SVEC09005		Manufacturer: Svar	ntek
Date of calibration: Date of the recommended re-calibration:	22/01/2021 22/01/2022	Certificate No.: Handle by:	0025913 E0002

Measuring results

Reference value	Indication value	Deviation	Allowed deviation	Object
94.0dB	93.5dB	-0.5dB	+/- 1.5dB	1
114.0dB	113.3dB	-0.7dB	+/- 1.5dB	1

Measuring equipment

index Calibrator / Master		Traceability
1	Master Sound Meter, SVAN949,sn:8571	IEC61672
2	Sound Calibrator, SV30A sn:32580	IEC60942

Ambient conditions

Temperature (20...26)°C

Humidity (20...60)%RH

Measuring procedure

Calibrated by Type 1 Sound Calibrator with Master Sound Level Meter under 1kHz Frequency.

Uncertainty

+/- 0.2 dB for probability not less than 95%.

Conformity

- 1. The resulted values were those obtained at the time of test and applies only to the item calibrated.
- 2. The measurement uncertainty was calculated according to the regulations of GUM with the coverage factor k=2 and contains the uncertainty of the measuring procedure and the uncertainty of the measuring system.
- 3. The equipment being used in this calibration are regularly calibrated by laboratory according to ISO/IEC17025.
- 4.HKAS has accredited this laboratory (HOKLAS 267) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories.
- 5. The calibrations certificate may not be reproduced.

Measured v	value(s)	within	the	allowable	deviation.
-------------------	----------	--------	-----	-----------	------------

Performed by

Approved by

Calibration Technician

Quality Manager



0025914

Object 1: SVAN957 SLM Customer: Cinotech Consultants Limited Serial No. /Ref. No. : 23851 / N-08-12 RM 1710, Technology Park, Object 2: Microphone Serial No. /Ref. No. : 18 On Lai Street, Shatin, N.T. 43676 Hong Kong Customer Code: Manufacturer: SVEC09005 Svantek 0025914 Date of calibration: 22/01/2021 Certificate No.: Date of the recommended re-calibration: 22/01/2022 Handle by: E0002

Measuring results

Reference value	Indication value	Deviation	Allowed deviation	Object
94.0dB	93.6dB	-0.4dB	+/- 1.5dB	1
114.0dB	113.5dB	-0.5dB	+/- 1.5dB	1

Measuring equipment

index Calibrator / Master		Traceability
1	Master Sound Meter, SVAN949,sn:8571	IEC61672
2	Sound Calibrator, SV30A sn:32580	IEC60942

Ambient conditions

Temperature (20...26)°C

Humidity (20...60)%RH

Measuring procedure

Calibrated by Type 1 Sound Calibrator with Master Sound Level Meter under 1kHz Frequency.

Uncertainty

+/- 0.2 dB for probability not less than 95%.

Conformity

- 1.The resulted values were those obtained at the time of test and applies only to the item calibrated.
- 2. The measurement uncertainty was calculated according to the regulations of GUM with the coverage factor k=2 and contains the uncertainty of the measuring procedure and the uncertainty of the measuring system.
- 3. The equipment being used in this calibration are regularly calibrated by laboratory according to ISO/IEC17025.
- 4.HKAS has accredited this laboratory (HOKLAS 267) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories.
- 5. The calibrations certificate may not be reproduced.

Measured value(s)	within	the allowable deviation.
-------------------	--------	--------------------------

Performed by

Approved by

Calibration Technician

Quality Manager

Appleone Calibration Laboratory Ltd.

Rm1309, 13/F, No.77 Wing Hong St, Kln, HKSAR

Tel: +852 2370 4437 Fax: +852 2114 0393



0025916

Customer: Cinotech Consultants Limited RM 1710, Technology Park, 18 On Lai Street, Shatin, N.T.		Object 1: SV30A sound calibrator Serial No. /Ref. No.: 10965 / N-09-02 Object 2: Serial No. /Ref. No.:	
Hong Kong		14	
Customer Code: SVEC09005		Manufacturer : Svar	ntek
Date of calibration: Date of the recommended re-calibration:	22/01/2021 22/01/2022	Certificate No.: Handle by:	0025916 E0002

Measuring results

 Reference value	Indication value	Deviation	Allowed deviation	Object
94.0dB	94.1dB	+0.1dB	+/- 0.3dB	1
114.0dB	114.3dB	+0.3dB	+/- 0.3dB	1

Measuring equipment

index Calibrator / Master		Traceability
1	Master Sound Meter, SVAN949,sn:8571	IEC61672
2	Sound Calibrator, SV30A sn:32580	IEC60942

Ambient conditions

Temperature (20...26)°C

Humidity (20...60)%RH

Measuring procedure

Calibrated by Type 1 Sound Level Meter and 1kHz Sound Source .

Uncertainty

+/- 0.2 dB

for probability not less than 95%.

Conformity

- 1. The resulted values were those obtained at the time of test and applies only to the item calibrated.
- 2. The measurement uncertainty was calculated according to the regulations of GUM with the coverage factor k=2 and contains the uncertainty of the measuring procedure and the uncertainty of the measuring system.
- 3. The equipment being used in this calibration are regularly calibrated by laboratory according to ISO/IEC17025.
- 4.HKAS has accredited this laboratory (HOKLAS 267) for specific calibration activities as listed in the HOKLAS directory of accredited laboratories.
- 5. The calibrations certificate may not be reproduced.

Measured value(s)	within	the allowable deviation.	
-------------------	--------	--------------------------	--

Performed by

Approved by

Calibration Technician

Quality Manager

Appleone Calibration Laboratory Ltd.

Rm1309, 13/F, No.77 Wing Hong St, Kln, HKSAR

Tel: +852 2370 4437 Fax: +852 2114 0393

APPENDIX H NOISE MONITORING RESULTS AND GRAPHICAL PRESENTATIONS

Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)


Location CKL1 - Flat 121 Cha Kwo Ling Village								
				Unit: dB	(A) (30-min			
Date	Time	Weather	Meas	sured Noise I	_evel	Baseline Level	Construction Noise Level	
Date	Tillie	vveatrier						
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	
9-Dec-21	15:00	Sunny	68.9	71.1	65.4	72.4	68.9 Measured ≦ Baseline	
15-Dec-21	14:30	Fine	69.3	70.4	67.5	72.4	69.3 Measured ≦ Baseline	
21-Dec-21	9:30	Rainy	68.8	70.2	65.9	72.4	68.8 Measured ≦ Baseline	
30-Dec-21	14:00	Sunny	68.4	71.2	66.1	72.4	68.4 Measured ≦ Baseline	


Location CKL2 - Flat 103 Cha Kwo Ling Village								
				Unit: dB	(A) (30-min)		
Date	Time	Weather	Meas	sured Noise I	_evel	Baseline Level	Construction Noise Level	
Date	Tillie	VVCatrici						
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	
9-Dec-21	13:50	Sunny	69.8	72.2	65.3	71.4	69.8 Measured ≦ Baseline	
15-Dec-21	14:00	Fine	68.7	71.6	65.1	71.4	68.7 Measured ≦ Baseline	
21-Dec-21	10:00	Rainy	69.2	71.6	66.7	71.4	69.2 Measured ≦ Baseline	
30-Dec-21	14:50	Sunny	69.1	71.9	66.7	71.4	69.1 Measured ≦ Baseline	

Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)									
				Unit: dB (A) (30-min)					
Date	Time	Weather	Measured Noise Level		Baseline Level	Construction Noise Level			
Date	Tillie	VVCatrici							
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}		
9-Dec-21	14:00	Fine	70.1	73.2	67.2	78.0	70.1 Measured ≦ Baseline		
15-Dec-21	10:45	Sunny	68.2	72.3	65.1	78.0	68.2 Measured ≦ Baseline		
21-Dec-21	11:15	Cloudy	74.1	76.9	70.0	78.0	74.1 Measured ≦ Baseline		
30-Dec-21	11:45	Sunny	70.2	73.1	67.0	78.0	70.2 Measured ≦ Baseline		

Location KER1 - Future Residential Development at Kerry Godown								
				Unit: dB (A) (30-min)				
Date	Time	Weather	Meas	sured Noise I	_evel	Baseline Level	Construction Noise Level	
Date	Tillie	VVCatrici						
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	
9-Dec-21	13:00	Fine	71.1	74.4	68.1	65.0	70	
15-Dec-21	11:35	Sunny	70.1	72.2	68.4	65.0	68	
21-Dec-21	10:10	Cloudy	70.8	73.1	65.5	65.0	69	
30-Dec-21	11:00	Sunny	72.2	75.3	69.4	65.0	71	

Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area								
				Unit: dB (A) (30-min)				
Date	Time	Weather	Measured Noise Level		Level	Baseline Level	Construction Noise Level	
Date	Tillic	VVCatrici	_	_				
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}	
9-Dec-21	9:00	Fine	62.1	64.9	58.3	64.0	62 Measured ≦ Baseline	
15-Dec-21	9:00	Sunny	67.1	68.9	63.2	64.0	64	
21-Dec-21	13:45	Cloudy	61.7	62.6	58.4	64.0	62 Measured ≦ Baseline	
30-Dec-21	9:00	Sunny	63.3	65.1	61.1	64.0	63 Measured ≦ Baseline	

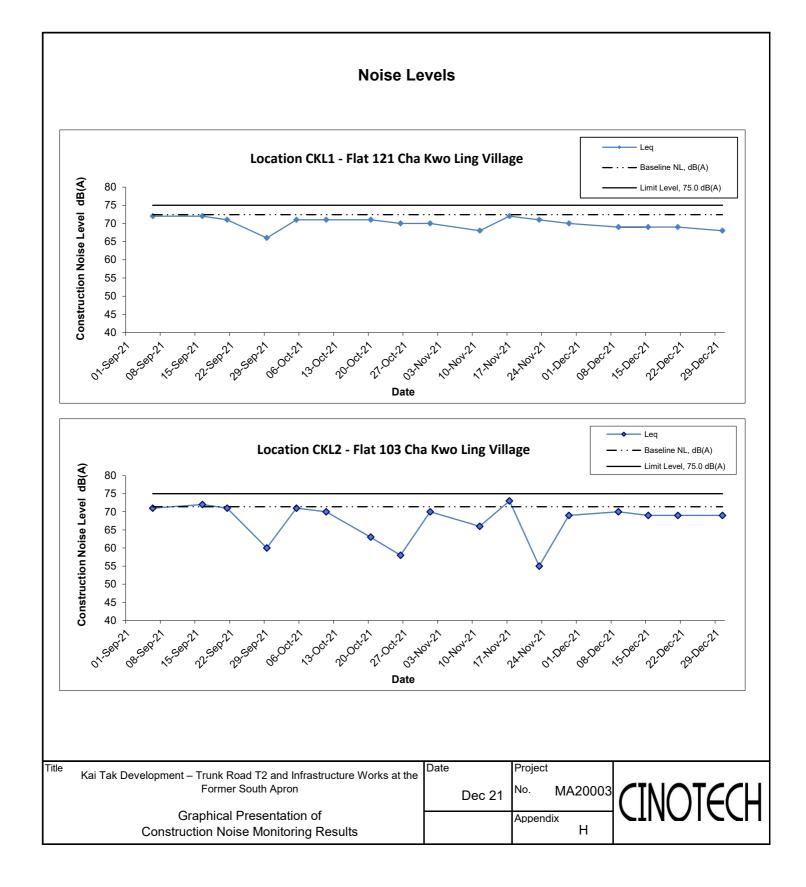

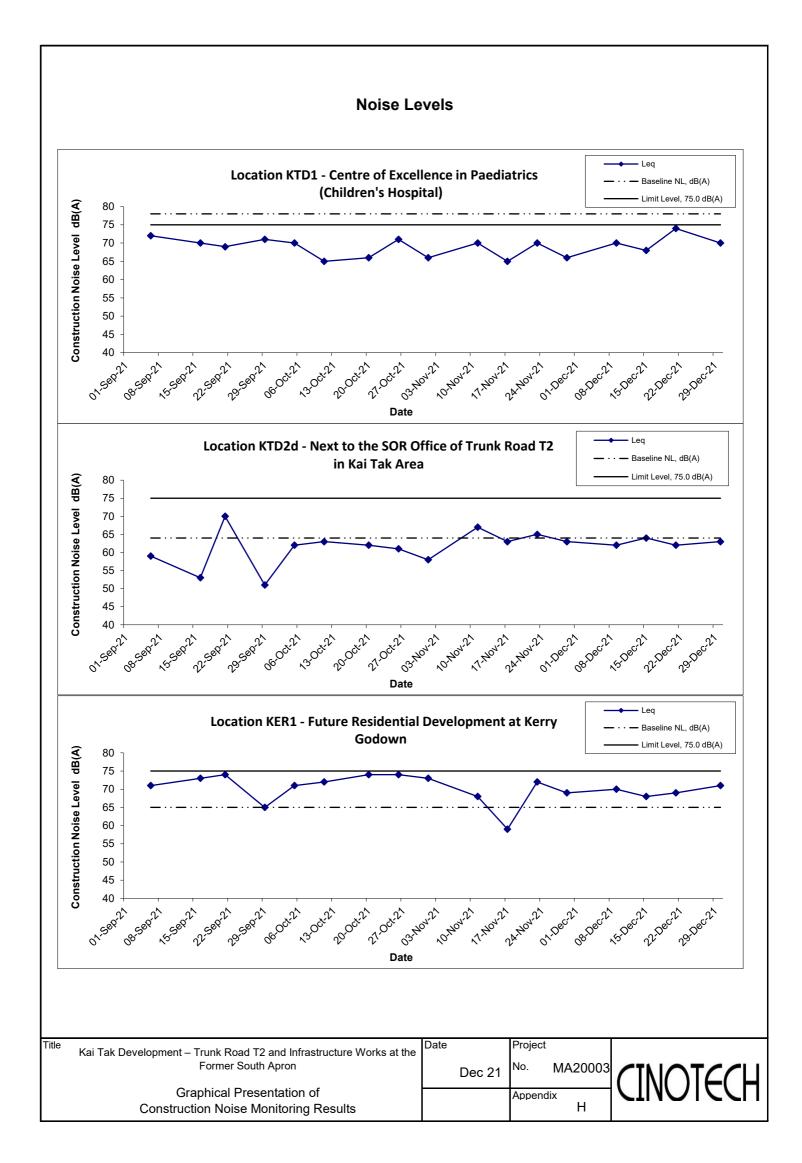

APPENDIX I SITE AUDIT SUMMARY

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	211202
Date	02 December 2021 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	Follow up on the previous session (Ref No.:211125), no environmental deficiency was identified on previous session.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	02 December 2021
Checked by	Karina Chan	Zelle	02 December 2021

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	211209
Date	09 December 2021 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:211202), no environmental deficiency was identified on previous session.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	09 December 2021
Checked by	Karina Chan	Zalle	09 December 2021

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	211216
Date	16 December 2021 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
211216 – R2	B. Water Quality Manhole outside the launching shaft area shall be sealed to prevent silt from discharging into drainage system.	<i>B8</i>
	C. Air Quality No environmental deficiency was identified during site inspection	
	 D. Construction Noise Impact No environmental deficiency was identified during site inspection. 	
211216 – R1	 E. Waste/Chemical Management Contractor is reminded to avoid accumulation and timely dispose of construction waste on site. 	E4ii
	 F. Visual and Landscape No environmental deficiency was identified during site inspection. 	
	 G. Permits/Licences No environmental deficiency was identified during site inspection. 	
	 H. Marine Ecology No environmental deficiency was identified during site inspection. 	
	 I. Others Follow up on the previous session (Ref No.:211209), no environmental deficiency was identified on previous session. 	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	16 December 2021
Checked by	Karina Chan	Zalle	16 December 2021

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	211223
Date	23 December 2021 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
	No environmental deficiency was identified during site inspection.	
	F. Visual and Landscape	
	No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:211216), item 211216 – R1 and 211216 – R2 were rectified.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	23 December 2021
Checked by	Karina Chan	John	23 December 2021

Environmental Team for Trunk Road T2 and Infrastructure Works at the Former South Apron

Checklist Reference Number	211230
Date	30 December 2021 (Thursday)
Time	09:30 – 12:00

Ref. No.	Non-Compliance	Related Item No.
-	None identified	-

Ref. No.	Remarks/Observations	Related Item No.
	B. Water Quality	
	No environmental deficiency was identified during site inspection.	
	C. Air Quality	
	No environmental deficiency was identified during site inspection	
	D. Construction Noise Impact	
	No environmental deficiency was identified during site inspection.	
	E. Waste/Chemical Management	
211230 - R1	Oil drum and grease were observed on site. Drip tray should be provided.	E9
	F. Visual and Landscape	
	• No environmental deficiency was identified during site inspection.	
	G. Permits/Licences	
	No environmental deficiency was identified during site inspection.	
	H. Marine Ecology	
	No environmental deficiency was identified during site inspection.	
	I. Others	
	• Follow up on the previous session (Ref No.:211223), no environmental deficiency was identified on previous session.	

	Name	Signature	Date
Recorded by	Tim Lui	Cyli	30 December 2021
Checked by	Karina Chan	John	30 December 2021

APPENDIX J EVENT AND ACTION PLANS

Table J-1 Event/Action Plan for Air Construction Dust Monitoring

Table J-1	Event/Action Fian for Air Construction Dust Worldowing								
Event		Action							
Event	ET	IEC	ER	Contractor					
Action Level									
1. Exceedance for	1. Identify source, investigate	Check monitoring data	1. Notify Contractor.	1. Rectify any unacceptable					
one sample	the causes of complaint and	submitted by ET;		practice;					
	propose remedial measures;	2. Check Contractor's working		2. Amend working methods					
	2. Inform IEC and ER;	method.		agreed with the ER as					
	3. Repeat measurement to			appropriate.					
	confirm finding;								
	4. Increase monitoring								
	frequency.								
2. Exceedance by	1. Identify source;	Check monitoring data	1. Notify Contractor;	1. Submit proposals for					
two or more	2. Inform IEC and ER;	submitted by ET;	2. Ensure remedial measures	remedial actions to IEC					
consecutive	3. Advise the ER on the	2. Check Contractor's working	properly implemented.	within three working days of					
samples	effectiveness of the proposed	method;		notification;					
	remedial measures;	3. Discuss with ET, ER and		2. Implement the agreed					
	4. Repeat measurements to	Contractor on possible		proposals;					
	confirm findings;	remedial measures if		3. Amend proposal if					
	5. Increase monitoring	required;		appropriate.					
	frequency to daily;	4. Advise the ER on the							
	6. Discuss with IEC, ER and	effectiveness of the proposed							
	Contractor on remedial	remedial measures;							
	actions required;								

E	Action							
Event	ET	IEC	ER	Contractor				
Limit level 1. Exceedance for one sample	 If exceedance continues, arrange meeting with IEC, Contractor and ER; If exceedance stops, cease additional monitoring. Identify source, investigate the causes of exceedance and propose remedial measures; Inform the IEC, ER, and Contractor; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC and ER 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET, ER and Contractor on possible remedial measures; Advise the ER and ET on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented.	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to the ER and copy to the ET and IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate. 				
	informed of the results.							
2. Exceedance for	1. Notify IEC, ER and	1. Discuss amongst ER, ET, and	1. Confirm receipt of	1. Take immediate action to				
two or more	Contractor;	Contractor on the potential	notification of exceedance in	avoid further exceedance;				
consecutive	2. Identify source;	remedial actions;	writing;	2. Submit proposals for remedial				

Event		Ac	tion	
EVERT IEC		ER	Contractor	
samples	3. Repeat measurement to	2. Review Contractor's	2. Notify Contractor;	actions to ER and copy to the
	confirm findings;	remedial actions whenever	3. In consolidation with the IEC	IEC and ET within three
	4. Increase monitoring	necessary to assure their	and ET, agree with the	working days of notification;
	frequency to daily;	effectiveness and advise the	Contractor on the remedial	3. Implement the agreed
	5. Carry out analysis of	ER and ET accordingly;	measures to be implemented;	proposals;
	Contractor's working	3. Supervise the	4. Ensure remedial measures	4. Resubmit proposals if
	procedures with the ER to	implementation of remedial	properly implemented;	problem still not under
	determine possible mitigation	measures.	5. If exceedance continues,	control;
	to be implemented;		consider what portion of the	5. Stop the relevant portion of
	6. Arrange meeting with IEC		work is responsible and	works as determined by the
	and ER to discuss the		instruct the Contractor to	ER until the exceedance is
	remedial actions to be taken;		stop that portion of work	abated.
	7. Assess effectiveness of		until the exceedance is	
	Contractor's remedial actions		abated.	
	and keep IEC, EPD and ER			
	informed of the results;			
	8. If exceedance stops, cease			
	additional monitoring.			

Table J-2 Event/Action Plan for Construction Noise Monitoring

TO 4	Action									
Event	ET	IEC ER	Contractor							
Action Level	1. Notify IEC, ER and	1. Review the monitoring data 1. Notify Contractor;	1. Submit noise mitigation							
	Contractor;	submitted by the ET; 2. Require Contractor to propose	proposals to the ER and copy							
	2. Carry out investigation;	2. Review the construction remedial measures for	to the IEC and ET;							
	3. Report the results of	methods and proposed redial implementation if required.	2. Implement noise mitigation							
	investigation to the IEC and	measures by the Contractor,	proposals.							
	Contractor;	and advise the ET and ER if								
	4. Discuss jointly with the ER	the proposed remedial								
	and formulate remedial	measures would be								
	measures;	sufficient.								
	5. Increase monitoring									
	frequency to check									
	mitigation effectiveness.									
Limit Level	1. Notify IEC, ER and	1. Discuss amongst ER, ET, and 1. Confirm receipt of	1. Take immediate action to							
	Contractor;	Contractor on the potential notification of failure in	avoid further exceedance;							
	2. Identify source;	remedial actions; writing;	2. Submit proposals for							
	3. Repeat measurements to	2. Review the Contractor's 2. Notify Contractor;	remedial actions to the ER							
	confirm findings;	remedial actions whenever 3. Require Contractor to	and copy to the ET and IEC							
	4. Carry out analysis of	necessary to assure their propose remedial measures	within 3 working days of							
	Contractor's working	effectiveness and advise the for the analysed noise	notification;							

T4	Action						
Event	ET	IEC	ER	Contractor			
	procedures to determine	ER accordingly;	problem;	3. Implement the agreed			
	possible mitigation to be	3. Supervise the	4. Ensure remedial measures	proposals;			
	implemented;	implementation of remedial	properly implemented;	4. Resubmit proposals if			
	5. Record the causes and action	measures.	5. If exceedance continues,	problem still not under			
	taken for the exceedances;		consider what portion of the	control;			
	6. Increase the monitoring		work is responsible and	5. Stop the relevant portion of			
	frequency;		instruct the Contractor to stop	works as determined by the			
	7. Assess the effectiveness of		that portion of work until the	ER until the exceedance is			
	the Contractor's remedial		exceedance is abated.	abated.			
	action with the ER and keep						
	the IEC informed of the						
	results;						
	8. If exceedance stops, cease						
	additional monitoring.						

Table J-3 Event/Action Plan for Landscape and Visual

Event	Action							
	ET	IEC	ER	Contractor				
Non-conformity	1. Identify Source;	1. Check report;	1. Notify Contractor;	1. Amend working methods;				
on one occasion	2. Inform the IEC and the ER;	2. Check Contractor's working	2. Ensure remedial measures	2. Rectify damage and undertake				
	3. Discuss remedial actions with	method;	are properly implemented.	any necessary replacement.				
	IEC, ER and Contractor	3. Discuss with ET and the						
	4. Monitor remedial actions until	Contractor on possible						
	rectification has been	remedial measures;						
	completed.	4. Advise ER on effectiveness						
		of proposed remedial						
		measures;						
		5. Check implementation of						
		remedial measures						

Event	Action						
	ET	IEC	ER	Contractor			
Repeated	1. Identify source;	1. Check monitoring report; 1.	Notify Contractor;	1. Amend working methods;			
Non-conformity	2. Inform the IEC and the ER;	2. Check Contractor's working 2.	Ensure remedial measures	2. Rectify damage and undertake			
	3. Increase monitoring frequency;	method;	are properly implemented.	any necessary replacement.			
	4. Discuss remedial actions with	3. Discuss with ET and the					
	the IEC, the ER and the	Contractor on possible					
	Contractor;	remedial measures;					
	5. Monitor remedial actions until	4. Advise ER on effectiveness					
	rectification has been	of proposed remedial					
	completed;	measures;					
	6. If exceedance stops, cease	5. Check implementation of					
	additional monitoring.	remedial measures					

APPENDIX K ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE (EMIS)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Relevant Standard or Requirement	Implen	nentatio	Status												
						D	С	0											
Air Quality Imp	act																		
S2.3.1.1	The specific mitigation comprises the following: watering of the construction areas 12 times per day to reduce dust emissions by 91.7%, with reference to the "Control of Open Fugitive Dust Sources" (USEPA	To minimize dust emission during construction works	All relevant works sites, conveyor belts and stockpiles	Contractor and Sub- contractors	APCO / EIAO	Y	Y		^										
	AP-42). The amount of water to be applied would be 0.91L/m ² for the respective watering frequency;																		
	Dust enclosures with watering would be provided along the loading ramps and conveyor belts for unloading the C&D materials to the barge for dust suppression; and								N/A(1)										
	3-sided barriers around the stockpiling areas WA3 and WA4.								٨										
S2.3.1.2	The dust control measures detailed below shall also be incorporated into the Contract Specification where practicable as an integral part of good construction practice:	To minimize dust emission during construction works	All relevant works sites	Contractor and Sub- contractors	APCO / EIAO	Y	Y		۸										
	Use of regular watering to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather;																		
	Use of frequent watering for particularly dusty construction areas and areas close to ASRs;								۸										
	Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines;								۸										

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages		n Stages	Status
						D	С	0	
	Open stockpiles shall be avoided or covered. Prevent placing dusty material storage piles near ASRs;								۸
	Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations;								۸
	Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;								۸
	Imposition of speed controls for vehicles on unpaved site roads, 8 km per hour is the recommended limit;								N/A(1)
	Routing of vehicles and position of construction plant should be at the maximum possible distance from ASRs;								^
	Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;								^
	Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; and								N/A(1)
	Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system.								N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	1			Status
						D	С	0	
Noise Impact									
S3.4.1.1	The use of quieter plant, including Quality Powered Mechanical Equipment (QPME) is specified for the list of equipment: - Concrete lorry mixer - Dump Truck, 5.5 tonne < gross vehicle weight ≤ 38 tonne - Generator, Super Silenced, 70 dB(A) at 7m - Poker, vibratory, Hand-held (electric) - Water Pump, Submersible (Electric) - Mobile Crane - KOBELCO CKS900 - Excavator, wheeled/tracked - HYUNDAI R80CR-9	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		^
S3.4.1.1	Use of temporary or fixed noise barriers with a surface density of at least 10kg/m^2 to screen noise from movable and stationary plant.	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		٨
S3.4.1.1	Use of enclosures with covers at top and three sides and a surface density of at least 10kg/m ² to screen noise from generally static noisy plant such as air compressors.	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y		N/A(1)
S3.4.1.1	Use of acoustic fabric for the silent piling system, drill rigs, rock drills etc.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub-contractors	NCO / EIAO		Y		^
S3.4.1.1	Proper fitting of silencers and mufflers on the ventilation fans.	To minimise air- borne noise impacts	All relevant works sites	Contractor and Sub-contractors	NCO / EIAO		Y		N/A(1)
	Implementation of good site practice: Only well-maintained plant should be operated on-site and plants should be serviced regularly during the construction period; Mobile plant, if any, should be sited as far from NSRs as possible; Plant known to emit noise strongly in one direction should, wherever possible,	To minimise airborne noise impacts	All relevant works sites	Contractor and Sub- contractors	NCO / EIAO		Y	-	^
	be properly orientated so that the noise is directed away from the nearby NSRs;								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	t		Implementation Stages		Implementation Stages		Implementation Stages		Implementation Stages		Implementation Stages	
						D	C	0									
	Use of site hoarding as a noise barrier to screen noise at low level NSRs;								^								
	Machines and plant that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum; and								٨								
	Any material stockpiles and other structures should be effectively utilised, wherever practicable, to screen the noise from on-site construction activities.								٨								
	The advancing speed of the TBM should be restricted to 2m/hr in order to ensure compliance with the daytime ground-borne noise limits.								N/A								
Water Quality																	
S4.2.1.1	Surface run-off from the construction site, including all Works Areas, will be	construction site runoff and general construction activities	All works sites	Contractor and Sub- contractors	Water Pollution Control Ordinance / ProPECC PN 1/94		Y		*								
	Dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas and Works Areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap;								^								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	nentatio	1 Stages	Status
						D	C	0	
	The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. The sizes may vary depending upon the flow rate, but for a flow rate of $0.1 \text{m}^3/\text{s}$, a sedimentation basin of 30m^3 would be required and for a flow rate of $0.5 \text{m}^3/\text{s}$ the basin would be 150m^3 . All effluent discharged from the construction site should comply with the standards stipulated in the TM-DSS. The detailed design of the sand/silt traps shall be undertaken by the Contractor prior to the commencement of construction;								N/A(1)
	In accordance with ProPECC PN 1/94, the construction works should be programmed to minimise surface excavation works during rainy seasons (April to September), as far as practicable. All exposed earth areas should be completed and vegetated as soon as possible after the earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means;							•	^
	The overall slope of works sites should be kept to a minimum to reduce the erosive potential of surface water flows, and all trafficked areas and access roads should be protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during the prolonged periods of inclement weather and the reduction of surface sheet flows;								۸
	All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure their proper and efficient operation at all times particularly following rainstorms. Deposited silts and grits should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;								^
	Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet season is inevitable, they should be dug and backfilled in short sections wherever practicable. The water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities;								^

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	С	О	
	Open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system;								^
	Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers;								*
	Precautions to be taken at any time of the year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted and during or after rainstorms, are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storm events;								N/A(1)
	All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at the exit of every construction site where practicable. Wash- water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-washing bay to public roads should be paved with sufficient backfall toward the wheel- washing bay to prevent vehicle tracking of soil and silty water to public roads and drains;								^
	Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources, specifically Works Areas WA1, WA2, WA4 and WA5 where plant maintenance is proposed. Oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for oil interceptors to prevent flushing during heavy rain;								N/A(1)
	The construction solid waste, debris and rubbish on-site should be collected, handled and disposed of properly to avoid causing any water quality impacts. The requirements for solid waste management are detailed in Section 11 Waste Management of this EIA report; and								^
	All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching the nearby WSRs.								۸

EM&A Ref.	Recommended Mitigation Measures		Recommended Ager Measures & Main	mmended res & Main	ing Implementation Agent	Relevant Standard or Requirement	Impler	mentatio	n Stages	Status
						D	C	0		
S4.2.1.1 and 4.3.1.5	There is a need to apply to the EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Minimum distances of 100m should be maintained between the discharge points of construction site effluent and the existing seawater intakes. The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc, can minimise water consumption and reduce the effluent discharge volume. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license		All works sites	Contractor and Sub- contractors	Water Pollution Control Ordinance		Y		N/A(1)	
S4.2.1.1	Specific mitigation measures for the tunnelling works using TBM, soft ground and mechanical excavation techniques should include the following: The cut-and-cover tunnelling works should be conducted sequentially as far as practicable to limit the amount of construction wastewater generated from the exposed areas during the wet season (April to September);	To minimize construction water quality impact from tunnelling and excavation works	All tunnelling and excavation portion	Contractor and Sub- contractors	TMEIA TMwater ProPECC PN 1/94 WPCO		Y		N/A	
	Uncontaminated discharge should pass through settlement tanks prior to discharge;							-	N/A	
	If contaminated groundwater is found during the course of the works, no direct discharge of groundwater from contaminated areas should be adopted. Any contaminated groundwater should be properly treated in compliance with the requirements of the TM-DSS. If wastewater treatment is to be deployed for treating the contaminated groundwater, the wastewater treatment unit should deploy suitable treatment processes (e.g. oil interceptor/activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (such as TPH) to an undetectable range;								N/A	
	If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS;								N/A	

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implen	Implementation Stages		Status
						D	C	0	
	The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as TPH products should be removed as necessary by installing the petrol interceptor;								N/A
	The wastewater with high concentrations of SS should be treated such as by settlement in tanks with sufficient retention time before discharge. Oil interceptors would also be required to remove the oil, lubricants and grease from the wastewater.								N/A
S4.2.1.1	In order to prevent any accidental release of bentonite slurry from getting into the surrounding environment, the following specific control measures shall be followed to reduce the risk and impacts of accidental spillage: All bentonite slurry should be stored in a container that resistant to corrosion, maintained in good conditions and securely closed;	To control water quality impact from bentonite slurry	All relevant works sites	Contractor and Sub- contractors	WPCO		Y		^
	The container should be labelled in English and Chinese and note that the container is for storage of bentonite slurry only; The storage container should be placed on an area of impermeable flooring and bunded with capacity to accommodate 110% of the volume of the container size or 20% by volume stored in the area and enclosed with at least 3 sides;								^ N/A(1)
	The storage container should be sufficiently covered to prevent rainfall entering the container or bunded area (water collected within the bund must be tested and disposed of as chemical waste, if necessary);								^
	An emergency clean up kit shall be readily available where bentonite fluid will be stored or used; and								N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement			n Stages	Status
						D	С	0	
	The handling and disposal of bentonite slurries should be undertaken in accordance within ProPECC PN 1/94. Surplus bentonite slurries used in construction works shall be reconditioned and reused wherever practicable. Residual bentonite slurry shall be disposed of from the site as soon as possible as stipulated in Clause 8.56 of the General Specification for Civil Engineering Works. The Contractor should explore alternative disposal outlets for the residual bentonite slurry (dewatered bentonite slurry to be disposed to a public filling area and liquid bentonite slurry, if mixed with inert fill material, to be disposed to a public filling area) and disposal at landfill should be the last resort.								N/A(1)
S4.2.1.1		To minimize construction water quality impact from barging point	Barging Point	Contractor and Sub- contractors	EIAO-TM WPCO		Y		N/A(1)
	generated by turbulence from vessel movement or propeller wash; All hopper barges should be fitted with tight fitting seals to their bottom								۸
	openings to prevent leakage of material;								
	Construction activities should not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site; and								N/A(1)
	Loading of barges and hoppers should be controlled to prevent splashing of material into the surrounding water. Barges or hoppers should not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation.								N/A
S4.2.1.1	If chemical toilets and sewage holding tanks are required for handling sewage generated by the construction workforce, a licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	To minimize construction water quality impact from sewage and effluent	All works sites	Contractor	WPCO		Y		۸

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	d Agent	Implementation Agent	Relevant Standard or Requirement			n Stages	Status
						D	С	0	
S4.2.1.1	In order to protect against impacts to the surrounding marine waters of the KTTS and Victoria Harbour in the event of an accidental spillage of fuel or oil, the Contractor will be required to prepare a spill response plan to the satisfaction of AFCD, EPD, FSD, Police, TD and WSD to define procedures for the control, containment and clean-up of any spillage that could occur on the construction site.		All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	The Contractor must, also, register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		N/A(1)
S4.2.1.1	Storage of Chemical Wastes published under the Waste Disposal Ordinance	To control water quality impact from accidental chemical spillage	All works sites	Contractor	EIAO-TM WPCO WDO		Y		#
	Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;								
	Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents; and								N/A(1)
	Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.								N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Recommended Agent or Requirement Measures & Main						n Stages	Status
						D	C	0		
S4.2.1.1	The road drainage in the tunnel should pass through oil interceptors to remove oil, and grease before being discharged into the public storm water drainage system;	To mitigate runoff from tunnel during the operational phase	Tunnel	CEDD	WPCO			Y	N/A	
	Silt traps and oil interceptors should be cleaned and maintained regularly; and								N/A	
	The oily contents of oil interceptors should be transferred to an appropriate disposal facility, or to be collected for reuse, if possible.								N/A	
Marine Ecology										
S5.3.1.1	Good construction practice measures have been recommended to be implemented as follows: Avoid damage and disturbance to the remaining and surrounding natural habitat;	Minimize waste generation during construction	Contractor	Work Sites	Construction phase of Main Works Stage 1, Stage 2 and Stage 3		Y		N/A(1)	
	Placement of equipment in designated areas within the existing disturbed land;								N/A(1)	
	Spoil heaps should be covered at all times;								N/A(1)	
	Construction activities should be restricted to the designated works areas; and								N/A(1)	
	Disturbed areas to be reinstated immediately after completion of the works.								N/A(1)	
Fisheries				•						
S6.2.1.2	No fisheries specific mitigation measures.									

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address		Implementation Agent	Relevant Standard or Requirement	Impler	nentatio	n Stages	Status
						D	C	0	
Landscape and V	Jisual								
S7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y	Y		^
S7.2.1.2	Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y	Y		N/A
S7.2.1.2	Large temporary stockpiles of excavated material shall be covered with unobtrusive sheeting to prevent dust and dirt spreading to adjacent landscape areas and vegetation, and to create a neat and tidy visual appearance.	To prevent unnecessary dust and dirt contaminating the air and adjacent areas.	All relevant works sites	CEDD's Contractor	EIAO TM		Y		^
S7.2.1.2	Construction plant and building material shall be orderly and carefully stored in order to create a neat and tidy visual appearance.	To mitigate potential visually obtrusive areas	All relevant works sites	CEDD's Contractor	EIAO TM		Y		^
S7.2.1.2	Erection of decorative screen hoarding should be designed to be compatible with the existing urban context.	To mitigate and screen any potential visually obtrusive areas and enhance urban environment	All relevant works sites	CEDD's Contractor	EIAO TM		Y		^
S7.2.1.2	All lighting in construction site shall be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC user. The contractor shall consider other security measures, which shall minimize the visual impacts.	To mitigate light pollution and adverse visual impacts on surrounding environment	All relevant works sites	CEDD's Contractor	EIAO TM		Y		^
S7.2.1.2	Compensatory tree planting shall be incorporated along all roadside amenity areas affected by the construction works. The required numbers and locations of compensatory trees shall be determined and agreed with the Government during Tree Removal Application process under ETWB TCW No. 3/2006.		All relevant works sites	CEDD's Contractor	EIAO TM		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address		Implementation Agent	Relevant Standard or Requirement	Implen	nentation	1 Stages	Status
						D	С	0	
S7.2.1.2	1	To reinstate and maximise compensatory tree	All relevant works sites	CEDD's Contractor	EIAO TM		Y		N/A(1)
S7.2.1.2	Trees and shrubs and climbers etc. shall be planted to soften and screen proposed roads, central strip and associated structure, and to enhance streetscape greening effect where appropriate.	To mitigate hard surfaces and hard standing landscape areas and to soften and enhance proposed design features	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	All works area, excavated area and disturbed area for tunnel construction and temporary road diversion or any other proposed works shall be reinstated to former conditions or better, with reasonable landscape treatment and to the satisfaction of the relevant Government departments.	To reinstate and maximise hard and soft landscape areas to equal or greater conditions	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	Tunnel portals and all above ground structures shall be sensitively designed to ensure the element with colour, texture and tonal quality being compatible to the existing urban context. Trees and shrub planting to minimize the potential adverse landscape and visual impacts shall be included where space permits. Roof top greening and vertical greening shall also be provided.	To mitigate hard surfaces and hard standing landscape areas and to soften and enhance proposed design features	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	All works shall be carefully designed to minimize impacts on existing landscape resources and visually sensitive receivers. Existing trees within works area shall be retained and protected.		All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
S7.2.1.2	Existing trees of good quality and condition that are unavoidably affected by the works should be transplanted.	To minimise impact on existing trees	All relevant works sites	CEDD's Contractor	EIAO TM	Y		Y	N/A
Cultural Heritag	ge								
S8.2.1.1 and 8.2.1.2	No culture heritage specific mitigation measures								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	1	Implementation Agent	Relevant Standard or Requirement	1 1			1 Stages	Status
						D	С	0		
Waste Managen	l nent Implication									
S9.2.1.2	The requirements as stipulated in the ETWB TC(W) No.19/2005 Environmental Management on Construction Sites and the other relevant guidelines should be included in the Particular Specification for the future contractor as appropriate.	To keep trace of the generation, minimization, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A	
S9.2.1.2	The future contractor should be requested to submit an outline Waste Management Plan (WMP) prior to the commencement of construction work, in accordance with the ETWB TC(W) No.19/2005 so as to provide an overall framework of waste management and reduction. The WMP should include: - Waste management policy; - Record of generated waste; - Waste reduction target; - Waste reduction programme; - Role and responsibility of waste management team; - Benefit of waste management; - Analysis of waste materials; - Reuse, recycling and disposal plans; - Transportation process of waste products; and - Monitoring and action plan.		All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A(1)	
S9.2.1.2	The waste management hierarchy should be strictly followed. This hierarchy should be adopted to evaluate the waste management options in order to maximise the extent of waste reduction and cost reduction. The records of quantities of waste generated, recycled and disposed (locations) should be properly documented.	To keep trace of the generation, minimization, reuse and disposal of C&D	All areas / throughout construction period	Contractor	ETWB TC(W) No.19/2005		Y		N/A(1)	
S9.2.1.2	A trip-ticket system should be established in accordance with DevB TC(W) No. 6/2010 and Waste Disposal (Charges for Disposal of Construction Waste) Regulation to monitor the disposal of public fill and solid wastes at public filling facilities and landfills, and to control fly-tipping. A trip-ticket system would be included as one of the contractual requirements for the future contractor to strictly implement. The Engineer would also regularly audit the effectiveness of the system.	1	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)	

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Implementation Agent	Relevant Standard or Requirement	I Implementation Stages			Status	
						D	С	0	
S9.2.1.2	A recording system for the amount of waste generated, recycled and disposed (locations) should be established. The future contractor should also provide proper training to workers regarding the appropriate concepts of site cleanliness and waste management procedures, e.g. waste reduction, reuse and recycling all the time.	To monitor disposal of waste and control fly-tipping	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	The CEDD should be timely notified of the estimated spoil volumes to be generated and the PFC should be notified and agreement sort on the disposal of surplus inert C&D materials e.g. good quality rock during detailed design of the Trunk Road T2 Project. Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and to ensure acceptability at public filling areas or reclamation sites.	of waste and control	All areas / throughout construction period	Contractor	DEVB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimise the	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)
S9.2.1.2	Inert C&D materials from road pavement would be reused for backfilling where possible	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)
S9.2.1.2	TBM generated alluvium and other C&D materials should be treated at a slurry treatment plant prior to transferring to Public Fill Reception Facilities.	To minimize, reuse and disposal of C&D materials	TMB works area / during TBM works	Contractor	DevB TC(W) No.6/2010		Y		N/A
S9.2.1.2	The site and surroundings should be kept tidy and litter free.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address		Implementation Agent	Relevant Standard or Requirement	Implen	nentatior	Status	
						D	C	0	
S9.2.1.2		To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^
S9.2.1.2	Make provisions in contract documents to allow and promote the use of recycled aggregates where appropriate.	To implement good site practice for handling, sorting reuse and recycling of wastes	Detailed Design	Design Consultant	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010	Y			N/A(1)
S9.2.1.2	disposal sites in the WMP for approval before implementation.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	Stockpiled C&D materials should be covered by tarpaulin and/or watered as appropriate to prevent windblown dust and surface run off.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^
S9.2.1.2	Excavated C&D materials in trucks should be covered by tarpaulins to reduce the potential for spillage and dust generation.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^
S9.2.1.2	Wheel washing facilities should be used by all trucks leaving the site to prevent transferring mud trails onto public roads.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^
S9.2.1.2	Excavated marine deposit (sediment) should be disposed of in a gazetted marine disposal ground under the requirements of the DASO or treated for backfilling.	To ensure proper disposal of marine sediment	All areas / throughout construction period	Contractor	ETWB TC(W) No.34/2002		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement			Implementation Stages			Status
						D	С	0			
S9.2.1.2	Standard formwork or pre-fabrication should be used as far as practicable to minimise the C&D materials arising. The use of more durable formwork or plastic facing for construction works should also be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should be carefully planned in order to avoid over-ordering and wastage.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)		
S9.2.1.2	The future contractor should recycle as many C&D materials as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		^		
S9.2.1.2	All falsework should be steel instead of wood as far as practicable.	To minimize, reuse and disposal of C&D materials	All areas / throughout construction period	Contractor	DevB TC(W) No.6/2010		Y		N/A(1)		

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	1		n Stages	Status
						D	C	0	
S9.2.1.2	Chemical waste producers should register with the EPD and chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: - Suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; - Having a capacity of <450L unless the specifications have been approved by the EPD; and - Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations Clearly labelled and used solely for the storage of chemical wastes; - Enclosed with at least 3 sides; - Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; - Adequate ventilation; - Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and - Incompatible materials are adequately separated.	To properly store the chemical waste within works sites and works areas	All areas / throughout construction period	Contractor	Code of Practice on the Packaging, Handling and Storage of Chemical Wastes		Y		^
S9.2.1.2	Waste oils, chemicals or solvents should not be disposed of to drain.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	EIAO TM		Y		^

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Location/Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages		Status	
						D	С	О	
S9.2.1.2	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them. Night soil should be regularly collected by licensed collectors.	To ensure proper disposal of sewage sludge	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance, DevB TC(W) No. 6/2010		Y		N/A(1)
S9.2.1.2	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins should be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By- laws. In addition, general refuse should be cleared daily and disposed of to the nearest licensed landfill. Burning of refuse on construction sites is prohibited.	To separate the general refuse from other waste types and proper disposal of the refuse	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		*
S9.2.1.2	All waste containers should be in a secure area on hardstanding.	To implement good site practice for handling, sorting reuse and recycling of wastes	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		^
S9.2.1.2	Aluminium cans should be collected and recovered from the waste stream by reputable collectors if they are segregated and easily accessible. Separately labelled bins for their deposition should be provided as far as practicable.	To implement on-site sorting facilitating reuse and recycling of materials as well as proper disposal of waste	All areas / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)
S9.2.1.2	aluminium cans, plastic bottles, etc should be provided on-site.	To separate the general refuse from other waste types and proper disposal of the refuse	Site Offices / throughout construction period	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)

EM&A Ref.	Recommended Mitigation Measures Objectives of the Recommended Measures & Main Concern to Address			Recommended Agent or Measures & Main	Recommended Agent Measures & Main	Recommended Agent Measures & Main	Recommended Agent or Requirement Measures & Main	ommended ures & Main	ded Agent	9 -	-	Implementation Stages		Implementation Stag			Status
						D	C	0									
S9.2.1.2	Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	To implement good site practice for handling, sorting reuse and recycling of wastes	Contract Mobilisation	Contractor	WDO, Land (Miscellaneous Provisions) Ordinance		Y		N/A(1)								
S9.2.1.2	During construction phase, regular site inspections and supervision of the waste management procedures shall be undertaken as part of the EM&A procedures.	To ensure proper control, all waste is removed from site areas as appropriate and illegal disposal of waste is not being undertaken	All areas / throughout construction period	Contractor	EIAO TM		Y		۸								

Remarks: EM	I&A Programme under EP-451/2013
D	Design
С	Construction
Y	Yes
О	Operation
^	Compliance of mitigation measure;
N/A N/A(1)	Not applicable at this stage; Not observed;
*	Recommendation was made during site audit but improved/retified by the contractor;
#	Recommendation was made during site audit but not yet improved/retified by the contractor;
X	Non-compliance of mitigation measure;
•	Non-compliance but rectified by the contractor.

APPENDIX L SUMMARIES OF ENVIRONMENTAL COMPLAINT, WARNING, SUMMON AND NOTIFICATION OF SUCCESSFUL PROSECUTION

Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Development at the Former South Apron

Reporting Month: December 2021

Log Ref.	Location	Received Date	Details of Complaint/war ning/summon and prosecution	Investigation/Mitigation Action	Status
-	-	-	-	-	-

Remarks:

No environmental complaint/warning/summon and prosecution were received in the reporting period.

APPENDIX M SUMMARY OF EXCEEDANCE

Environmental Permit No.: EP-451/2013 Environmental Team for Trunk Road T2

Appendix M – Summary of Exceedance

Reporting Month: December 2021

(A) Exceedance Report for Air Quality

No Action Level and Limit Level exceedance of 24hr TSP monitoring was recorded in this reporting month.

(B) Exceedance Report for Construction Noise

Action Level for Construction Noise


No Action Level exceedance was recorded in this reporting month.


Limit Level for Construction Noise


No Limit Level exceedance for daytime construction noise monitoring was recorded in the reporting month.


(C) Summary of Landscape and Visual Non-Conformity (NIL in the reporting month)


APPENDIX N TENTATIVE CONSTRUCTION PROGRAMME

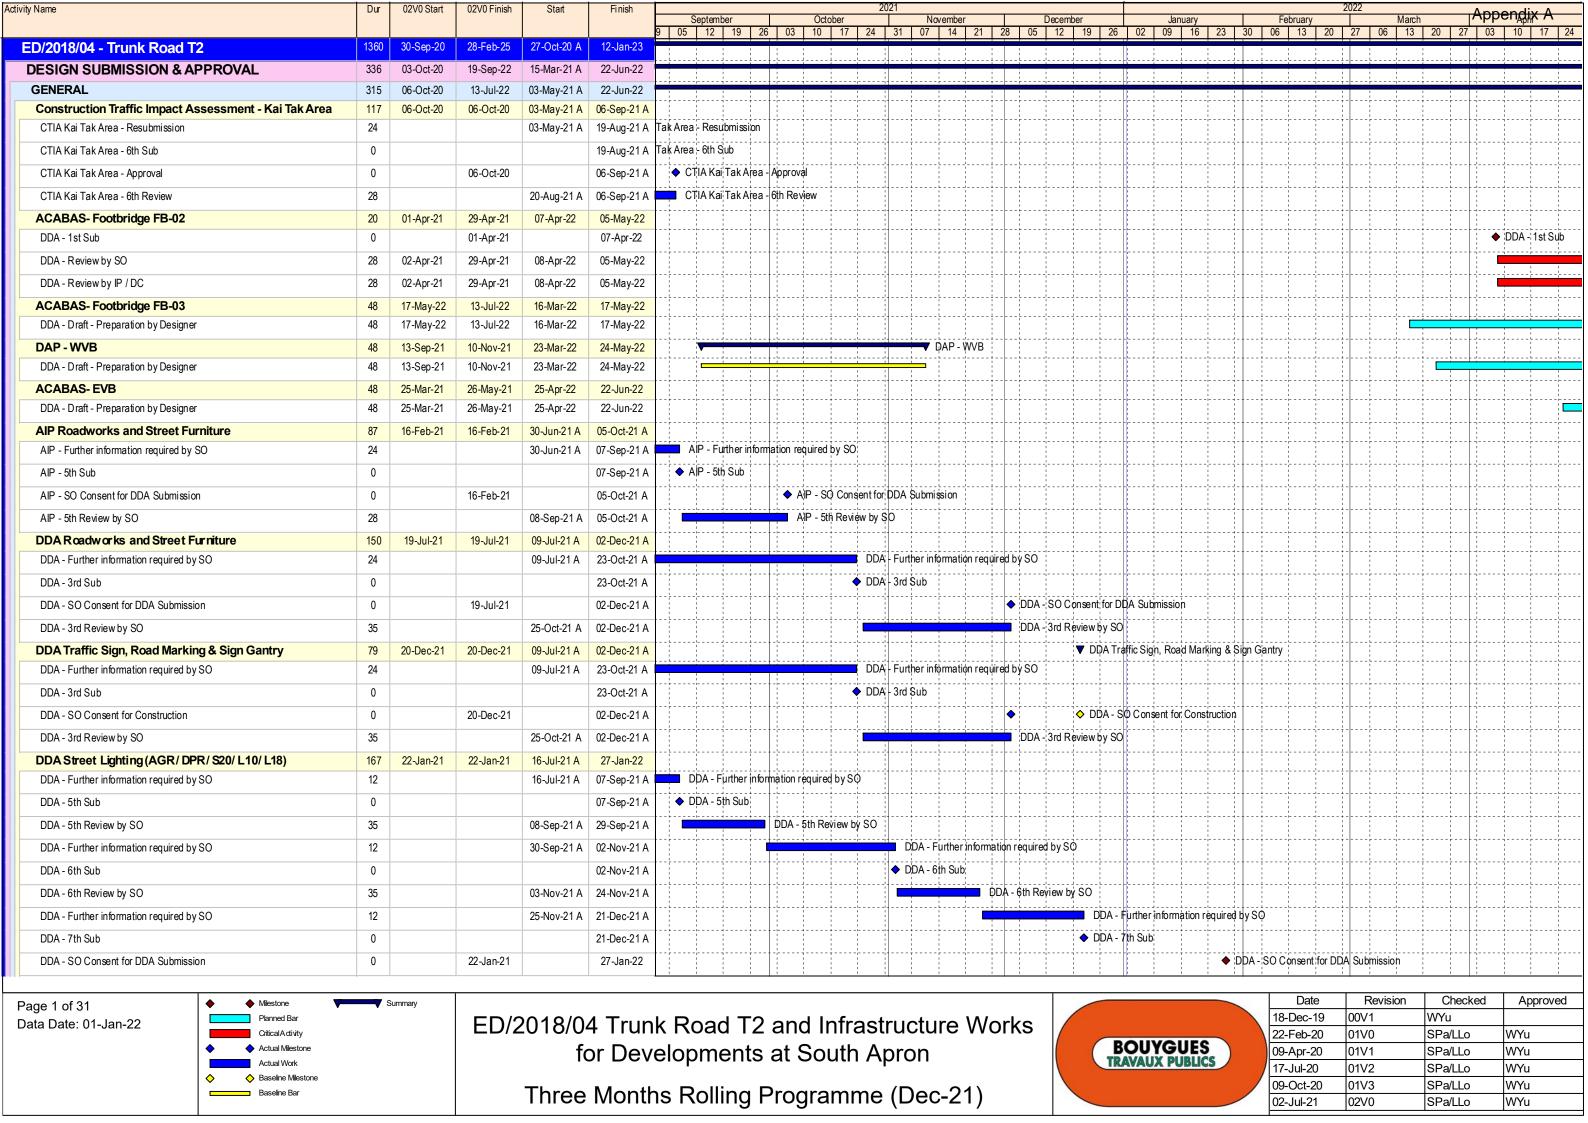


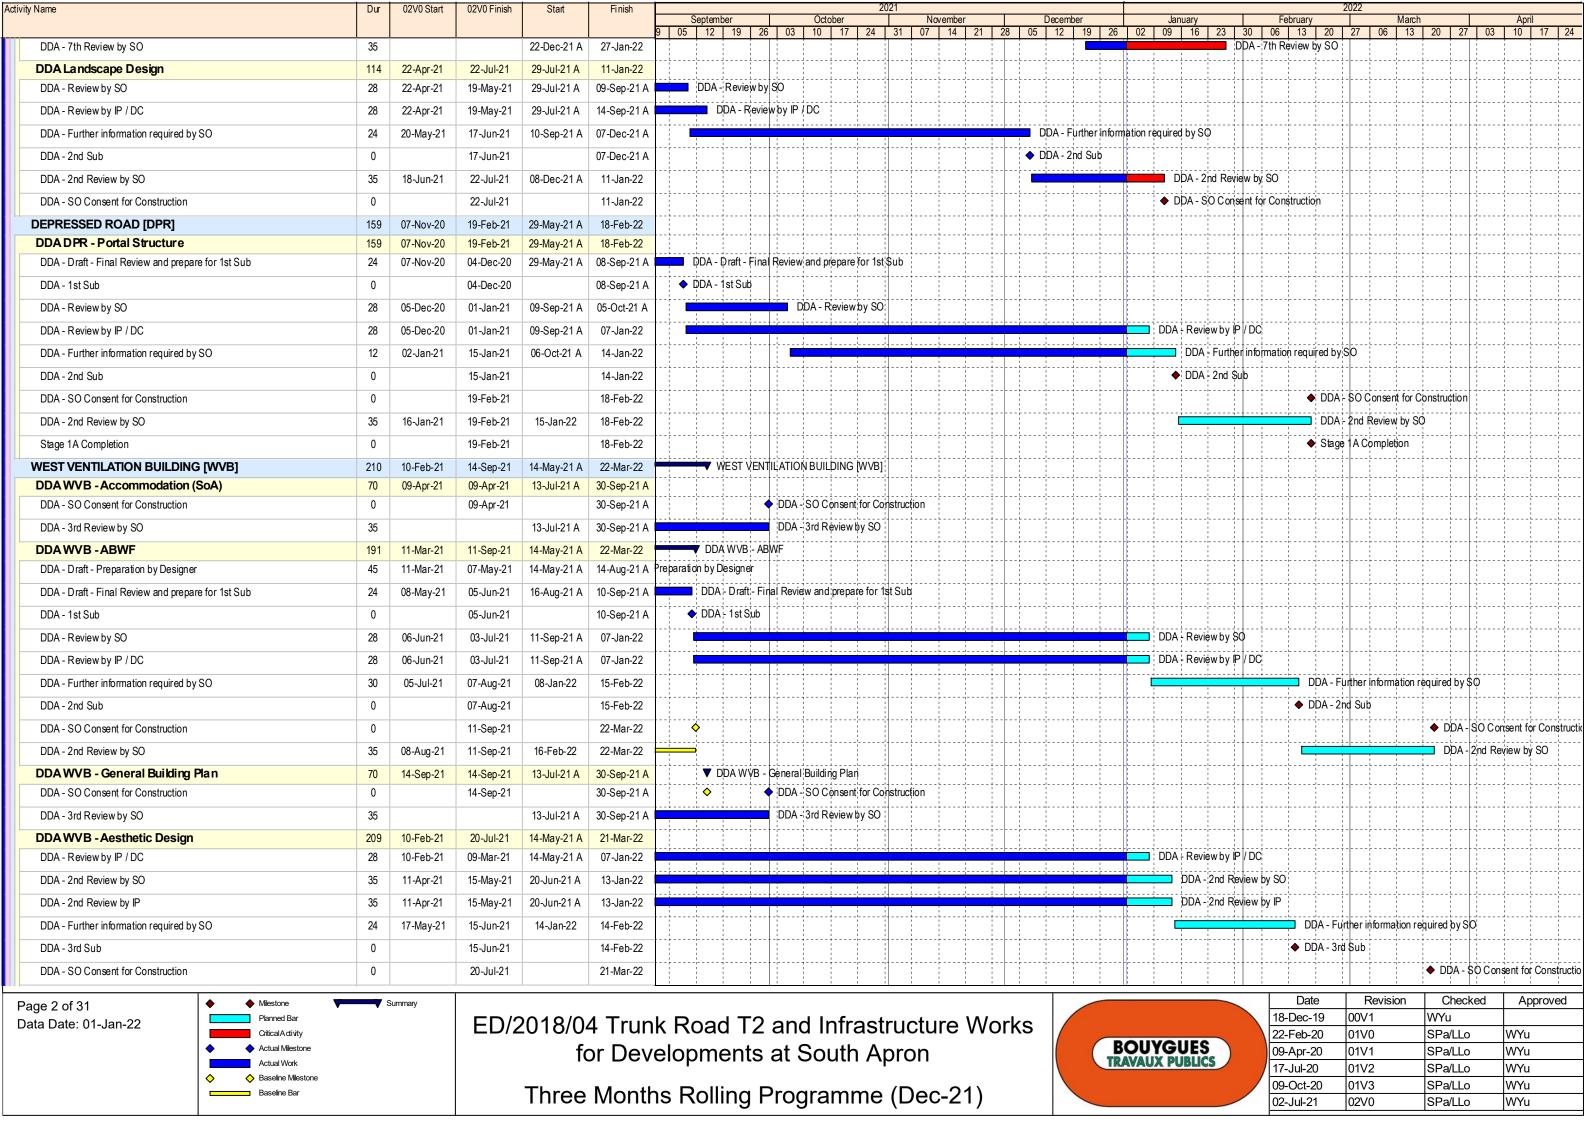


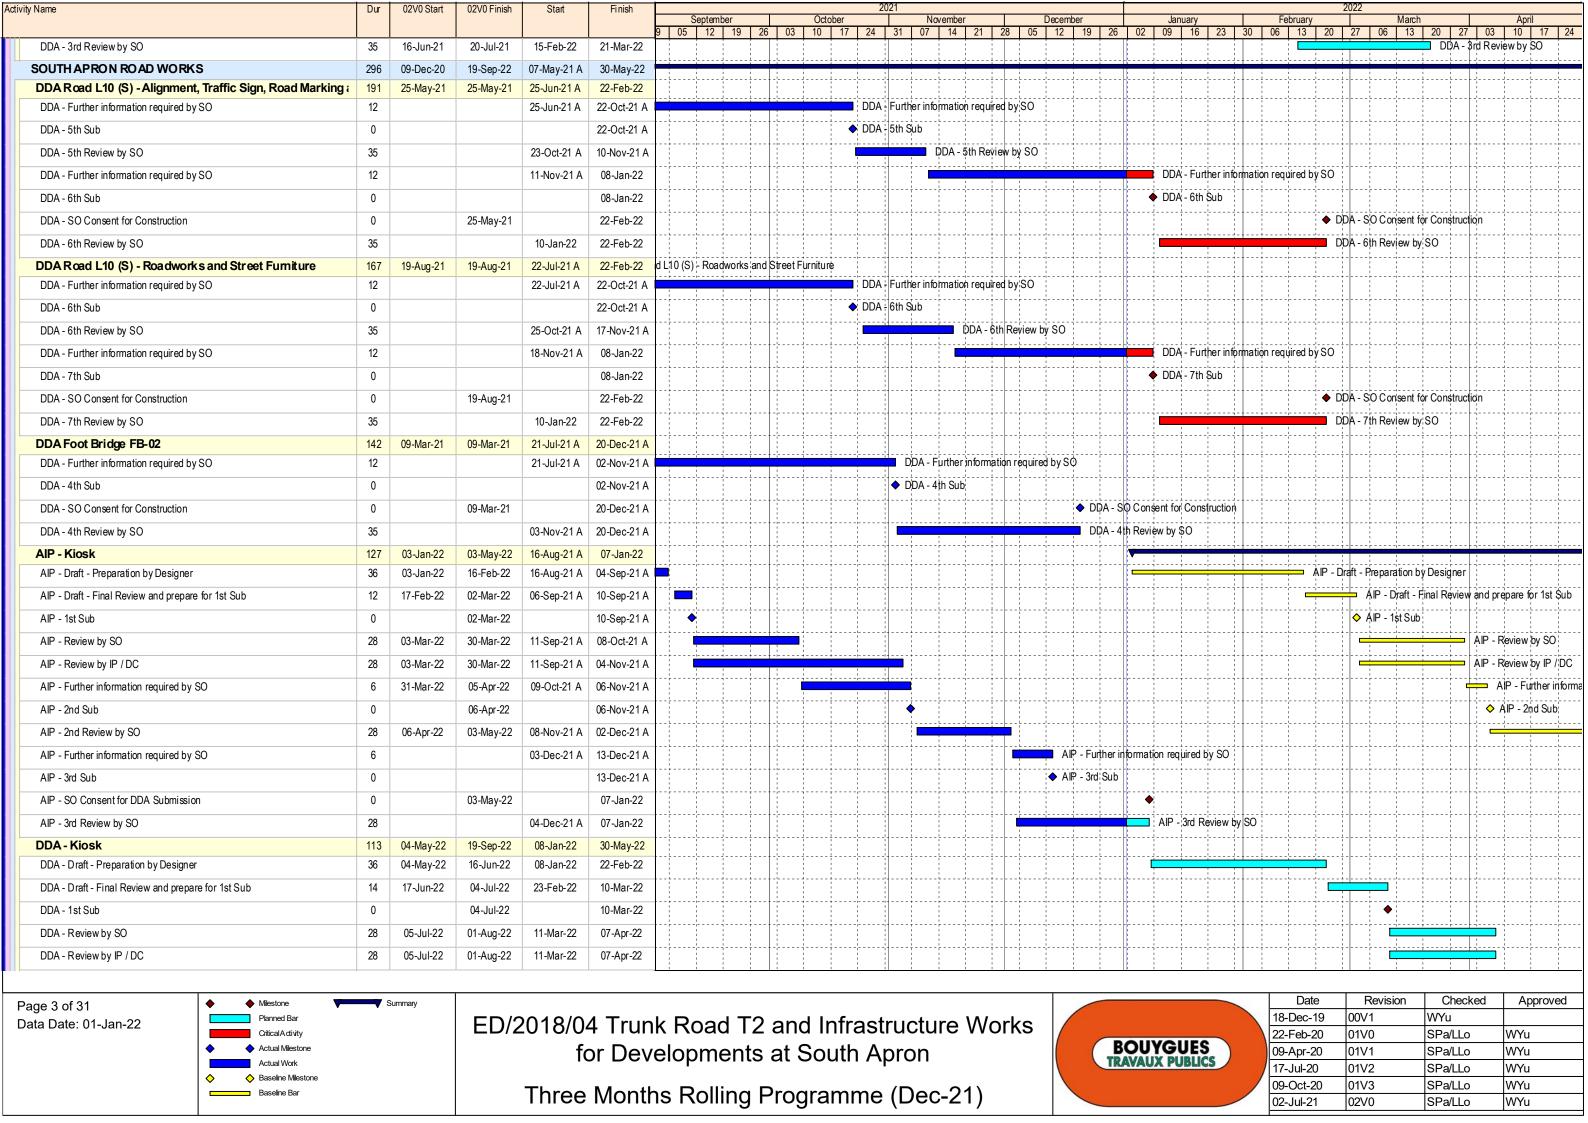


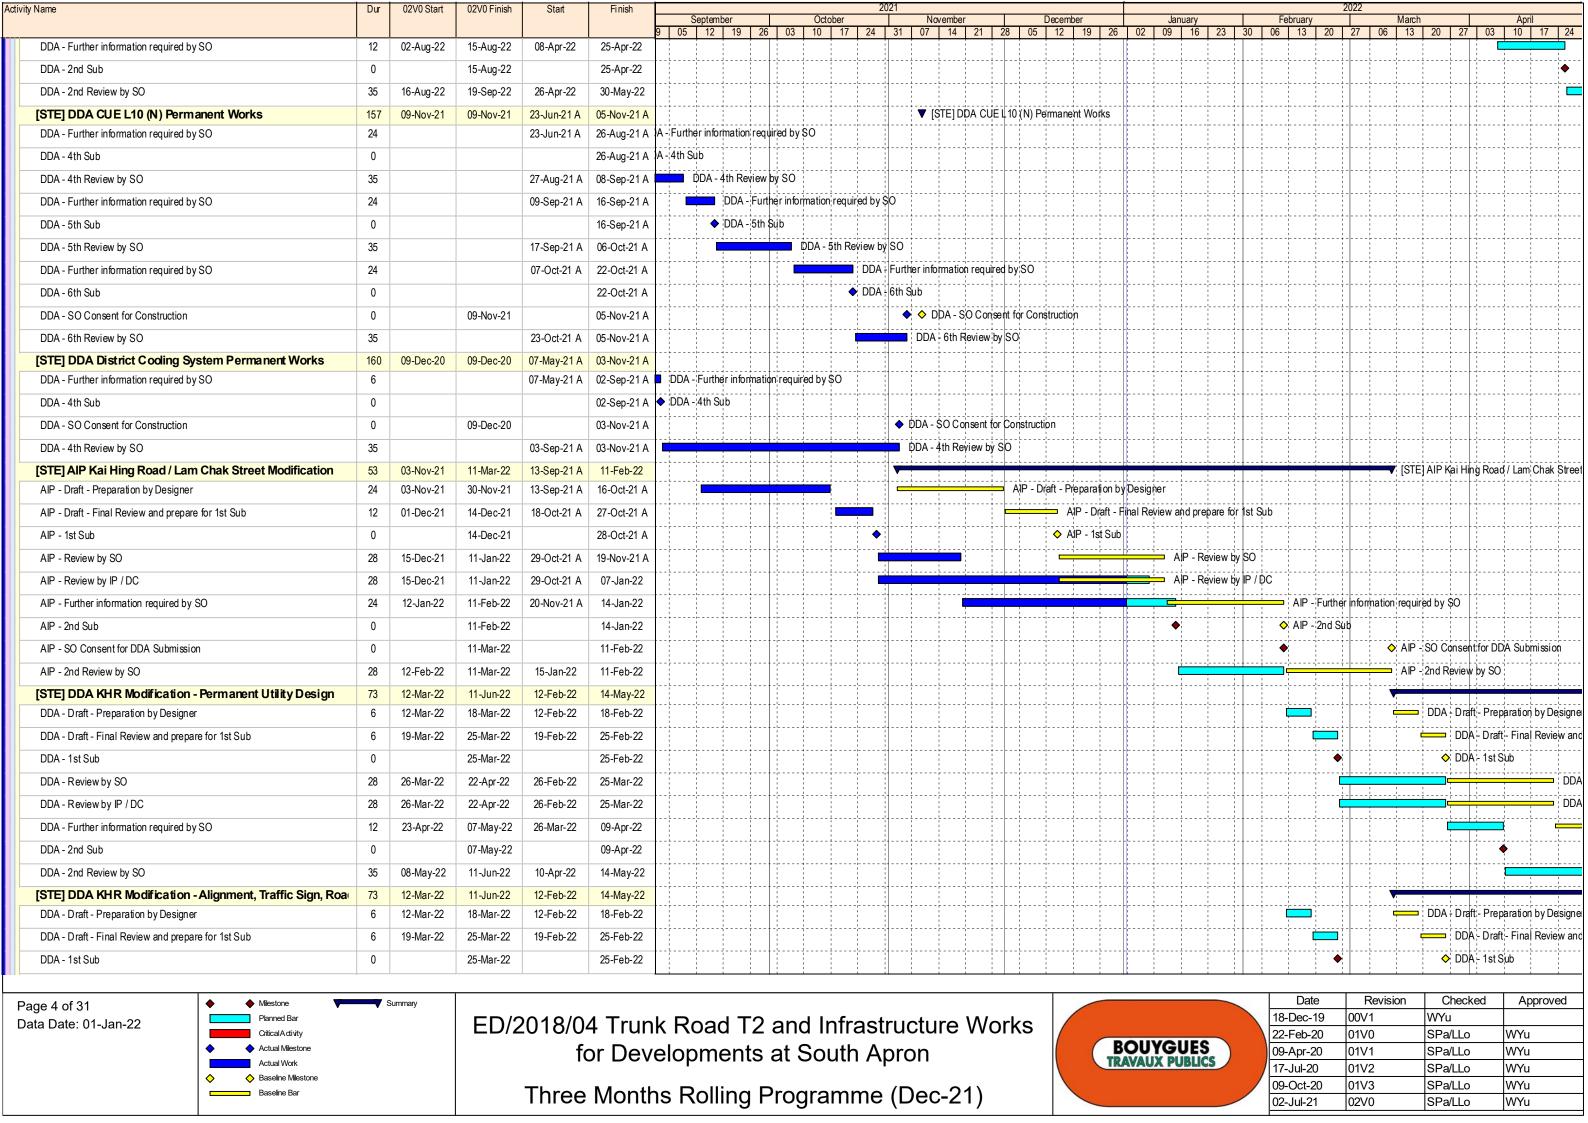


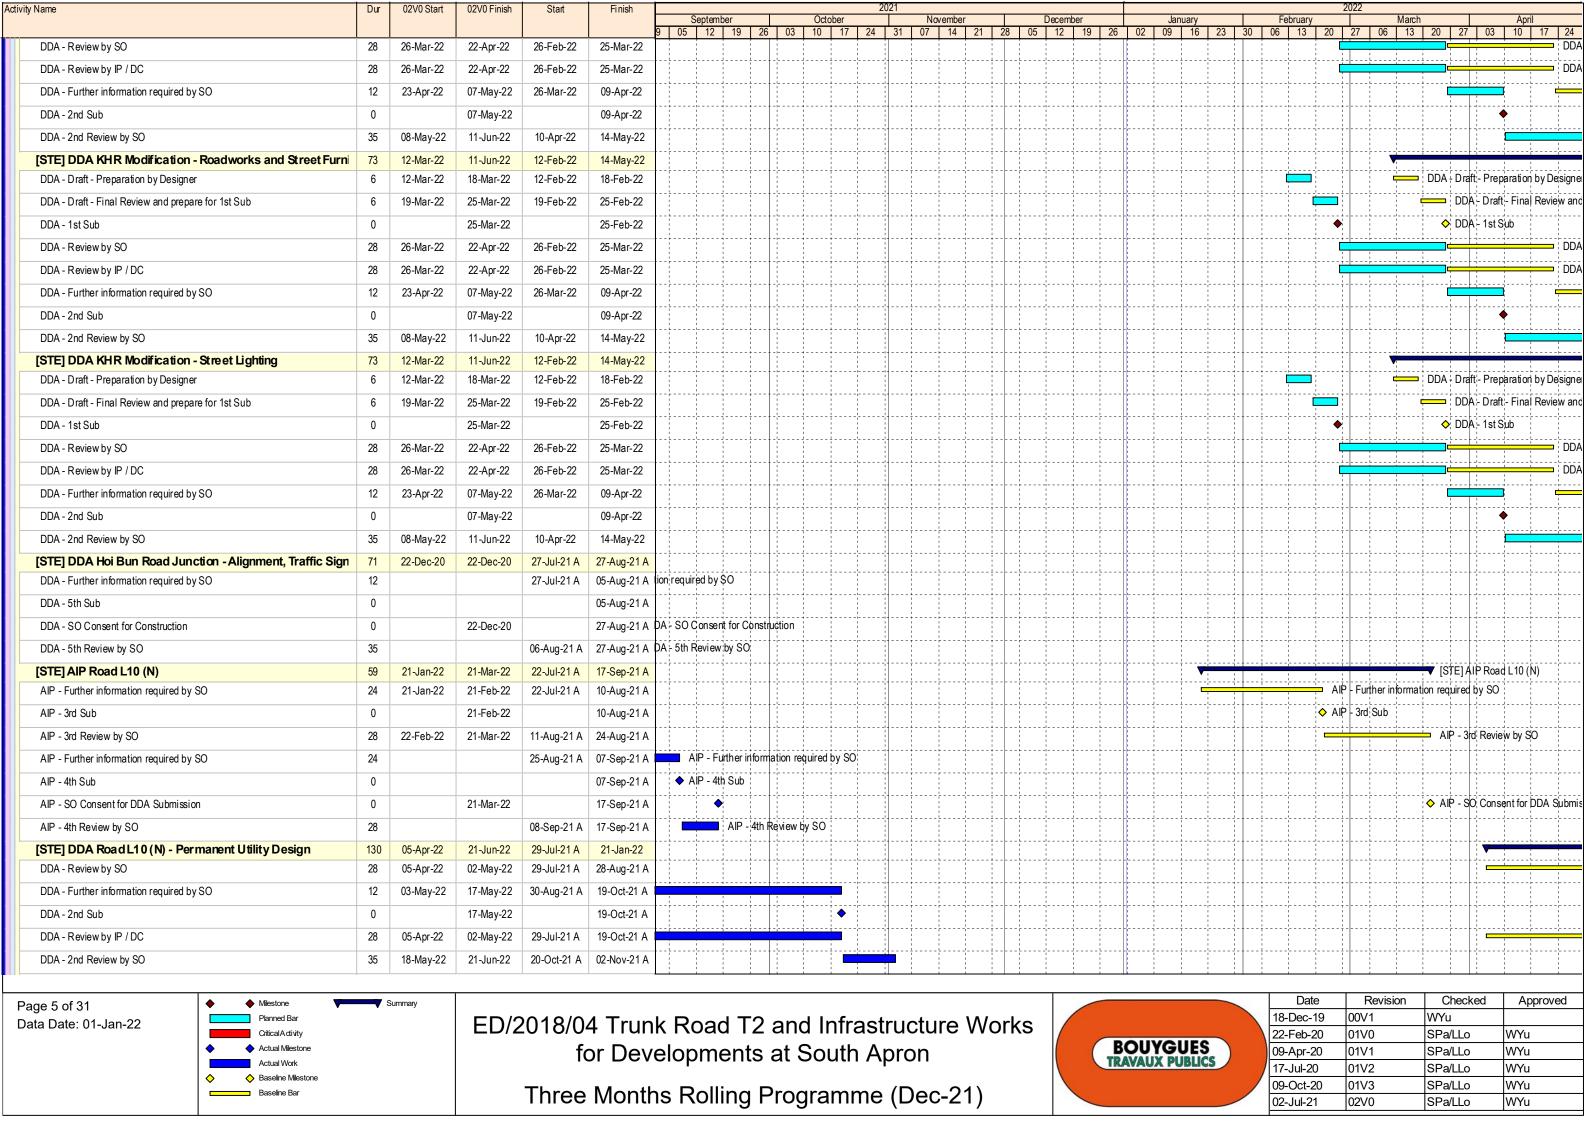


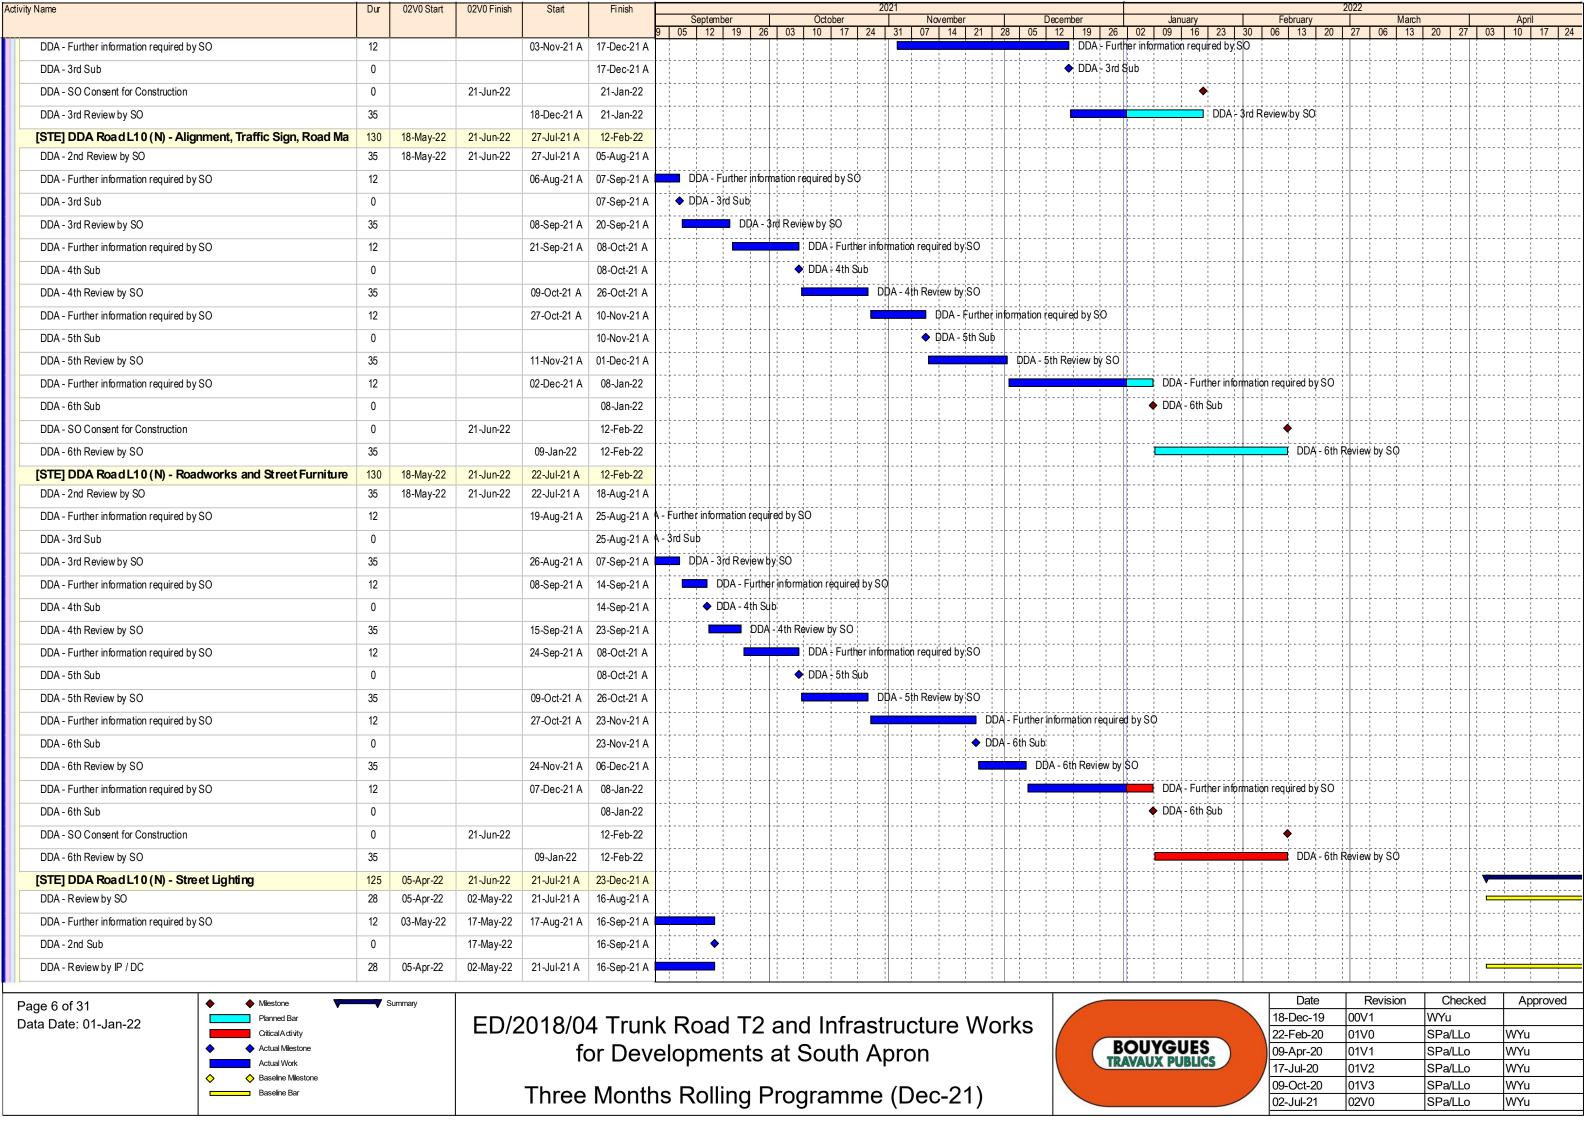


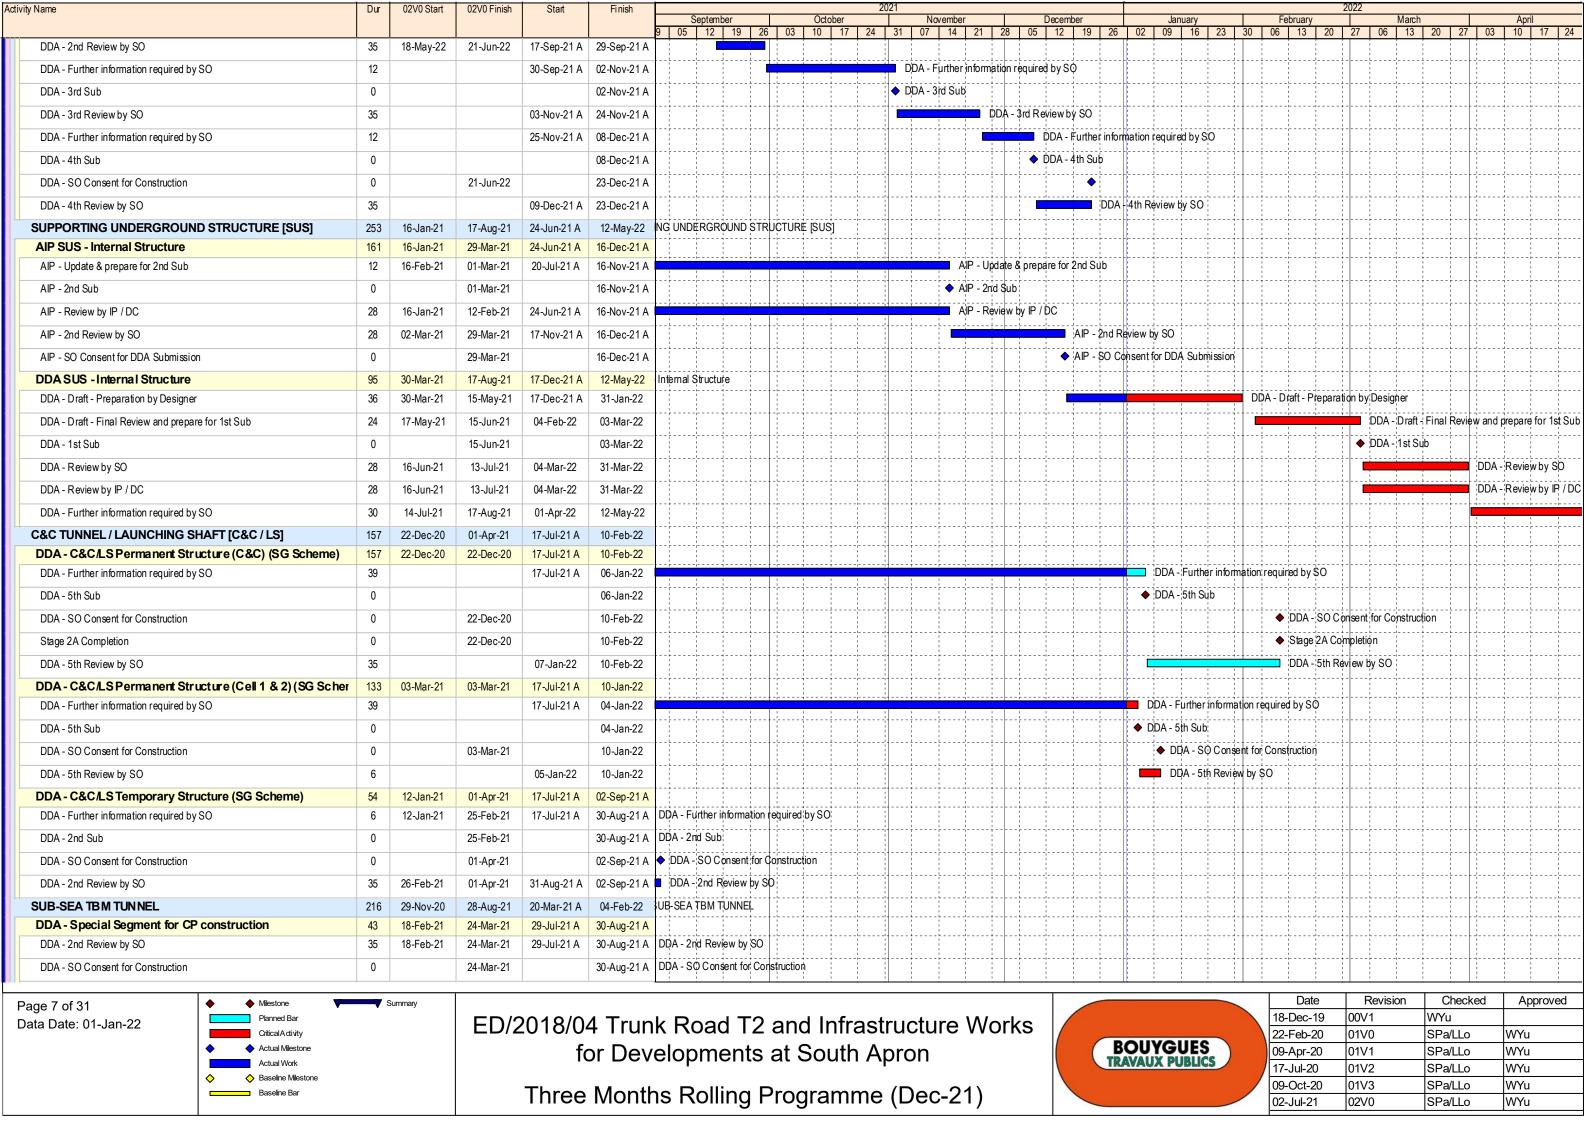


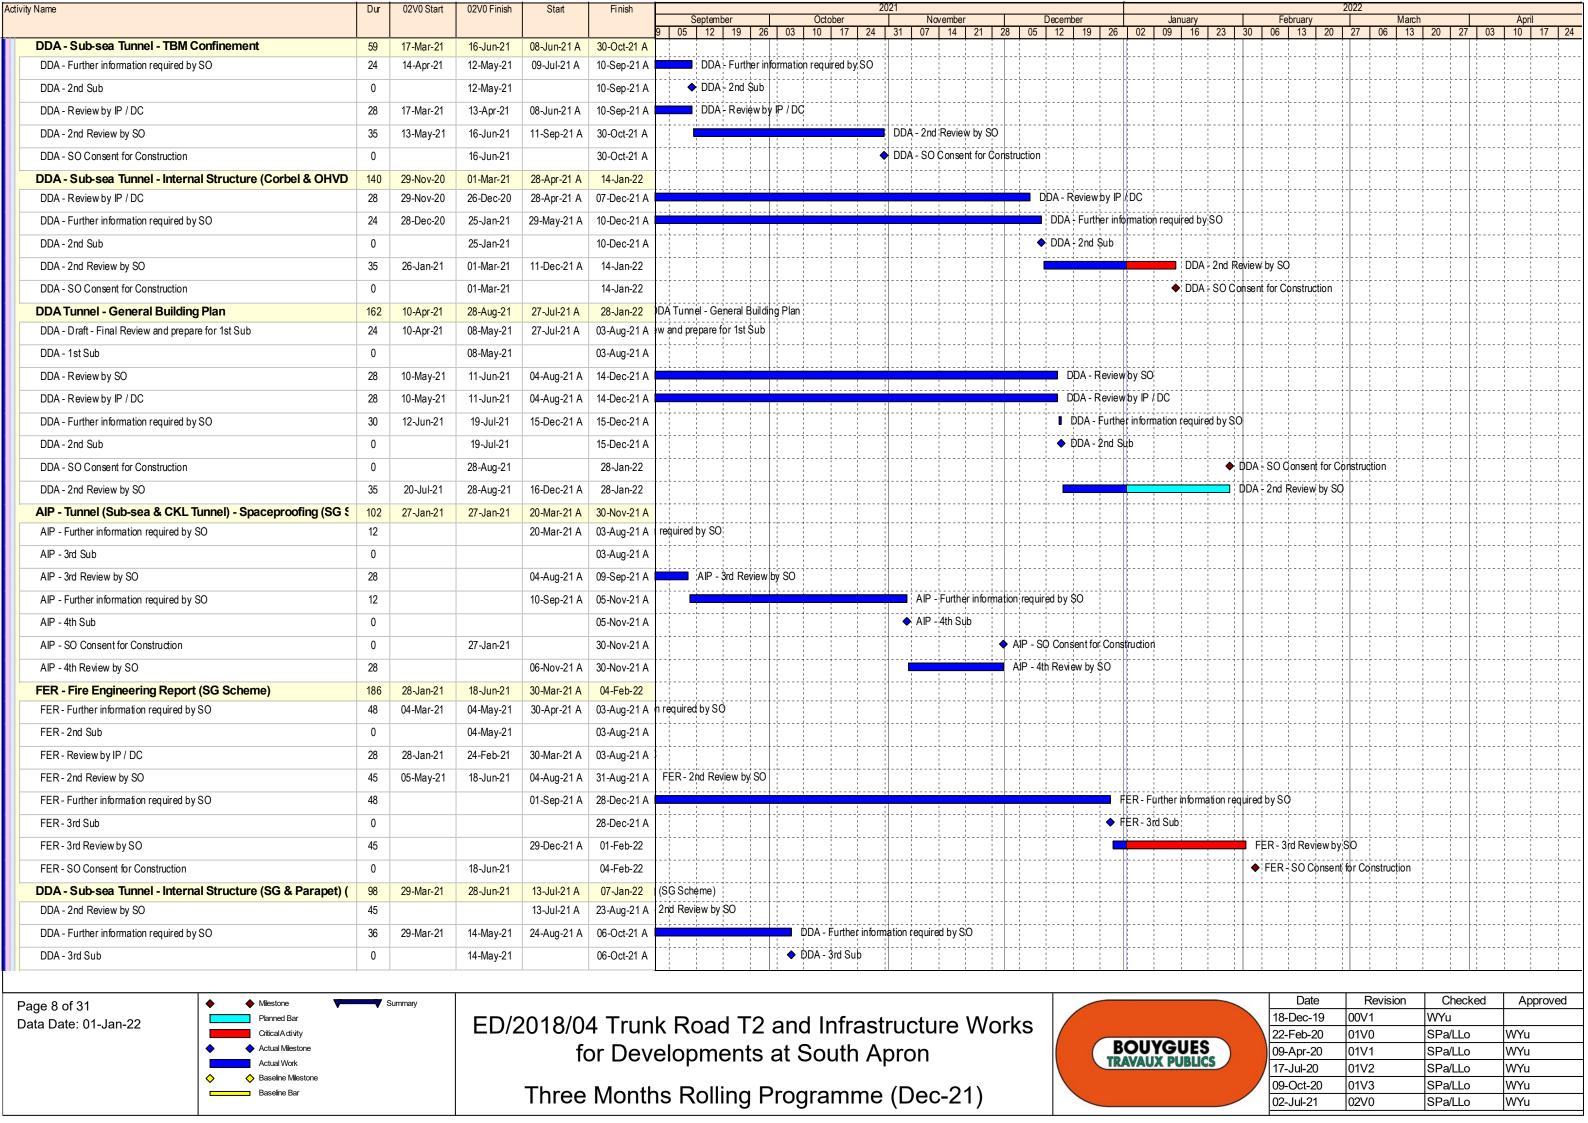


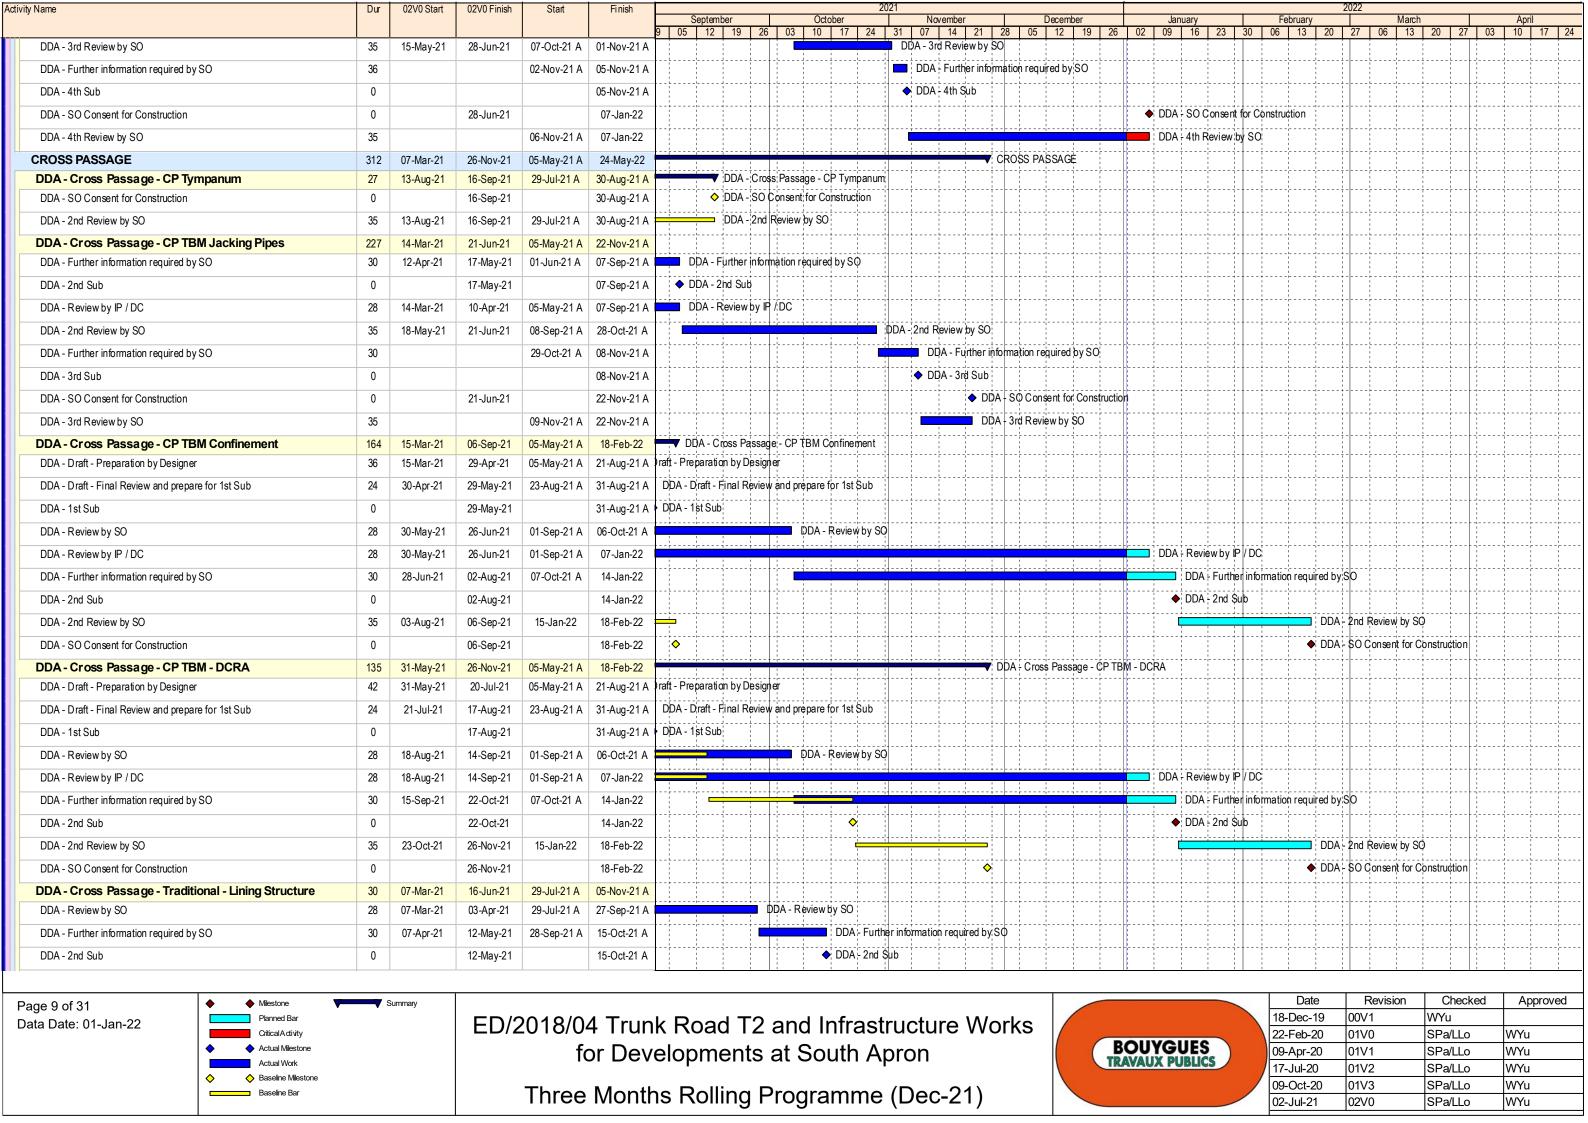

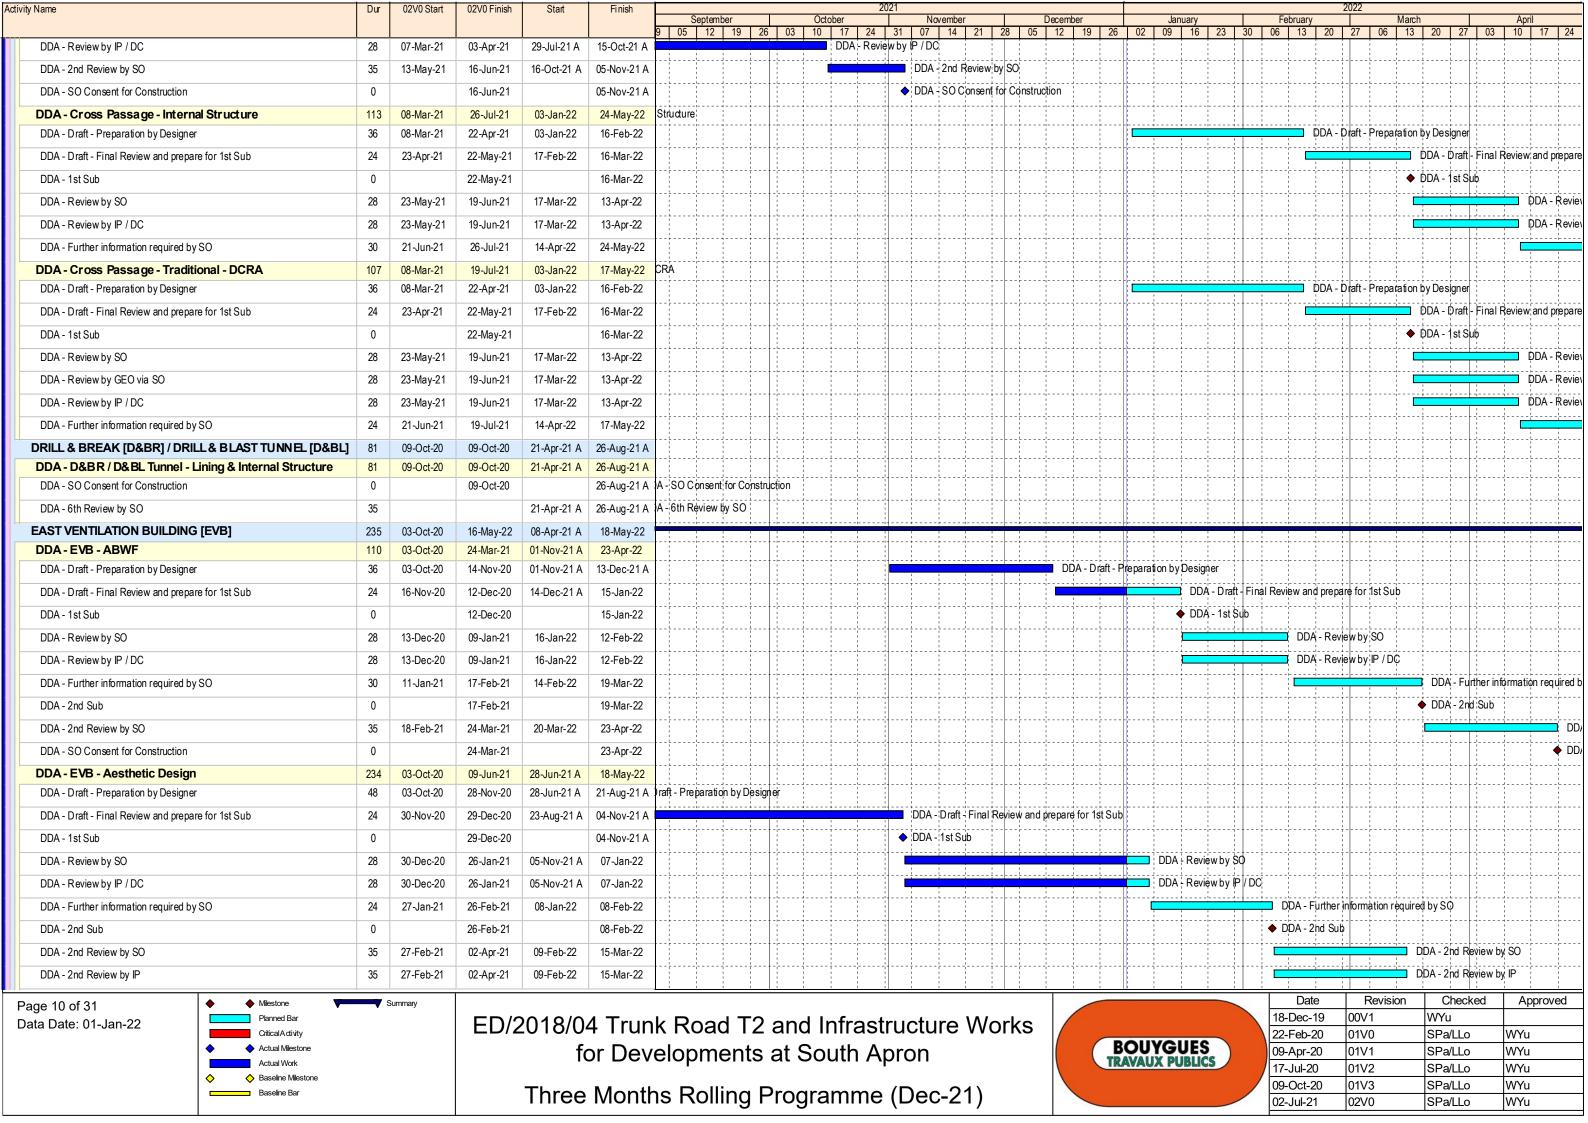

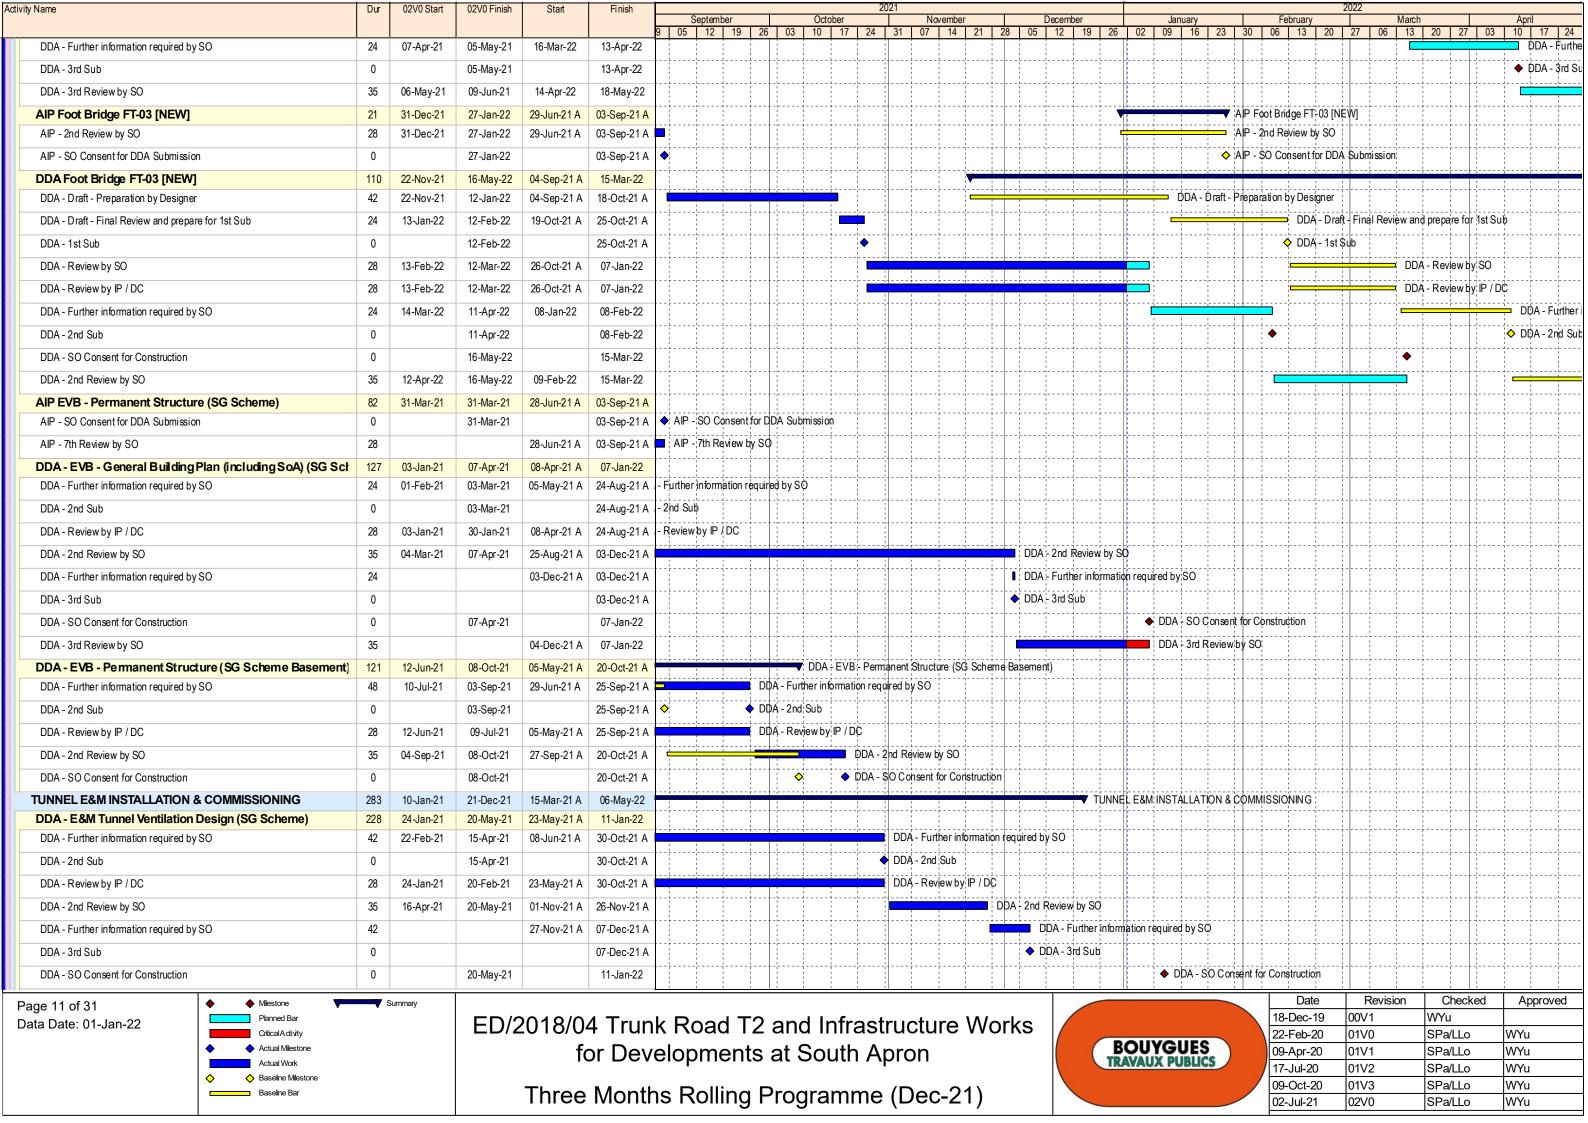

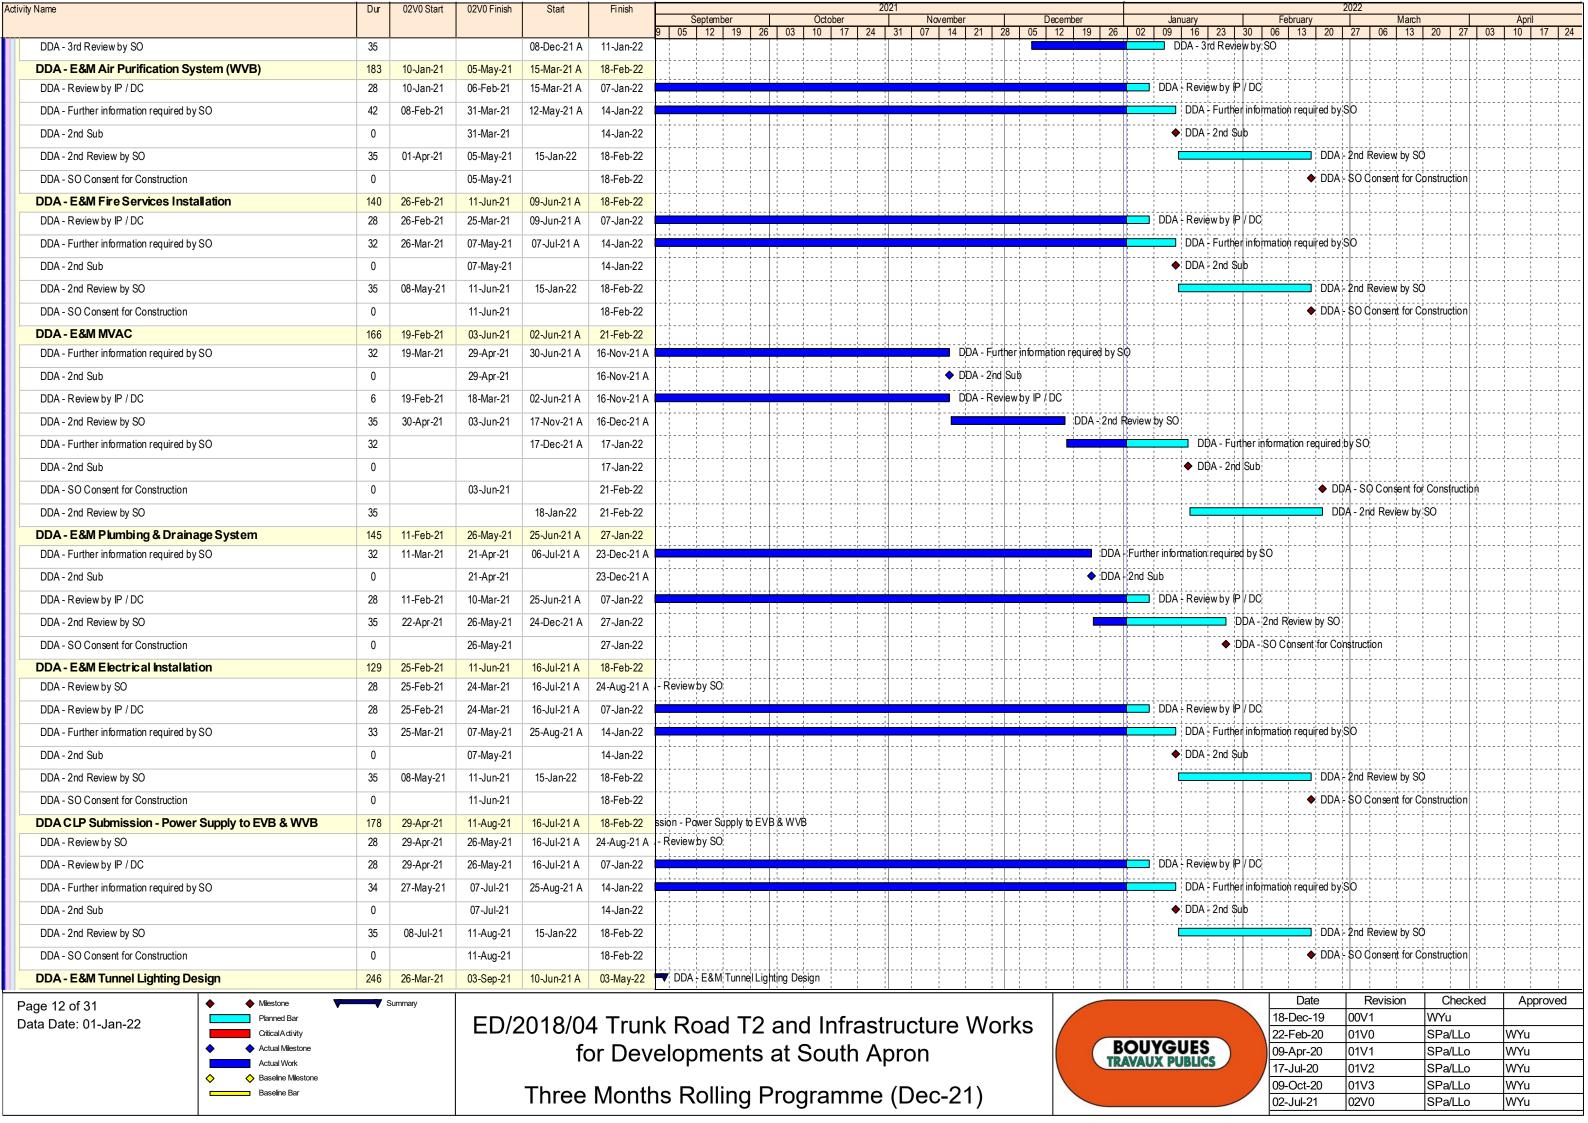

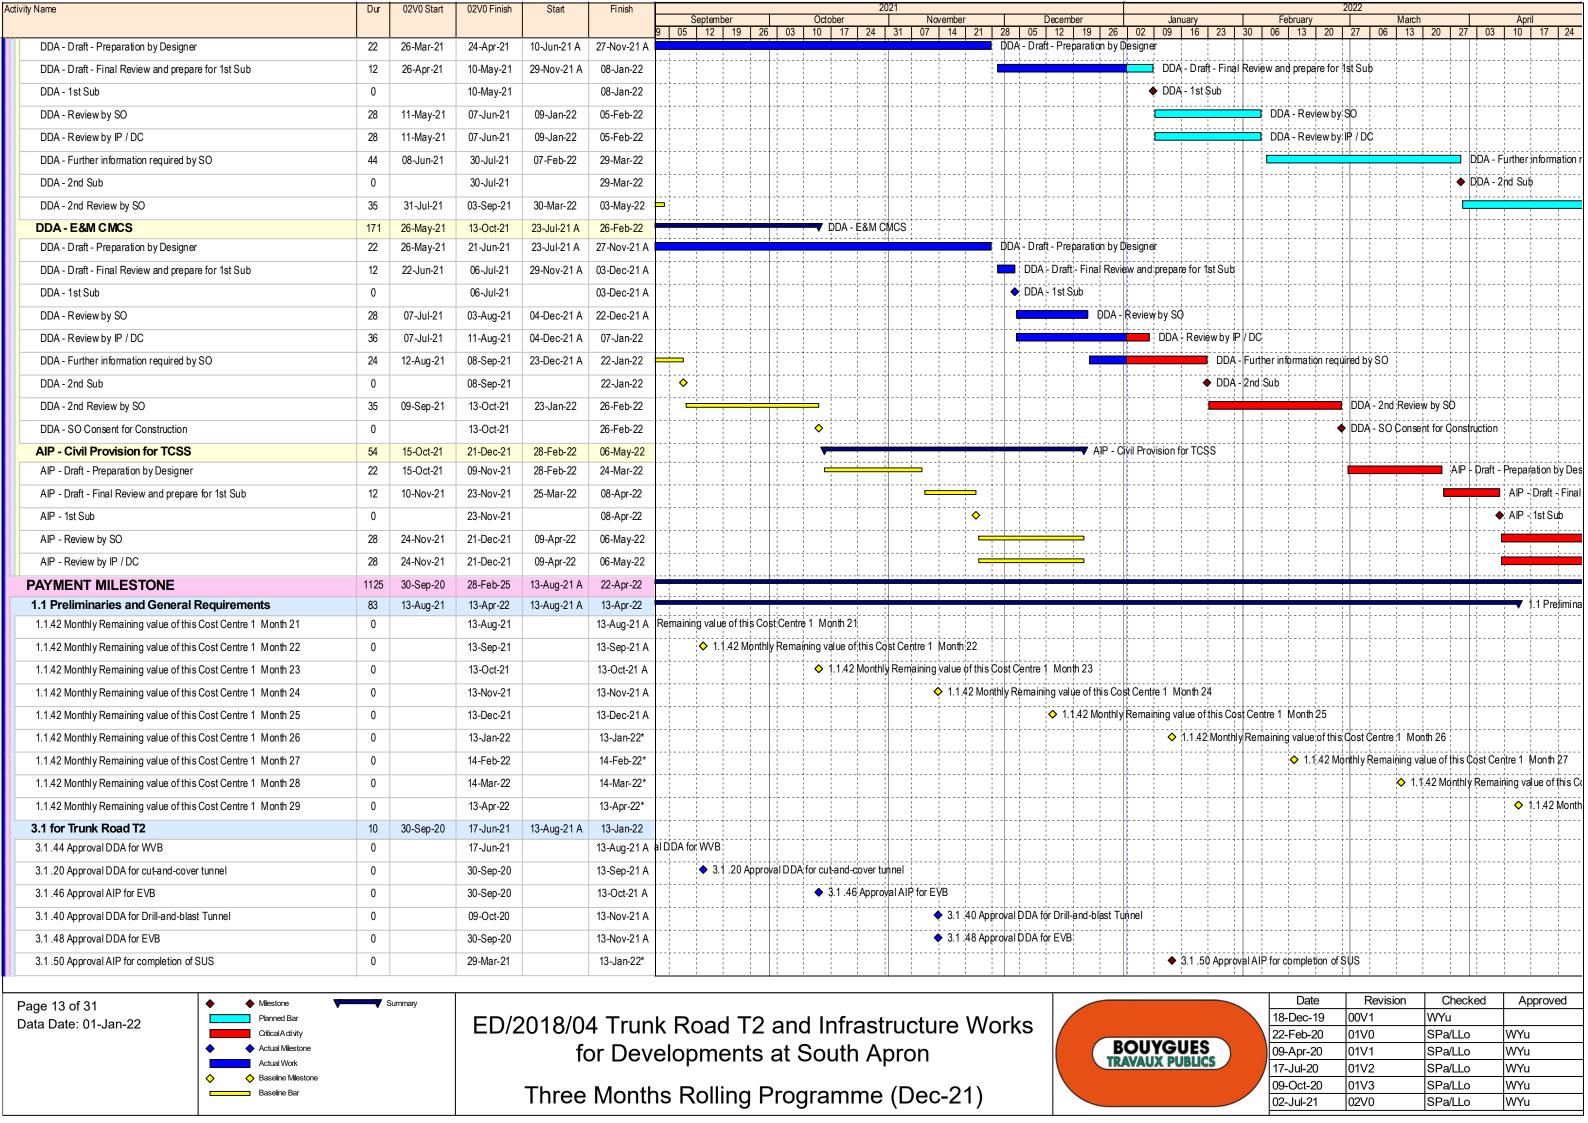



Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021 2022	
						September October November December January February March 9 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06 13 20 27 06	April 10 17 24
3.2 for Road S20 and Associated Infrastructure Works for C	0	30-Sep-20	30-Sep-20	13-Sep-21 A		─ ─	
3.2 .24 Approval DDA for landscape works	0		30-Sep-20		13-Sep-21 A		
3.2 .27 Complete whole activities of this cost centre	0		30-Sep-20		13-Dec-21 A		
3.3 for the Remaining Stage 5 Infrastructure Works - Road I	10	26-Feb-21	03-Jun-21	13-Dec-21 A	13-Jan-22	and Road L18	
3.3 .23 Submit DDA for landscape works	0		03-Jun-21		13-Dec-21 A		
3.3 .16 Approval DDA for waterworks	0		26-Feb-21		13-Jan-22*	◆ 3.3 .16 Approval DDA for waterworks	
3.4 for the Remaining Stage 5 Infrastructure Works - FT02	10	30-Sep-20	09-Mar-21	13-Sep-21 A	13-Jan-22		
3.4 .9 Submit AIP for modification of existing footbridge	0		30-Sep-20		13-Sep-21 A		
3.4 .8 Approval DDA for Landscaped elevated walkway	0		09-Mar-21		13-Oct-21 A		
3.4 .11 Submit Demolition plan for existing footbridge	0		22-Dec-20		13-Nov-21 A		
3.4 .10 Approval DDA for modification of existing footbridge	0		09-Mar-21		13-Jan-22*	◆ 3.4 .10 Approval DDA for modification of existing footbridge	
3.4 .12 Approval Demolition plan for existing footbridge	0		09-Mar-21		13-Jan-22*	◆ 3.4 .12 Approval Demolition plan for existing footbridge	
3.4 .13 Complete whole activities of this cost centre	0		09-Mar-21		13-Jan-22*	◆ 3.4 .13 Complete whole activities of this cost centre	
3.5 for Lam Chak Street and Kai Hing Road	0	14-Dec-21	14-Dec-21	13-Dec-21 A	13-Dec-21 A		
3.5 .5 Submit AIP for roadworks	0		14-Dec-21		13-Dec-21 A		
3.5 .9 Submit AIP for stormwater drainage works	0		14-Dec-21		13-Dec-21 A	♦ 3,5.9 Sµbmit AIP for stormwater drainage works	
3.5 .13 Submit AIP for waterworks	0		14-Dec-21		13-Dec-21 A	♦ 3.5 .13 Şubmit AIP for waterworks	
3.5 .17 Submit AIP for sewage works	0		14-Dec-21		13-Dec-21 A	♦ 3:5 .17 Submit AIP for sewage works	
3.5 .21 Submit AIP for landscape works	0		14-Dec-21		13-Dec-21 A		
3.6 for Road L10 (Northern Section)	33	21-Mar-22	21-Jun-22	13-Oct-21 A	14-Feb-22	<u> </u>	
3.6 .6 Approval AIP for Road L10 (northern section)	0		21-Mar-22		13-Oct-21 A	♦ 3.6 .6 Approv	al AIP for Road L10 (
3.6 .8 Approval DDA for Road L10 (northern section)	0		21-Jun-22		14-Feb-22*		
3.6 .9 Complete whole activities of this cost centre	0		21-Jun-22		14-Feb-22*		
3.8 for Improvement Works at the Junction of Hoi Bun Road	0	03-Dec-20	03-Dec-20	13-Nov-21 A	13-Nov-21 A		
3.8.9 Complete whole activities of this cost centre	0		03-Dec-20		13-Nov-21 A	◆ 3.8.9 Complete whole activities of this cost centre	
3.9 for the Pipelines for District Cooling System for Commis	0	30-Sep-20	30-Sep-20	13-Nov-21 A	03-Jan-22		
3.9.5 Submit GI report for pipelines of DCS for AMAWBC	0		30-Sep-20		13-Nov-21 A	♦ 3.9.5 Submit GI report for pipelines of DCS for AMAWBC	
3.9.6 Approval GI report for pipelines of DCS for AMAWBC	0		30-Sep-20		13-Nov-21 A	♦ 3.9.6 Approval G{ report for pipelines; of DCS for AMAWBC	
3.9.10 Approval DDA for pipelines of DCS	0		30-Sep-20		13-Nov-21 A	♦ 3.9.10 Approval DDA for pipellines of DCS	
3.9.11 Submit O&M manual for DCS pipelines	0		30-Sep-20		03-Jan-22	◆ 3.9.11 Submit O&M manual for DC\$ pipelines	
3.10 for the Remaining Pipelines for District Cooling Systen	0	30-Sep-20	09-Dec-20	13-Nov-21 A	13-Nov-21 A		
3.10.5 Submit GI report for remaining pipelines of DCS for AMAWBC	0		30-Sep-20		13-Nov-21 A	◆ 3.10.5 Submit GI report for remaining pipe lines of DCS for AMAWBC	
3.10.6 Approval GI report for remaining pipelines of DCS for AMAWBC	0		30-Sep-20		13-Nov-21 A	◆ 3.10.6 Approval GI report for remaining pipelines of DCS for AMAWBC	
3.10.10 Approval DDA for remaining pipelines of DCS	0		09-Dec-20		13-Nov-21 A	♦ 3.10.10 Approval DDA for remaining pipelines of DCS	·
3.12 for Improvement Works at Junctions of Cha Kwo Ling	0	30-Sep-20	30-Sep-20	13-Oct-21 A	13-Oct-21 A		
3.12.9 Complete whole activities of this cost centre	0		30-Sep-20		13-Oct-21 A	◆ 3.12.9 Complete whole activities of this cost centre	
4.2 Depressed Road and Remaining Ventilation Adits at the	10	20-Apr-21	14-Sep-21	13-Aug-21 A	13-Jan-22	▼ 4:2 Depressed Road and Remaining Ventilation Adits at the South Apron	
4.2 .12 Complete excavation of South Apron Adist 1	0		16-Jun-21			te excavation of South Apron Adist 1	
4.2 .13 Complete South Apron Adist permanent structure 0.2	0		28-May-21		13-Aug-21 A	te South Apron Adist permanent structure 0.2	
4.2 .14 Complete South Apron Adist permanent structure 0.4	0		22-Jun-21		13-Sep-21 A	A	
4.2 .15 Complete South Apron Adist permanent structure 0.6	0		16-Jul-21		13-Oct-21 A	◆ 4.2 .15 Complete South Apron Adist permanent structure 0.6	
4.2 .24 Complete foundation of Depressed Road by length 0.9	0		20-Apr-21		13-Nov-21 A	◆ 4.2.24 Complete foundation of Depressed Road by length 0.9	
4.2 .25 Complete permanent structure of Depressed Road by length 0.4	0		15-Jun-21		13-Nov-21 A	♦ 4.2 .25 Complete permanent structure of Depressed Road by length 0.4	
		J			<u> </u>		
Page 14 of 31	9	Summary				Date Revision Checked	Approved
Data Date: 01-Jan-22			ED/2	2018/04	4 Trun	nk Road T2 and Infrastructure Works	WYu
◆ Actual Milestone				fc	or Dev	Alenments at South Anron BOUYGUES 09-Apr-20 01V1 SPa/LLo	WYu
Actual Work Baseline Miestone				10		TRAVAUX PUBLICS 17-Jul-20 01V2 SPa/LLo	WYu
Baseline Bar				hs Rolling Programme (Dec-21) 09-Oct-20 01V3 SPa/LLo 02-Jul-21 02V0 SPa/LLo	WYu		
						TIS ROTTING Programme (Dec-21)	WYu


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021
						September October November December January February March April 9 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 03 10 17 24
4.2 .26 Complete permanent structure of Depressed Road by length 0.5	0		29-Jun-21		13-Nov-21 A	
4.2 .27 Complete permanent structure of Depressed Road by length 0.6	0		29-Jun-21		13-Nov-21 A	A 4.2 .27 Complete permanent structure of Depressed Road by length 0.6
4.2 .28 Complete permanent structure of Depressed Road by length 0.7	0		19-Jul-21		13-Nov-21 A	4.2.28 Complete permanent structure of Depressed Road by length 0.7
4.2 .29 Complete permanent structure of Depressed Road by length 0.8	0		16-Aug-21		13-Nov-21 A	4.2 .29 Complete permanent structure of Depressed Road by length 0.8
4.2 .30 Complete permanent structure of Depressed Road by length 0.9	0		14-Sep-21		13-Nov-21 A	A ♦ 4.2 .30 Complete: permanent structure of Depressed Road by length 0.9
4.2 .16 Complete South Apron Adist permanent structure 0.8	0		09-Aug-21		13-Dec-21 A	A
4.2 .17 Complete South Apron Adist permanent structure 1	0		31-Aug-21		13-Jan-22*	◆ 4.2 .17 Complete South Apron Adist permanent structure 1
4.2 .23 Complete foundation of Depressed Road by length 1	0		20-Apr-21		13-Jan-22*	◆ 4.2 .23 Complete foundation of Depressed Road by length 1
4.2 .31 Complete permanent structure of Depressed Road by length 1	0		14-Sep-21		13-Jan-22*	♦ 4.2 .31 Complete permanent structure of Depressed Road by length 1
5.1 Cut-and-Cover Tunnel at South Apron	96	07-Sep-21	07-Sep-21	13-Oct-21 A	13-Oct-21 A	A ▼ 5.1 Cut-and-Cover Tunnel at South Apron
5.1.18 Complete base slab of Cut-and-cover Tunnel by length 0.1	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1.18 Complete base slab of Cut-and-cover Tunnel by length 0.1
5.1 .19 Complete base slab of Cut-and-cover Tunnel by length 0.2	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1.19 Complete base slab of Cut-and-cover Tunnel by length 0.2
5.1 .20 Complete base slab of Cut-and-cover Tunnel by length 0.3	0		07-Sep-21		13-Oct-21 A	A ♦ \$.1.20 Complete base slab of Cut-and-cover Tunnel by length 0.3
5.1 .21 Complete base slab of Cut-and-cover Tunnel by length 0.4	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1.21 Complete base slab of Cut-and-cover Tunnel by length 0.4
5.1 .22 Complete base slab of Cut-and-cover Tunnel by length 0.5	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1.22 Complete base slab of Cut-and-cover Tunnel by length 0.5
5.1 .23 Complete base slab of Cut-and-cover Tunnel by length 0.6	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1 .23 Complete base slab of Cut-and-cover Tunnel by length 0.6
5.1 .24 Complete base slab of Cut-and-cover Tunnel by length 0.7	0		07-Sep-21		13-Oct-21 A	A ♦ 5.1 .24 Complete base slab of Cut-and-cover Tunnel by length 0.7
5.1 .25 Complete base slab of Cut-and-cover Tunnel by length 0.8	0		07-Sep-21		13-Oct-21 A	A ♦ \$1.25 Complete base slab of Cut-and-cover Tunnel by length 0.8
5.1 .26 Complete base slab of Cut-and-cover Tunnel by length 0.9	0		07-Sep-21		13-Oct-21 A	A ♦ \$.1.26 Complete base slab of Cut-and-cover Tunnel by length 0.9
6.1 Tunnel Boring Machine and Back-up Equipment	0	29-Mar-21	26-May-21	13-Aug-21 A	13-Dec-21 A	
6.1 .14 Complete establishment on site of Slurry Treatment Plant	0		26-May-21		13-Aug-21 A	4 te establishment on site of Slurry Treatment Plant
6.1 .6 Approval design of hyperbaric intervention facilities	0		26-May-21		13-Sep-21 A	A ♦ 6.1.6 Approval design of hyperbaric intervention facilities
6.1 .11 Complete establishment on site of TBMs 0.5	0		29-Mar-21		13-Sep-21 A	A ♦ 6.1.11 Complete establishment on site of TBMs; 0.5
6.1.15 Complete establishment on Site of hyperbaric intervention facilities 0	0		29-Mar-21		13-Sep-21 A	A ♦ 6.1 .15 Complete establishment on Site of hyperbaric intervention facilities 0.5
6.1 .12 Complete establishment on site of TBMs 1	0		26-May-21		13-Dec-21 A	A ♦ 6.1 .12 Complete establishment on site of TBMs 1
6.1 .16 Complete establishment on Site of hyperbaric intervention facilities 1	0		26-May-21		13-Dec-21 A	A ♦ 6.1.16 Complete establishment on Site of hyperbaric intervention facilities 1
6.1 .17 Complete whole activities of this cost centre	0		26-May-21		13-Dec-21 A	A ♦ 6.1 .17 Complete whole activities of this cost centre
7.1 Western Ventilation Building	0	21-Jul-21	09-Sep-21	13-Aug-21 A	13-Dec-21 A	
7.1 .1 Complete mobilization of excavation equipment 0.5	0		21-Jul-21		13-Aug-21 A	A e mobilization of excavation equipment 0.5
7.1 .3 Complete excavation for WVB 0.5	0		09-Sep-21		13-Dec-21 A	A ◆ 7.1.3 Complete excavation for WVB 0.5
9.1 Launching Shaft	65	14-Jul-21	13-Aug-21	13-Sep-21 A	13-Oct-21 A	A Shaft
9.1 .13 Complete bottomslab for Launching Shaft by area 0.2	0		14-Jul-21		13-Sep-21 A	A ♦ 9.1.13 Complete bottomslab for Launching Shafft by area 0.2
9.1 .14 Complete bottomslab for Launching Shaft by area 0.4	0		14-Jul-21		13-Oct-21 A	A
9.1 .15 Complete bottomslab for Launching Shaft by area 0.6	0		26-Jul-21		13-Oct-21 A	A
9.1 .16 Complete bottomslab for Launching Shaft by area 0.8	0		04-Aug-21		13-Oct-21 A	A
9.1 .17 Complete bottomslab for Launching Shaft by area 1	0		13-Aug-21		13-Oct-21 A	A
11.1 Drill and Break Tunnel	33	13-Jul-21	21-Dec-21	13-Dec-21 A	14-Feb-22	
11.1.2 Complete tunnel excavation 0.2 by length	0		13-Jul-21		13-Dec-21 A	
11.1.2 Complete tunnel excavation 0.5 by length	0		19-Oct-21		13-Jan-22*	◆ 11.1.2 Complete tunnel excavation 0.5 by length
11.1.2 Complete tunnel excavation 0.3 by length	0		13-Aug-21		13-Jan-22*	
11.1.2 Complete tunnel excavation 0.4 by length	0		14-Sep-21		13-Jan-22*	♦ 11.1.2 Complete tunnel excavation 0.4 by length
11.1.3 Complete tunnel excavation 0.6 by length	0		19-Nov-21		14-Feb-22*	◆ 11,1.3 Complete tunnel excavation 0.6 by length
Page 15 of 31 ♦ Milestone	Su Su	ummary		0.40.15	. —	Date Revision Checked Approved 18-Dec-19 00V1 WYu
Data Date: 01-Jan-22			ED/2	:018/04	4 Trun	nk Road 12 and initastructure vvorks
♦ Actual Milestone				fo	or Dev	velopments at South Apron BOUYGUES 09-Apr-20 01V1 SPa/LLo WYu
Actual Work						17-Jul-20 01V2 SPa/LLo WYu
Baseline Bar				Three	Month	ths Rolling Programme (Dec-21)
						, <u> </u>

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	
						September October November December January February March April 9 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 06 13 20 27 03 10 17
11.1.5 Complete tunnel excavation 0.7 by length	0		21-Dec-21		14-Feb-22*	
12.1 Drill and Blast Tunnel	93	16-Sep-21	14-Feb-22	13-Oct-21 A	13-Jan-22	
12.1.7 Complete tunnel excavation 0.6 by length	0		16-Sep-21		13-Oct-21 A	
12.1.8 Complete tunnel excavation 0.7 by length	0		05-Nov-21		13-Oct-21 A	
12.1.9 Complete tunnel excavation 0.8 by length	0		22-Dec-21		13-Dec-21 A	
12.1.10 Complete tunnel excavation 0.9 by length	0		14-Feb-22		13-Jan-22*	◆ 12.1.10 Complete tunnel excavation 0.9 by length
15.0 E&M Design Works	148	02-Jan-21	06-Jul-21	13-Aug-21 A	14-Feb-22	
15.0 .9 Submit DDA for electrical system (power supply)	0		28-Apr-21			1.A DDA for electrical system (power supply)
15.0 .12 Approval AIP for Tunnel extra low voltage system	0		02-Jan-21			1 A val AIP for Tunnel extra low voltage system
15.0 .21 Submit DDA for Tunnel plumbing & drainage	0		10-Feb-21			1 A It DDA for Tunnel plumbing & draina'ge
15.0 .29 Submit DDA for remaining tunnel and at-grade E&M systems	0		06-Jul-21		13-Aug-21 A	1 A It DDA for remaining tunnel and at-grade E&M systems
15.0 .33 Submit DDA for E&M in WVB	0		24-Feb-21		13-Aug-21 A	1 A It DDA for E&Min WVB
15.0 .37 Submit DDA for E&M in EVB	0		11-Jun-21		13-Aug-21 A	1 A t DDA for E&M in EVB
15.0 .25 Submit DDA for Tunnel lighting system	0		10-May-21		14-Feb-22*	22*
17.1 Works under Sections 6A, 6C and 12 and Associated L	33	23-Dec-20	04-Oct-21	13-Aug-21 A	14-Feb-22	22 17 1 Works under Sections 6A, 6C and 12 and Associated Landscape Works
17.1 .42 Complete watermain installation 0.25	0		23-Dec-20		13-Aug-21 A	1 A lete watermain installation 0.25
17.1 .46 Complete anchor blocks, thrust block etc for waterworks 0.25	0		23-Dec-20		13-Aug-21 A	1 A lete anchor blocks, thrust block etc for waterworks 0.25
17.1 .3 Complete excavation and disposal of material works 0.8	0		23-Jun-21		13-Oct-21 A	1 A
17.1 .13 Complete footpath 0.25	0		21-Sep-21		14-Feb-22*	22*
17.1 .17 Complete street furnitures of at-grade roads 0.25	0		04-Oct-21		14-Feb-22*	22* ♦ 17.1.17 Complete street furnitures of at-grade roads 0.25
17.4 Remaining Stage 5 Infrastructure Works - Road L10 (S	13	02-Aug-22	04-Mar-23	26-Jan-22	14-Feb-22	22
17.4 .1 Complete excavation and disposal of material works 0.25	0		17-Feb-23		26-Jan-22	22
17.4 .2 Complete excavation and disposal of material works 0.5	0		04-Mar-23		14-Feb-22*	22*
17.4 .21 Complete drainage installation 0.2	0		18-Oct-22		14-Feb-22*	22*
17.4 .25 Complete manhole for drainage 0.25	0		18-Oct-22		14-Feb-22*	22*
17.4 .31 Complete sewerage installation 0.25	0		02-Aug-22		14-Feb-22*	22*
17.4 .35 Complete manhole for sewerage 0.25	0		02-Aug-22		14-Feb-22*	22*
17.5 Remaining Stage 5 Infrastructure Works - Landscaped	88	05-Jun-21	28-Mar-22	13-Sep-21 A	22-Apr-22	22 ▼ 17.5 Remaining Stage
17.5 .5 Complete piled foundations of FB02 0.25	0		05-Jun-21		13-Sep-21 A	1 A 17.5 .5 Complete piled foundations of FB02 0.25
17.5 .6 Complete piled foundations of FB02 0.5	0		15-Jul-21		13-Oct-21 A	1 A
17.5 .11 Complete concrete works of pile caps 0.5	0		23-Dec-21		17-Jan-22	22 ♦ 17,5.11 Complete concrete works of pile caps 0.5
17.5 .12 Complete concrete works of pile caps 0.8	0		08-Jan-22		29-Jan-22	22 ♦ 17.5, 12 Complete concrete works of pile caps 0.8
17.5.16 Complete concrete works of piers 0.25	0		07-Mar-22		14-Feb-22*	22* ♦ 17.5 .16 Complete concrete works of piers
17.5.13 Complete concrete works of pile caps 1	0		20-Jan-22		14-Feb-22	22 ♦ 17:5.13 Complète concrete works of pile caps 1
17.5.18 Complete concrete works of piers 0.8	0		07-Mar-22		28-Mar-22	22 ♦ 17.5 .18 Complete cor
17.5.19 Complete concrete works of piers 1	0		28-Mar-22		22-Apr-22	22
21.1 Improvement Works at the Junction of Hoi Bun Road/C	0	08-Jun-21	15-Sep-21	13-Aug-21 A	13-Dec-21 A	
21.1 .4 Complete sub-base and roadbase works 0.25	0		23-Jun-21	Ŭ.		1 A te şub-başe and roadbase works 0.25
21.1 .2 Complete drainage installation 0.5	0		14-Aug-21		13-Nov-21 A	1 A ♦ 21.1, 2 Complete drainage installation 0.5
21.1 .3 Complete drainage installation 1	0		08-Sep-21		13-Nov-21 A	1 A ♦ 21.1.3 Complete drainage installation 1
21.1.5 Complete sub-base and roadbase works 0.5	0		22-Jul-21		13-Nov-21 A	1 A \$\leftrightarrow 21.1; .5 Complete sub-base and roadbase works 0.5
21.1.6 Complete sub-base and roadbase works 0.8	0		19-Aug-21		13-Nov-21 A	1 A
Page 16 of 21	.9	Summary				Date Revision Checked Approve
Page 16 of 31 Data Date: 01-Jan-22	•	,	ED/2	/በ1ደ/በ	1 Trun	unk Road T2 and Infrastructure Works
Ortical A divity						22-Feb-20 01V0 SPa/LLO WYU
Actual Work				10	or Dev	evelopments at South Apron BOUYGUES 09-Apr-20 01V1 SPa/LLo WYu 17-Jul-20 01V2 SPa/LLo WYu 17-Jul-20 01V2 SPa/LLo WYu 18-Apr-20 01V2 SPa/Llo WYu 18-Apr-20
♦ Baseline Milestone Baseline Bar				These	114	00 0+20 04/2 CDall a MAK
baseine Bar				rnree	iviontr	nths Rolling Programme (Dec-21)


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021
						September October November December January February March April 9 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 06 13 20 27 06 13 20 27 03 10 17 24
21.1.7 Complete sub-base and roadbase works 1	0		15-Sep-21		13-Nov-21 A	
21.1.8 Complete kerb line modification and pavement 0.25	0		08-Jun-21		13-Dec-21 A	◆ 21,1.8 Complete kerb line modification and pavement 0.25
	1049	31-Dec-24	28-Feb-25	13-Nov-21 A	13-Nov-21 A	
21.2 .1 Complete irrigation system 0.3	0		31-Dec-24		13-Nov-21 A	
21.2.2 Complete irrigation system 0.6	0		01-Feb-25		13-Nov-21 A	
21.2 .3 Complete irrigation system 1	0		28-Feb-25		13-Nov-21 A	
21.2 .4 Complete whole activities of this cost centre 1	0		28-Feb-25		13-Nov-21 A	
21.4 Improvement Works at the Junctions of Cha Kwo Ling	12	12-Jan-21	31-May-21	13-Aug-21 A	13-Nov-21 A	
21.4 .11 Complete kerb line modification and pavement 1	0		22-Apr-21		13-Aug-21 A	ete kerb line modification and pavement 1
21.4 .14 Complete light posts, lamps, lanterns, ducting and cabling	0		23-Apr-21		13-Sep-21 A	◆ 21.4 .14 Complète light posts, lamps, lanterns, ducting and cabling
21.4.1 Complete temporary traffic diversion 1	0		12-Jan-21		13-Nov-21 A	◆ 21.4.1 Complete temporary traffic diversion 1
21.4.12 Complete road marking, traffic sign and traffic signal installation	0		23-Apr-21		13-Nov-21 A	♦ 21.4 .12 Complete road marking, traffic sign and traffic signal installation
21.4 .13 Complete roadside planter	0		23-Apr-21		13-Nov-21 A	◆ 21.4 .13 Complete roadside planter
21.4 .15 Complete T&C of drainage and waterworks system	0		31-May-21		13-Nov-21 A	♦ 21.4 .15 Complete T&C of drainage and waterworks system
21.4 .16 Complete whole activities of this cost centre	0		31-May-21		13-Nov-21 A	◆ 21.4 .16 Complete whole activities of this cost centre
21.5 Establishment Works for Improvement Works at the Ju	0	31-May-21	31-May-21	13-Nov-21 A	13-Nov-21 A	Road
21.5.1 Complete establishment works for 3 mths completion of softworks	0		31-May-21		13-Nov-21 A	◆ 21.5.1 Complete establishment works for 3 mths completion of softworks
22.1 Pipelines for District Cooling System for Commissionii	56	17-Apr-21	16-Nov-21	13-Aug-21 A	06-Apr-22	▼ 22.1 Pipelines for District Cooling System for Commissioning of AMAWBC
22.1 .1 Complete DCS installation length 0.2	0		17-Apr-21		13-Aug-21 A	te DCS installation length 0.2
22.1 .3 Complete DCS installation length 0.8	0		17-Jul-21		14-Feb-22*	◆ 22:1.3 Complete DCS installation length 0.8
22.1.5 Complete T&C of DCS system 1	0		16-Nov-21		06-Apr-22	◆ 22.1 .5 Complete T
22.1.6 Complete whole activities of this cost centre 1	0		16-Nov-21		06-Apr-22	◆ 22.1 .6 Complete w
34.2 Common Utilities Enclosure (CUE) under Section 13 of	0	23-Nov-21	23-Nov-21	13-Oct-21 A	13-Oct-21 A	▼ 34.2 Common Utilities Enclosure (CUE) under Section 13 of the Works
34.2 .1 Complete excavation of CUE 0.5	0		23-Nov-21		13-Oct-21 A	♦ 34.2 1 Complète excavation of CUE 0.5
35 Services Gallery	122	31-Mar-21	04-Feb-22	13-Sep-21 A	14-Feb-22	▼ 35 Services Gallery
35.7 Approval of AIP for Services Gallery E&M design by the SO	0		31-Mar-21		13-Sep-21 A	♦ 35.7 Approval of AIP for Services Gallery #&M design by the SO
35.8 Submit DDA submission for Services Gallery E&M design to the SO	0		11-Jun-21		13-Sep-21 A	
35.10 Mobilisation of 50% of excavation equipment to be deployed for Works	0		09-Sep-21		13-Sep-21 A	♦ 35; 10 Mobilisation of 50% of;excavation equipment to be deployed for Works under this Cost Centre
35.11 Complete 20% of total length (measured on plan) of SG excavation in	0		12-Aug-21		13-Sep-21 A	♦ 35.11 Complete 20% of total length (measured on plan) of SG excavation in Drill-and-Break and Drill-and-Blast Tunnel
35.12 Complete 40% of total length (measured on plan) of SG excavation in	0		15-Oct-21		13-Sep-21 A	♦ 35.12 Complete 40% of total length (measured on plan) of SG excavation in Drill-and-Break and Drill-and-Blast Tunnel
35.13 Complete 60% of total length (measured on plan) of SG excavation in	0		08-Dec-21		13-Sep-21 A	♦ 35.13 Complete 60% of total length (measured on plan) of SG excavation in Drill-and-Break and Drill-and-Blast Tunnel
35.4 Submit DDA submission for Services Gallery Structures to the SO	0		11-Jun-21		13-Nov-21 A	♦ 35.4 Submit DDA submission for Services Gallery Structures to the SO
35.5 Approval of DDA submission for Services Gallery Structures by the SO	0		08-Oct-21		13-Nov-21 A	♦ 35.5 Approval of DDA submission for Services Gallery Structures by the SO
35.31 Complete 25% of total volume (measured on plan) of excavation for Lo	0		19-Oct-21		13-Dec-21 A	♦ 35 31 Complete 25% of total volume (measured on plan) of excavation for Lower Basement of East Ventilation Building
35.9 Approval of DDA submission for Services Gallery E&M design by the SO	0		08-Oct-21		14-Feb-22*	♦ 35;9 Apptoval of DDA submission for Services Gallery E&M design
35.16 Complete 20% of total length (measured on plan) of SG structures in [0		04-Feb-22		14-Feb-22	♦ 35:16 Complete:20% of total length (measured on plan) of SG struc
35.17 Complete 40% of total length (measured on plan) of SG structures in [0		04-Feb-22		14-Feb-22*	♦ 35:17 Complete:40% of total length (measured on plan) of SQ struc
35.32 Complete 50% of total volume (measured on plan) of excavation for Lc	0		29-Nov-21		14-Feb-22*	♦ 35,32 Complete 50% of total volume (measured on plan) of excavat
SOUTH APRON EXTERNAL WORKS	449	29-Jan-21	17-Oct-22	22-Mar-21 A	12-Jan-23	
Road S20	250	22-Mar-21	17-Jan-22	24-Jun-21 A	10-Jun-22	▼ Road S20
CUE	250	21-Apr-21	17-Jan-22	24-Jun-21 A	10-Jun-22	VCÚE
CUE FSI Forms submission to FSD (if applicable)	0		21-Oct-21		10-Mar-22	◆ CUE FSI Forms submission to FSD (if applic
CUE FS Inspection & Commissioning (if applicable)	48	19-Nov-21	17-Jan-22	09-Apr-22	10-Jun-22	
Page 17 of 21		ummary				Date Revision Checked Approved
Page 17 of 31 Data Date: 01-Jan-22	→ 3		ED/2	019/0	1 Trun	ok Road T2 and Infrastructure Works
Critical Activity			$\square U/Z$			22-rep-20 0100 SPa/LLO WYU
◆ Actual Milestone Actual Work				to	or Dev	relopments at South Apron BOUYGUES 09-Apr-20 01V1 SPa/LLo WYu 17-Jul-20 01V2 SPa/LLo WYu SPa/LLo WYu 17-Jul-20 01V2 SPa/LLo WYu 18-Jul-20 01V2 SPa/Llo W
♦ Asseline Milestone				Tla	N / = 41	00 Oct 20 041/2 CDc/Llc 140/4
Baseline Bar				ınree	iviontr	hs Rolling Programme (Dec-21)

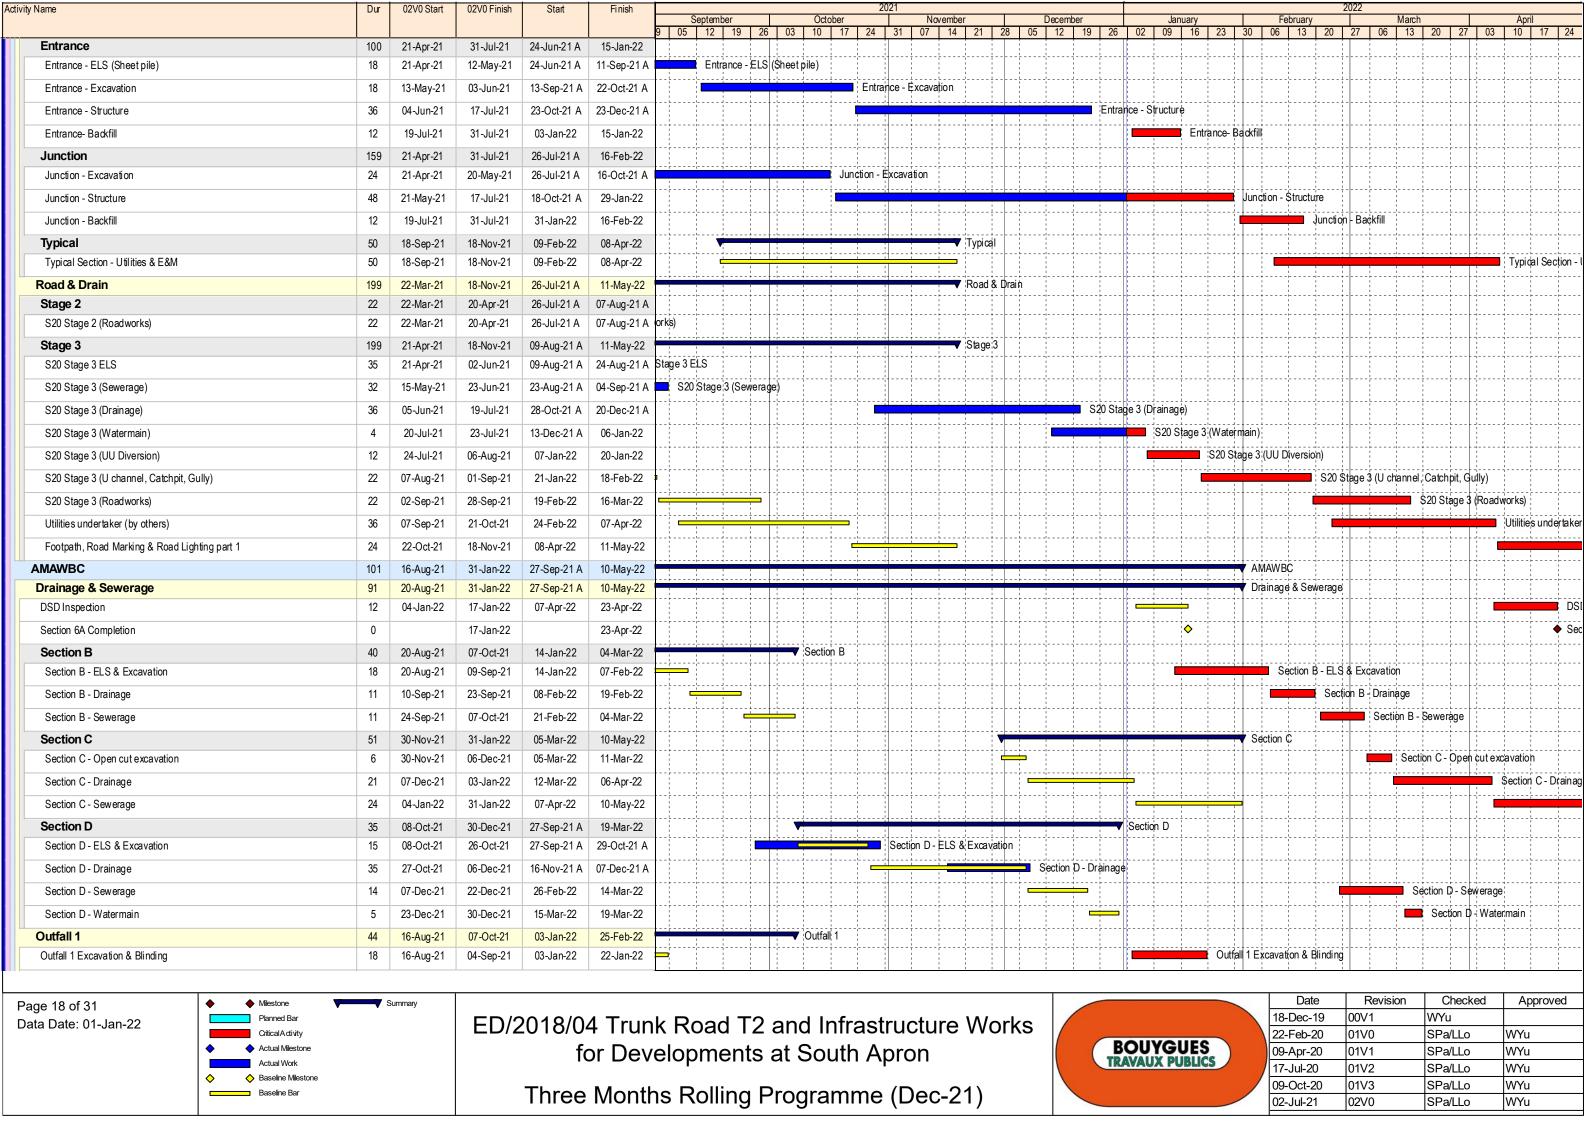


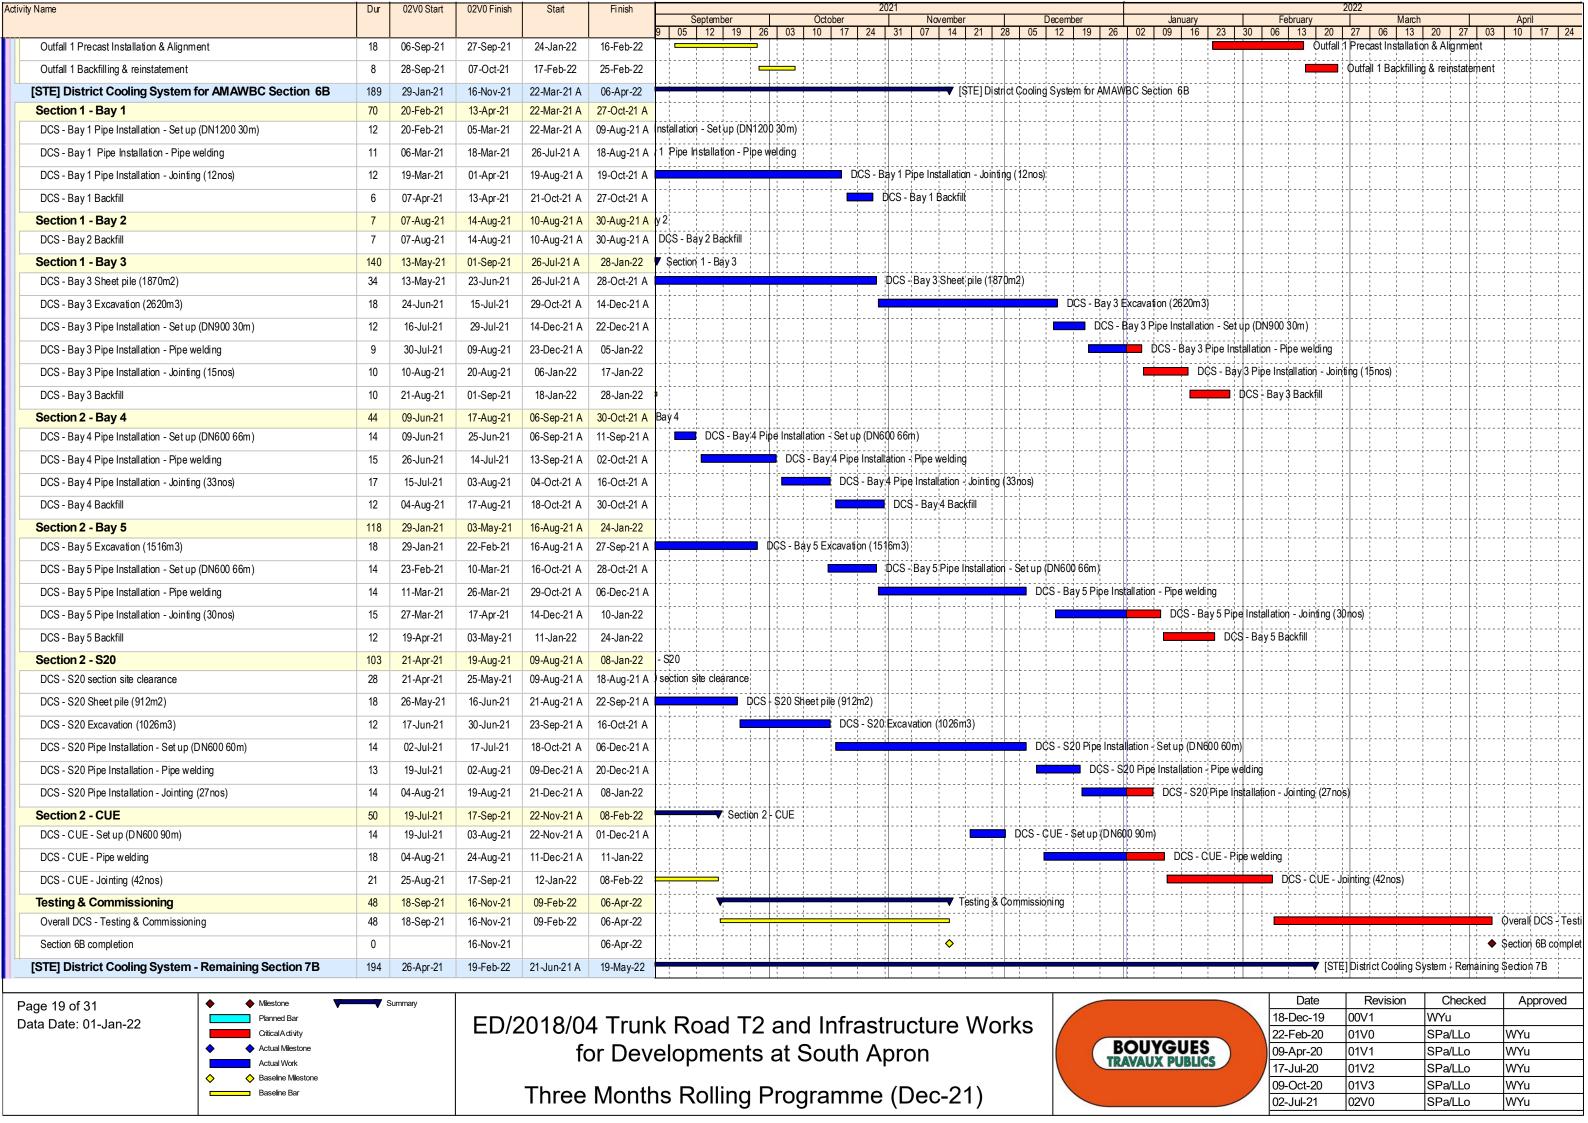

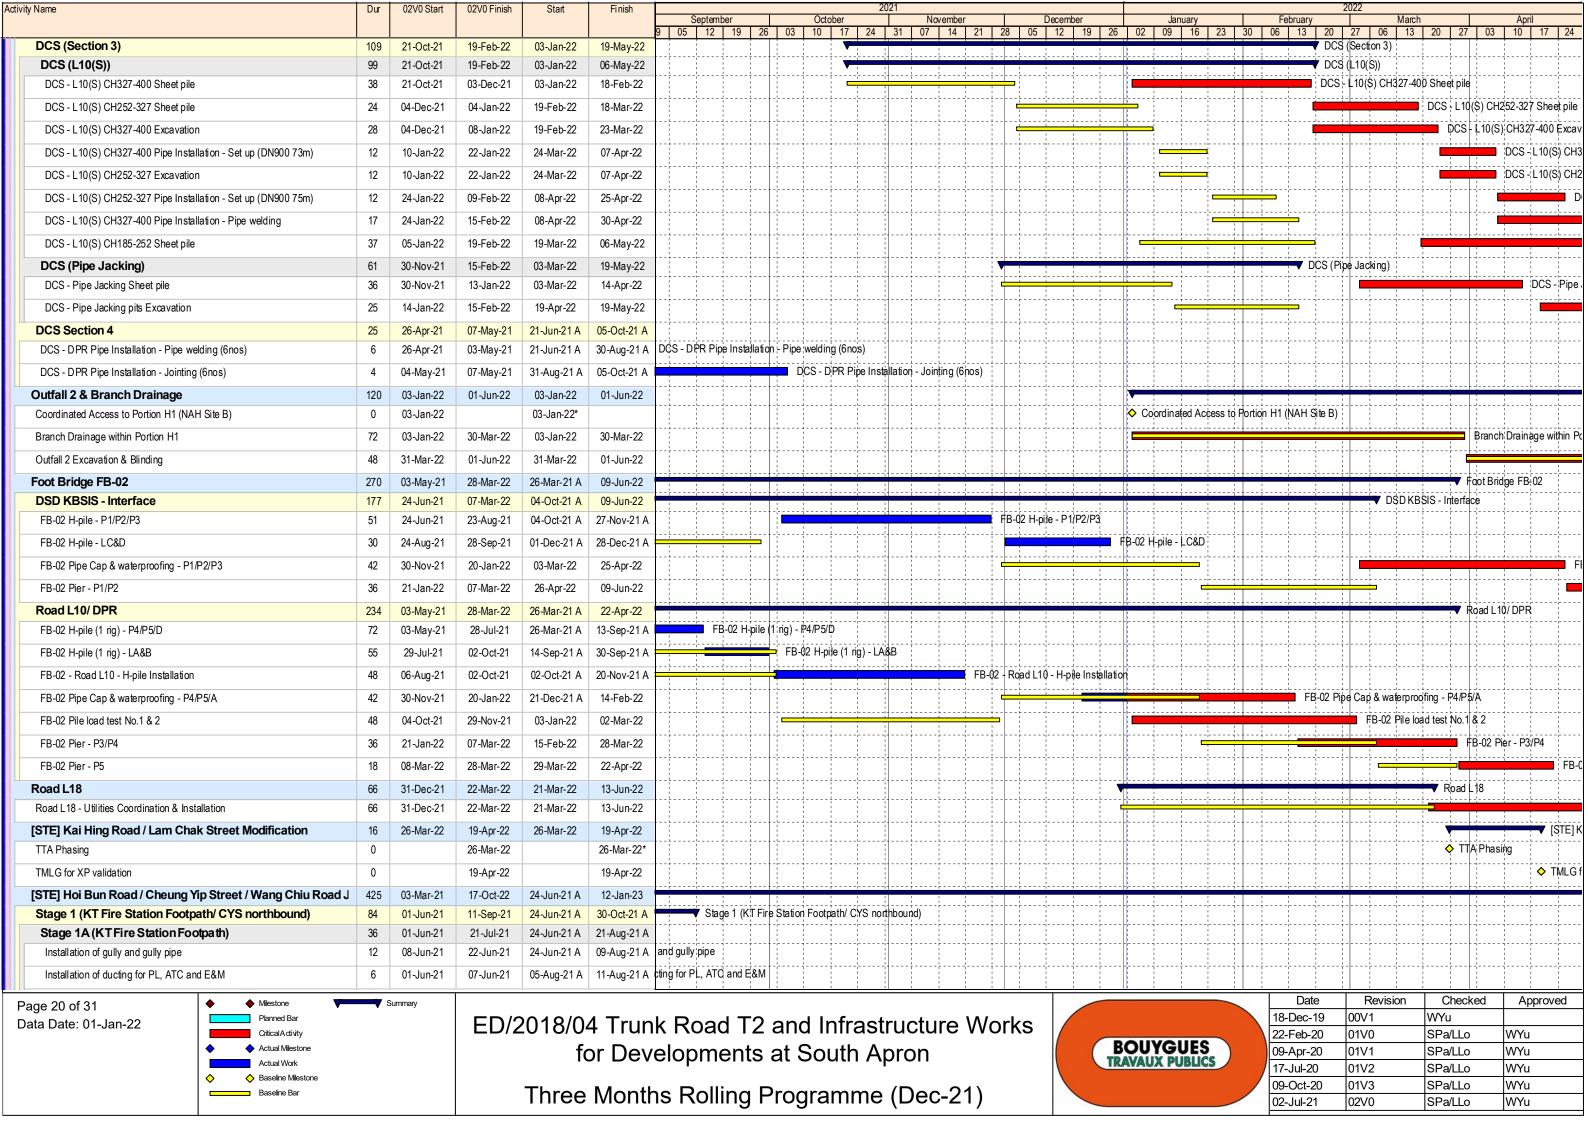



Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021 2022 September October November December January February March April
						9 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 06 13 20 27 03 10 17 24
Reinstatement of footpath & carriageway	24	23-Jun-21	21-Jul-21	07-Jul-21 A		tement of footpath & carriageway
Stage 1B (CYS northbound Lane 2)	15	22-Jul-21	07-Aug-21	25-Aug-21 A	· ·	bound Lane 2)
Installation of ducting for PL, ATC and E&M	3	22-Jul-21	24-Jul-21	25-Aug-21 A	01-Sep-21 A	
Installation of gully and gully pipe	3	26-Jul-21	28-Jul-21	03-Sep-21 A	07-Sep-21 A	Installation of gully and gully pipe
Reinstatement of carriageway	9	29-Jul-21	07-Aug-21	08-Sep-21 A	15-Sep-21 A	Reinstatement of carriageway
Stage 1C (CYS northbound Lane 3)	15	09-Aug-21	25-Aug-21	16-Sep-21 A	08-Oct-21 A	ge 1C (CYS northbound Lane 3)
Installation of ducting for PL, ATC and E&M	3	09-Aug-21	11-Aug-21	16-Sep-21 A	21-Sep-21 A	Install atton of ducting for PL, ATC and E&M
Installation of gully and gully pipe	3	12-Aug-21	14-Aug-21	22-Sep-21 A	29-Sep-21 A	Installation of gully and gully pipe:
Reinstatement of carriageway	9	16-Aug-21	25-Aug-21	30-Sep-21 A	08-Oct-21 A	Reinstatement of carriageway
Stage 1D (CYS northbound Lane 4)	15	26-Aug-21	11-Sep-21	09-Oct-21 A	30-Oct-21 A	▼ Stage 1D (CYS northbound Lane 4)
Installation of ducting for PL, ATC and E&M	3	26-Aug-21	28-Aug-21	09-Oct-21 A	12-Oct-21 A	☐ Installation of ducting for PL, ATC and E&M
Installation of gully and gully pipe	3	30-Aug-21	01-Sep-21	13-Oct-21 A	19-Oct-21 A	Install ation of gully and gully pipe
Reinstatement of carriageway	9	02-Sep-21	11-Sep-21	20-Oct-21 A	30-Oct-21 A	Reinstatement of/carriageway
Stage 2 (CYS central traffic island)	42	26-Aug-21	16-Oct-21	04-Oct-21 A	16-Nov-21 A	▼ Stage 2 (CYS central traffic island)
Demolition of existing traffic island	6	26-Aug-21 26-Aug-21	01-Sep-21		09-Oct-21 A	Demolition of existing traffic island
Connection gully and gully pipe	6	02-Sep-21	08-Sep-21	11-Oct-21 A	16-Oct-21 A	Connection gully and guilly pipe
	10	·	·			Connection for PL, ATC and E&M
Connection for PL, ATC and E&M	12	09-Sep-21	23-Sep-21	18-Oct-21 A	26-Oct-21 A	
Construction of new traffic island	18	24-Sep-21	16-Oct-21	27-Oct-21 A	16-Nov-21 A	Construction of new traffic island
Stage 3 (Wang Chiu Road)	63	09-Jun-21	15-Sep-21	12-Jul-21 A	10-Nov-21 A	▼ Stage 3 (Wang Chiu Road)
Stage 3A (WCR central traffic island)	24	09-Jun-21 09-Jun-21	08-Jul-21 08-Jul-21	12-Jul-21 A 12-Jul-21 A	13-Aug-21 A	of from the Continuous V
Reinstatement of footpath & carriageway	24					of footpath & carriageway
Stage 3B (WCR westbound Lane 2)	12	22-Jul-21	04-Aug-21		31-Aug-21 A	
Installation of ducting for PL, ATC and E&M	3	22-Jul-21	24-Jul-21	-		of ducting for PL, ATC and E&M
Reinstatement of carriageway	9	26-Jul-21	04-Aug-21		31-Aug-21 A	
Stage 3C (WCR westbound Lane 1)	12	05-Aug-21	18-Aug-21	01-Sep-21 A		WCR westbound Lane 1)
Installation of ducting for PL, ATC and E&M	3	05-Aug-21	07-Aug-21	·	·	
Reinstatement of carriageway	9	09-Aug-21	18-Aug-21	16-Sep-21 A	·	Reinstatement of carriageway
Stage 3D (WCR westbound new traffic island)	36	05-Aug-21	15-Sep-21	02-Oct-21 A	10-Nov-21 A	▼ \$tage 3D (WCR westbound new traffic island)
Demolition of existing pavement	6	05-Aug-21	11-Aug-21			Demolition of existing pavement
Connection for PL, ATC and E&M	12	12-Aug-21	25-Aug-21		20-Oct-21 A	Connection for PL, ATC and E&M
Construction of new traffic island	18	26-Aug-21	15-Sep-21	21-Oct-21 A	10-Nov-21 A	Construction of new traffic island
Stage 4 (Hoi Bun Road)	70	03-Mar-21	04-Aug-21	02-Aug-21 A		
Stage 4A (HBR Planter)	30	03-Mar-21	16-Jun-21	02-Aug-21 A	-	
Lower down existing manhole	6	03-Mar-21	09-Mar-21	-	10-Aug-21 A	
Reinstatement of footpath & carriageway	24	18-May-21	16-Jun-21		08-Sep-21 A	Reinstatement of footpath & carriageway
Stage 4B (HBR Fast Lane)	12	22-Jul-21	04-Aug-21	01-Sep-21 A	•	lne)
Installation of ducting for PL, ATC and E&M	3	22-Jul-21	24-Jul-21	·	08-Sep-21 A	Installation of blueting for PL, ATC and E&M
Reinstatement of carriageway	9	26-Jul-21	04-Aug-21	09-Sep-21 A		Reinstatement of carriageway
Stage 5 (Gas Station & HBR)	106	10-Mar-21	17-Oct-21	24-Aug-21 A		▼ Stage 5 (Gas Station & HBR)
Stage 5A (Gas Station Footpath)	74	10-Mar-21	16-Jun-21	25-Aug-21 A		
Installation of ducting for PL, ATC and E&M	6	10-Mar-21	16-Mar-21		20-Sep-21 A	Installation of ducting for PL, ATC and E&M
Reinstatement of footpath & carriageway	24	18-May-21	16-Jun-21	21-Sep-21 A		Reinstatement of footpath & carriageway
Stage 5B (HBR traffic island)	36	05-Aug-21	15-Sep-21	24-Aug-21 A	· ·	▼ \$tage 5B (HBR traffic island)
Demolition of existing traffic island	6	05-Aug-21	11-Aug-21	24-Aug-21 A	31-Aug-21 A	Demolition of existing traffic island
Page 21 of 31	9.0	ummary				Date Revision Checked Approved
Page 21 of 31 Data Date: 01-Jan-22	— ▼ 3	on i ii i i i i i i	ED/2	019/0	1 Trus	k Road T2 and Infrastructure Works
CriticalActivity			ピリ/ 2		_	1/22-Feb-20 101V0 15Pa/LLO 1WYU
♦ Actual Miestone Actual Work			fo	or Dev	relopments at South Apron BOUYGUES 109-Apr-20 01V1 SPa/LLo WYu 17- lul 20 01V2 SPa/L o WYu	
♦ Asseline Miestone						17-04-20 01V2 ST 8/LLO WTU
Baseline Bar				Three	Month	ns Rolling Programme (Dec-21)
<u> </u>						, , , , , , , , , , , , , , , , , , , ,

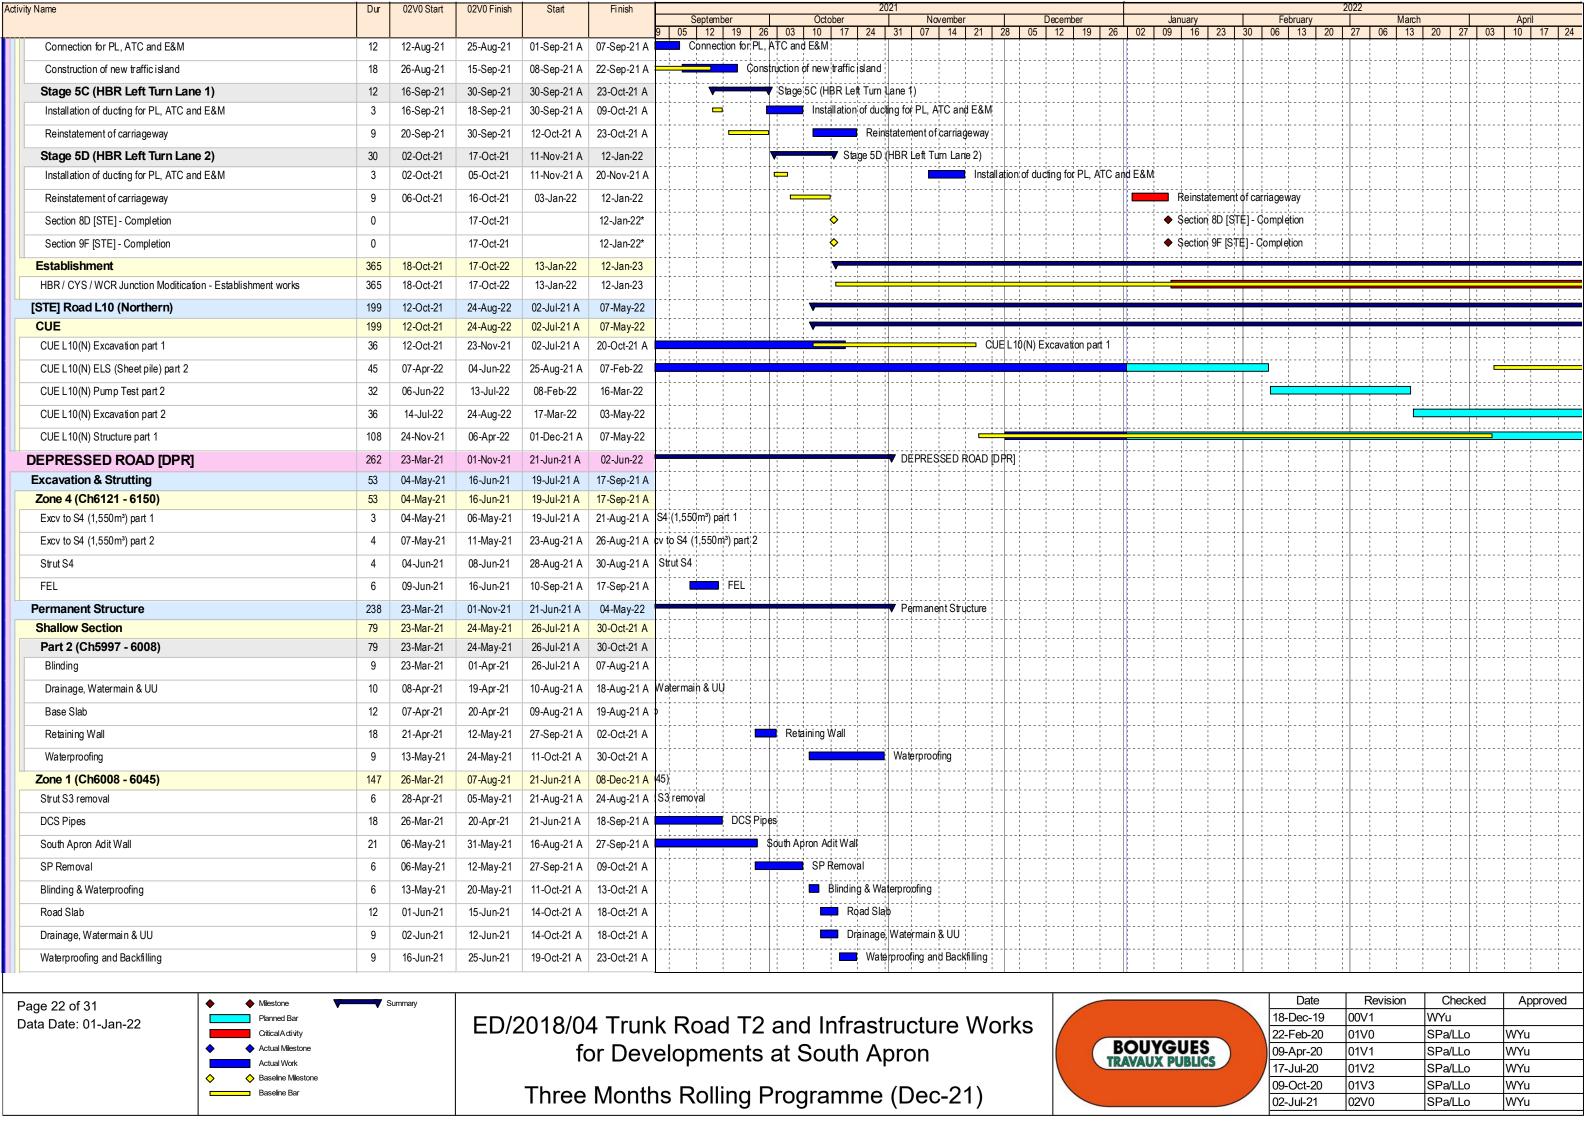


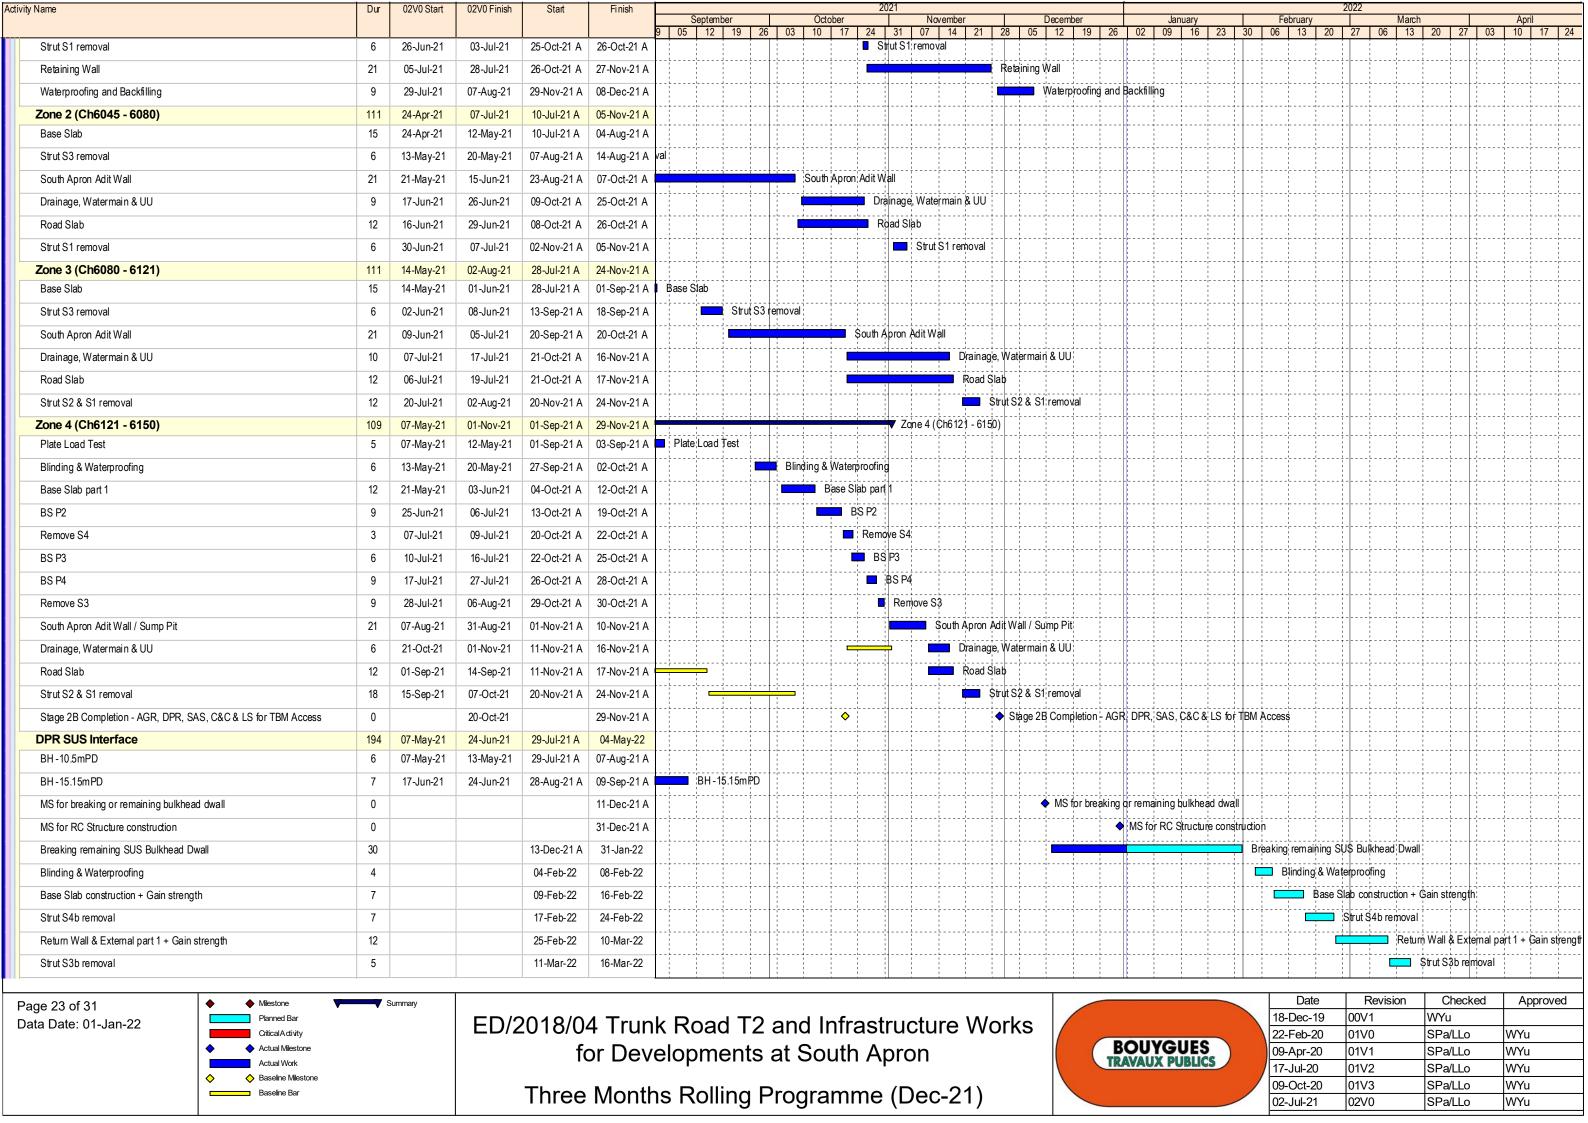


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	Comban				2021	Maria								1 -		20	022	Mamb			A:'1
						Septer 9 05 12		26 (03 10	ctober 17 24 31	Nover 1 07			ecember 12 1	19 26	02	Januar 09 1			ebruary 13	20	27 06	March 13	20 27	03 1	April 0 17 24
Remaining adit wall part 1 + Gain strength	14			17-Mar-22	01-Apr-22																	<u> </u>			Remaini	ng adit wall pa
Concrete strut & lateral beam + Gain strength	9			02-Apr-22	13-Apr-22																					Concrete st
Strut S3 removal	3			14-Apr-22	20-Apr-22																			1		Strut
Return Wall & External part 2 + Gain strength	11			21-Apr-22	04-May-22																					
Portal Structure	121			03-Jan-22	02-Jun-22																					
Falsework erection	15			03-Jan-22*	19-Jan-22													Falsewo	rk erection					į		i i
Capping Beam + Portal Beam part 1 (B4-B5)	18			20-Jan-22	12-Feb-22															■ Capp	ing Bea	1	- i	part 1 (B4-B	10 1	
Capping Beam + Portal Beam part 2 (B6-B7)	18			14-Feb-22	05-Mar-22																	Ca	pping B	eam + Portal	Beam par	t 2 (B6-B7)
Capping Beam + Portal Beam part 3 (B8-B10)	24			07-Mar-22	02-Apr-22																	_		;	Cappin	g Beam + Porta
Alternative Access available	0				08-Apr-22																				◆ A	ternative Acce
Portal secondary structure - Wall part 1 (B4-B10)	9			04-Apr-22	14-Apr-22														· 				·-ii		į <u>i</u>	□ Portal seco
Removal of existing walkway	6			09-Apr-22	19-Apr-22	†													· 					·	ļ <u>i-</u>	Remo
Capping Beam + Portal Beam part (B11-12)	18			04-Apr-22	28-Apr-22														·							
Portal secondary structure - Slab part 1 (B4-B10)	15			19-Apr-22	06-May-22														· 	-						
Portal secondary structure - Wall part 2 (B11-B12)	12			29-Apr-22	14-May-22														· 	-						
DCS Works	36			20-Apr-22	02-Jun-22														·			-		·		
WEST VENTILATION BUILDING [WVB]	282	21-May-21	26-Feb-22	21-Jun-21 A	16-Jun-22														ļ <u></u>	<u> </u>		WE\$T VE	NTILAT	ION BUILDI	NG [WVB]	
ELS system & Foundation	117	21-May-21	19-Jul-21	21-Jun-21 A	20-Oct-21 A																					
King Post	117	02-Jun-21	19-Jul-21	21-Jun-21 A	20-Oct-21 A														·						1	
Steel Platform Location	117	02-Jun-21	19-Jul-21	21-Jun-21 A																						
KP Drilling (DP1 - DP6) 6 nos @ 3d/no	18	02-Jun-21	23-Jun-21	21-Jun-21 A	_	DP6) 6 nos @	_ i i		1								1							i ! !		i i I I I I
KP Installation (DP1 - DP6) 6 nos @ 2d/no	18	05-Jun-21	26-Jun-21	05-Jul-21 A	14-Aug-21 A	(DP1 - DP6) 6	6 nos @ 2	2d/no																		
Steel Deck Erection	18	28-Jun-21	19-Jul-21	06-Oct-21 A	20-Oct-21 A					Steel Deck	Erection															
Wells Installation	15	21-May-21	08-Jul-21	26-Jul-21 A	04-Sep-21 A																	L	. j j			
North	7	21-May-21	16-Jun-21	26-Jul-21 A	02-Sep-21 A																				ļ	
Pumping Well Installation - 6 nos x 2 rigs (Zone 3)	6	21-May-21	27-May-21			allation - 6 nos	_11															ļ				
Pumping Well Installation - 6 nos x 2 rigs (Zone 1)	6	01-Jun-21	07-Jun-21	_	_	umping Well li	i i	1 i	i i	i i il												L				
Pumping Well Installation - 7 nos x 2 rigs (Zone 2)	7	08-Jun-21	16-Jun-21	30-Aug-21 A	02-Sep-21 A	Pumping V	Vell Instal	lation - 7	nos x 2	rigs (Zone 2)							! !									1 1
South	15	28-May-21	08-Jul-21	_	04-Sep-21 A	ļ	-1		5													ļ				
Pumping Well Installation - 2 nos x 2 rigs (Zone 5)	2	07-Jul-21	08-Jul-21	_	_	nping Well Inst	- 1	1 1	- 1										ļ <u>.</u>	ļ					ļļ	
Pumping Well Installation - 3 nos x 2 rigs (Zone 6)	3	28-May-21	31-May-21	-		Pumping	Well Inst	allation 	3 nos x	2 rigs (Zone 6)																
Steel Platform Location	8	24-Jun-21	03-Jul-21		18-Aug-21 A	V-1 1			(7 4)										·			ļ <u>-</u>	·		ļ	
Pumping Well Installation - 11 nos x 3 rigs (Zone 4)	8	24-Jun-21	03-Jul-21	_		Vel Installation	1 - 11 nos	x 3 rigs	(Zone 4))												ļ				
Excavation & Strutting	146 12	09-Jul-21 09-Jul-21	11-Dec-21	06-Sep-21 A 06-Sep-21 A			Dum	oing Toe						Excava	ation & Str	rutting				-						
Pumping Test	12		20-Jul-21		10-3ep-21 A		_ii		ation Sta										· -			ļ				
Bulk Excavation Start	47	21-Jul-21	00 00	20-Sep-21 A	40 Nov. 04 A	ļ		· ···					bolow Ctart	C1 10 0	10 m3							<u> </u>				
Excavation to below Strut S1 10,010m³	1/	21-Jul-21	09-Aug-21	20-Sep-21 A		 						xcavation to		۰۰۰۰۰ 								<u> </u>			ļ	
Strut S1 Installation	20	26-Jul-21	17-Aug-21	30-Sep-21 A		-						Strut S1 In							ļ 	ļļ		ļ	 			
Strut S1 Pre-loading	2	18-Aug-21	19-Aug-21		18-Nov-21 A							Strut \$1					0.44.0=5		.			ļ				
Excavation to below Strut S2 11,076m³	18	20-Aug-21	09-Sep-21		07-Dec-21 A		_						Ex		to below		∠ 11,U/6r 	n*				ļ				
Strut S2 Installation	20	26-Aug-21	17-Sep-21	29-Nov-21 A											rut \$2 Ins				.			ļ				
Strut S2 Pre-loading	2	18-Sep-21	20-Sep-21		18-Dec-21 A	 									Strut S2 F	re-loadi	ng ¦		.			J			 	
Excavation to below Strut S3 11,905m³	20	21-Sep-21	16-Oct-21	20-Dec-21 A	22-Jan-22				1						i		i	Exca	vation to be	elow Stri	ut S3 11	,905m³		; 1 1 1		; ; ; ; ; ; ; ; ; ; ; ; ; ; ; ; ; ; ;
David 04 - 6 04		lumman.																		Date	<u> </u>	Revis	ion	Check	ed	Approved
Page 24 of 31 Data Date: 01-Jan-22	S	Summary	ED/2	0/010	1 Trus	k Doo	ч	2 ~	ו אם	Infrastru	ioti ir	o \\/o	rko						18	3-Dec-1		00V1		WYu		
CriticalAdivity			CU /2									e vvo	ıns			OII)	(CIII	9:	\ \	2-Feb-2 9-Apr-20		01V0		SPa/LLo		Yu
◆ Actual Miestone Actual Work				for Developments at Sou							South Apron					BOUYGUES TRAVAUX PUBLICS						01V1 01V2		SPa/LLo SPa/LLo		Yu Yu
♦ Baseline Milestone				There a Mandha Dallina a Dua amanana (Dan CA)																7-Jul-20 9-Oct-20		01V2 01V3		SPa/LLo		<u>Yu</u> Yu
Baseline Bar				Three	Mont	ns Rol	ling	Pro	ogra	amme (I	Dec-	21)								2-Jul-21		02V0		SPa/LLo		Yu
										Three Months Rolling Programme (Dec-21)																

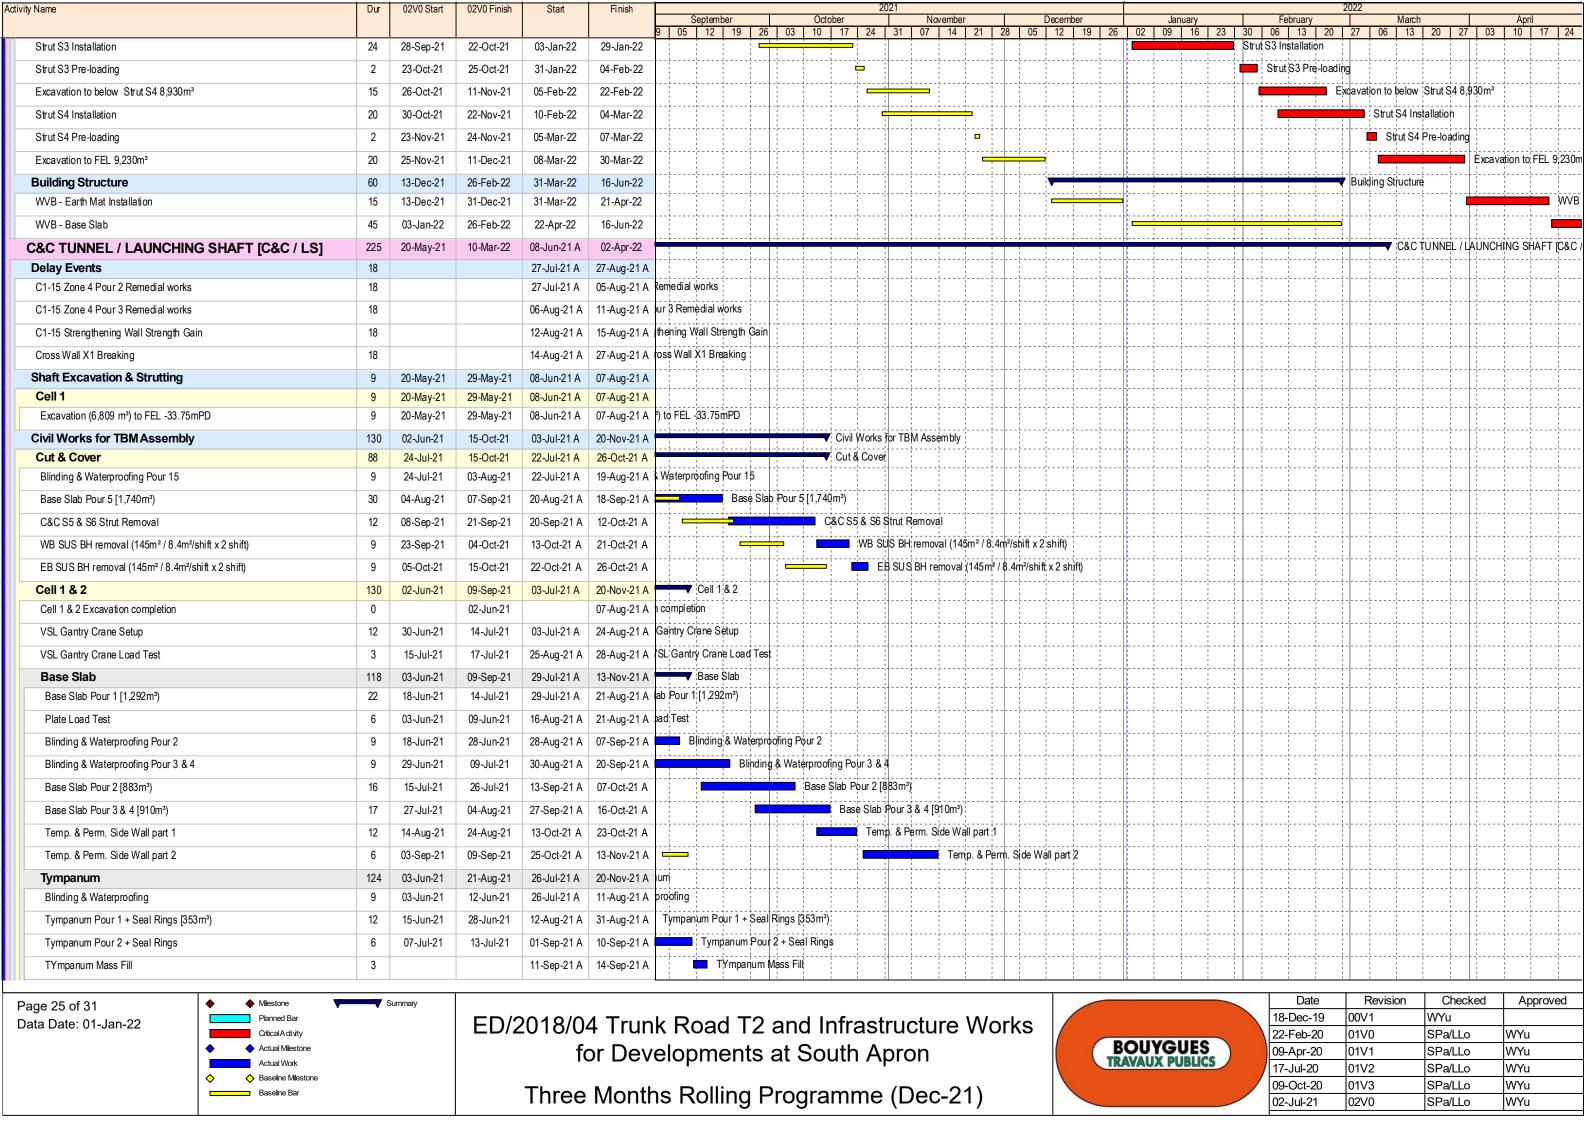


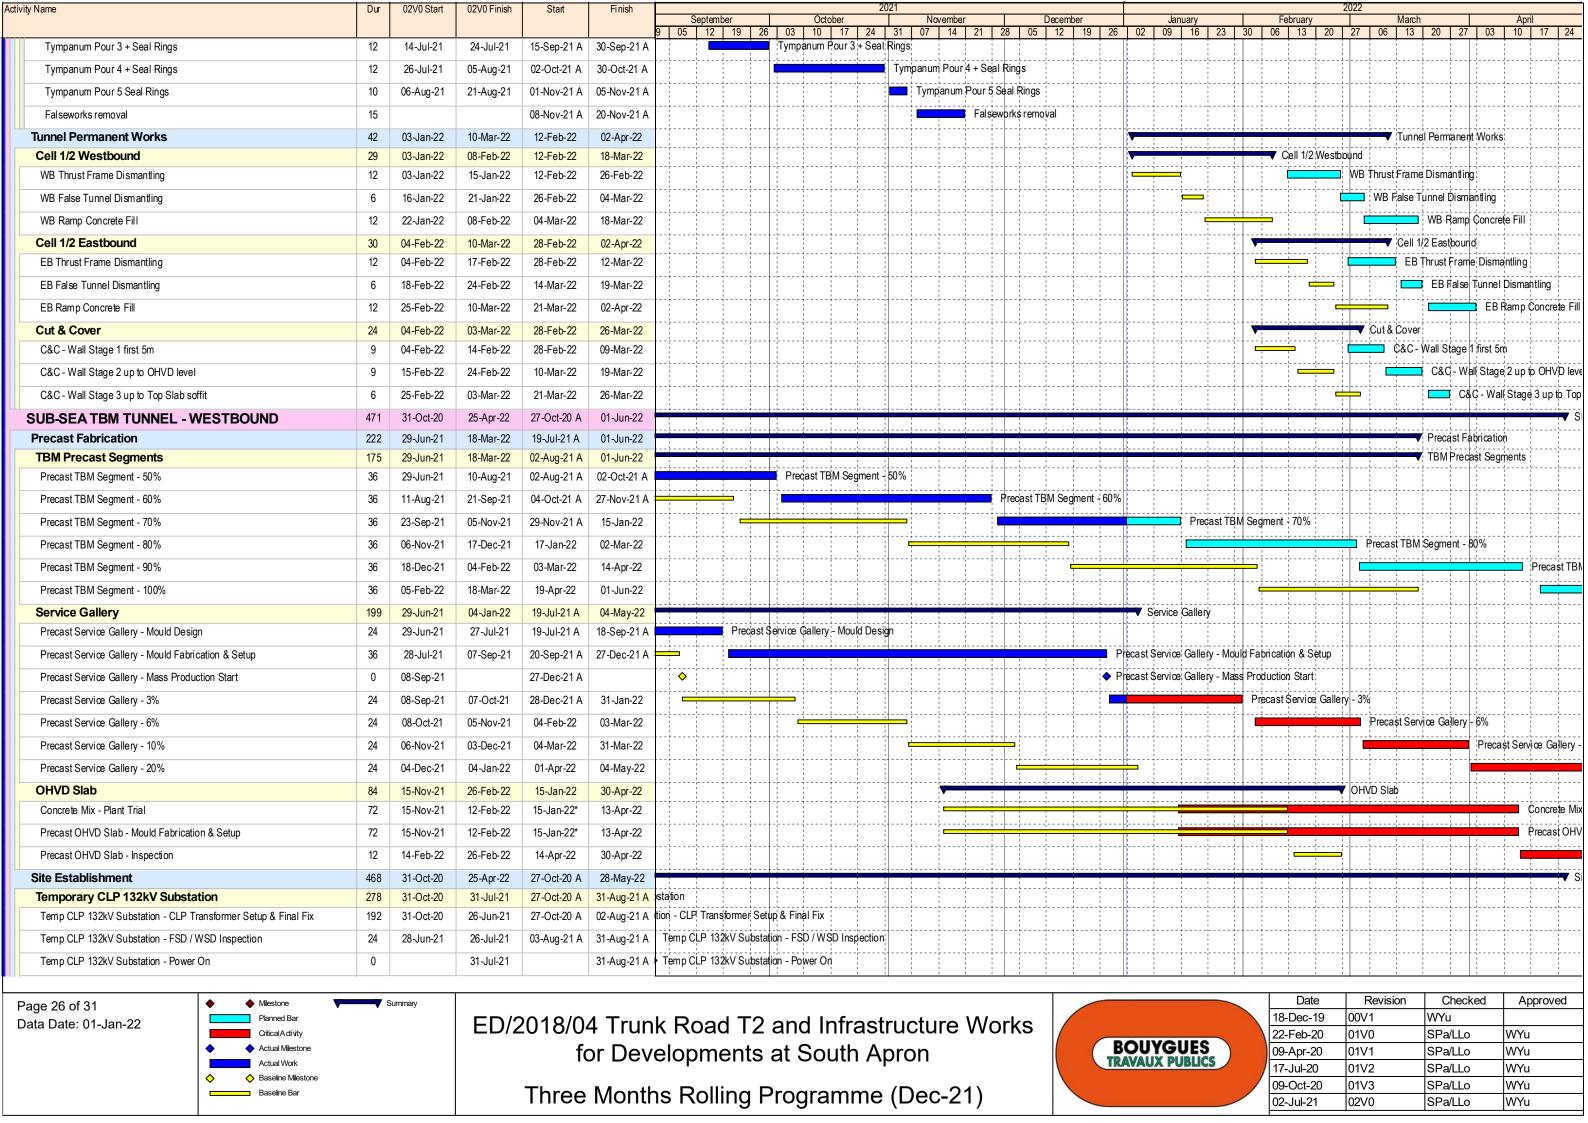


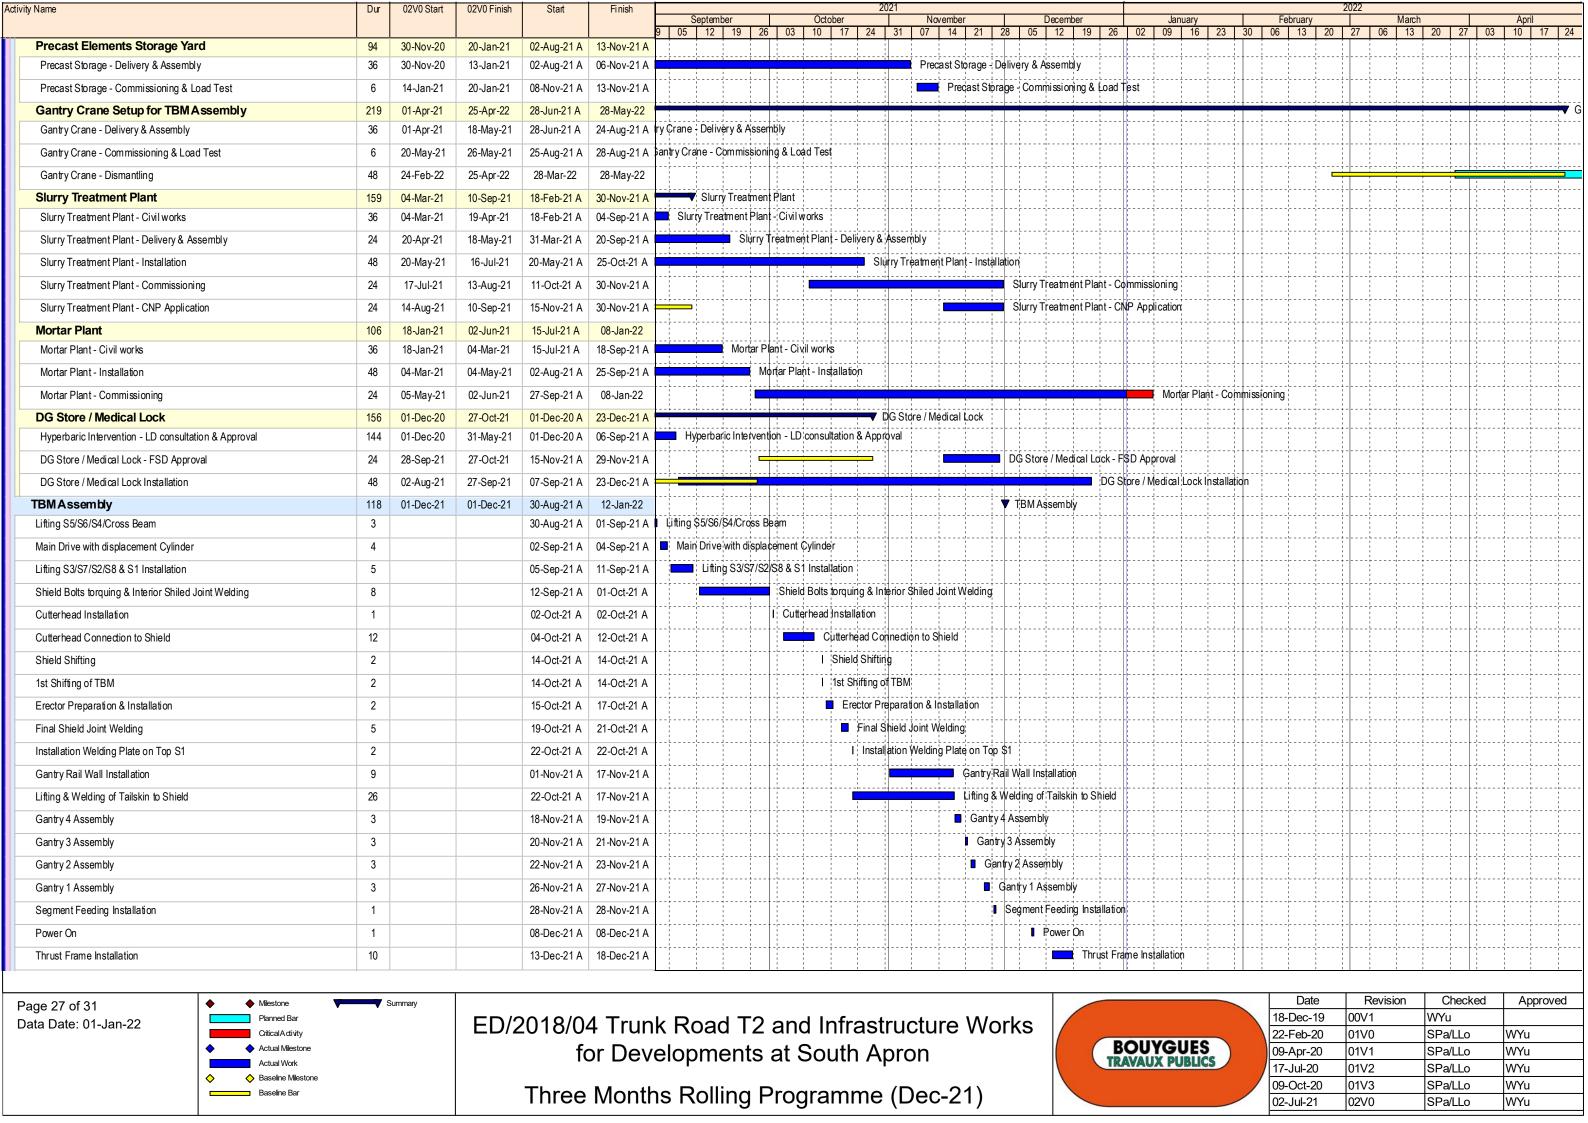

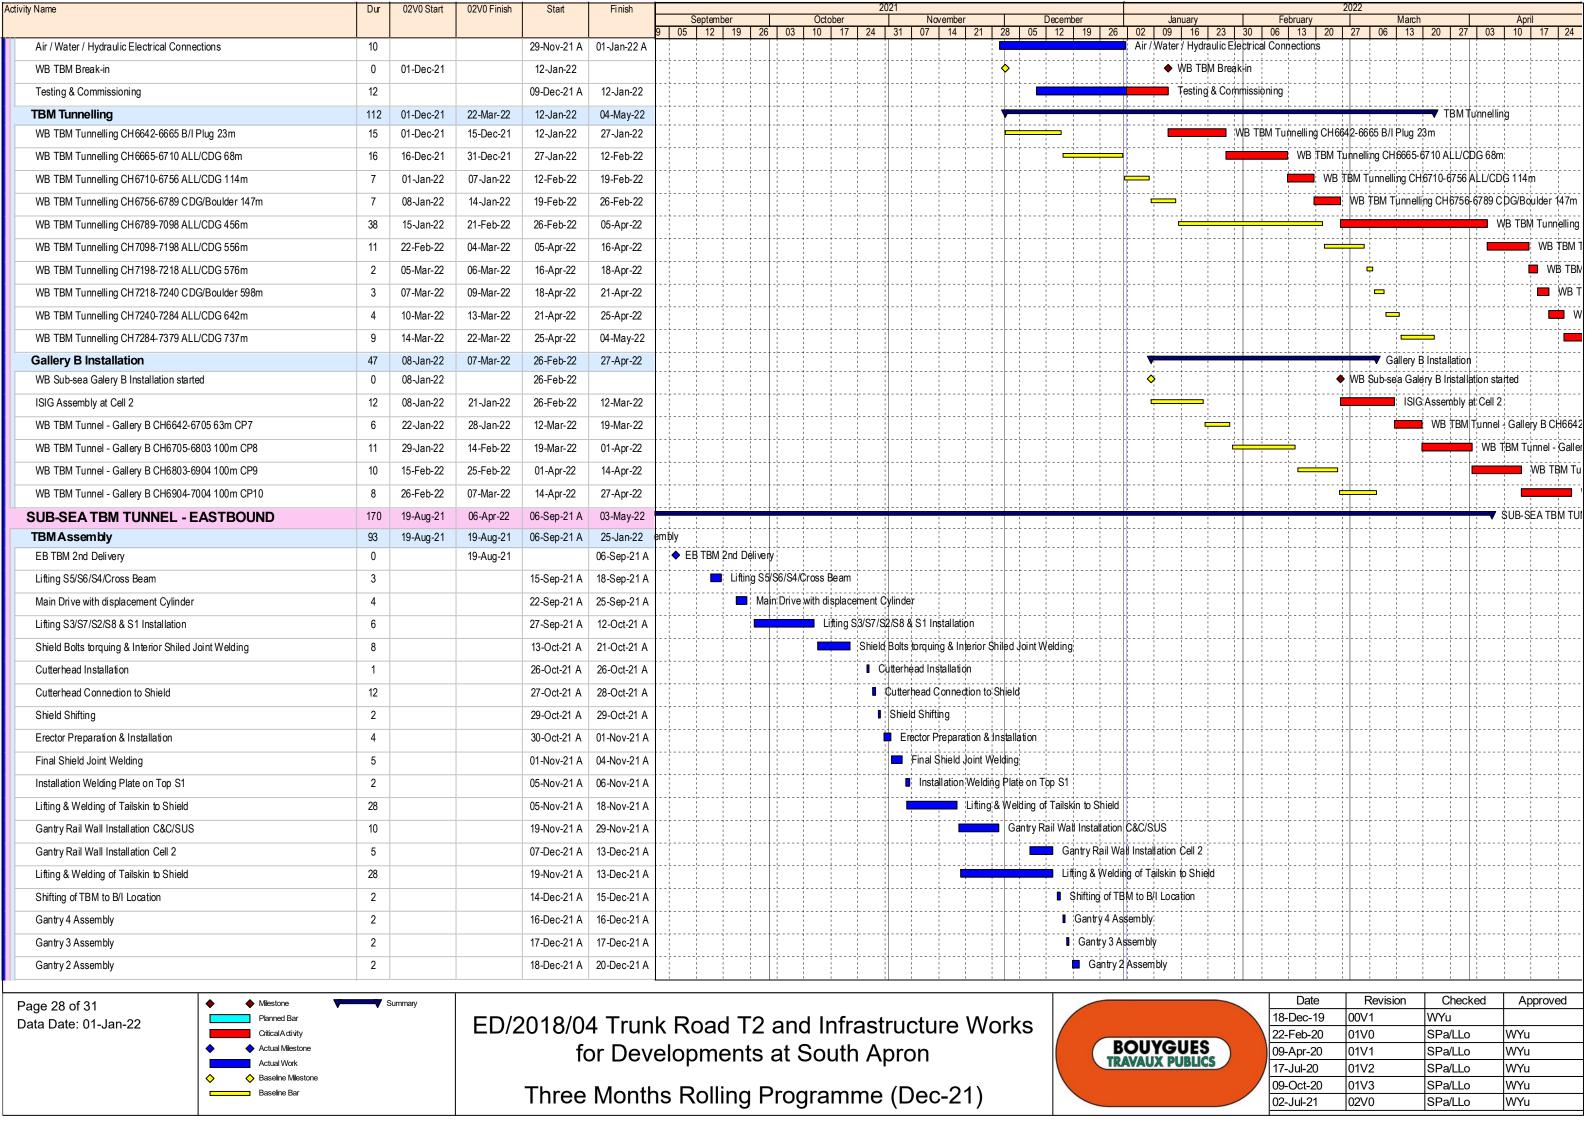

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish				0.1.1	2021					mber January				-	2022				
						September 9 05 12 19) 26	03	Octobe 10	er 17 24 31	November 07 14			ecember			09 1	6 23		February 6 13	20 27	06 M	arch 13 20 27	April 03 10 17 24
Segment Feeding Installation	1			27-Dec-21 A	28-Dec-21 A				i						1			Installation						
Gantry 1 Assembly	3			29-Dec-21 A	29-Dec-21 A										I	Gantry 1	1	1 1						
Thrust Frame Installation	10			01-Jan-22	10-Jan-22												Thrus	Frame Ins	stallation					
Air / Water / Hydraulic Electrical Connections	10			01-Jan-22	10-Jan-22												Air/V	Vater / Hyd	Iraulic Ele	ectrical Con	nections			
Power On	1			10-Jan-22	12-Jan-22				·		-						■ Pow	er On			 	;;		
Lifting & Welding of Tailskin to Shield	28			14-Dec-21 A	15-Jan-22	1			· 			÷						fting & We	lding of T	Γailskin to S	hield	·}		
Testing & Commissioning	12			12-Jan-22	25-Jan-22						<u>-</u>							Tes	sting & C	ommissioni	ng			
S1282 EB TBM Break-in	0				25-Jan-22													◆ S12	282 EB T	BM Break-i	n			
TBM Tunnelling	94	03-Jan-22	06-Apr-22	27-Jan-22	01-May-22																			▼ TBM Tunnelling
EB TBM Tunnelling CH6640-6665 B/I Plug 25m	16	03-Jan-22	18-Jan-22	27-Jan-22	12-Feb-22														· 	= ЕВ ТВ	M Tunnelli	ng CH664	10-6665 B/I Plug 25	im
EB TBM Tunnelling CH6665-6710 ALL/CDG 70m	15	19-Jan-22	02-Feb-22	12-Feb-22	27-Feb-22				·		 								 		EB	TBM Tur	nelling CH6665-67	10 ALL/CDG 70m
EB TBM Tunnelling CH6710-6756 ALL/CDG 116m	7	03-Feb-22	09-Feb-22	27-Feb-22	06-Mar-22																	■ EB TE	BM Tunnelling CH6	710-6756 ALL/CDG 116
EB TBM Tunnelling CH6756-6789 CDG/Boulder 149m	7	10-Feb-22	16-Feb-22	06-Mar-22	13-Mar-22	1																	EB TBM Tunnellin	g CH6756-6789 CDG/B
EB TBM Tunnelling CH6789-7098 ALL/CDG 458m	38	17-Feb-22	26-Mar-22	13-Mar-22	20-Apr-22																	<u> </u>		EB TBI
EB TBM Tunnelling CH7098-7198 ALL/CDG 558m	11	27-Mar-22	06-Apr-22	20-Apr-22	01-May-22			- -																
Gallery B Installation	39	10-Feb-22	26-Mar-22	14-Mar-22	03-May-22				·											V			Galler	y B Installation
EB Sub-sea Galery B Installation started	0	10-Feb-22	LO Mai LL	14-Mar-22	00 may 22														·	♦		ļ ļ -	1 1 1	y B Installation started
ISIG Assembly at Cell 2	12	10-Feb-22	23-Feb-22	14-Mar-22	26-Mar-22																-			ssembly at Cell 2
EB TBM Tunnel - Gallery B CH6642-6705 63m CP7	8	24-Feb-22	04-Mar-22	28-Mar-22	06-Apr-22																			■ EB TBM Tunnel - G
EB TBM Tunnel - Gallery B CH6705-6803 100m CP8	10	05-Mar-22	16-Mar-22	07-Apr-22	21-Apr-22																			EBTE
EB TBM Tunnel - Gallery B CH6803-6904 100m CP9	0	17-Mar-22	26-Mar-22	22-Apr-22	03-May-22																			
SUB-SEA TUNNEL CROSS PASSAGE (CP7-CP27a	144	31-Jul-21	07-Jul-22	10-May-21 A	21-May-22		-					ļļ							ļļ			·		
CP TBM Design / Fabrication / FAT / Delivery	144	31-Jul-21	22-Mar-22	10-May-21 A	30-Mar-22																		CP TRM I	Design / Fabrication / FA
Fabrication / Refurbishment	144	31-Jul-21	21-Jan-22	10-May-21 A	29-Jan-22											ļļ.			Fabrica	tion / Refurb	ishment			Joseph T. aprication T. T.
FAT	24	22-Jan-22	22-Feb-22	31-Jan-22	02-Mar-22														<u> </u>			FAT		
Delivery of TBM components to the Site	24	23-Feb-22	22-Mar-22	03-Mar-22	30-Mar-22				·															elivery of TBM compone
CP Precast Lining Fabrication	108	26-Nov-21	07-Jul-22	26-Oct-21 A	18-May-22									·					ļ <u>-</u>					
Concrete Mix - Plant Trial	40	26-Nov-21	14-Jan-22	26-Oct-21 A	29-Nov-21 A				·			<u> </u>			 		<u> </u>	ncrete Mix	∖- Plant 1	Trial				
CP Precast Lining Segment - Mould Fabrication & Setup	24	15-Jan-22	15-Feb-22	30-Nov-21 A					·										·	CP	Precast Lir	ning Segn	nent - Mould Fabric	ation & Setup
CP Precast Lining Segment - Master Ring Erection & Inspection	6	16-Feb-22	22-Feb-22	16-Dec-21 A	16-Dec-21 A																		iii	r Ring Erection & Inspec
CP Precast Lining Segment - 3%	18	23-Feb-22	15-Mar-22	17-Dec-21 A	22-Jan-22																			ng Segment - 3%
CP Precast Lining Segment - 6%	18	16-Mar-22	06-Apr-22	24-Jan-22	16-Feb-22														.ļļ					■ CP Precast Lining §
CP Precast Lining Segment - 10%	24	07-Apr-22	10-May-22	17-Feb-22	16-Mar-22	 																		
			,						·										·					
CP Precast Lining Segment - 20%	24	11-May-22	08-Jun-22	17-Mar-22	14-Apr-22											ļļ.								
CP Precast Lining Segment - 30%	24	09-Jun-22	07-Jul-22	19-Apr-22	18-May-22											ļļ.			ļ <u>.</u>	1 1 1 1 1 1			I AMP	CD Tyma days Ct.
WB CP Tympanum Structure CP7 - WB - Tympanum Civil works CH6705	48 24	29-Jan-22 29-Jan-22	29-Mar-22 01-Mar-22	19-Mar-22 19-Mar-22	21-May-22 21-Apr-22														·				VVB	CP Tympanum Structu
CP8 - WB - Tympanum Civil works CH6803	24	15-Feb-22	14-Mar-22	01-Apr-22	05-May-22	 		- -	·															
CP9 - WB - Tympanum Civil works CH6904	24	02-Mar-22	29-Mar-22	21-Apr-22	21-May-22																	ļ 		
	34			•					·							ļļ.	!		·					ER CD Turns
EB CP Tympanum Structure CP7 - EB - Tympanum Civil works CH6705	24	05-Mar-22 05-Mar-22	14-Apr-22 01-Apr-22	07-Apr-22 07-Apr-22	21-May-22 10-May-22																			▼ EB CP Tymr
CP8 - EB - Tympanum Civil works CH6803	24	17-Mar-22	14-Apr-22	22-Apr-22	21-May-22																			
CHA KWO LING ROAD WORKS	76	24-Apr-21	31-May-21	19-Apr-21 A	15-Jan-22	 						- 										ļ <u>i</u>		
		·	or-ividy-21	13-Apr-21 A	IJ-JdII-ZZ	<u> </u>	!		- !			<u> </u>		<u>;</u>			!	<u> </u>	<u> </u>	<u> </u>	- -]]	01	1
Page 29 of 31	-	Summary		04010	4 T	L D 11	т^	_		C 1	1.	۱۸/	1						-	Date 18-Dec-19		Revision ′1	Checked WYu	I Approved
Data Date: 01-Jan-22 CriticalActivity Actual Milestone Actual Work			L D/2	D/2018/04 Trunk Road 12 and Infrastructure Works							22-Feb-20			SPa/LLo	WYu									
				for Developments at South Apron										BOUYGUES TRAVAUX PUBLICS						09-Apr-20			SPa/LLo	WYu
Actual Work Baseline Milestone			·									17-5					17-Jul-20	01V		SPa/LLo	WYu WYu			
Baseline Bar			Three Months Rolling Programme (Dec-21)										09-Oct-20 01V3 SPa/LLo 02-Jul-21 02V0 SPa/LLo							WYu				
						_			`									<u> </u>		1			<u> </u>	

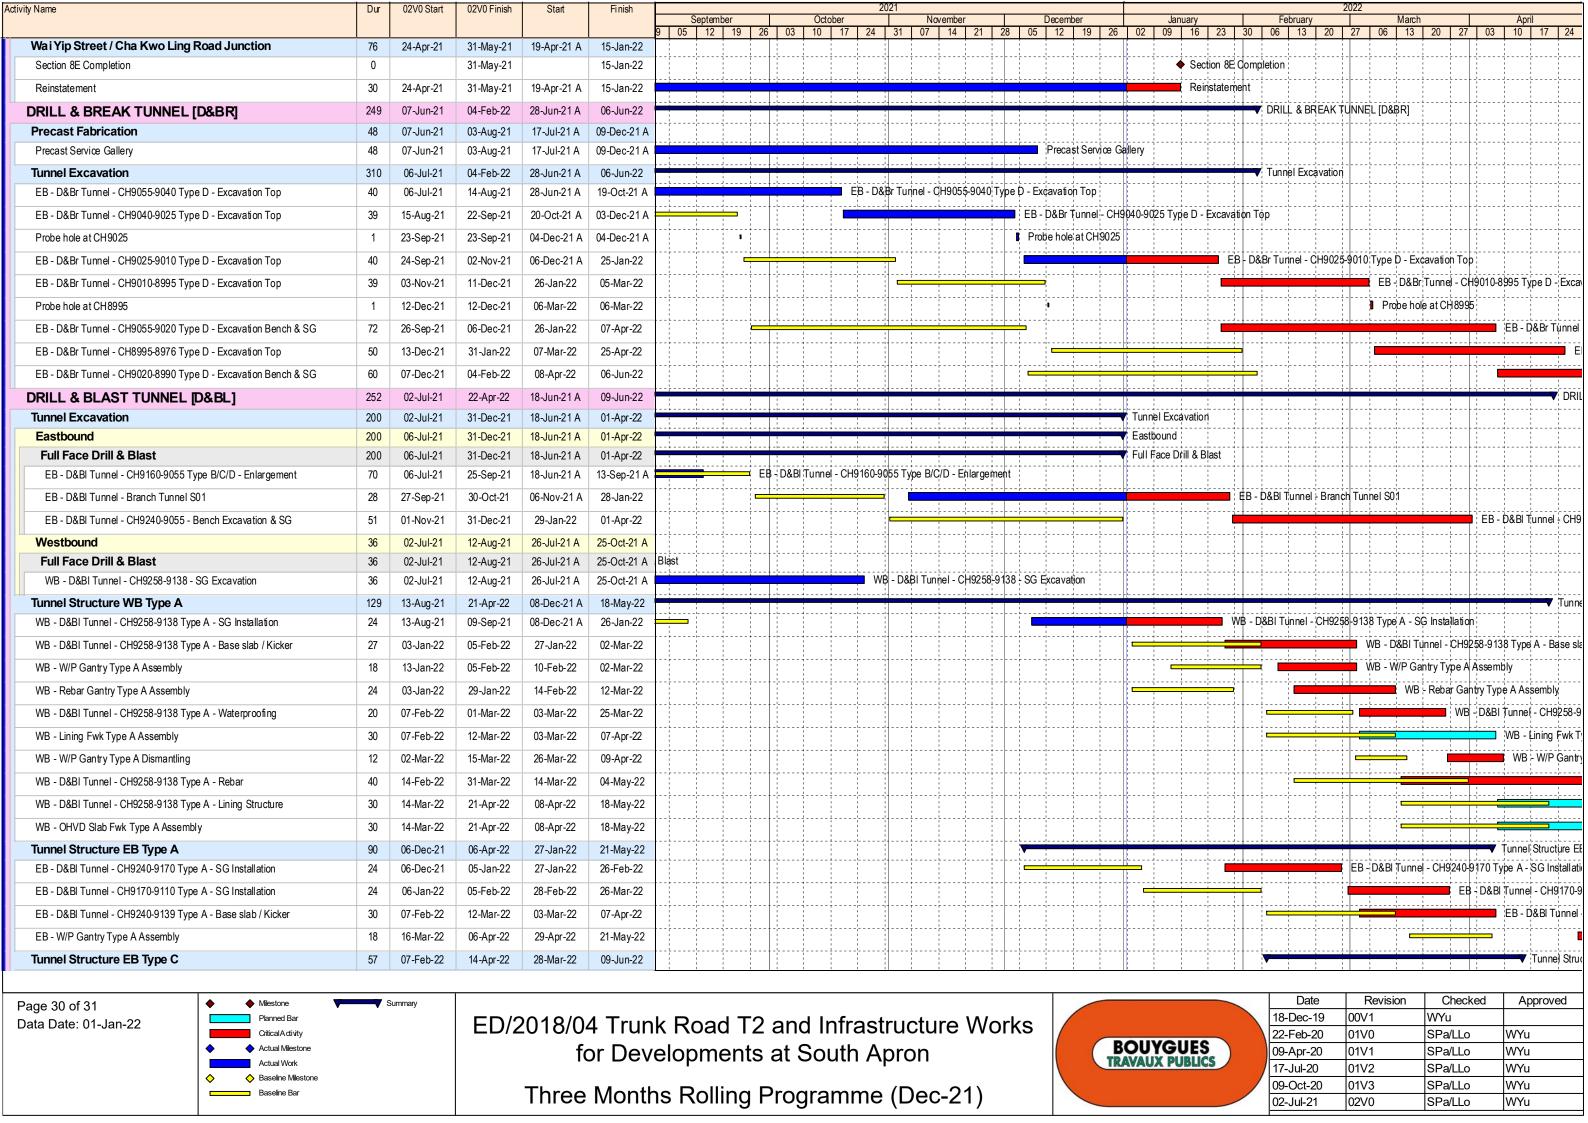

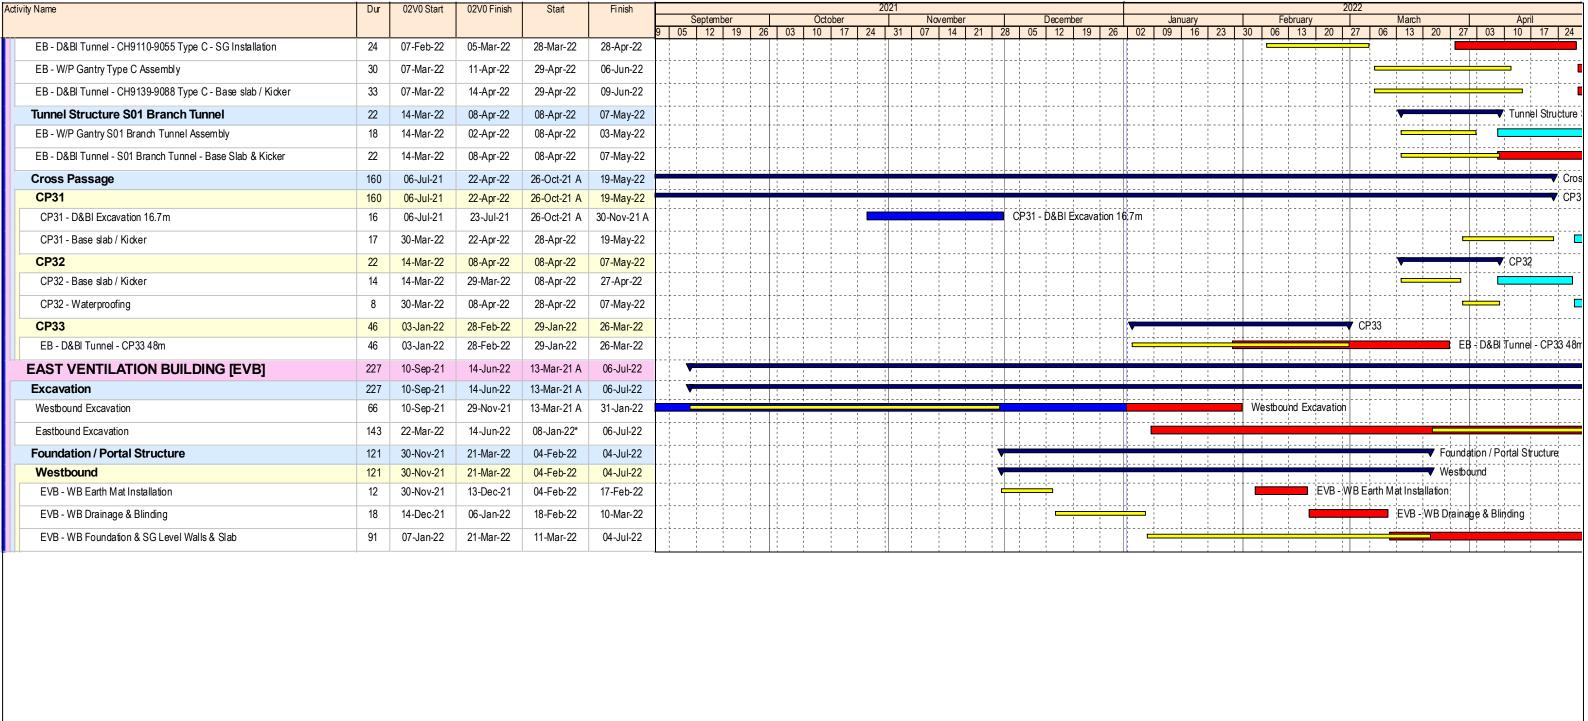

Milestone
 Planned Bar
 Critical Activity
 Actual Milestone
 Actual Work
 Baseline Milestone
 Baseline Bar

Page 31 of 31

Data Date: 01-Jan-22

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron
Three Months Rolling Programme (Dec-21)

Checked

WYu

SPa/LLo

SPa/LLo

SPa/LLo

SPa/LLo

SPa/LLo

Approved


WYu

WYu WYu

WYu

WYu

APPENDIX O WASTE GENERATED IN THE REPORTING MONTH





Name of Department: CEDD

Monthly Summary Waste Flow Table for 2021 (KT)

	Actu	al Quantities	of Inert C&D	Materials G	enerated Mo	nthly	Actual	Quantities of	C&D Waste	s Generated I	Monthly
Month	a.Total Rock Quantity and Large Generated Broken (a=c+d+e) Concrete		c. Reused in the Contract	d. Reused in Other Projects	e. Disposed as Public Fill	f. Imported Fill	g. Metals	h. Paper / Cardboard Packaging	i. Plastics	j. Chemical Waste	k. Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m³)
January	22.430	4.842	0.500	21.540	0.390	0.000	173.190	0.200	0.000	0.600	0.130
February	23.765	5.428	0.390	23.240	0.135	0.000	50.360	0.000	0.000	0.000	0.090
March	41.630	5.679	0.000	41.497	0.133	0.000	295.980	0.000	0.000	2.400	0.120
April	26.409	9.446	0.820	24.043	1.546	0.000	273.540	0.660	0.000	3.000	0.100
May	33.370	9.878	0.397	11.781	21.192	0.000	113.200	0.000	0.000	0.000	0.080
June	39.039	5.817	0.450	37.130	1.459	0.000	97.600	0.340	0.000	2.800	0.090
Sub-total	186.642	41.091	2.557	159.230	24.855	0.000	1003.870	1.200	0.000	8.800	0.610
July	6.177	0.000	2.250	0.000	3.927	0.000	237.580	0.719	0.000	0.000	0.127
August	20.108	0.312	0.000	0.312	19.796	0.000	227.250	0.000	0.000	0.000	0.183
September	0.490	0.000	0.000	0.000	0.490	0.000	204.350	0.484	0.000	2.200	0.279
October	13.693	0.000	0.000	13.626	0.067	0.000	76.670	0.000	0.000	4.000	0.167
November	14.395	0.000	0.000	14.380	0.015	0.000	22.000	0.220	0.000	3.200	0.200
December	9.140	0.000	0.000	9.140	0.000	0.000	0.000	0.460	0.000	0.000	0.210
Total	250.645	41.403	4.807	196.688	49.150	0.000	1771.720	3.083	0.000	18.200	1.776

Monthly Summary Waste Flow Table

Notes:

- (1) The performance targets are given in ER Appendix 8I Clause 14 and the EM&A Manual(s).
- (2) The waste flow table shall also include C&D materials to be imported for use at the Site.
- (3)Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- (4)The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m3. (ER Part 8 Clause 8.8.5 (d) (ii) refers).
