

**Noise Impact Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD 1a: Centre of Excellence in Paediatrics (Children's Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
03-Apr-19	15:39	74	77	63	0.3	Fine
09-Apr-19	9:10	70	73	69	0.3	Fine
15-Apr-19	11:15	70	74	64	0.4	Cloudy
18-Apr-19	13:37	70	72	70	0.3	Cloudy
24-Apr-19	9:52	70	72	68	0.3	Sunny
30-Apr-19	10:45	71	74	66	1.2	Cloudy
	Max	74				
	Min	70				
	Limit Level	75				

KTD 2b: G/C Zone next to Kwun Tong Bypass (Next to the site of the New Acute Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
03-Apr-19	16:23	74	76	72	0.4	Fine
09-Apr-19	10:00	73	75	71	0.3	Fine
15-Apr-19	10:24	71	75	69	0.6	Cloudy
18-Apr-19	14:15	74	75	70	0.4	Cloudy
24-Apr-19	10:31	73	76	71	0.4	Sunny
30-Apr-19	10:10	72	74	71	1.4	Cloudy
	Max	74				
	Min	71				
	Limit Level	75				

KER 1b: Site Boundary at Cheung Yip Street




Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
03-Apr-19	14:59	69	71	67	0.3	Fine
09-Apr-19	8:31	68	70	67	0.1	Fine
15-Apr-19	12:00	72	76	68	0.4	Cloudy
18-Apr-19	13:00	68	71	65	0.3	Cloudy
24-Apr-19	9:15	73	76	72	0.0	Sunny
30-Apr-19	9:30	70	72	68	1.6	Cloudy
	Max	73				
	Min	68				
	Limit Level	75				

Note:

KTD1a: Façade Measurement

KTD2b & KER1b: Free-field measurement (+3dB(A) correction has been applied)

No raining or wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.

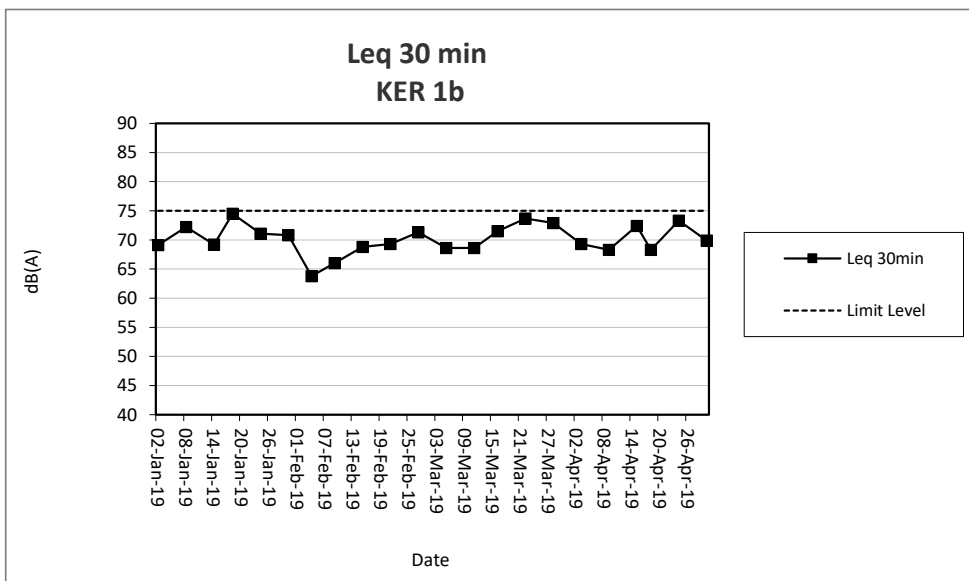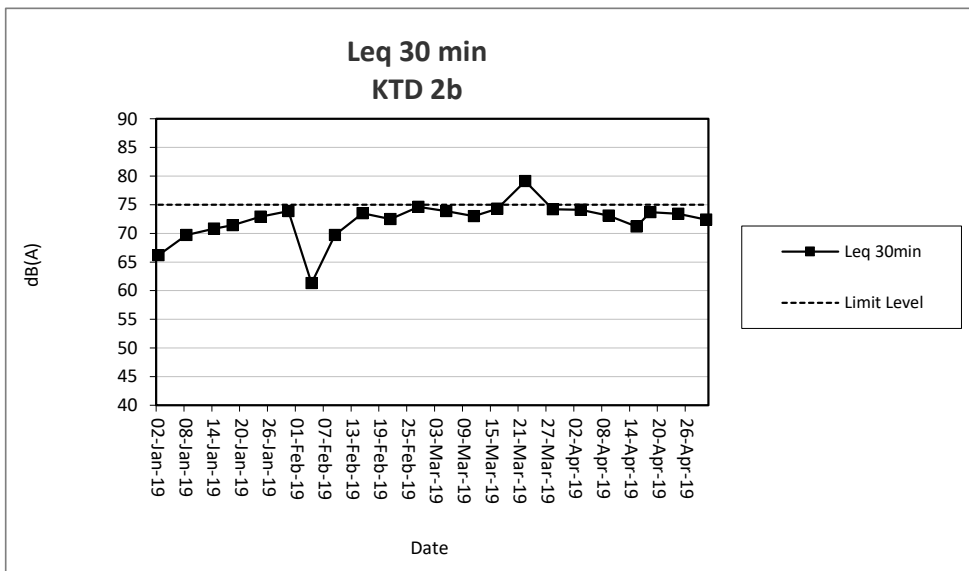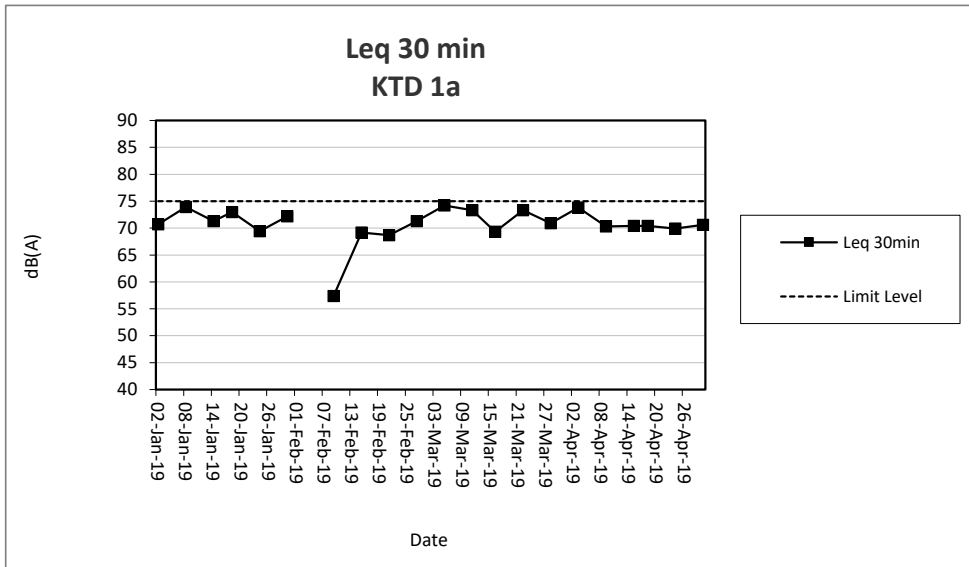

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
- 2) The weather conditions during the reporting period can be referred to Appendix K.
- 3) Any other factors which might affect the monitoring results can be referred to Section 3.7.2.
- 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.
- 5) Impact noise monitoring was not conducted at KTD1a due to the site was closed on 4 February 2019.
