

**Noise Impact Monitoring Result for
Kai Tak Development - Stage 3 Infrastructure Works for
Developments at the Southern Part of the Former Runway**

KTD 1a: Centre of Excellence in Paediatrics (Children's Hospital)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
3-Apr-20	15:20	71	72	67	0.4	Cloudy
9-Apr-20	09:00	69	70	66	0.6	Fine
15-Apr-20	09:08	69	72	66	0.3	Fine
21-Apr-20	10:47	68	70	65	1.0	Sunny
27-Apr-20	09:30	68	71	63	0.3	Sunny
	Max	71				
	Min	68				
	Limit Level	75				

***KTD 2b: G/IC Zone next to Kwun Tong Bypass (Next to the site of the New Acute Hospital) /**

KTD 2c: G/IC Zone next to Kwun Tong Bypass (Next to the Kowloon Bay Sewage Interception Station)

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
3-Apr-20	15:59	68	70	64	0.2	Cloudy
9-Apr-20	10:31	75	76	72	0.5	Fine
15-Apr-20	10:43	73	74	71	0.2	Fine
21-Apr-20	09:51	70	72	66	0.0	Sunny
27-Apr-20	11:04	68	69	67	0.9	Sunny
	Max	75				
	Min	68				
	Limit Level	75				

KER 1b: Site Boundary at Cheung Yip Street

Date	Start Time	Leq 30min dB(A)	L10 dB(A)	L90 dB(A)	Wind Speed (m/s)	Weather
3-Apr-20	14:45	69	72	66	0.9	Cloudy
9-Apr-20	09:42	71	72	66	0.3	Fine
15-Apr-20	09:48	74	79	70	0.2	Fine
21-Apr-20	11:26	68	69	67	0.8	Sunny
27-Apr-20	10:12	72	75	69	0.8	Sunny
	Max	74				
	Min	68				
	Limit Level	75				




Note:

KTD1a: Façade Measurement

KTD2b, KTD2c & KER1b: Free-field measurement (+3dB(A) correction has been applied)

No raining or wind with speed over 5 m/s was observed during noise monitoring according to the onsite observation.

*KTD 2b was relocated to KTD 2c on 8 April 2020

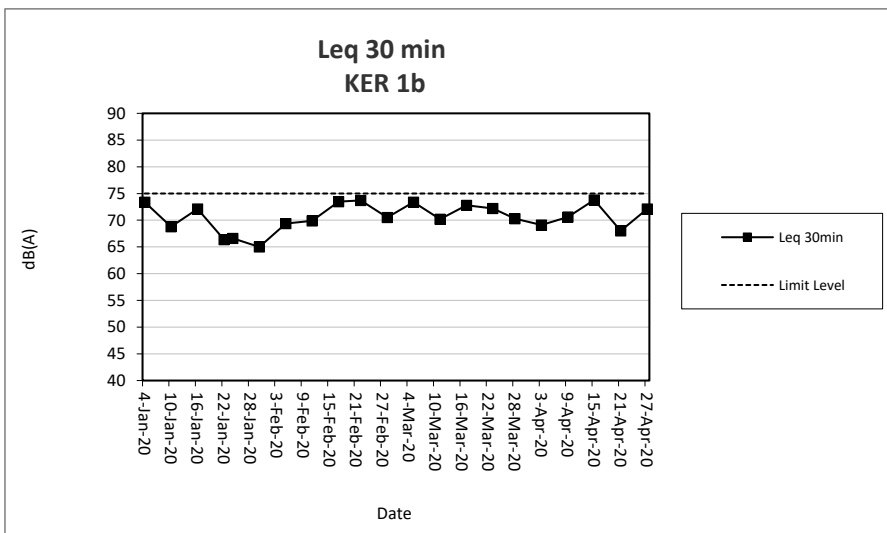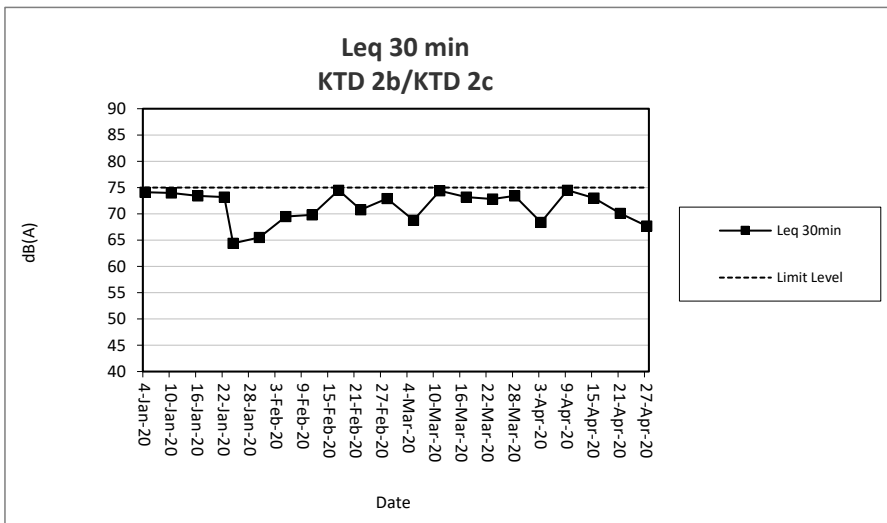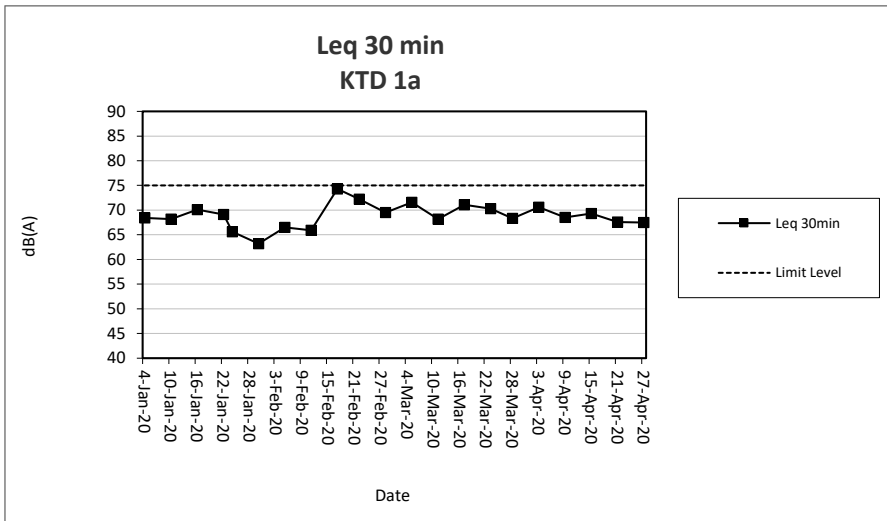

Note:

- 1) The major activities being carried out on site during the reporting period can be referred to Section 1.3.2.
- 2) The weather conditions during the reporting period can be referred to Appendix K.
- 3) Any other factors which might affect the monitoring results can be referred to Section 3.7.2.
- 4) QA/QC results, calibration results and detection limits can be referred to Appendix D.
- 5) KTD 2b was relocated to KTD 2c on 8 April 2020
