

Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CKL1 - Flat 121 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
8-Jan-26	17:00	Sunny	72.6	76.6	61.8	72.4	59
14-Jan-26	9:45	Fine	73.4	76.9	60.6	72.4	67
20-Jan-26	10:53	Cloudy	76.3	80.2	64.9	72.4	74
26-Jan-26	9:06	Sunny	76.6	80.2	63.3	72.4	75



Location CKL2 - Flat 103 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
8-Jan-26	16:25	Sunny	74.0	77.8	62.8	71.4	71
14-Jan-26	10:20	Fine	73.4	77.0	60.9	71.4	69
20-Jan-26	11:24	Cloudy	76.2	79.5	62.4	71.4	74
26-Jan-26	9:37	Fine	76.0	80.0	63.2	71.4	74

Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
8-Jan-26	14:50	Sunny	69.8	70.8	67.4	78.0	69.8 Measured ≤ Baseline
14-Jan-26	12:50	Fine	68.9	70.2	67.1	78.0	68.9 Measured ≤ Baseline
20-Jan-26	13:43	Fine	69.2	70.8	67.1	78.0	69.2 Measured ≤ Baseline
26-Jan-26	11:37	Fine	68.6	70.8	66.3	78.0	68.6 Measured ≤ Baseline

Location KER1 - Future Residential Development at Kerry Godown							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
8-Jan-26	15:30	Sunny	73.5	75.7	67.6	65.0	73
14-Jan-26	12:05	Fine	72.7	75.1	70.0	65.0	72
20-Jan-26	12:57	Cloudy	72.6	76.7	66.8	65.0	72
26-Jan-26	10:42	Fine	73.7	74.6	68.8	65.0	73




Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
8-Jan-26	13:45	Sunny	60.3	62.1	56.5	64.0	60 Measured ≤ Baseline
14-Jan-26	13:50	Fine	65.2	66.6	58.4	64.0	59
20-Jan-26	14:39	Fine	69.5	74.9	57.0	64.0	68
26-Jan-26	13:15	Fine	66.4	71.3	56.7	64.0	63

Noise Levels

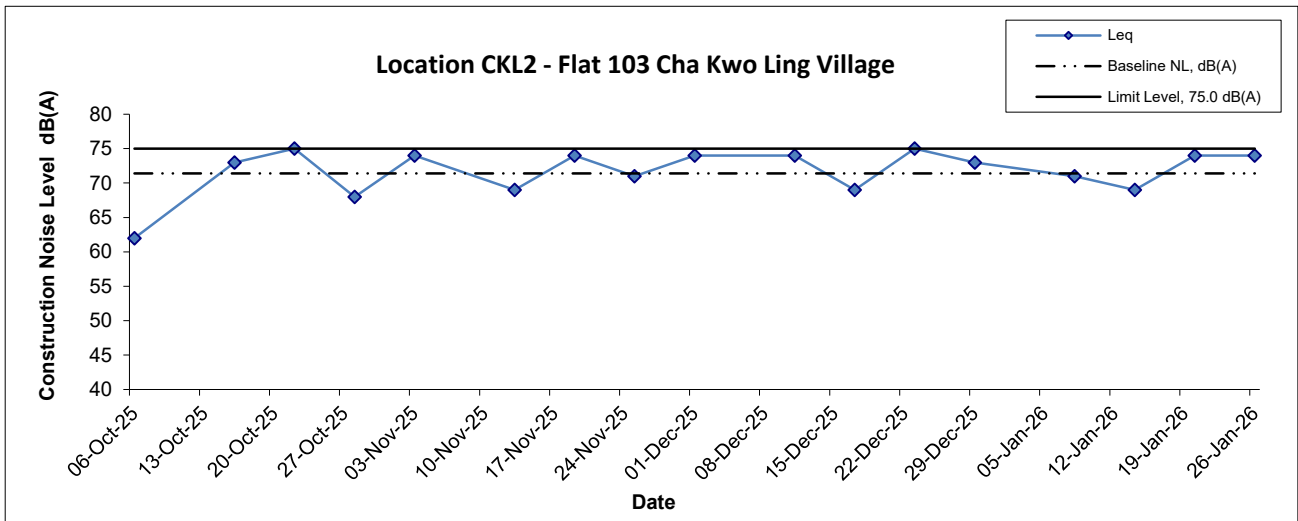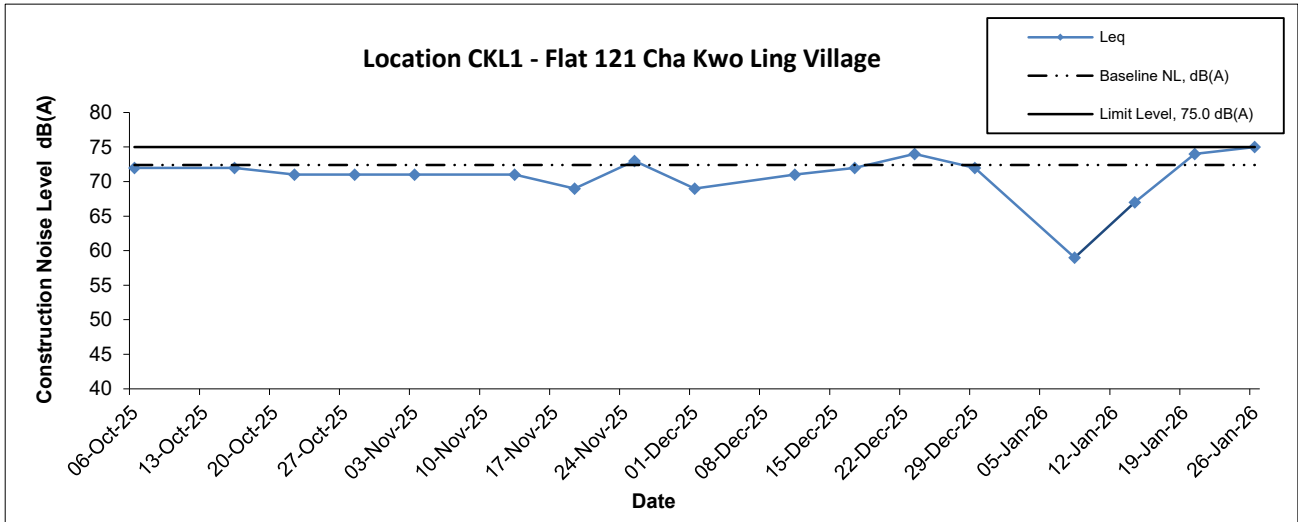

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date	Project	CINOTECH
	Jan 26	No. MA20003	
		Appendix H	

Noise Levels

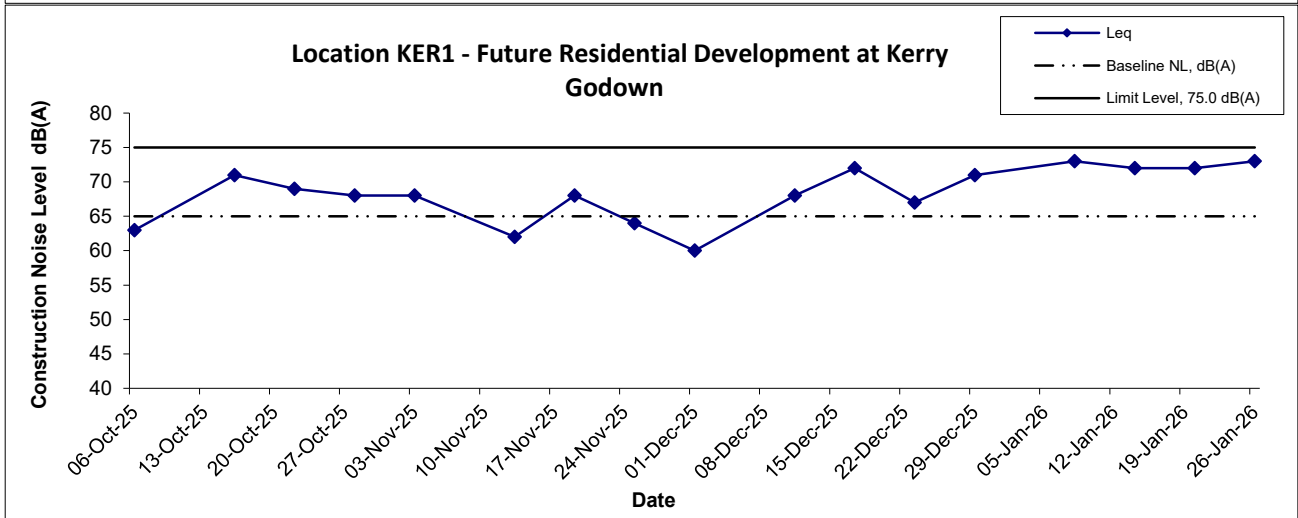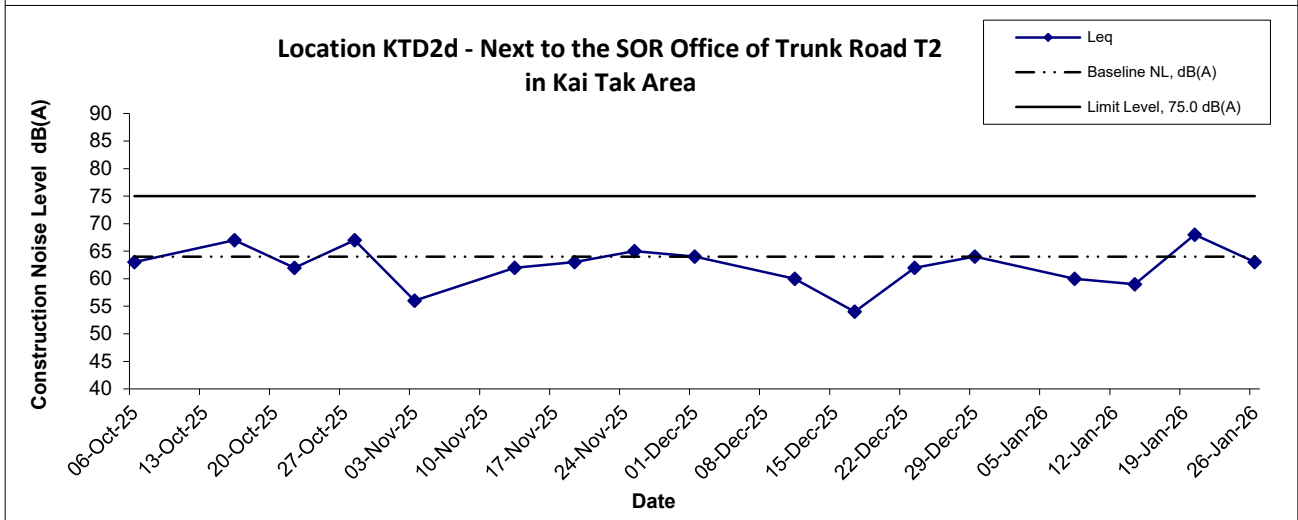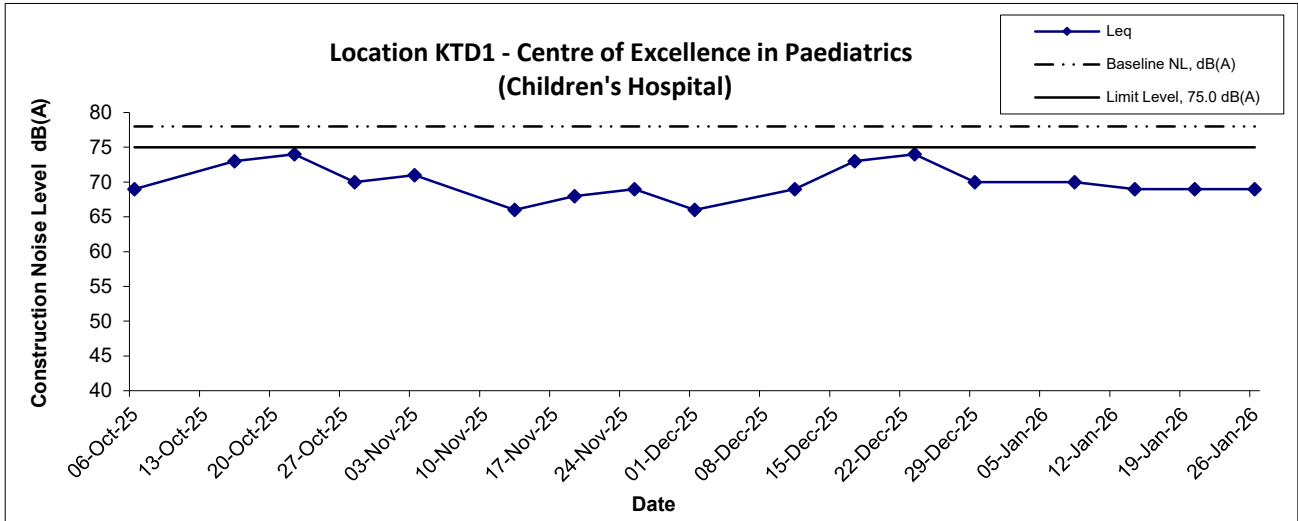

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date Jan 26	Project No. MA20003	
		Appendix H	
