

Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
4 Jul 2025	9:45	Sunny	63.7	65.1	61.6	65.5	64 Measured $\leq$ Baseline
9 Jul 2025	13:45	Cloudy	68.4	70.0	66.4	65.5	65
15 Jul 2025	13:40	Sunny	69.1	70.4	67.7	65.5	67
21 Jul 2025	9:00	Cloudy	70.3	73.7	66.8	65.5	69
31 Jul 2025	16:00	Sunny	69.9	73.1	64.2	65.5	68


Location CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
4 Jul 2025	9:00	Sunny	64.9	66.5	63.1	63.6	59
9 Jul 2025	10:30	Cloudy	68.4	69.4	67.1	63.6	67
15 Jul 2025	13:00	Sunny	68.0	69.2	66.6	63.6	66
21 Jul 2025	9:50	Cloudy	70.5	73.7	66.4	63.6	70
31 Jul 2025	9:00	Sunny	69.7	73.4	63.3	63.6	68

Location CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
4 Jul 2025	10:30	Sunny	64.8	65.8	62.4	65.6	65 Measured $\leq$ Baseline
9 Jul 2025	14:50	Cloudy	66.2	67.8	64.3	65.6	57
15 Jul 2025	12:15	Sunny	66.5	67.8	65.1	65.6	59
21 Jul 2025	10:40	Cloudy	70.1	73.3	65.4	65.6	68
31 Jul 2025	11:00	Sunny	70.2	73.9	65.4	65.6	68

Location CM4 - Tin Hau Temple, Cha Kwo Ling							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
4 Jul 2025	13:30	Sunny	54.6	57.1	50.5	62.0	55 Measured $\leq$ Baseline
9 Jul 2025	17:10	Cloudy	57.2	59.6	53.7	62.0	57 Measured $\leq$ Baseline
15 Jul 2025	10:45	Sunny	59.6	61.7	56.5	62.0	60 Measured $\leq$ Baseline
21 Jul 2025	14:00	Cloudy	63.7	66.9	57.9	62.0	59
31 Jul 2025	14:00	Sunny	63.7	68.1	59.4	62.0	59


Location CM5 - CCC Kei Faat Primary School, Yau Tong							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
4 Jul 2025	14:05	Sunny	63.4	66.2	59.5	68.2	63 Measured $\leq$ Baseline
9 Jul 2025	16:00	Cloudy	67.2	69.6	63.6	68.2	67 Measured $\leq$ Baseline
15 Jul 2025	11:30	Sunny	67.6	70.1	63.9	68.2	68 Measured $\leq$ Baseline
21 Jul 2025	11:30	Cloudy	67.7	70.9	63.6	68.2	68 Measured $\leq$ Baseline
31 Jul 2025	13:00	Sunny	67.5	70.6	63.1	68.2	68 Measured $\leq$ Baseline

Noise Levels

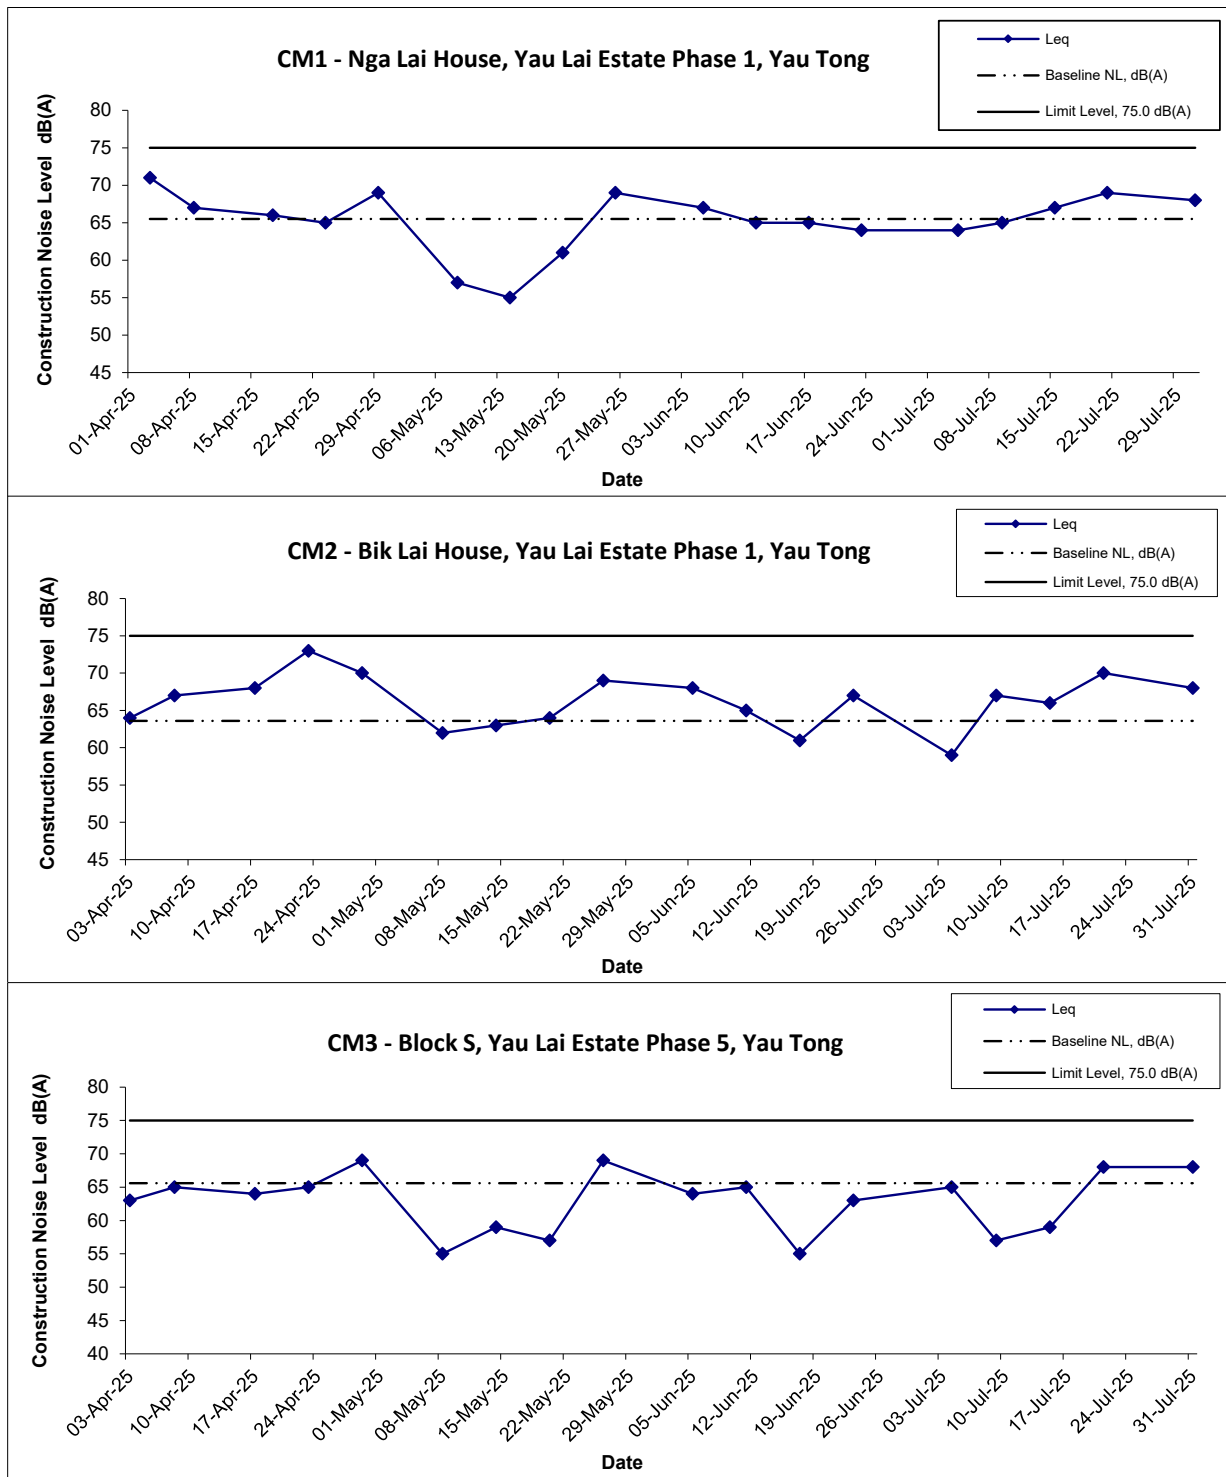

Title	Contract No. ED/2018/04	Scale	Project	CINOTECH
	Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron	N.T.S	No. MA20003	
	Graphical Presentation of Construction Noise Monitoring Results	Date	Appendix	
		July 25	G	

Noise Levels

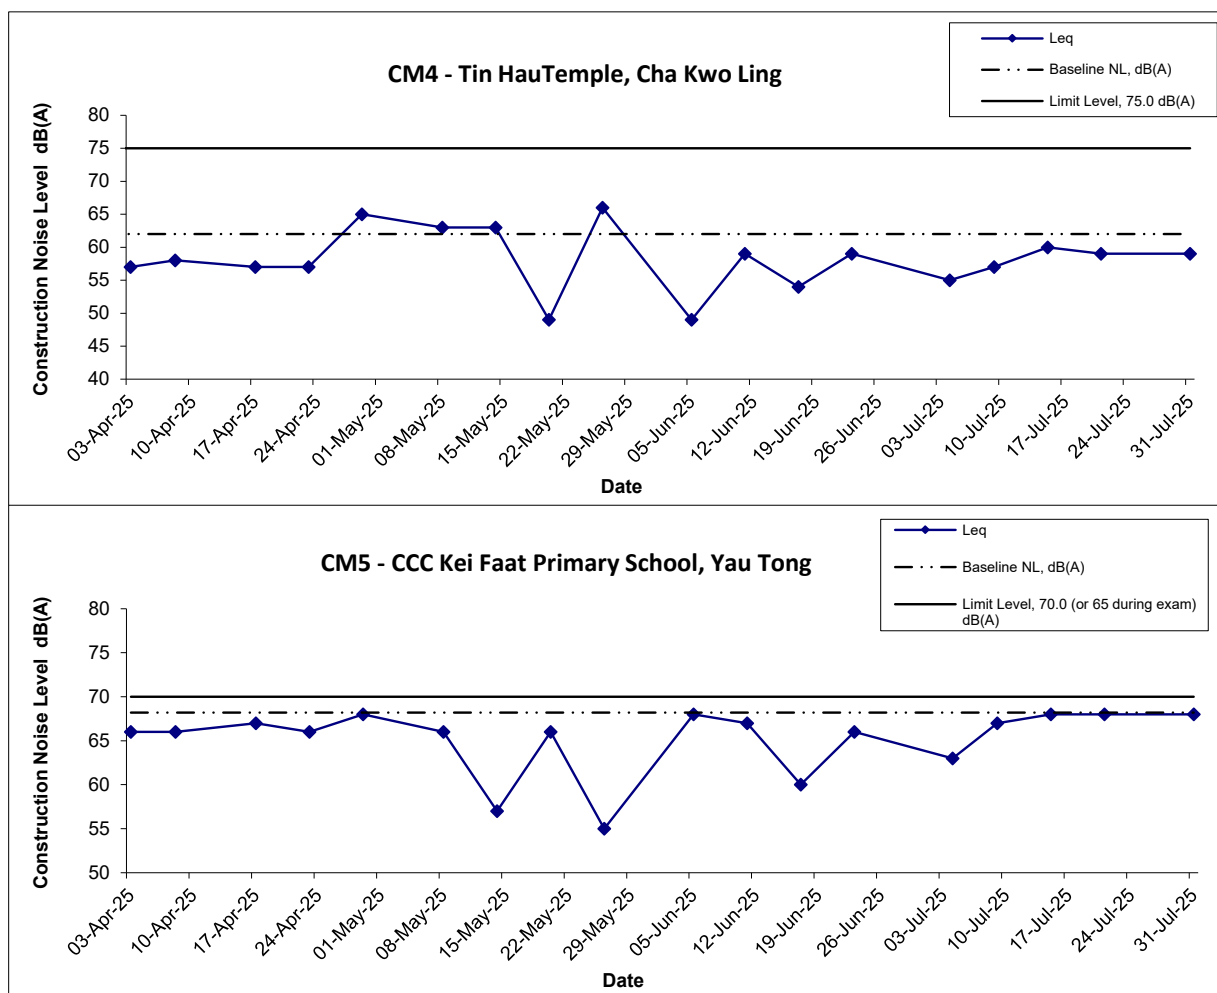

Notes:

- 1) The major activitie(s) being carried out on site during the reporting period is/are presented in Section 1.10
- 2) The weather conditions during the reporting month are presented in Appendix C.
- 3) Other factors which might affect the monitoring results are presented in Section 3.13.

Title Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA20003	
	Date July 25	Appendix G	
